



Government of India
Ministry of Statistics and
Programme Implementation



OCMS

Ministry of Statistics & Programme Implementation



466th

Flash Report on Central Sector Infrastructure Projects

(Rs. 150 crore
& above)

(Part - I)*

Synopsis

August 2024

*Refer Part-II for tables comprising detailed project listing.



www.mospi.gov.in



@GoIStats



/GoIStats

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects (1783, Rs. 27,38,539.25 crore)

Mega*
(620 projects,
Rs. 22,21,461.55
crore)

Major*
(1163 projects,
Rs. 5,17,077.70
crore)

Completed@
projects during
August 2024
(16 projects,
Rs. 12772.92
crore)








**Newly Added/
elevated\$**
Projects during
August 2024
(16 projects,
Rs. 15663.95
crore)

Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
other Indicated legends are in format (Project count, Original Cost)


* Mega Project if having original cost $\geq$ Rs. 1000 crore

* Major Project if original cost < Rs. 1000 crore

\$ reported Anticipated cost more than Rs. 150 crore

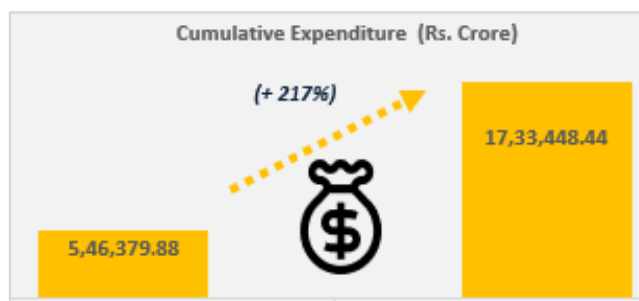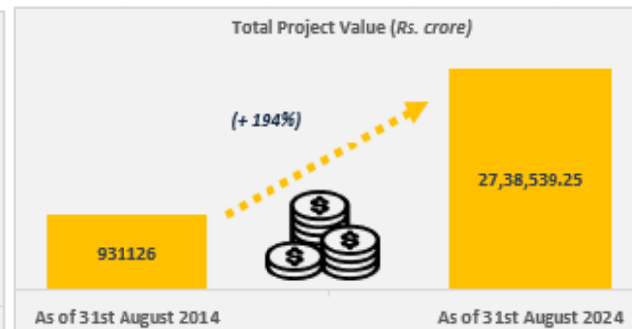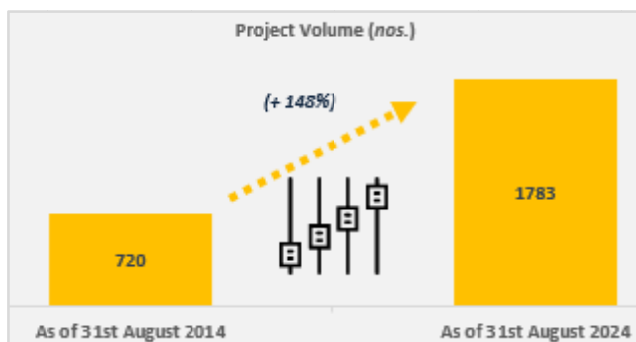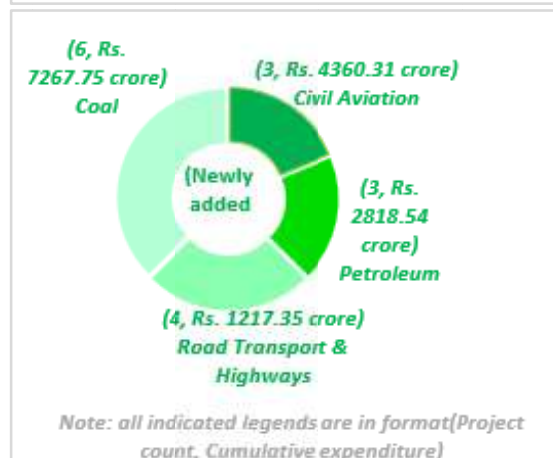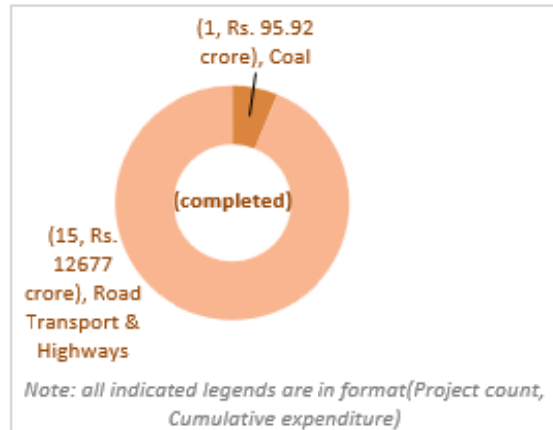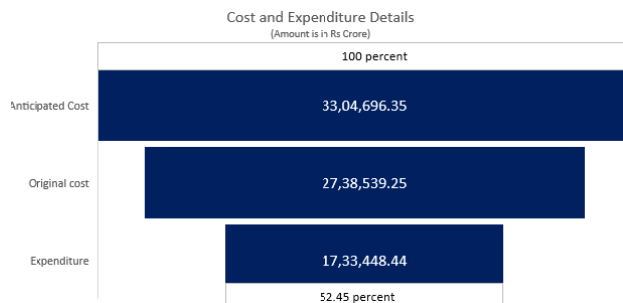


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

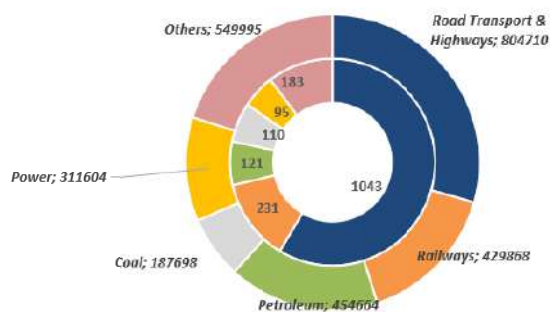


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

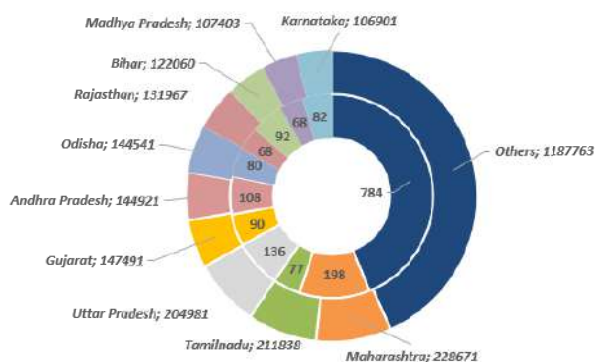

*Others include Jharkhand, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Assam, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N

Sectoral Distribution of total 641 projects with reported Physical Progress between 80-100%

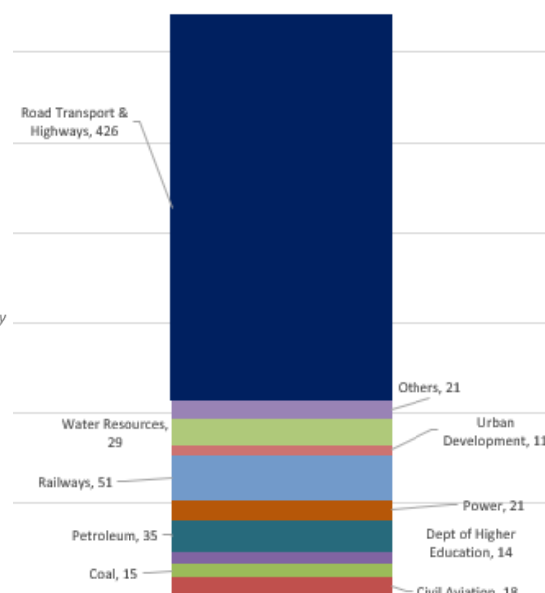

Note: This report is as of August 2024, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/ implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th September 2024



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
