

**453th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
July, 2023**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for July 2023 contains information on the status of the 1646 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, out of 1646 projects, 12 projects (11 projects of Road and 1 project of Telecommunications Sectors) are added and 7 projects (4 projects of Road and 3 projects of Petroleum Sectors) are completed. Total of 809 projects are delayed with respect to their original schedules and 213 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 213 projects, 43 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

EXECUTIVE SUMMARY COSTING Rs.		150	Crore and above	
Sl.No.	Sector	Projects on Monitor	Delayed Projects w.r.t original schedule	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	972	419	161
2	PETROLEUM	148	81	10
3	RAILWAYS	148	98	9
4	COAL	123	51	3
5	POWER	89	55	14
6	WATER RESOURCES	41	25	4
7	CIVIL AVIATION	27	22	4
8	URBAN DEVELOPMENT	26	16	0
9	DEPARTMENT OF HIGHER EDUCATION	21	13	4
10	STEEL	8	5	1
11	HEALTH AND FAMILY WELFARE	8	4	0
12	MINES	7	7	0
13	ATOMIC ENERGY	5	4	0
14	TELECOMMUNICATIONS	5	3	0
15	HOME AFFAIRS	5	4	2
16	FINANCE	3	0	0
17	FERTILISERS	2	0	0
18	DPIIT	2	1	1
19	SHIPPING AND PORTS	1	1	0
20	SOCIAL JUSTICE	1	0	0
21	DEFENCE PRODUCTION	1	0	0
22	COMMERCE	1	0	0
23	DONER	1	0	0
24	RENEWABLE ENERGY	1	0	0
Total		1643	809	213

3. Total original cost of implementation of the 1646 projects was ₹23,92,837.89 crore and their anticipated completion cost is likely to be ₹28,58,394.39 crore, which reflects overall cost overruns of ₹4,65,556.50 crore (19.46% of original cost). The expenditure incurred on these projects till July 2023 is ₹15,21,550.38 crore, which is 53.23% of the anticipated cost of the projects. The information can be viewed graphically as:

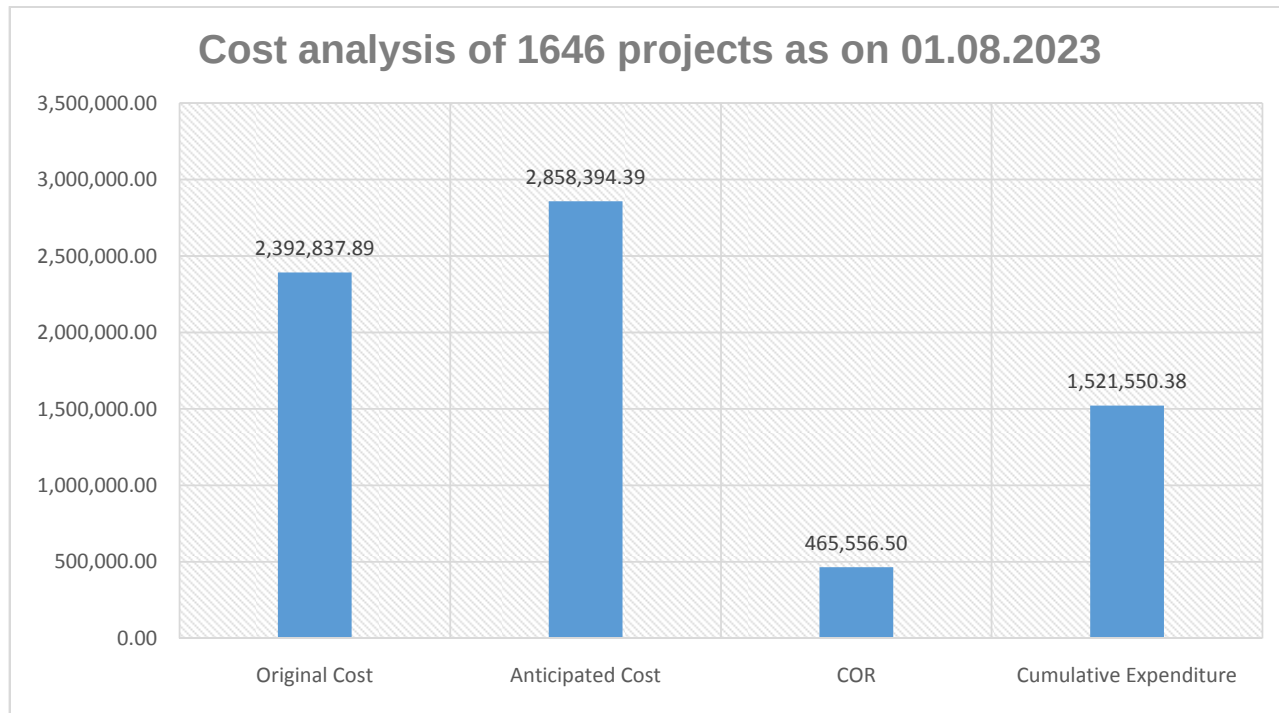


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.

5. Out of the 1646 projects, 17 projects are ahead of schedule, 475 are on schedule, 809 are delayed, 388 projects reported cost overrun and 253 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 602 if delay is calculated on the basis of latest schedule of completion. Further, for 345 projects neither the year of commissioning nor the tentative gestation period has been reported.


Status of projects (as on 01.08.2023)

(All the figures corresponds to number of project)

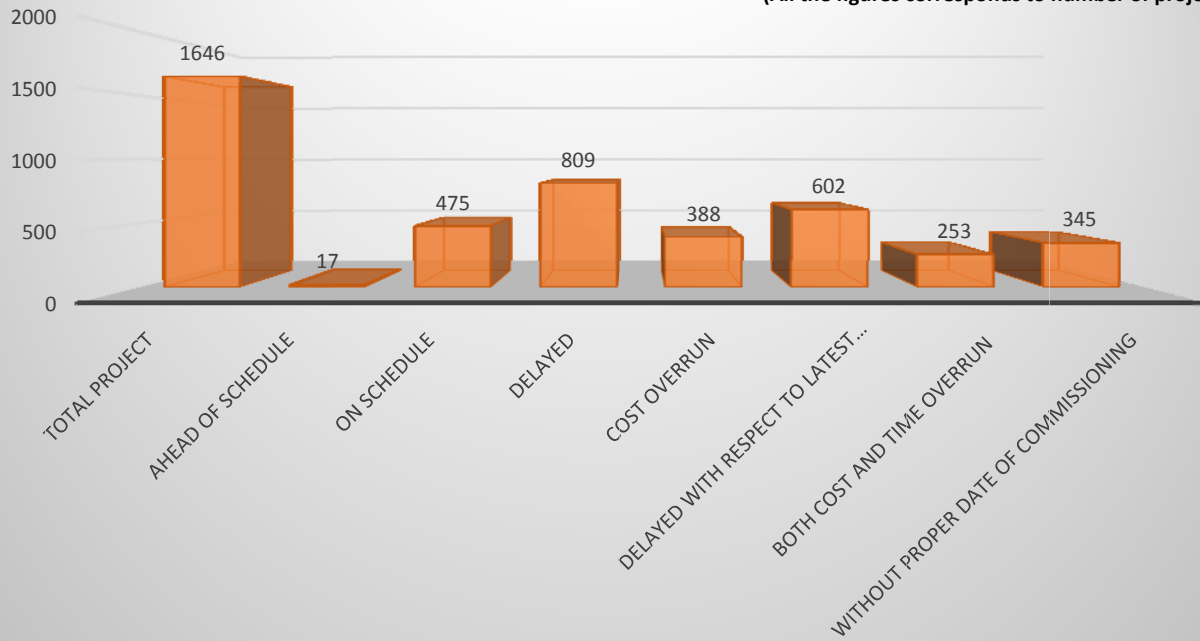


6. Out of 809 delayed projects, 177 (22%) projects have overall delay in the range of 1 to 12 months, 192 (24%) projects have delay in the range of 13 to 24 months, 318 (39%) projects have delay in the range of 25 to 60 months and 122 (15%) projects have delay of more than 60 months. The above information can be viewed graphically as shown below:

BREAK UP OF 809 DELAYED PROJECTS IN MONTHS

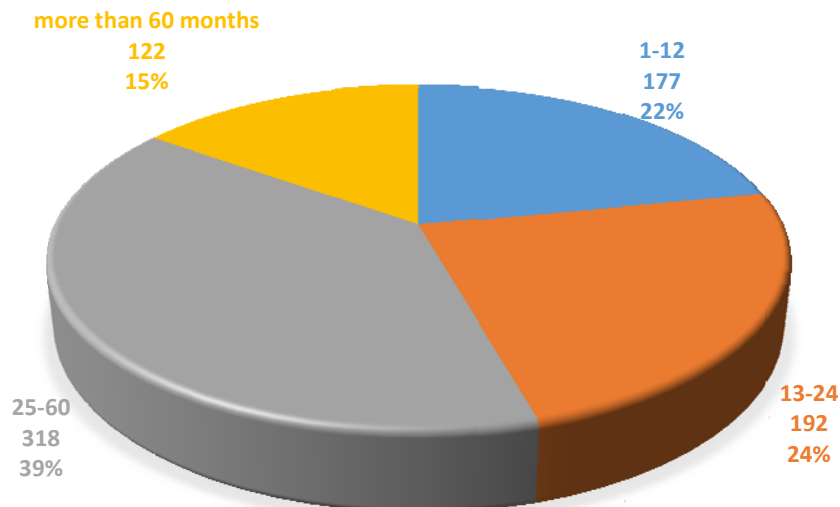

7. The status of online reporting of projects can be viewed month wise as:

The average time overrun in these 809 delayed projects is 37.44 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

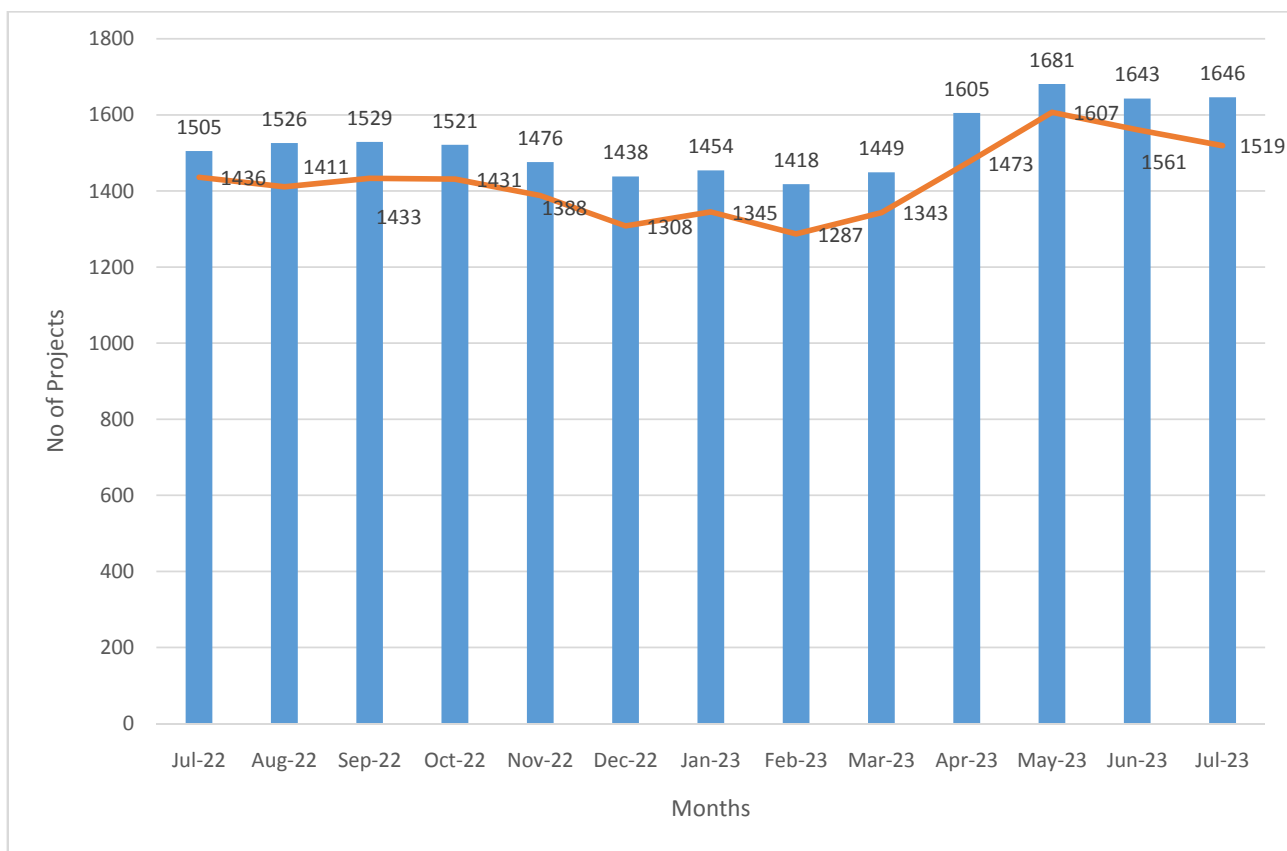

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19
- Litigation (NGT).

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project

agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures may be under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-08-2023)**

SN	PROJECT	DATE OF APPROVAL	COST ORIGINAL (Rs in crore)	COST ANTICIPATED (Rs in crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3,492	7,670	120
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11,459	19,220	68
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12,320	17,079	39
	CIVIL AVIATION				
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1,383	3,292	138
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417	708	70
6	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01	03/2021	242	328	35
7	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	480	640	33
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	304	351	16
	COAL				
9	HURA - C OC (3 MTY)	10/2015	360	859	139
10	RANIGANJ MASTER PLAN	08/2009	2,662	5,146	93
11	ANANTA OCP EXPANSION PH III	08/2008	228	398	75
12	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5,907	8,990	52
13	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243	334	38
	DEPARTMENT OF HIGHER EDUCation				
14	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676	1,085	61
15	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	304	364	20
16	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	09/2018	393	446	14
17	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	01/2018	223	230	3
	DPIIT				
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4,773	5,401	13
	FINANCE				
19	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	209	262	25
	HEALTH AND FAMILY WELFARE				
20	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	210	273	30
	HOME AFFAIRS				
21	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1,219	1,900	56
22	NSG AT KOLKATA	10/2014	163	211	29
23	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277	290	5
	MINES				
24	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	355	581	64

25	UTKAL D AND E COAL BLOCK	05/2016	534	667	25
26	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4,103	5,055	23
	PETROLEUM				
27	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678	1,732	155
28	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2,915	5,909	103
29	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	04/2018	207	341	65
30	NUMALIGARH REFINERY EXPANSION PROJECT 6 MTPA REFINERY	01/2019	12,366	18,968	53
31	DEVANGONTHI MARKETING TERMINAL	06/2020	200	304	52
	POWER				
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6,285	21,248	238
33	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1,657	4,826	191
34	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3,920	11,135	184
35	BARH STPP(3X660MW) NTPC	02/2005	8,693	21,312	145
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2,978	7,103	138
	RAILWAYS				
37	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	248	8,249	3,231
38	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	121	2,053	1,601
39	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2,500	37,012	1,380
40	NEW BG LINE FROM BYRNIHAT TO SHILLONG	04/2010	906	8,324	818
41	RAMGANJMUUNDI-BHOPAL (NL),WCR	04/2001	425	3,032	614
	RENEWABLE ENERGY				
42	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	272	366	35
	ROAD TRANSPORT AND HIGHWAYS				
43	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	667	3,007	351
44	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	218	884	306
45	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	01/2016	1,028	2,628	156
46	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	09/2020	183	440	140
47	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	03/2018	479	1,137	137
	STEEL				
48	NMDC INTEGRATED STEEL PLANT	01/2010	15,525	23,840	54
49	SCREENING PLANT-III AT KIRANDUL	03/2021	2,093	2,222	6
	URBAN DEVELOPMENT				
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23,136	37,276	61
51	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14,600	18,380	26
52	KOCHI METRO RAIL PROJECT	07/2012	5,182	6,218	20
53	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10,773	12,925	20
54	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11,420	13,656	20
	WATER RESOURCES				
55	POLAVARAM IRRIGATION PROJECT	02/2009	10,151	55,549	447
56	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	08/2017	307	654	113
57	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	226	399	77
58	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254	413	63
59	SAIDPUR SEWER NETWORK PATNA	04/2015	269	431	61

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)****(as on 01-08-2023)**

SN	PROJECT	DATE OF APPROVAL	COST ORIGINAL (Rs in crore)	COST ANTICIPATED (Rs in crore)	COR (Rs in crore)
	ATOMIC ENERGY				
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11,459	19,220	7,761
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12,320	17,079	4,759
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3,492	7,670	4,178
	CIVIL AVIATION				
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1,383	3,292	1,909
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417	708	291
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	480	640	160
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1,142	1,232	90
8	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01	03/2021	242	328	86
	COAL				
9	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5,907	8,990	3,083
10	RANIGANJ MASTER PLAN	08/2009	2,662	5,146	2,485
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17,237	19,406	2,169
12	HURA - C OC (3 MTY)	10/2015	360	859	500
13	ANANTA OCP EXPANSION PH III	08/2008	228	398	170
	DEPARTMENT OF HIGHER EDUCation				
14	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676	1,085	409
15	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	304	364	60
16	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	09/2018	393	446	54
17	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	01/2018	223	230	7
	DPIIT				
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4,773	5,401	628
	FINANCE				
19	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	209	262	53
	HEALTH AND FAMILY WELFARE				
20	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	210	273	63
	HOME AFFAIRS				
21	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1,219	1,900	681
22	NSG AT KOLKATA	10/2014	163	211	48
23	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277	290	13
	MINES				
24	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4,103	5,055	952
25	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	355	581	226

26	UTKAL D AND E COAL BLOCK	05/2016	534	667	133
	PETROLEUM				
27	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINERY	01/2019	12,366	18,968	6,602
28	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20,928	26,264	5,336
29	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2,915	5,909	2,994
30	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4,497	6,025	1,528
31	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678	1,732	1,054
	POWER				
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6,285	21,248	14,962
33	BARH STPP(3X660MW) NTPC	02/2005	8,693	21,312	12,619
34	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3,920	11,135	7,215
35	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4,754	9,129	4,375
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2,978	7,103	4,125
	RAILWAYS				
37	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11,589	51,219	39,630
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2,500	37,012	34,512
39	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16,592	51,101	34,509
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4,454	14,323	9,869
41	RISHIKESH - KARNAPRAYAG NEW LINE	04/2011	16,216	24,659	8,443
	RENEWABLE ENERGY				
42	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	272	366	94
	ROAD TRANSPORT AND HIGHWAYS				
43	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	667	3,007	2,340
44	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU	07/2020	2,272	3,916	1,644
45	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	01/2016	1,028	2,628	1,601
46	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1,587	3,064	1,477
47	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX.	06/2021	2,595	3,995	1,400
	STEEL				
48	NMDC INTEGRATED STEEL PLANT	01/2010	15,525	23,840	8,315
49	SCREENING PLANT-III AT KIRANDUL	03/2021	2,093	2,222	129
	URBAN DEVELOPMENT				
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23,136	37,276	14,140
51	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14,600	18,380	3,780
52	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11,420	13,656	2,236
53	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10,773	12,925	2,152
54	DELHI MRTS PHASE-III	09/2011	38,585	40,181	1,596
	WATER RESOURCES				
55	POLAVARAM IRRIGATION PROJECT	02/2009	10,151	55,549	45,398
56	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	08/2017	307	654	347
57	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	226	399	173
58	SAIDPUR SEWER NETWORK PATNA	04/2015	269	431	163
59	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254	413	159

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-08-2023)**

SN	PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING	TOR (in month)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	12/2024	171
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	03/2024	99
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	12/2023	84
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2023	57
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	03/2021	03/2025	48
7	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	12/2025	46
8	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	10/2023	44
9	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	08/2023	41
COAL					
10	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2024	156
11	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	04/2013	06/2015	09/2027	147
12	KARTALI (EAST) OCP (2.50 MTY)	07/2008	03/2014	03/2026	144
13	MURAI DIH UG TURN-KEY PROJECT	02/2011	04/2014	10/2025	138
14	KARMA OCP (1.0MTY)	06/2009	03/2014	03/2024	120
DEFENCE PRODUCTION					
15	RESIDENTIAL QUATERS FOR HAL, BANGLORE	12/2016	02/2020	03/2023	37
DEPARTMENT OF HIGHER EDUCATION					
16	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	12/2023	111
17	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	10/2023	76
18	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	01/2018	07/2020	09/2023	38
19	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	01/2018	05/2020	06/2023	37
20	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	03/2020	06/2020	07/2023	37
DPIIT					
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	09/2023	45

	FINANCE				
22	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	10/2022	36
23	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021	11/2022	12
	HEALTH AND FAMILY WELFARE				
24	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	06/2021	08/2025	50
25	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	05/2017	05/2021	10/2023	29
26	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR	12/2018	07/2024	10/2024	3
27	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	03/2019	09/2023	10/2023	1
	HOME AFFAIRS				
28	NSG AT KOLKATA	10/2014	04/2018	12/2024	80
29	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	12/2023	50
30	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	07/2022	05/2024	22
31	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAUJI	05/2019	01/2022	03/2023	14
32	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)"	01/2020	10/2023	03/2024	5
	MINES				
33	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	09/2025	58
34	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	12/2023	54
35	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	03/2025	47
36	UTKAL D AND E COAL BLOCK	05/2016	01/2020	11/2023	46
37	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	04/2019	04/2022	10/2025	42
	PETROLEUM				
38	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	11/2024	143
39	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	01/2026	107
40	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	04/2018	05/2026	97
41	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	03/2019	12/2024	69
42	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	06/2019	02/2025	68
	POWER				
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	05/2025	176
44	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2024	174
45	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	06/2026	156
46	BARH STPP(3X660MW) NTPC	02/2005 ¹⁶	10/2011	07/2024	153

47	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	12/2024	141
	RAILWAYS				
48	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	01/2024	254
49	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	03/2009	03/2027	216
50	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	03/2009	12/2026	213
51	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	05/2008	03/2025	202
52	MANOHARABAD-KOTHPALL NEW LINE(SCR)	04/2006	03/2010	03/2025	180
	RENEWABLE ENERGY				
53	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	04/2022	29
	ROAD TRANSPORT AND HIGHWAYS				
54	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	06/2023	152
55	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	06/2023	152
56	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	03/2011	06/2023	147
57	PATNA-MUZZAFFARPUR	08/2010	02/2013	06/2023	124
58	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	12/2023	124
	SHIPPING AND PORTS				
59	JAL MARG VIKAS PROJECT	01/2018	03/2023	12/2026	45
	STEEL				
60	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	08/2023	99
61	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	09/2025	95
62	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	06/2023	05/2025	23
63	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023	04/2025	16
64	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	05/2023	02/2024	9
	TELECOMMUNICATIONS				
65	NETWORK FOR SPECTRUM	03/2012	07/2015	09/2023	98
66	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	03/2018	12/2023	69
67	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	12/2023	30
	URBAN DEVELOPMENT				
68	DELHI MRTS PHASE-III	09/2011	03/2016	08/2021	65
69	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	12/2023	60
70	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2021	03/2025	49
71	BHOPAL METRO RAIL	11/2018	02/2023	12/2026	46
72	INDORE METRO RAIL	11/2018	02/2023	12/2026	46
	WATER RESOURCES				
73	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	08/2017	09/2022	12/2026	51
74	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER	03/2017 ¹⁷	12/2019	12/2023	48

	BRAHMAPUTRA				
75	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	03/2024	48
76	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	03/2024	42
77	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	03/2019	07/2021	04/2024	33

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-08-2023)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	COAL						
1	EPR ROHINI KARKATA OCP	01/2021	1,020	1,020	79	03/2025	03/2025
2	EXPANSION OF ASHOK OCP	05/2021	2,898	2,898	174	03/2026	03/2026
3	REVISED PROJECT REPORT MAGADH EXPANSION OCP	08/2020	7,254	7,254	902	03/2028	03/2028
4	EXPANSION PROJECT AMRAPALI OCP	08/2020	5,136	5,136	573	03/2028	03/2028
5	SONEPUR BAZARI EXPANSION OC	07/2021	5,366	5,366	316	03/2029	03/2029
	MINES						
6	POTTANGI BAUXITE MINES	05/2018	1,437	1,381	603	12/2024	05/2025
	POWER						
7	KIRU HYDRO ELECTRIC PROJECT	03/2019	4,288	4,288	1,169	08/2024	03/2026
8	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8,112	8,112	3,194	04/2020	09/2026
9	TEESTA VI HE PROJECT	03/2019	5,748	5,748	2,643	03/2024	08/2026
10	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	5,111	6,700	4,578	12/2018	01/2024
11	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	08/2017	1,931	2,636	1,953	02/2020	03/2024
	PETROLEUM						
12	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678	1,732	31	02/2017	01/2026
13	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL	04/2021	1,165	1,165	170	06/2024	07/2025
14	CITY GAS DISTRIBUTION NETWORK PROJECT AT SANGLI AND SATARA	04/2019	2,338	2,338	636	11/2028	11/2028
15	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	2,998	2,998	288	03/2030	03/2030
16	CGD PROJECT AT SALEM DISTRICT	10/2018	1,304	1,304	96	03/2030	03/2030
	HEALTH AND FAMILY WELFARE						
17	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	03/2019	1,404	1,404	96	09/2023	10/2023
18	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	03/2019	1,828	1,828	740	09/2025	09/2025
	RAILWAYS						
19	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	2,272	4,805	3,492	03/2021	03/2026
20	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF,	04/1991	329	1,510	2,103	N.A.	03/2024

21	PIRPAINTI-JASIDIH	04/2013	916	2,138	980	03/2022	03/2025
22	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	04/2010	2,398	2,398	197	03/2016	03/2016
23	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	2,923	3,792	2,904	03/2009	12/2026
ROAD TRANSPORT AND HIGHWAYS							
24	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	09/2011	1,979	2,037	1,253	N.A.	05/2023
25	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	01/2014	1,409	2,138	1,560	10/2016	11/2023
26	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	1,083	1,414	1,060	06/2018	08/2023
27	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	1,047	1,047	1,855	06/2014	12/2023
28	SIX-LANING OF BARWA ADDA-PANAGARH	04/2014	1,665	2,361	4,657	09/2016	12/2023
TELECOMMUNICATIONS							
29	NETWORK FOR SPECTRUM	03/2012	13,334	13,334	21,913	07/2015	09/2023
URBAN DEVELOPMENT							
30	KOCHI METRO RAIL PROJECT	07/2012	5,182	6,218	6,059	07/2017	09/2020
31	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23,136	37,276	24,124	03/2020	12/2023
32	NAGPUR METRO RAIL PROJECT PHASE II	12/2022	6,708	6,708	0	12/2027	12/2027
33	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11,420	13,656	10,829	11/2021	12/2023
34	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	1,128	1,128	166	03/2022	06/2024
DPIIT							
35	NATIONAL INDUSTRIAL CORRIDOR PROJECT	09/2011	20,084	20,084	9,683	03/2027	03/2027
36	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4,773	5,401	4,072	12/2019	09/2023

N.A.: Not Available.

Table-E

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates
(as on 01-08-2023)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	CIVIL AVIATION				
1	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	01/2019	390	0	392
	COAL				
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5,907	0	7,657
3	ANANTA OCP EXPANSION PH III	08/2008	228	0	398
4	MADHUBAND NLW WASHERY	08/2010	289	0	297
	FINANCE				
5	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	209	0	249
	POWER				
6	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1,657	0	5,601
7	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4,754	0	5,601
8	NAITWAR MORI HEP	10/2017	648	0	1,172
9	NORTH KARANPURA STPP (3X660 MW)	02/2014	14,367	0	14,881
10	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	01/2016	10,599	0	10,831
	RAILWAYS				
11	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16,592	0	47,476
12	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11,589	0	31,304
13	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	248	0	2,427
14	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	04/2010	3,952	0	5,943
15	SEVOK RANGPO, NEFR	04/2008	1,339	0	3,291
	ROAD TRANSPORT AND HIGHWAYS				
16	SIX-LANING OF BARWA ADDA-PANAGARH	04/2014	1,665	0	4,657
17	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	218	0	2,298
18	4-LANING OF BRAHAMPORE-FARAKA	02/2011	999	0	2,170
19	4LBERKHEDI TO GODPEHRA NH-44	02/2022	525	0	1,600
20	PATNA-MUZZAFFARPUR	08/2010	671	0	1,592
	TELECOMMUNICATIONS				
21	NETWORK FOR SPECTRUM	03/2012	13,334	0	21,913
	URBAN DEVELOPMENT				

22	DELHI MRTS PHASE-III	09/2011	38,585	0	40,217
23	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10,773	0	11,787
24	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23,136	0	24,124
25	KOCHI METRO RAIL PROJECT	07/2012	5,182	0	6,059
WATER RESOURCES					
26	POLAVARAM IRRIGATION PROJECT	02/2009	10,151	0	21,728
27	SAIDPUR SEWER NETWORK PATNA	04/2015	269	0	478
28	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	226	0	361

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-08-2023)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
2	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	09/2020	N.A.	09/2020
3	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	09/2020	N.A.	09/2020
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	09/2019
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	12/2019
COMMERCE					
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	10/2020
DEPARTMENT OF HIGHER EDUCATION					
7	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	N.A.	00/2016
8	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	03/2020	07/2022	N.A.	07/2022
9	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	10/2012
DONER					
10	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	N.A.	09/2017
FINANCE					
11	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021	N.A.	11/2022
12	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA	07/2018	04/2022	N.A.	04/2022
HEALTH AND FAMILY WELFARE					
13	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	03/2020	N.A.	N.A.
14	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	09/2017	03/2020	N.A.	03/2020
15	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	03/2018	09/2020	N.A.	09/2020

	POWER				
16	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	08/2017
	RAILWAYS				
17	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	04/2010	03/2017	N.A.	12/2022
18	BHADRACHALAM-KOVVUR	04/2012	N.A.	N.A.	N.A.
19	ROHTAK-MEHAM HANSI	04/2012	12/2011	N.A.	12/2011
20	NADIKUDE-SRI KALAHASTI	04/2011	03/2021	N.A.	03/2021
21	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	04/2008	03/2014	N.A.	03/2014
	ROAD TRANSPORT AND HIGHWAYS				
22	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	03/2015	01/2017	N.A.	00/2017
23	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	03/2015	N.A.	N.A.	12/2022
24	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	06/2015	N.A.	N.A.	N.A.
25	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	03/2015	N.A.	N.A.	06/2019
26	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	N.A.	N.A.	N.A.
	URBAN DEVELOPMENT				
27	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	12/2015
	WATER RESOURCES				
28	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	03/2017	11/2019	N.A.	02/2022
29	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	05/2017	09/2021	N.A.	09/2021
30	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	01/2021	N.A.	03/2022
31	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	05/2020
32	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	04/2020	N.A.	04/2020

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	972	161
2	PETROLEUM	148	10
3	RAILWAYS	148	9
4	COAL	123	3
5	POWER	89	14
6	WATER RESOURCES	41	4
7	CIVIL AVIATION	27	4
8	URBAN DEVELOPMENT	26	0
9	DEPARTMENT OF HIGHER EDUCATION	21	4
10	STEEL	8	1
11	HEALTH AND FAMILY WELFARE	8	0
12	MINES	7	0
13	ATOMIC ENERGY	5	0
14	TELECOMMUNICATIONS	5	0
15	HOME AFFAIRS	5	2
16	FINANCE	3	0
17	FERTILISERS	2	0
18	DPIIT	2	1
19	SHIPPING AND PORTS	1	0
20	SOCIAL JUSTICE	1	0
21	DEFENCE PRODUCTION	1	0
22	COMMERCE	1	0
23	DONER	1	0
24	RENEWABLE ENERGY	1	0
	Total	1646	213

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2023			
	<u>PETROLEUM</u>			
1	SITARGANJ LPG PROJECT Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000282]	160.10	02/2020	125.58
2	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR (INDIAN OIL CORPORATION LIMITED) - [N16000303]	318.80	08/2021	224.25
3	LPG BP PROJECT JODHPUR (INDIAN OIL CORPORATION LIMITED) - [N16000318]	229.80	-	165.84
4	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT (INDIAN OIL CORPORATION LIMITED) - [N16000336]	588.20	-	393.17
5	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000353]	598.00	02/2020	679.20
6	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000355]	286.42	08/2020	241.80
7	CITY GAS DISTRIBUTION NETWORK PROJECT AT RUPNAGAR Central Sector Projects(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000476]	172.70	06/2023	122.76
	<u>POWER</u>			
8	EASTERN REGION STRENGTHENING SCHEME-XII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000164]	522.29	11/2016	481.11
9	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000242]	322.30	02/2019	206.86
10	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000245]	379.95	12/2019	277.82
11	EASTERN REGION STRENGTHENING SCHEME-XVIII Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000258]	3,500.00	07/2020	3,183.32
12	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000301]	1,031.00	08/2021	1,024.67
13	NORTHERN REGION SYSTEM STRENGTHENING - XL (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000308]	572.98	12/2020	306.67
14	EASTERN REGION STRENGTHENING SCHEME - XXIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000315]	239.89	06/2021	167.56
	<u>HEALTH AND FAMILY WELFARE</u>			
15	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) (HLL Infra Tech Services Limited) - [N21000025]	785.00	04/2020	642.64
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2023-2024

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000616]	245.79	12/2019	188.33
17	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000690]	198.22	11/2020	164.05
18	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001182]	205.95	01/2021	164.00
19	SINNAR-SHIRDI (INCLUDING SINNAR BYPASS) PPP BOT (Hybrid Annuity)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001496]	1,026.00	08/2022	868.51
	<u>URBAN DEVELOPMENT</u>			
20	NAGPUR METRO RAIL (NAGPUR METRO RAIL CORPORATION LTD) - [N28000085]	8,680.00	03/2018	8,491.14
	May,2023			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
21	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000866]	404.17	02/2021	324.05
22	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001152]	160.00	09/2021	142.53
23	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001243]	166.94	12/2020	113.72
24	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001250]	278.46	03/2022	246.11
25	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001295]	347.78	03/2027	276.79
26	KAILASHAHAR TO KHOWAI PKG-2 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001311]	206.78	07/2022	197.72
27	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-08) (CH. 214.260 - CH. 247.31) [START OF ROB NEAR EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001577]	1,297.25	11/2022	950.33
28	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-8) EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001578]	580.79	10/2022	552.88
29	RASISAR (NEAR BIKANER)-DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-5) EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001583]	820.02	11/2021	405.35

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2023-2024

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
30	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (AJ/SR-PACKAGE-4) EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001585]	542.70	06/2022	444.17
	June,2023			
	<u>PETROLEUM</u>			
31	BOKARO-ANGUL PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000274]	3,437.00	12/2020	2,463.30
32	PIPELINE REPLACEMENT PROJECT (PRP-VI) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000370]	763.92	12/2020	830.87
33	SULPHUR FORMING UNIT IN SRU EPC(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000408]	210.94	08/2021	177.86
	<u>POWER</u>			
34	AMELIA COAL MINE Central Sector Projects(THDC INDIA LIMITED) - [N18000252]	2,104.21	09/2020	890.47
35	NOKHRA EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000282]	1,722.14	09/2021	1,710.02
	<u>HEALTH AND FAMILY WELFARE</u>			
36	LHMC NEW DELHI-RE-DEVELOPMENT (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000003]	414.11	11/2013	586.50
37	LGBRIMH-TEZPUR, ASSAM (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000007]	175.57	12/2014	179.15
38	AIIMS - MOTHER AND CHILD BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000008]	204.44	05/2017	285.00
39	AIIMS - OPD(NEW) (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000009]	293.65	05/2017	299.76
40	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000010]	168.90	05/2017	182.10
41	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000011]	505.58	03/2018	586.96
42	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000012]	152.95	02/2018	171.90
43	NEIGRIHMS SHILLONG MEGHALYA (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000013]	363.99	05/2018	321.00
44	CNCI KOLKATA WEST BENGAL (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000015]	244.00	09/2018	224.92
45	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000016]	274.19	03/2019	259.46

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
46	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000017]	272.19	03/2019	268.59
47	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000018]	355.15	03/2019	321.31
48	GERIATRICS BLOCK- AIIMS DLEHI (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000019]	156.56	-	145.94
49	HOSPITAL AND TEACHING- AIIMS GUNTUR Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000020]	601.02	-	590.20
50	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000021]	268.84	-	269.92
51	SUPER SPECIALITY BLOCK PMSSY GOA Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000022]	249.01	-	244.64
52	HOSPITAL AND TEACHING- AIIMS NAGPUR Central Sector Projects(HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000023]	582.99	-	562.03
53	HOSPITAL AND TEACHING- AIIMS KALYANI (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000024]	651.99	-	622.18
54	AIIMS BILASPUR (NBCC FOR HEALTH) - [N21000028]	1,351.00	09/2021	1,185.10
	<u>RAILWAYS</u>			
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) (METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100164]	495.44	03/2004	1,920.57
56	KODERMA-RANCHI VIA BARKAKANA (NL), ECR (EAST CENTRAL RAILWAYS) - [220100222]	1,033.07	-	3,881.88
57	SUKINDA ROAD - ANGUL (NL)(ECOR) (RAIL VIKAS NIGAM LTD.) - [220100325]	1,202.70	02/2015	2,488.95
58	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) (WESTERN RAILWAY) - [N22000121]	829.74	03/2020	2,248.41
59	PALANPUR-SAMAKHAYALI (DL) (RAIL VIKAS NIGAM LTD.) - [N22000144]	1,548.66	12/2021	2,814.97
60	VIRAMGAM-SAMAKHIALI (DL) (WESTERN RAILWAY) - [N22000145]	1,037.15	03/2021	1,539.79
61	MADURAI-BODINAYAKKANUR (SOUTHERN RAILWAY) - [N22000201]	164.41	-	513.97
62	BANDEL-BOINCHI 3RD LINE (EASTERN RAILWAYS) - [N22000221]	288.35	-	603.92
63	BOINCHI-SHAKTIGARH 3RD LINE (EASTERN RAILWAYS) - [N22000238]	175.80	-	454.29
64	BAZAR SAU -AZIMGANJ JN. DOUBLING (EASTERN RAILWAYS) - [N22000302]	255.64	-	415.43
65	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) (RAIL VIKAS NIGAM LTD.) - [N22000313]	1,503.71	03/2020	4,483.77
66	HUBLI- CHIKJAJUR (SOUTH WESTERN RAILWAY) - [N22000325]	1,156.94	03/2020	1,590.73

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2023-2024

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
67	HAJIPUR - BACHAWARA (EAST CENTRAL RAILWAYS) - [N22000334]	678.54	03/2019	1,089.30
68	SURENDRA NAGAR RAJKOT (WESTERN RAILWAY) - [N22000392]	1,002.39	03/2021	867.09
69	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY (RAIL INDIA TECHNICAL AND ECONOMIC SERVICE) - [N22000394]	636.38	03/2021	1,081.75
70	ROURKELA JHARSUGUDA THIRD LINE 101 KM (SOUTH EASTERN RAILWAY) - [N22000395]	969.83	03/2020	1,396.80
71	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) (RAIL VIKAS NIGAM LTD.) - [N22000407]	713.48	03/2020	3,240.14
72	SAMBALPUR - TITLAGARH - DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000410]	948.04	03/2020	2,517.11
73	RAIPUR - TITLAGARH - DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000411]	1,402.02	03/2020	1,479.06
74	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000413]	1,183.25	12/2020	2,256.64
75	BINA - KOTA DOUBLING WITH RE (RAIL VIKAS NIGAM LTD.) - [N22000414]	1,485.85	12/2020	2,606.08
76	INDARA - DOHRIGHAT GAUGE CONVERSION. (NORTH EASTERN RAILWAY) - [N22000456]	213.00	04/2016	277.23
77	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) (NORTH WESTERN RAILWAY) - [N22000466]	808.85	08/2022	806.65
78	AUNRIHAR - JAUNPUR PATCH DOUBLING . (NORTH EASTERN RAILWAY) - [N22000469]	600.00	01/2022	406.77
79	GEVRA ROAD PENDRA ROAD (Indian Railway Construction Company Limited) - [N22000488]	2,288.00	03/2022	2,139.95
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
80	FOUR LANING OF KOILWAR TO BHOJPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000482]	814.04	01/2020	1,089.89
81	FOUR LANING OF BHOJPUR TO BUXAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000506]	642.41	10/2020	786.78
82	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000722]	305.00	07/2019	236.44
83	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000792]	809.07	06/2022	1,202.13
84	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001279]	216.49	07/2022	370.83
	July, 2023			
	<u>PETROLEUM</u>			
85	DHAMRA-ANGUL PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000272]	1,933.00	12/2020	2,103.90
86	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000390]	217.92	04/2021	148.40

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
87	CITY GAS DISTRIBUTION NETWORK PROJECT AT SAHARANPUR Central Sector Projects(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000475]	186.70	06/2023	184.32
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
88	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000678]	284.09	03/2021	284.02
89	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000679]	195.23	11/2020	209.93
90	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000680]	203.36	11/2020	211.33
91	4L FROM KM 42.000 TO KM 80.00 OF DODABALLAPUR BYPASS TO HOSKOTE SECTION OF NH-648 (OLD NH- 207) ON H PPP BOT (Hybrid Annuity)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001510]	1,278.00	02/2021	950.43

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	April,2023			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000801]	1,052.21	12/2020	570.86
	May,2023			
	<u>PETROLEUM</u>			
2	ENNORE-TRICHY-MADURAI LPG PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000162]	711.00	06/2020	11.12

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1643
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects added in Current Month	12
No of Projects in Current Month	1646

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	809 (49.15%)	17 (1.03%)	475 (28.86%)	30 (1.82%)	315 (19.14%)	1646
Latest Approved (Date)	602 (36.57%)	30 (1.82%)	672 (40.83%)	26 (1.58%)	316 (19.20%)	1646

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1239	18,64,474.55	20,52,555.26	9,70,869.04	47.30	1,88,080.71	10.10
Project with Revision in Cost	407	7,62,556.44	8,05,839.13	5,50,681.34	68.30	43,282.69	5.70
Total	1,646.00	26,27,030.99	28,58,394.39	15,21,550.38	53.23	2,31,363.40	8.81
Original Cost of All Projects							
Original Cost	1,646.00	23,92,837.89	28,58,394.39	15,21,550.38	53.23	4,65,556.50	19.46

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	809	12,85,604.56	16,16,933.75	10,14,388.39	62.70	3,31,329.19	25.77
Latest Approved (RCE)	602	11,06,659.84	12,64,770.22	8,01,259.32	63.40	1,58,110.38	14.29

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	213	1,83,919.46	2,71,207.11	2,11,536.98	78.00	87,287.65	47.50
Total	213	1,83,919.46	2,71,207.11	2,11,536.98	78.00	87,287.65	47.46

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,439.00	14.30	3	27,271.00	43,969.00	61.23
2	CIVIL AVIATION	27	17,964.63	19,854.46	10.52	6	3,968.50	6,550.75	65.07
3	COAL	123	1,71,148.45	1,78,417.46	4.25	10	28,093.45	36,716.44	30.69
4	FINANCE	3	786.27	831.04	5.69	1	209.00	262.00	25.36
5	FERTILISERS	2	425.57	425.57	0.00	0	0.00	0.00	0.00
6	MINES	7	7,333.99	8,585.77	17.07	3	4,992.00	6,303.23	26.27
7	STEEL	8	23,656.32	32,100.21	35.69	2	17,617.97	26,061.86	47.93
8	PETROLEUM	148	3,64,674.15	3,86,358.19	5.95	21	63,331.64	86,201.68	36.11
9	POWER	89	2,50,060.99	3,05,013.33	21.98	18	71,575.73	1,26,545.05	76.80
10	HEALTH AND FAMILY WELFARE	8	6,032.68	6,080.84	0.80	1	209.84	273.00	30.10
11	RAILWAYS	148	3,50,140.21	5,93,520.10	69.51	109	1,78,930.38	4,28,496.39	139.48
12	ROAD TRANSPORT AND HIGHWAYS	972	7,20,090.40	7,56,570.16	5.07	189	1,65,333.36	2,08,906.26	26.35
13	SHIPPING AND PORTS	1	5,369.18	5,362.27	-0.13	0	0.00	0.00	0.00
14	TELECOMMUNICATIONS	5	14,874.02	14,874.02	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	26	2,82,284.07	3,07,705.30	9.01	7	1,17,061.56	1,42,561.99	21.78
16	WATER RESOURCES	41	23,466.28	69,700.98	197.03	9	12,532.31	58,856.49	369.64
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
18	DEFENCE PRODUCTION	1	246.31	195.00	-20.83	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	21	9,763.78	10,117.16	3.62	4	1,595.78	2,125.47	33.19
21	HOME AFFAIRS	5	2,025.73	2,767.45	36.61	3	1,659.44	2,401.16	44.70
22	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	13.16

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	RENEWABLE ENERGY	1	271.90	366.12	34.65	1	271.90	366.12	34.65
Total		1646	23,92,837.89	28,58,394.39	19.46	388	6,99,426.86	11,81,997.89	69.00

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	74	1,22,477.51	1,79,092.00	46.22	30	58,422.57	1,15,434.10	97.58
2	ARUNACHAL PRADESH	32	52,608.96	67,629.07	28.55	2	8,264.33	23,284.44	181.75
3	ASSAM	56	57,074.33	65,950.38	15.55	8	17,965.27	28,244.25	57.22
4	BIHAR	86	1,08,768.60	1,32,337.99	21.67	32	39,659.53	64,302.97	62.14
5	GOA	10	6,242.45	6,302.55	0.96	1	303.90	364.00	19.78
6	GUJARAT	73	1,30,509.95	1,43,803.25	10.19	17	35,569.80	49,618.97	39.50
7	HARYANA	32	67,853.02	70,747.30	4.27	7	7,657.41	10,551.73	37.80
8	HIMACHAL PRADESH	24	24,989.50	36,960.75	47.91	6	10,082.89	22,271.69	120.89
9	JAMMU AND KASHMIR	38	63,381.49	98,398.39	55.25	3	4,997.72	40,014.62	700.66
10	KARNATAKA	60	94,167.93	1,01,868.75	8.18	17	14,729.47	23,451.02	59.21
11	KERALA	29	61,846.14	66,765.25	7.95	12	27,408.52	33,070.75	20.66
12	MADHYA PRADESH	79	67,847.14	75,829.53	11.77	11	12,299.94	20,477.91	66.49
13	MAHARASHTRA	220	2,10,341.93	2,32,272.90	10.43	29	74,170.47	1,02,875.11	38.70
14	MANIPUR	33	14,725.78	24,594.40	67.02	1	4,454.17	14,322.79	221.56
15	MEGHALAYA	14	5,372.73	12,735.93	137.05	1	906.46	8,324.28	818.33
16	MIZORAM	23	12,027.85	22,182.15	84.42	15	8,315.11	18,497.78	122.46
17	NAGALAND	32	11,768.33	16,118.74	36.97	2	2,699.59	7,050.00	161.15
18	ODISHA	77	1,19,944.28	1,26,879.62	5.78	19	19,246.58	26,381.94	37.07
19	PUNJAB	32	29,317.70	29,178.81	-0.47	1	170.57	192.48	12.85
20	RAJASTHAN	69	79,172.72	84,416.89	6.62	3	13,624.08	18,978.32	39.30
21	SIKKIM	20	14,011.54	20,897.41	49.14	5	2,361.46	9,371.18	296.84
22	TAMIL NADU	73	2,11,480.10	2,34,102.82	10.70	29	49,576.32	73,424.15	48.10
23	TRIPURA	17	4,962.74	5,272.25	6.24	8	2,076.57	2,386.08	14.90
24	UTTAR PRADESH	97	1,38,486.46	1,54,094.86	11.27	27	41,491.27	57,355.62	38.24
25	WEST BENGAL	60	69,153.64	88,373.28	27.79	22	31,678.10	51,523.88	62.65
26	ANDAMAN AND NICOBAR ISLANDS	8	2,611.46	2,882.82	10.39	2	655.03	945.73	44.38
27	DELHI	28	91,635.39	95,346.65	4.05	9	50,300.61	54,099.30	7.55
28	PUDUCHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
29	CHHATTISGARH	44	77,804.08	87,320.20	12.23	9	27,259.88	36,793.33	34.97
30	JHARKHAND	52	76,888.01	83,943.49	9.18	15	23,415.91	30,676.06	31.01
31	UTTARAKHAND	30	36,188.46	54,008.18	49.24	7	25,172.12	42,991.84	70.79
32	TELANGANA	46	32,326.07	35,213.70	8.93	7	13,264.18	16,151.81	21.77
33	LADAKH	8	2,767.29	2,926.96	5.77	1	480.33	640.00	33.24
34	MULTI STATE	69	2,93,889.31	3,99,752.12	36.02	30	70,746.70	1,77,929.76	151.50

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						150	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
Total		1646	23,92,837.89	28,58,394.39	19.46	388	6,99,426.86	11,81,997.89	69.00

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,439.00	14.30	4	67,120.00	83,818.00	36 - 171
2	CIVIL AVIATION	27	17,964.63	19,854.46	10.52	22	15,019.08	17,286.96	1 - 48
3	COAL	123	1,71,148.45	1,78,417.46	4.25	51	67,739.03	72,359.95	12 - 156
4	FINANCE	3	786.27	831.04	5.69	0	0.00	0.00	-
5	FERTILISERS	2	425.57	425.57	0.00	0	0.00	0.00	-
6	MINES	7	7,333.99	8,585.77	17.07	7	7,333.99	8,585.77	5 - 58
7	STEEL	8	23,656.32	32,100.21	35.69	5	20,385.43	28,700.43	9 - 99
8	PETROLEUM	148	3,64,674.15	3,86,358.19	5.95	81	1,90,392.98	2,06,256.56	2 - 143
9	POWER	89	2,50,060.99	3,05,013.33	21.98	55	1,59,310.66	2,13,747.98	2 - 176
10	HEALTH AND FAMILY WELFARE	8	6,032.68	6,080.84	0.80	4	3,649.55	3,634.55	1 - 50
11	RAILWAYS	148	3,50,140.21	5,93,520.10	69.51	98	2,66,666.73	4,06,606.01	3 - 254
12	ROAD TRANSPORT AND HIGHWAYS	972	7,20,090.40	7,56,570.16	5.07	419	2,72,843.85	2,94,086.86	1 - 124
13	SHIPPING AND PORTS	1	5,369.18	5,362.27	-0.13	1	5,369.18	5,362.27	45 - 45
14	TELECOMMUNICATIONS	5	14,874.02	14,874.02	0.00	3	14,043.62	14,043.62	30 - 98
15	URBAN DEVELOPMENT	26	2,82,284.07	3,07,705.30	9.01	16	1,64,605.84	1,83,614.81	3 - 60
16	WATER RESOURCES	41	23,466.28	69,700.98	197.03	25	18,473.78	64,370.53	9 - 51
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
18	DEFENCE PRODUCTION	1	246.31	195.00	-20.83	0	0.00	0.00	-
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	21	9,763.78	10,117.16	3.62	13	6,051.42	6,490.31	8 - 111
21	HOME AFFAIRS	5	2,025.73	2,767.45	36.61	4	1,826.42	2,568.14	5 - 80
22	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45 - 45
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
24	RENEWABLE ENERGY	1	271.90	366.12	34.65	0	0.00	0.00	-
Total		1646	23,92,837.89	28,58,394.39	19.46	809	12,85,604.56	16,16,933.75	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,22,477.51	1,79,092.00	46.22	26	83,329.93	1,37,119.76	3 - 216
2	ARUNACHAL PRADESH	32	52,608.96	67,629.07	28.55	16	12,993.15	27,955.36	8 - 176
3	ASSAM	56	57,074.33	65,950.38	15.55	17	10,206.61	12,086.61	2 - 102
4	BIHAR	86	1,08,768.60	1,32,337.99	21.67	44	74,922.65	92,548.86	2 - 153
5	GOA	10	6,242.45	6,302.55	0.96	3	1,742.75	1,802.85	18 - 33
6	GUJARAT	73	1,30,509.95	1,43,803.25	10.19	41	75,263.87	88,931.59	2 - 144
7	HARYANA	32	67,853.02	70,747.30	4.27	19	19,608.30	21,048.33	2 - 69
8	HIMACHAL PRADESH	24	24,989.50	36,960.75	47.91	6	8,810.48	16,737.44	19 - 174
9	JAMMU AND KASHMIR	38	63,381.49	98,398.39	55.25	22	34,346.83	69,268.13	1 - 254
10	KARNATAKA	60	94,167.93	1,01,868.75	8.18	30	49,375.43	53,584.04	5 - 153
11	KERALA	29	61,846.14	66,765.25	7.95	8	8,943.60	10,421.68	13 - 72
12	MADHYA PRADESH	79	67,847.14	75,829.53	11.77	40	44,500.35	52,573.32	1 - 77
13	MAHARASHTRA	220	2,10,341.93	2,32,272.90	10.43	96	96,432.58	1,18,351.62	3 - 97
14	MANIPUR	33	14,725.78	24,594.40	67.02	11	7,580.06	17,448.68	5 - 168
15	MEGHALAYA	14	5,372.73	12,735.93	137.05	6	2,065.06	2,010.44	11 - 111
16	MIZORAM	23	12,027.85	22,182.15	84.42	19	10,827.75	20,161.33	3 - 119
17	NAGALAND	32	11,768.33	16,118.74	36.97	18	7,664.94	12,015.35	3 - 132
18	ODISHA	77	1,19,944.28	1,26,879.62	5.78	48	61,847.77	67,057.95	5 - 213
19	PUNJAB	32	29,317.70	29,178.81	-0.47	13	10,737.73	10,673.84	2 - 108
20	RAJASTHAN	69	79,172.72	84,416.89	6.62	28	44,562.63	49,823.78	2 - 84
21	SIKKIM	20	14,011.54	20,897.41	49.14	16	12,569.53	19,497.21	3 - 96
22	TAMIL NADU	73	2,11,480.10	2,34,102.82	10.70	42	81,986.85	93,336.15	2 - 171
23	TRIPURA	17	4,962.74	5,272.25	6.24	8	1,921.47	1,992.80	11 - 24
24	UTTAR PRADESH	97	1,38,486.46	1,54,094.86	11.27	43	94,944.32	1,05,588.38	1 - 92
25	WEST BENGAL	60	69,153.64	88,373.28	27.79	41	47,114.41	66,818.15	4 - 141
26	ANDAMAN AND NICOBAR ISLANDS	8	2,611.46	2,882.82	10.39	5	1,699.09	1,699.09	26 - 50
27	DELHI	28	91,635.39	95,346.65	4.05	13	40,204.29	42,110.33	6 - 69
28	PUDUCHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATTISGARH	44	77,804.08	87,320.20	12.23	28	56,262.86	65,635.83	4 - 144
30	JHARKHAND	52	76,888.01	83,943.49	9.18	24	45,949.58	50,775.61	3 - 156
31	UTTARAKHAND	30	36,188.46	54,008.18	49.24	12	27,894.94	45,714.39	3 - 156
32	TELANGANA	46	32,326.07	35,213.70	8.93	18	19,147.09	21,475.16	3 - 180
33	LADAKH	8	2,767.29	2,926.96	5.77	5	2,048.83	2,208.50	7 - 30
34	MULTI STATE	69	2,93,889.31	3,99,752.12	36.02	43	1,88,098.83	2,18,461.19	3 - 202
Total		1646	23,92,837.89	28,58,394.39	19.46	809	12,85,604.56	16,16,933.75	

TABLE-9

Extent of time overrun in projects with respect to latest schedule						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,439.00	0.63	4	82,988.00	83,818.00	36 - 171
2	CIVIL AVIATION	27	18,388.40	19,854.46	7.97	16	11,447.73	13,606.21	15 - 48
3	COAL	123	1,70,345.14	1,78,417.46	4.74	43	63,023.94	67,108.05	12 - 156
4	FINANCE	3	786.27	831.04	5.69	0	0.00	0.00	-
5	FERTILISERS	2	425.57	425.57	0.00	0	0.00	0.00	-
6	MINES	7	8,585.77	8,585.77	0.00	3	6,691.37	6,691.37	5 - 47
7	STEEL	8	32,100.21	32,100.21	0.00	5	28,700.43	28,700.43	9 - 99
8	PETROLEUM	148	3,82,073.32	3,86,358.19	1.12	43	79,979.87	80,097.17	2 - 97
9	POWER	89	2,84,278.03	3,05,013.33	7.29	38	1,41,731.06	1,56,974.47	2 - 156
10	HEALTH AND FAMILY WELFARE	8	6,082.95	6,080.84	-0.03	4	3,664.69	3,634.55	1 - 50
11	RAILWAYS	148	4,73,375.78	5,93,520.10	25.38	84	2,89,050.00	3,57,317.64	0 - 254
12	ROAD TRANSPORT AND HIGHWAYS	972	7,51,636.82	7,56,570.16	0.66	313	2,15,610.20	2,18,626.75	0 - 124
13	SHIPPING AND PORTS	1	4,633.10	5,362.27	15.74	1	4,633.10	5,362.27	45 - 45
14	TELECOMMUNICATIONS	5	14,874.02	14,874.02	0.00	3	14,043.62	14,043.62	30 - 98
15	URBAN DEVELOPMENT	26	2,84,520.29	3,07,705.30	8.15	10	1,36,669.15	1,53,441.90	3 - 60
16	WATER RESOURCES	41	23,478.30	69,700.98	196.87	24	18,045.59	64,131.42	9 - 51
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
18	DEFENCE PRODUCTION	1	200.00	195.00	-2.50	0	0.00	0.00	-
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	21	10,200.20	10,117.16	-0.81	7	3,384.66	3,414.21	15 - 37
21	HOME AFFAIRS	5	2,589.74	2,767.45	6.86	3	2,223.43	2,401.16	22 - 80
22	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45 - 45
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
24	RENEWABLE ENERGY	1	366.12	366.12	0.00	0	0.00	0.00	-
Total		1646	26,27,030.99	28,58,394.39	8.81	602	11,06,659.84	12,64,770.22	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,439.00	0.63	1	6,840.00	7,670.00	12.13
2	CIVIL AVIATION	27	18,388.40	19,854.46	7.97	3	3,005.33	5,163.81	71.82
3	COAL	123	1,70,345.14	1,78,417.46	4.74	10	28,414.72	37,236.28	31.05
4	FINANCE	3	786.27	831.04	5.69	1	209.00	262.00	25.36
5	FERTILISERS	2	425.57	425.57	0.00	0	0.00	0.00	0.00
6	MINES	7	8,585.77	8,585.77	0.00	0	0.00	0.00	0.00
7	STEEL	8	32,100.21	32,100.21	0.00	0	0.00	0.00	0.00
8	PETROLEUM	148	3,82,073.32	3,86,358.19	1.12	3	13,135.45	19,877.11	51.32
9	POWER	89	2,84,278.03	3,05,013.33	7.29	13	47,904.75	68,640.05	43.28
10	HEALTH AND FAMILY WELFARE	8	6,082.95	6,080.84	-0.03	1	244.97	273.00	11.44
11	RAILWAYS	148	4,73,375.78	5,93,520.10	25.38	87	1,77,764.97	3,04,503.27	71.30
12	ROAD TRANSPORT AND HIGHWAYS	972	7,51,636.82	7,56,570.16	0.66	130	1,12,625.53	1,34,908.19	19.78
13	SHIPPING AND PORTS	1	4,633.10	5,362.27	15.74	1	4,633.10	5,362.27	15.74
14	TELECOMMUNICATIONS	5	14,874.02	14,874.02	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	26	2,84,520.29	3,07,705.30	8.15	6	1,05,641.56	1,28,905.77	22.02
16	WATER RESOURCES	41	23,478.30	69,700.98	196.87	9	13,784.94	60,370.90	337.95
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
18	DEFENCE PRODUCTION	1	200.00	195.00	-2.50	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	21	10,200.20	10,117.16	-0.81	2	726.96	810.43	11.48
21	HOME AFFAIRS	5	2,589.74	2,767.45	6.86	2	2,012.60	2,190.33	8.83
22	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	13.16
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	RENEWABLE ENERGY	1	366.12	366.12	0.00	0	0.00	0.00	0.00
Total		1646	26,27,030.99	28,58,394.39	8.81	270	5,21,716.88	7,81,574.41	49.81

[^] - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,439.00	0.63	1	6,840.00	7,670.00	171- 171
2	CIVIL AVIATION	27	18,388.40	19,854.46	7.97	3	3,005.33	5,163.81	30- 48
3	COAL	123	1,70,345.14	1,78,417.46	4.74	5	20,780.46	25,613.68	25- 114
4	FINANCE	3	786.27	831.04	5.69	0	0.00	0.00	0- 0
5	FERTILISERS	2	425.57	425.57	0.00	0	0.00	0.00	0- 0
6	MINES	7	8,585.77	8,585.77	0.00	0	0.00	0.00	0- 0
7	STEEL	8	32,100.21	32,100.21	0.00	0	0.00	0.00	0- 0
8	PETROLEUM	148	3,82,073.32	3,86,358.19	1.12	1	543.91	661.21	43- 43
9	POWER	89	2,84,278.03	3,05,013.33	7.29	12	47,372.75	62,616.16	20- 141
10	HEALTH AND FAMILY WELFARE	8	6,082.95	6,080.84	-0.03	0	0.00	0.00	0- 0
11	RAILWAYS	148	4,73,375.78	5,93,520.10	25.38	53	89,741.10	1,60,191.58	3- 216
12	ROAD TRANSPORT AND HIGHWAYS	972	7,51,636.82	7,56,570.16	0.66	54	43,507.72	53,553.58	2- 123
13	SHIPPING AND PORTS	1	4,633.10	5,362.27	15.74	1	4,633.10	5,362.27	45- 45
14	TELECOMMUNICATIONS	5	14,874.02	14,874.02	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	26	2,84,520.29	3,07,705.30	8.15	3	47,274.77	64,126.72	3- 60
16	WATER RESOURCES	41	23,478.30	69,700.98	196.87	6	13,036.56	59,263.37	21- 51
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	200.00	195.00	-2.50	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	21	10,200.20	10,117.16	-0.81	1	334.45	364.00	27- 27
21	HOME AFFAIRS	5	2,589.74	2,767.45	6.86	2	2,012.60	2,190.33	22- 50
22	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45- 45
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	RENEWABLE ENERGY	1	366.12	366.12	0.00	0	0.00	0.00	0- 0
Total		1646	26,27,030.99	28,58,394.39	8.81	143	2,83,855.75	4,52,177.71	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,439.00	14.30	3	27,271.00	43,969.00	84- 171
2	CIVIL AVIATION	27	17,964.63	19,854.46	10.52	5	3,551.27	5,843.02	9- 48
3	COAL	123	1,71,148.45	1,78,417.46	4.25	7	21,444.28	26,814.31	25- 114
4	FINANCE	3	786.27	831.04	5.69	0	0.00	0.00	0- 0
5	FERTILISERS	2	425.57	425.57	0.00	0	0.00	0.00	0- 0
6	MINES	7	7,333.99	8,585.77	17.07	3	4,992.00	6,303.23	46- 58
7	STEEL	8	23,656.32	32,100.21	35.69	1	15,525.00	23,840.00	99- 99
8	PETROLEUM	148	3,64,674.15	3,86,358.19	5.95	19	50,055.08	65,934.66	2- 143
9	POWER	89	2,50,060.99	3,05,013.33	21.98	17	66,083.84	1,20,521.16	20- 176
10	HEALTH AND FAMILY WELFARE	8	6,032.68	6,080.84	0.80	0	0.00	0.00	0- 0
11	RAILWAYS	148	3,50,140.21	5,93,520.10	69.51	73	1,20,404.94	2,60,835.53	3- 254
12	ROAD TRANSPORT AND HIGHWAYS	972	7,20,090.40	7,56,570.16	5.07	107	90,504.59	1,15,417.64	2- 123
13	SHIPPING AND PORTS	1	5,369.18	5,362.27	-0.13	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	5	14,874.02	14,874.02	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	26	2,82,284.07	3,07,705.30	9.01	4	58,694.77	77,782.94	3- 60
16	WATER RESOURCES	41	23,466.28	69,700.98	197.03	6	11,806.12	57,792.35	22- 51
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	246.31	195.00	-20.83	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	21	9,763.78	10,117.16	3.62	4	1,595.78	2,125.47	8- 38
21	HOME AFFAIRS	5	2,025.73	2,767.45	36.61	3	1,659.44	2,401.16	22- 80
22	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45- 45
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	RENEWABLE ENERGY	1	271.90	366.12	34.65	0	0.00	0.00	0- 0
Total		1646	23,92,837.89	28,58,394.39	19.46	253	4,78,361.11	8,14,981.47	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month					Rs. 150		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	<u>COAL</u>							
1	GAURI PAUNI EXPANSION OC	08/2020	337.38	03/2029	337.38	03/2029	48.04	
	<u>PETROLEUM</u>							
2	DHAMRA-ANGUL PIPELINE PROJECT	03/2017	1,933.00	12/2020	2,451.00	06/2023	2,103.90	
3	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	08/2018	217.92	04/2021	180.00	06/2023	148.40	
4	CITY GAS DISTRIBUTION NETWORK PROJECT AT SAHARANPUR Central Sector Projects	05/2016	186.70	06/2023	198.80	06/2023	184.32	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
5	4L FROM KM 42.000 TO KM 80.00 OF DODABALLAPUR BYPASS TO HOSKOTE SECTION OF NH-648 (OLD NH- 207) ON H PPP BOT (Hybrid Annuity)	01/2020	1,278.00	02/2021	1,278.00	07/2023	950.43	
6	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	02/2018	486.78	01/2022	486.78	05/2024	181.99	
7	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	03/2017	284.09	03/2021	323.49	12/2022	284.02	
8	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	02/2017	195.23	11/2020	252.79	01/2023	209.93	
9	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	02/2017	203.36	11/2020	263.31	03/2023	211.33	

TABLE-14

List of projects added Rs. 150 Crore and above					(July 2023)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
1	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA EPC	3/2022	535.03	4/2025	535.03	4/2025
2	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA HAM(Hybrid Annuity Mode)	12/2022	912.94	9/2025	912.94	9/2025
3	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 HAM(Hybrid Annuity Mode)	12/2022	750.81	11/2025	750.81	11/2025
4	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH HAM(Hybrid Annuity Mode)	12/2022	992.89	11/2025	992.89	11/2025
5	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. HAM(Hybrid Annuity Mode)	12/2022	1,058.90	10/2025	1,058.90	10/2025
6	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 HAM(Hybrid Annuity Mode)	2/2023	1,253.24	10/2025	1,253.24	10/2025
7	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 EPC	3/2022	995.04	9/2025	995.04	9/2025
8	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. HAM(Hybrid Annuity Mode)	2/2023	1,200.42	10/2025	1,200.42	10/2025
9	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA HAM(Hybrid Annuity Mode)	1/2023	956.14	11/2025	956.14	11/2025
10	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK HAM(Hybrid Annuity Mode)	2/2023	909.02	10/2025	909.02	10/2025
11	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 HAM(Hybrid Annuity Mode)	5/2022	1,063.72	7/2025	1,063.72	7/2025
	<u>TELECOMMUNICATIONS</u>					
12	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT Central Sector	5/2023	645.13	8/2024	645.13	8/2024

List of projects added Rs. 150 Crore and above					(July 2023)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	Projects					

TABLE-15

Milestones (Cumulative due & achieved)	Rs. 150	Crore and above
Total	5590	
Achieved up to month	3054	

TABLE-16

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(July 2023)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA AAI	458.00	458.00	03/2020	07/2023	08/2023	1
2	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. AAI EPC	353.25	353.25	02/2021	07/2023	09/2023	2
3	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT AAI	177.10	177.10	02/2020	07/2023	10/2023	3
4	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI AAI	2,467.00	2,467.00	02/2022	07/2025	12/2025	5
	<u>COAL</u>						
5	PATHERDIH 2.5 NLW COAL WASHERY BCCL	243.00	334.27	04/2018	01/2024	03/2024	2
6	MADHUBAND NLW WASHERY BCCL	289.45	302.00	05/2014	08/2023	11/2023	3
7	JAYANT EXPANSION OCP 10 TO 20 MTPA NCL Central Sector Projects	1,783.09	1,783.09	03/2021	07/2023	10/2023	3
	<u>STEEL</u>						
8	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	23,840.00	05/2015	07/2023	08/2023	1
	<u>PETROLEUM</u>						
9	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY IOCL	255.40	255.40	08/2020	07/2023	08/2023	1
10	MUZAFFARPUR-MOTIHARI LPG PIPELINE IOCL	403.00	403.00	08/2022	08/2023	09/2023	1
11	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECT GAIL	225.54	247.90	02/2021	10/2023	12/2023	2
12	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY IOCL	909.00	909.00	01/2021	07/2023	09/2023	2
13	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT IOCL	278.60	278.60	06/2021	07/2023	09/2023	2
14	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT IOCL	1,636.00	1,636.00	08/2020	07/2023	11/2023	4

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
15	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY IOCL	199.36	199.36	10/2020	07/2023	12/2023	5
16	ADDITIONAL STORAGE TANKS AT PARADIP IOCL	462.30	543.00	09/2021	09/2023	04/2024	7
17	R and D CAMPUS II AT FARIDABAD IOCL	2,281.94	3,219.94	12/2022	11/2024	07/2025	8
18	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY IOCL Central Sector Projects	13,805.00	13,805.00	01/2024	01/2024	07/2025	18
	<u>POWER</u>						
19	BARH STPP(3X660MW) NTPC	8,692.97	21,312.11	10/2011	06/2024	07/2024	1
20	NAITWAR MORI HEP SJVN	648.33	1,272.29	12/2021	07/2023	08/2023	1
21	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C PGCIL PPP (BOT)	1,326.00	1,326.00	03/2023	08/2023	09/2023	1
22	Bagodara Solar Power Project SJVN	339.35	339.35	10/2022	10/2023	12/2023	2
23	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. PGCIL PPP (BOT)	176.22	176.22	03/2023	08/2023	10/2023	2
24	NORTH EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	576.42	576.42	03/2023	11/2023	02/2024	3
25	DAYAPAR WIND ENERGY PROJECT 150MW NTPC	937.80	937.80	05/2023	03/2024	06/2024	3
26	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B PGCIL Central Sector Projects	4,546.26	4,546.26	06/2023	03/2024	06/2024	3
27	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) NTPC EPC	1,442.60	1,442.60	03/2024	03/2024	06/2024	3
28	TEHRI PUMPED STORAGE PLANT(1000MW) THDCIL	1,657.00	4,825.60	02/2016	02/2024	06/2024	4
29	WESTERN REGION EXPANSION SCHEME XXV PGCIL Central Sector Projects	385.84	385.84	11/2023	11/2023	03/2024	4
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	6,285.33	21,247.54	09/2010	12/2024	05/2025	5
31	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	2,635.55	02/2020	09/2023	03/2024	6

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (July 2023)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
32	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCIL	2,491.58	3,860.35	06/2013	06/2025	06/2026	12
	<u>RAILWAYS</u>						
33	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	37,012.26	11/2002	12/2023	01/2024	1
34	ROSA-SITAPUR CANTT-BURHWAL DOUBLING NER	1,295.42	2,560.00	03/2022	09/2023	10/2023	1
35	BONDAMUNDA RANCHI DOUBLING SER	1,724.20	3,029.04	03/2021	02/2024	03/2024	1
36	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) SER	390.39	513.92	12/2021	07/2023	08/2023	1
37	PHULERA - DIGANA DOUBLING NWR	600.00	701.81	03/2020	12/2023	02/2024	2
38	MONIGRAM- NIMTITA ER	250.93	310.70	N.A.	07/2023	11/2023	4
39	GADAG-WADI NL SWR	2,841.84	2,841.84	12/2018	06/2025	03/2026	9
40	PIRPAINTI-JASIDIH ER	915.98	2,137.81	03/2022	03/2024	03/2025	12
41	SHIMOGA-HARIHAR NL SWR	832.47	832.47	03/2016	03/2026	12/2028	33
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
42	FOUR LANING OF FORBESGANJ - JOGBANI NHAI	322.09	322.09	04/2018	07/2023	08/2023	1
43	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] NHAI	1,587.49	3,063.99	04/2019	06/2023	07/2023	1
44	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T NHAI	804.97	571.45	06/2018	06/2023	07/2023	1
45	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI NHAI	400.25	304.07	03/2019	06/2023	07/2023	1
46	JUNAGADH BYPASS NHAI Central Sector Projects	232.49	290.69	04/2021	07/2023	08/2023	1
47	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. NHIDCL	387.00	387.00	09/2020	08/2023	09/2023	1
48	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA- ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO NHIDCL	285.68	285.68	09/2022	07/2023	08/2023	1
49	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA MoRTH	223.50	223.50	08/2018	09/2023	10/2023	1

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
50	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA MoRTH	214.23	214.23	08/2018	08/2023	09/2023	1
51	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA NHAI	743.88	743.89	12/2021	07/2023	08/2023	1
52	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V NHAI	656.98	840.00	11/2022	07/2023	08/2023	1
53	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA NHAI	1,094.97	1,094.97	02/2022	07/2023	08/2023	1
54	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM NHAI	217.96	884.00	12/2022	07/2023	08/2023	1
55	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE NHAI	990.97	990.97	12/2021	07/2023	08/2023	1
56	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO NHAI	847.00	847.00	03/2022	07/2023	08/2023	1
57	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE NHAI	1,047.00	1,047.00	05/2020	07/2023	08/2023	1
58	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T NHAI	996.27	996.27	03/2022	07/2023	08/2023	1
59	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T NHIDCL EPC	257.15	257.15	04/2022	06/2023	07/2023	1
60	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 NHAI EPC	731.89	731.99	01/2022	07/2023	08/2023	1
61	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 NHAI EPC	594.75	613.75	01/2022	07/2023	08/2023	1
62	INTEGRATED STRUCTURE WITH DEVELOPMENT OF OTHER ALLIED STRUCTURES ON BOTH SIDES OF CHANDNI CHOWK JUNC NHAI EPC	397.60	397.60	02/2022	07/2023	08/2023	1
63	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0 NHAI EPC	366.85	366.85	06/2023	07/2023	08/2023	1
64	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 NHAI EPC	200.00	154.73	03/2022	07/2023	08/2023	1

List of projects reporting additional delayed Rs. 150 Crore and above (July 2023)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
65	2ND FLYOVER (LCW) PARALLEL TO EXISTING FLYOVER IN KISHANGANJ TOWN. NHAI EPC	150.21	150.00	06/2020	07/2023	08/2023	1
66	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A NHAI EPC	2,312.26	2,312.26	09/2021	07/2023	08/2023	1
67	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN NHAI EPC	2,252.75	2,252.75	09/2021	07/2023	08/2023	1
68	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA NHAI EPC	1,935.61	1,935.61	09/2021	07/2023	08/2023	1
69	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR NHAI	1,396.74	1,396.74	10/2019	05/2023	07/2023	2
70	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN NHAI	754.54	668.74	03/2020	06/2023	08/2023	2
71	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 NHIDCL	373.07	387.00	09/2019	07/2023	09/2023	2
72	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING NHIDCL	500.09	500.09	11/2022	10/2023	12/2023	2
73	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. MoRTH	287.70	287.70	02/2017	08/2023	10/2023	2
74	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA MoRTH	199.16	199.16	08/2018	07/2023	09/2023	2
75	JINTUR TO PARBHANI MoRTH	356.66	356.66	N.A.	06/2023	08/2023	2
76	RALEGAON TO RAMTIRTH MoRTH	210.81	210.81	07/2019	06/2023	08/2023	2
77	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF BEAWAR-ASIND SECTION (K MoRTH	196.23	196.00	11/2022	07/2023	09/2023	2
78	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 NHIDCL EPC	242.97	242.97	06/2022	10/2023	12/2023	2
79	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) NHIDCL EPC	320.97	320.97	06/2022	06/2023	08/2023	2
80	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II MoRTH EPC	216.72	216.72	12/2022	07/2023	09/2023	2

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (July 2023)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
81	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29 NHAI EPC	1,523.77	1,523.77	04/2023	05/2023	07/2023	2
82	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP NHAI PPP BOT (Hybrid Annuity)	1,334.04	1,334.00	01/2024	01/2024	03/2024	2
83	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. NHAI EPC	440.16	440.16	12/2022	12/2023	02/2024	2
84	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS NHAI EPC	166.90	166.90	03/2021	07/2023	09/2023	2
85	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI NHAI EPC	157.05	157.05	10/2020	06/2023	08/2023	2
86	8L OF GUDUVANCHERY (KM 38.00) - MARAIMALAI NAGAR (KM 42.00) - SINGAPERUMAL KOIL (47.00) - CHETTIPU NHAI Joint Venture	230.69	230.69	02/2022	06/2023	08/2023	2
87	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S NHAI PPP BOT (Hybrid Annuity)	2,334.68	2,335.00	03/2023	09/2023	11/2023	2
88	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP MoRTH EPC	165.67	165.67	11/2015	06/2023	09/2023	3
89	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 NHAI	1,041.10	639.58	04/2019	12/2023	03/2024	3
90	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU NHAI	763.08	763.08	08/2019	07/2023	10/2023	3
91	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN NHAI	672.89	830.31	03/2020	12/2023	03/2024	3
92	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 NHIDCL	396.52	396.52	08/2019	06/2023	09/2023	3
93	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I NHAI	573.70	726.99	12/2021	12/2023	03/2024	3
94	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG NHAI	614.48	757.12	08/2021	07/2023	10/2023	3
95	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) NHAI EPC	806.11	767.45	04/2021	06/2023	09/2023	3

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
96	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA NHIDCL	253.44	253.44	07/2021	05/2023	08/2023	3
97	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND MoRTH	160.27	213.97	09/2023	03/2024	06/2024	3
98	HIMAYATNAGAR TO PHULSAWANGI MoRTH	294.87	294.87	12/2019	06/2023	09/2023	3
99	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT MoRTH	171.60	171.60	05/2018	07/2023	10/2023	3
100	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K NHIDCL EPC	210.79	210.79	04/2022	10/2023	01/2024	3
101	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT NHAI EPC	649.90	649.90	12/2020	09/2023	12/2023	3
102	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE NHAI EPC	446.97	446.97	11/2020	09/2023	12/2023	3
103	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA NHAI EPC	464.09	464.09	11/2020	09/2023	12/2023	3
104	MANU-SIMLUNG (PKG 4) NHIDCL EPC	354.79	354.79	12/2022	08/2023	11/2023	3
105	BALANCE WORK UNDER PHASE-I FOR 4L OF KHED SINNER SECTION COMPRISING OF THE STRETCHES (I) KHED BYPASS NHAI EPC	169.83	169.83	10/2022	03/2023	06/2023	3
106	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP NHAI PPP BOT (Hybrid Annuity)	1,690.23	2,010.17	12/2023	12/2023	03/2024	3
107	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI NHAI PPP BOT (Hybrid Annuity)	817.00	817.00	07/2022	08/2023	11/2023	3
108	6L JAKKUVA – KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) NHAI PPP BOT (Hybrid Annuity)	663.60	768.00	03/2024	03/2024	06/2024	3
109	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) NHAI PPP BOT (Hybrid Annuity)	922.50	1,128.68	03/2024	03/2024	06/2024	3
110	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 NHAI	1,408.00	1,659.12	07/2020	10/2023	02/2024	4

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
111	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST NHAI	723.64	723.64	09/2019	06/2023	10/2023	4
112	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI NHIDCL	403.36	403.36	11/2020	12/2023	04/2024	4
113	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA NHIDCL	417.24	417.24	11/2020	12/2023	04/2024	4
114	SIX / FOUR LANING OF NH 5 (NEW NH 16) FROM PUINTOLA TO TANGI (KM. 284.000 TO KM. 355.000) NHAI EPC	538.41	478.32	12/2020	06/2023	10/2023	4
115	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM NHIDCL	306.28	306.28	03/2022	06/2023	10/2023	4
116	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. NHIDCL	200.44	200.44	01/2020	04/2023	08/2023	4
117	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION MoRTH	335.32	335.32	06/2017	08/2023	12/2023	4
118	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V MoRTH	476.20	543.73	09/2016	08/2023	12/2023	4
119	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION MoRTH	624.98	731.50	10/2016	08/2023	12/2023	4
120	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. MoRTH	349.03	349.03	01/2019	08/2023	12/2023	4
121	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 NHIDCL EPC	295.97	295.97	04/2023	08/2023	12/2023	4
122	IMPHAL – MOREH PACKAGE- 3 NHIDCL EPC	259.31	259.31	12/2022	04/2023	08/2023	4
123	KHELLANI-KHANABAL PKG-5 NHIDCL EPC	497.09	497.09	02/2023	09/2023	01/2024	4
124	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH MoRTH EPC	223.35	223.35	02/2022	08/2023	12/2023	4
125	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) NHAI PPP BOT (Hybrid Annuity)	1,518.53	1,518.53	10/2022	08/2023	12/2023	4
126	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K NHAI EPC	510.97	510.97	03/2023	06/2023	10/2023	4
127	NAGPUR RING ROAD PACKAGE-2 NHAI	591.66	591.66	07/2019	10/2023	03/2024	5

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
128	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 NHIDCL	568.92	568.92	12/2019	04/2023	09/2023	5
129	AKOLA TO AKOT MoRTH	313.95	313.95	06/2019	03/2023	08/2023	5
130	WADI TO ASOLA MoRTH	363.82	363.82	09/2019	03/2023	08/2023	5
131	PUNE TO MALE VILLAGE MoRTH	228.31	228.31	12/2019	03/2023	08/2023	5
132	PUNE RAIGARH DISTRICT BORDER TO MANGAON MoRTH	223.46	223.46	12/2019	03/2022	08/2022	5
133	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH MoRTH	175.50	241.60	02/2017	07/2023	12/2023	5
134	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 MoRTH	306.59	306.59	06/2021	04/2023	09/2023	5
135	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL NHIDCL EPC	228.39	228.39	04/2022	10/2023	03/2024	5
136	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN NHAI EPC	1,100.88	1,100.88	11/2021	11/2023	04/2024	5
137	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 MoRTH EPC	302.88	302.88	02/2022	08/2023	01/2024	5
138	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE MoRTH EPC	867.97	913.49	11/2020	06/2023	12/2023	6
139	VITA TO NAGAJ MoRTH	304.58	304.58	12/2019	06/2023	12/2023	6
140	PARBHANI TO GANGKHED MoRTH	238.19	238.19	12/2019	02/2023	08/2023	6
141	KOTHARI TO DHANORA MoRTH	301.38	301.38	08/2020	03/2023	09/2023	6
142	OSMANNAGAR TO KUNDRAL MoRTH	344.25	344.25	08/2020	06/2023	12/2023	6
143	MHASWAD TO TEMBHURNI MoRTH	488.60	488.60	07/2019	06/2023	12/2023	6
144	KOLHA TO NASRATPUR MoRTH	281.78	281.78	04/2019	06/2023	12/2023	6
145	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N NHIDCL EPC	402.94	402.94	04/2022	07/2023	01/2024	6

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
146	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L NHIDCL EPC	183.31	439.56	05/2022	10/2023	04/2024	6
147	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY NHAI EPC	2,919.96	2,919.96	02/2024	02/2024	08/2024	6
148	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V NHAI PPP BOT (Hybrid Annuity)	1,060.29	1,060.29	01/2024	06/2023	12/2023	6
149	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 NHAI PPP BOT (Hybrid Annuity)	899.00	947.00	07/2022	05/2023	11/2023	6
150	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) NHAI EPC	536.03	536.03	09/2022	06/2023	12/2023	6
151	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) NHAI EPC	485.75	485.75	09/2022	06/2023	12/2023	6
152	VARANASI-AURANGABAD KM.786 TO KM.978.40 NHAI PPP (BOT)	2,848.00	3,379.45	03/2014	11/2023	06/2024	7
153	AJANTHA TO BULDHANA NHIDCL	401.00	401.00	07/2019	02/2023	09/2023	7
154	AMD I TO SAONER MoRTH	396.91	396.91	06/2019	01/2023	08/2023	7
155	SHIROD SHAHPURER TO NANDED MoRTH	211.34	211.34	07/2019	01/2023	08/2023	7
156	PALPHATA TO PHULAMBARI MoRTH	227.19	227.19	12/2019	02/2023	09/2023	7
157	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK MoRTH	217.14	217.14	02/2020	01/2023	08/2023	7
158	LATUR TO PANGAON MoRTH	336.47	336.47	12/2019	01/2023	08/2023	7
159	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER MoRTH	256.15	256.15	12/2019	01/2023	08/2023	7
160	WARDHA TO HINGAGHAT MoRTH	216.90	216.90	12/2019	01/2023	08/2023	7
161	KURUDWADI TO PANDHARPUR MoRTH	307.63	307.63	07/2019	02/2023	09/2023	7
162	PEN TO KHOPOLI MoRTH	301.39	301.39	03/2018	06/2023	01/2024	7
163	BARASGAON TO RAHATEE MoRTH	289.11	289.11	09/2018	02/2023	09/2023	7

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
164	WARDHA TO ARVI MoRTH	313.58	313.58	04/2020	01/2023	08/2023	7
165	KHELLANI-KHANABAL PKG-2 NHIDCL EPC	512.43	512.43	02/2023	03/2024	10/2024	7
166	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD MoRTH EPC	1,948.25	1,948.25	02/2024	02/2024	09/2024	7
167	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (NHAI	633.68	633.68	08/2022	07/2023	03/2024	8
168	DAHEGAON TO KUHI MoRTH	228.89	228.89	06/2019	01/2023	09/2023	8
169	KARAD TO VITA MoRTH	344.85	344.85	12/2019	02/2023	10/2023	8
170	NALDURG TO AKKALKOT MoRTH	274.50	274.50	12/2019	04/2023	12/2023	8
171	CHIKALI TO DHAD MoRTH	189.46	189.46	12/2019	07/2023	03/2024	8
172	WADIGODRI TO DHANGRIPIMPRI MoRTH	194.23	194.23	02/2020	01/2023	09/2023	8
173	JALGAON TO NANDURA MoRTH	177.84	177.84	12/2019	01/2023	09/2023	8
174	PANDHARPUR TO SANGOLA MoRTH	218.38	218.38	07/2019	01/2023	09/2023	8
175	MALEWADA TO CHIMUR MoRTH	322.55	322.55	06/2019	01/2023	09/2023	8
176	SAKOLI TO BHANDARA MoRTH	362.96	362.96	06/2019	01/2023	09/2023	8
177	SILLOD TO FARDAPUR MoRTH	337.46	337.46	06/2019	02/2023	10/2023	8
178	PARLI PIMPLA DAHIGUDA MoRTH	205.72	205.72	06/2019	12/2022	08/2023	8
179	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) NHIDCL EPC	157.86	157.86	04/2022	05/2023	01/2024	8
180	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B MoRTH EPC	282.41	319.96	04/2022	05/2023	02/2024	9
181	SELDOH TO PANVAR MoRTH	404.33	404.33	05/2020	06/2023	03/2024	9
182	NASRATPUR TO BARASGAON MoRTH	406.54	406.54	09/2019	03/2023	12/2023	9
183	PAITHAN TO SHIRUR MoRTH	341.80	341.80	06/2019	06/2023	03/2024	9
184	SHIRUR TO KHARDA MoRTH	381.77	381.77	06/2019	06/2023	03/2024	9

List of projects reporting additional delayed Rs. 150 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
185	KUMBHARI PHTA TO DEULGAON RAJA MoRTH	406.51	406.51	06/2019	03/2023	12/2023	9
186	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT MoRTH EPC	309.48	309.48	09/2023	03/2024	12/2024	9
187	DIGRAS DARWAH KARANJA MoRTH	391.06	391.06	06/2019	02/2023	12/2023	10
188	MORSHI TO ACHALPUR MoRTH	341.16	341.16	06/2019	02/2023	12/2023	10
189	KARWANDI TO RAJURI MoRTH	276.95	276.95	12/2019	01/2023	11/2023	10
190	DHAD BHOKARDAN TO BHOKARDHAN SILLOD MoRTH	336.21	336.21	12/2019	02/2023	12/2023	10
191	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N NHAI EPC	1,101.99	1,101.99	08/2023	02/2024	12/2024	10
192	JALKOT TO TOGRI MoRTH	299.92	299.92	08/2020	01/2023	12/2023	11
193	KHELLANI-KHANABAL PKG-6 NHIDCL EPC	285.28	285.28	09/2022	09/2022	08/2023	11
194	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY NHAI	701.40	701.40	03/2019	12/2023	12/2024	12
195	WAKAN PALI KHOPOLI MoRTH	376.19	376.19	05/2019	09/2022	10/2023	13
196	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 NHAI EPC	597.67	641.90	01/2020	06/2023	07/2024	13
197	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM NHIDCL EPC	292.80	292.80	05/2022	10/2023	11/2024	13
198	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION NHAI EPC	688.00	688.00	01/2023	12/2023	03/2025	15
199	SATARA MURVAD PILLOV PANDHARPUR MoRTH	388.44	388.44	N.A.	02/2023	06/2024	16
200	MEHKAR TO AJISPUR MoRTH	232.77	232.77	07/2019	03/2022	08/2023	17
201	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU MoRTH	1,979.00	2,036.90	N.A.	12/2021	05/2023	17
202	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 MoRTH	309.01	309.01	09/2015	09/2015	05/2018	32
	<u>WATER RESOURCES</u>						

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (July 2023)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
203	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L DJB	665.78	665.78	12/2022	06/2023	09/2023	3
204	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH KMDA	160.00	154.73	02/2022	03/2024	06/2024	3
205	I AND D AND STP AT CHAPPRA BUIDCO	236.15	236.15	12/2020	03/2023	08/2023	5
206	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA KMDA	307.12	653.67	09/2022	12/2024	12/2026	24
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
207	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) CPWD EDUCATION	424.93	424.93	07/2022	08/2023	09/2023	1
208	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA CPWD EDUCATION	496.18	460.00	06/2017	08/2023	10/2023	2
209	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. CPWD EDUCATION	303.90	364.00	08/2021	08/2023	11/2023	3
210	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. CPWD EDUCATION	348.24	348.24	05/2022	11/2023	03/2024	4
	<u>HOME AFFAIRS</u>						
211	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI CPWD FOR MHA EPC	277.35	290.33	07/2022	04/2024	05/2024	1
212	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD FOR MHA	1,219.21	1,900.00	10/2019	09/2023	12/2023	3
	<u>DPIIT</u>						
213	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE IICC FOR DPIIT	4,773.00	5,401.00	12/2019	07/2023	09/2023	2

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,326,09.00	1,33,439.00	92,937.75
CIVIL AVIATION	27	17,964.63	183,88.40	19,854.46	10,412.47
COAL	123	1,71,148.45	1,703,45.14	1,78,417.46	71,469.16
FINANCE	3	786.27	7,86.27	831.04	721.51
FERTILISERS	2	425.57	4,25.57	425.57	18.83
MINES	7	7,333.99	85,85.77	8,585.77	3,918.17
STEEL	8	23,656.32	321,00.21	32,100.21	26,775.25
PETROLEUM	148	3,64,674.15	3,820,73.32	3,86,358.19	1,63,771.71
POWER	89	2,50,060.99	2,842,78.03	3,05,013.33	1,63,456.26
HEALTH AND FAMILY WELFARE	8	6,032.68	60,82.95	6,080.84	2,153.60
RAILWAYS	148	3,50,140.21	4,733,75.78	5,93,520.10	3,68,880.63
ROAD TRANSPORT AND HIGHWAYS	972	7,20,090.40	7,516,36.82	7,56,570.16	3,62,069.78
SHIPPING AND PORTS	1	5,369.18	46,33.10	5,362.27	2,498.52
TELECOMMUNICATIONS	5	14,874.02	148,74.02	14,874.02	22,235.80
URBAN DEVELOPMENT	26	2,82,284.07	2,845,20.29	3,07,705.30	1,79,449.91
WATER RESOURCES	41	23,466.28	234,78.30	69,700.98	28,027.73
SOCIAL JUSTICE	1	170.99	1,70.99	170.99	73.80
DEFENCE PRODUCTION	1	246.31	2,00.00	195.00	187.02
COMMERCE	1	302.64	3,02.64	302.64	30.00
DEPARTMENT OF HIGHER EDUCATION	21	9,763.78	102,00.20	10,117.16	6,249.93
HOME AFFAIRS	5	2,025.73	25,89.74	2,767.45	1,980.06
DPIIT	2	24,857.00	248,57.00	25,485.00	13,754.67
DONER	1	151.33	1,51.33	151.33	148.33
RENEWABLE ENERGY	1	271.90	3,66.12	366.12	329.49
Grand total	1646	23,92,837.89	26,27,030.99	28,58,394.39	15,21,550.38

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,22,477.51	1,79,092.00	46.22	13	41,143.49	94,933.32	3 - 216
2	ARUNACHAL PRADESH	32	52,608.96	67,629.07	28.55	1	6,285.33	21,247.54	176 - 176
3	ASSAM	56	57,074.33	65,950.38	15.55	4	4,170.23	6,283.16	20 - 48
4	BIHAR	86	1,08,768.60	1,32,337.99	21.67	15	32,490.08	50,554.20	3 - 153
5	GOA	10	6,242.45	6,302.55	0.96	1	303.90	364.00	27 - 27
6	GUJARAT	73	1,30,509.95	1,43,803.25	10.19	15	34,569.24	48,324.28	2 - 144
7	HARYANA	32	67,853.02	70,747.30	4.27	4	5,077.80	6,517.87	3 - 44
8	HIMACHAL PRADESH	24	24,989.50	36,960.75	47.91	3	4,790.84	12,717.80	19 - 174
9	JAMMU AND KASHMIR	38	63,381.49	98,398.39	55.25	2	3,176.00	38,097.30	8 - 254
10	KARNATAKA	60	94,167.93	1,01,868.75	8.18	12	10,292.87	14,798.90	7 - 120
11	KERALA	29	61,846.14	66,765.25	7.95	6	7,385.00	9,096.60	13 - 72
12	MADHYA PRADESH	79	67,847.14	75,829.53	11.77	10	12,133.73	20,303.01	8 - 65
13	MAHARASHTRA	220	2,10,341.93	2,32,272.90	10.43	18	58,894.96	82,537.08	6 - 97
14	MANIPUR	33	14,725.78	24,594.40	67.02	1	4,454.17	14,322.79	168 - 168
15	MEGHALAYA	14	5,372.73	12,735.93	137.05	0	0.00	0.00	-
16	MIZORAM	23	12,027.85	22,182.15	84.42	11	7,115.01	16,476.96	3 - 119
17	NAGALAND	32	11,768.33	16,118.74	36.97	2	2,699.59	7,050.00	48 - 132
18	ODISHA	77	1,19,944.28	1,26,879.62	5.78	13	14,534.91	19,945.11	18 - 213
19	PUNJAB	32	29,317.70	29,178.81	-0.47	1	170.57	192.48	36 - 36
20	RAJASTHAN	69	79,172.72	84,416.89	6.62	3	13,624.08	18,978.32	41 - 84
21	SIKKIM	20	14,011.54	20,897.41	49.14	5	2,361.46	9,371.18	5 - 96
22	TAMIL NADU	73	2,11,480.10	2,34,102.82	10.70	16	20,480.18	33,054.59	2 - 171
23	TRIPURA	17	4,962.74	5,272.25	6.24	4	862.82	934.15	13 - 24
24	UTTAR PRADESH	97	1,38,486.46	1,54,094.86	11.27	18	33,523.90	44,252.17	5 - 92
25	WEST BENGAL	60	69,153.64	88,373.28	27.79	21	29,484.87	49,209.88	6 - 141
26	ANDAMAN AND NICOBAR ISLANDS	8	2,611.46	2,882.82	10.39	0	0.00	0.00	-
27	DELHI	28	91,635.39	95,346.65	4.05	6	11,148.03	13,133.27	15 - 50
28	PUDUCHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATTISGARH	44	77,804.08	87,320.20	12.23	7	23,311.32	32,701.62	43 - 99
30	JHARKHAND	52	76,888.01	83,943.49	9.18	8	18,625.23	23,655.93	12 - 114
31	UTTARAKHAND	30	36,188.46	54,008.18	49.24	6	24,711.39	42,530.84	3 - 156
32	TELANGANA	46	32,326.07	35,213.70	8.93	3	12,108.74	14,436.81	33 - 180
33	LADAKH	8	2,767.29	2,926.96	5.77	1	480.33	640.00	30 - 30
34	MULTI STATE	69	2,93,889.31	3,99,752.12	36.02	23	37,951.04	68,320.31	22 - 202
Total		1646	23,92,837.89	28,58,394.39	19.46	253	4,78,361.11	8,14,981.47	

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	245	21
2	RAILWAYS	101	5
3	PETROLEUM	58	3
4	POWER	48	9
5	COAL	35	1
6	URBAN DEVELOPMENT	22	0
7	ATOMIC ENERGY	5	0
8	CIVIL AVIATION	5	1
9	STEEL	4	1
10	HEALTH AND FAMILY WELFARE	3	0
11	MINES	2	0
12	DPIIT	2	1
13	SHIPPING AND PORTS	1	0
14	TELECOMMUNICATIONS	1	0
15	WATER RESOURCES	1	0
16	DEPARTMENT OF HIGHER EDUCATION	1	0
17	HOME AFFAIRS	1	1
	Total	535	43

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2023			
	<u>POWER</u>			
1	EASTERN REGION STRENGTHENING SCHEME-XVIII Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000258]	3,500.00	07/2020	3,183.32
2	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000301]	1,031.00	08/2021	1,024.67
	<u>URBAN DEVELOPMENT</u>			
3	NAGPUR METRO RAIL (NAGPUR METRO RAIL CORPORATION LTD) - [N28000085]	8,680.00	03/2018	8,491.14
	May,2023			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
4	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-08) (CH. 214.260 - CH. 247.31) [START OF ROB NEAR EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001577]	1,297.25	11/2022	950.33
	June,2023			
	<u>PETROLEUM</u>			
5	BOKARO-ANGUL PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000274]	3,437.00	12/2020	2,463.30
	<u>POWER</u>			
6	AMELIA COAL MINE Central Sector Projects(THDC INDIA LIMITED) - [N18000252]	2,104.21	09/2020	890.47
7	NOKHRA EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000282]	1,722.14	09/2021	1,710.02
	<u>HEALTH AND FAMILY WELFARE</u>			
8	AIIMS BILASPUR (NBCC FOR HEALTH) - [N21000028]	1,351.00	09/2021	1,185.10
	<u>RAILWAYS</u>			
9	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) (METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100164]	495.44	03/2004	1,920.57
10	KODERMA-RANCHI VIA BARKAKANA (NL),ECR (EAST CENTRAL RAILWAYS) - [220100222]	1,033.07	-	3,881.88
11	SUKINDA ROAD - ANGUL (NL)(ECOR) (RAIL VIKAS NIGAM LTD.) - [220100325]	1,202.70	02/2015	2,488.95

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) (WESTERN RAILWAY) - [N22000121]	829.74	03/2020	2,248.41
13	PALANPUR-SAMAKHAYALI (DL) (RAIL VIKAS NIGAM LTD.) - [N22000144]	1,548.66	12/2021	2,814.97
14	VIRAMGAM-SAMAKHIALI (DL) (WESTERN RAILWAY) - [N22000145]	1,037.15	03/2021	1,539.79
15	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) (RAIL VIKAS NIGAM LTD.) - [N22000313]	1,503.71	03/2020	4,483.77
16	HUBLI- CHIKJAJUR (SOUTH WESTERN RAILWAY) - [N22000325]	1,156.94	03/2020	1,590.73
17	HAJIPUR - BACHAWARA (EAST CENTRAL RAILWAYS) - [N22000334]	678.54	03/2019	1,089.30
18	SURENDRA NAGAR RAJKOT (WESTERN RAILWAY) - [N22000392]	1,002.39	03/2021	867.09
19	ROURKELA JHARSUGUDA THIRD LINE 101 KM (SOUTH EASTERN RAILWAY) - [N22000395]	969.83	03/2020	1,396.80
20	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) (RAIL VIKAS NIGAM LTD.) - [N22000407]	713.48	03/2020	3,240.14
21	SAMBALPUR - TITLAGARH - DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000410]	948.04	03/2020	2,517.11
22	RAIPUR - TITLAGARH - DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000411]	1,402.02	03/2020	1,479.06
23	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000413]	1,183.25	12/2020	2,256.64
24	BINA - KOTA DOUBLING WITH RE (RAIL VIKAS NIGAM LTD.) - [N22000414]	1,485.85	12/2020	2,606.08
25	GEVRA ROAD PENDRA ROAD (Indian Railway Construction Company Limited) - [N22000488]	2,288.00	03/2022	2,139.95
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
26	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000792]	809.07	06/2022	1,202.13
	<u>July, 2023</u>			
	<u>PETROLEUM</u>			
27	DHAMRA-ANGUL PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000272]	1,933.00	12/2020	2,103.90
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
28	4L FROM KM 42.000 TO KM 80.00 OF DODABALLAPUR BYPASS TO HOSKOTE SECTION OF NH-648 (OLD NH- 207) ON H PPP BOT (Hybrid Annuity)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001510]	1,278.00	02/2021	950.43

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2023-2024				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	April,2023			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000801]	1,052.21	12/2020	570.86

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	532
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	4
No of Projects in Current Month	535

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	280 (52.34%)	4 (.75%)	195 (36.45%)	15 (2.80%)	41 (7.66%)	535
Latest Approved (Date)	201 (37.57%)	14 (2.62%)	265 (49.53%)	13 (2.43%)	42 (7.85%)	535

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	393	14,85,903.10	16,73,805.76	7,89,373.90	47.20	1,87,902.66	12.60
Project with Revision in Cost	142	6,38,564.42	6,85,218.26	4,71,505.88	68.80	46,653.84	7.30
Total	535.00	21,24,467.52	23,59,024.02	12,60,879.78	53.45	2,34,556.50	11.04
Original Cost of All Projects							
Original Cost	535.00	19,00,616.36	23,59,024.02	12,60,879.78	53.45	4,58,407.66	24.12

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	280	10,61,346.70	13,85,268.11	8,79,316.18	63.50	3,23,921.41	30.52
Latest Approved (RCE)	201	9,38,332.59	10,94,754.83	7,01,354.30	64.10	1,56,422.24	16.67

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	43	1,17,106.08	2,02,261.59	1,60,926.04	79.60	85,155.51	72.70
Total	43	1,17,106.08	2,02,261.59	1,60,926.04	79.56	85,155.51	72.72

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 1000 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,439.00	14.30	3	27,271.00	43,969.00	61.23
2	CIVIL AVIATION	5	7,613.90	9,612.71	26.25	2	2,525.00	4,523.81	79.16
3	COAL	35	1,27,847.17	1,35,583.93	6.05	3	25,805.84	33,542.60	29.98
4	MINES	2	5,540.00	6,436.00	16.17	1	4,103.00	5,055.00	23.20
5	STEEL	4	21,558.98	30,002.87	39.17	2	17,617.97	26,061.86	47.93
6	PETROLEUM	58	3,27,413.35	3,48,582.80	6.47	15	61,322.26	83,677.71	36.46
7	POWER	48	2,30,995.67	2,85,738.15	23.70	14	70,309.71	1,25,052.19	77.86
8	HEALTH AND FAMILY WELFARE	3	4,342.55	4,342.55	0.00	0	0.00	0.00	0.00
9	RAILWAYS	101	3,22,502.64	5,64,923.95	75.17	79	1,67,689.78	4,10,506.09	144.80
10	ROAD TRANSPORT AND HIGHWAYS	245	4,00,194.43	4,31,965.41	7.94	77	1,16,356.96	1,50,012.57	28.92
11	SHIPPING AND PORTS	1	5,369.18	5,362.27	-0.13	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	22	2,80,260.24	3,05,681.47	9.07	7	1,17,061.56	1,42,561.99	21.78
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
15	DEPARTMENT OF HIGHER EDUCATION	1	676.00	1,085.04	60.51	1	676.00	1,085.04	60.51
16	HOME AFFAIRS	1	1,219.21	1,900.00	55.84	1	1,219.21	1,900.00	55.84
17	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	13.16
Total		535	19,00,616.36	23,59,024.02	24.12	207	6,26,882.33	10,88,897.73	73.70

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							1000	Crore and above	
(All Cost/ Expenditure in Rs. crore									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	24	99,763.08	1,55,356.81	55.73	14	50,921.87	1,06,580.72	109.30
2	ARUNACHAL PRADESH	4	41,859.31	56,879.42	35.88	2	8,264.33	23,284.44	181.75
3	ASSAM	9	35,636.05	43,904.80	23.20	4	16,125.52	25,564.27	58.53
4	BIHAR	32	84,576.34	1,05,956.47	25.28	13	31,483.82	53,500.09	69.93
5	GOA	1	1,183.16	1,183.16	0.00	0	0.00	0.00	0.00
6	GUJARAT	29	1,02,865.77	1,16,420.21	13.18	8	30,203.90	43,758.34	44.88
7	HARYANA	16	60,027.49	61,983.50	3.26	3	5,456.47	7,412.52	35.85
8	HIMACHAL PRADESH	10	19,567.14	31,702.02	62.02	5	9,690.38	21,825.26	125.23
9	JAMMU AND KASHMIR	18	55,528.29	90,545.19	63.06	3	4,997.72	40,014.62	700.66
10	KARNATAKA	25	78,944.18	86,556.10	9.64	9	12,602.07	20,679.99	64.10
11	KERALA	22	59,086.61	64,242.19	8.73	10	26,903.87	32,561.16	21.03
12	MADHYA PRADESH	19	38,765.87	46,007.69	18.68	6	10,122.58	17,364.40	71.54
13	MAHARASHTRA	48	1,32,665.72	1,61,064.24	21.41	20	70,323.34	98,765.74	40.45
14	MANIPUR	1	4,454.17	14,322.79	221.56	1	4,454.17	14,322.79	221.56
15	MEGHALAYA	1	906.46	8,324.28	818.33	1	906.46	8,324.28	818.33
16	MIZORAM	2	3,036.43	10,501.91	245.86	2	3,036.43	10,501.91	245.86
17	NAGALAND	1	2,326.52	6,663.00	186.39	1	2,326.52	6,663.00	186.39
18	ODISHA	35	99,922.61	1,05,376.28	5.46	9	14,866.26	20,375.93	37.06
19	PUNJAB	14	19,388.00	19,388.00	0.00	0	0.00	0.00	0.00
20	RAJASTHAN	24	55,166.12	59,925.12	8.63	1	12,320.00	17,079.00	38.63
21	SIKKIM	2	7,087.52	13,624.96	92.24	1	1,339.48	7,876.92	488.06
22	TAMIL NADU	36	1,92,748.40	2,15,411.37	11.76	16	43,907.09	66,965.06	52.52
23	UTTAR PRADESH	44	1,16,260.95	1,31,262.10	12.90	17	38,183.23	53,356.12	39.74
24	WEST BENGAL	22	53,463.56	72,530.13	35.66	13	29,169.64	48,252.21	65.42
25	DELHI	13	85,717.78	89,159.34	4.02	5	49,151.88	52,672.64	7.16
26	CHHATTISGARH	16	64,197.44	73,481.32	14.46	6	25,661.56	34,945.44	36.18
27	JHARKHAND	16	60,507.53	66,840.03	10.47	7	20,168.30	26,500.80	31.40
28	UTTARAKHAND	9	29,372.86	47,101.71	60.36	5	23,991.39	41,720.24	73.90
29	TELANGANA	5	15,405.53	17,658.07	14.62	2	11,759.46	14,012.00	19.16
30	MULTI STATE	37	2,80,185.47	3,85,651.81	37.64	23	68,544.59	1,74,017.84	153.88
Total		535	19,00,616.36	23,59,024.02	24.12	207	6,26,882.33	10,88,897.73	73.70

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,439.00	14.30	4	67,120.00	83,818.00	36 - 171
2	CIVIL AVIATION	5	7,613.90	9,612.71	26.25	5	7,613.90	9,612.71	16 - 48
3	COAL	35	1,27,847.17	1,35,583.93	6.05	11	50,165.09	54,818.96	17 - 96
4	MINES	2	5,540.00	6,436.00	16.17	2	5,540.00	6,436.00	5 - 47
5	STEEL	4	21,558.98	30,002.87	39.17	3	19,466.01	27,781.01	23 - 99
6	PETROLEUM	58	3,27,413.35	3,48,582.80	6.47	37	1,73,601.67	1,88,950.66	2 - 143
7	POWER	48	2,30,995.67	2,85,738.15	23.70	33	1,49,711.47	2,03,921.95	2 - 176
8	HEALTH AND FAMILY WELFARE	3	4,342.55	4,342.55	0.00	2	2,514.55	2,514.55	1 - 3
9	RAILWAYS	101	3,22,502.64	5,64,923.95	75.17	74	2,54,534.20	3,91,504.27	3 - 254
10	ROAD TRANSPORT AND HIGHWAYS	245	4,00,194.43	4,31,965.41	7.94	89	1,31,898.03	1,50,610.50	1 - 123
11	SHIPPING AND PORTS	1	5,369.18	5,362.27	-0.13	1	5,369.18	5,362.27	45 - 45
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	1	13,334.00	13,334.00	98 - 98
13	URBAN DEVELOPMENT	22	2,80,260.24	3,05,681.47	9.07	14	1,63,659.35	1,82,668.32	3 - 60
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	48 - 48
15	DEPARTMENT OF HIGHER EDUCATION	1	676.00	1,085.04	60.51	1	676.00	1,085.04	8 - 8
16	HOME AFFAIRS	1	1,219.21	1,900.00	55.84	1	1,219.21	1,900.00	50 - 50
17	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45 - 45
Total		535	19,00,616.36	23,59,024.02	24.12	280	10,61,346.70	13,85,268.11	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	24	99,763.08	1,55,356.81	55.73	9	76,397.72	1,29,392.79	3 - 216
2	ARUNACHAL PRADESH	4	41,859.31	56,879.42	35.88	2	8,003.92	22,966.13	24 - 176
3	ASSAM	9	35,636.05	43,904.80	23.20	3	4,700.32	6,617.65	6 - 48
4	BIHAR	32	84,576.34	1,05,956.47	25.28	15	61,984.36	79,168.76	2 - 153
5	GOA	1	1,183.16	1,183.16	0.00	1	1,183.16	1,183.16	18 - 18
6	GUJARAT	29	1,02,865.77	1,16,420.21	13.18	16	60,222.76	73,777.20	3 - 144
7	HARYANA	16	60,027.49	61,983.50	3.26	8	14,697.83	15,955.73	2 - 39
8	HIMACHAL PRADESH	10	19,567.14	31,702.02	62.02	4	8,157.97	16,031.01	32 - 174
9	JAMMU AND KASHMIR	18	55,528.29	90,545.19	63.06	9	28,790.33	63,711.63	1 - 254
10	KARNATAKA	25	78,944.18	86,556.10	9.64	11	40,610.16	44,651.76	9 - 120
11	KERALA	22	59,086.61	64,242.19	8.73	4	6,880.35	8,587.01	13 - 68
12	MADHYA PRADESH	19	38,765.87	46,007.69	18.68	12	29,745.01	36,986.83	17 - 57
13	MAHARASHTRA	48	1,32,665.72	1,61,064.24	21.41	20	66,159.84	89,729.01	6 - 97
14	MANIPUR	1	4,454.17	14,322.79	221.56	1	4,454.17	14,322.79	168 - 168
15	MEGHALAYA	1	906.46	8,324.28	818.33	0	0.00	0.00	-
16	MIZORAM	2	3,036.43	10,501.91	245.86	2	3,036.43	10,501.91	7 - 119
17	NAGALAND	1	2,326.52	6,663.00	186.39	1	2,326.52	6,663.00	132 - 132
18	ODISHA	35	99,922.61	1,05,376.28	5.46	18	49,275.00	53,477.38	5 - 213
19	PUNJAB	14	19,388.00	19,388.00	0.00	5	6,089.87	6,089.87	3 - 50
20	RAJASTHAN	24	55,166.12	59,925.12	8.63	15	38,760.66	43,519.66	2 - 84
21	SIKKIM	2	7,087.52	13,624.96	92.24	2	7,087.52	13,624.96	29 - 96
22	TAMIL NADU	36	1,92,748.40	2,15,411.37	11.76	19	69,339.64	81,045.48	2 - 171
23	UTTAR PRADESH	44	1,16,260.95	1,31,262.10	12.90	27	88,697.80	99,018.75	1 - 60
24	WEST BENGAL	22	53,463.56	72,530.13	35.66	16	39,085.68	58,031.48	5 - 141
25	DELHI	13	85,717.78	89,159.34	4.02	7	37,823.53	39,669.18	12 - 50
26	CHHATTISGARH	16	64,197.44	73,481.32	14.46	9	47,548.64	56,689.37	23 - 99
27	JHARKHAND	16	60,507.53	66,840.03	10.47	7	39,149.05	43,408.83	8 - 95
28	UTTARAKHAND	9	29,372.86	47,101.71	60.36	6	25,375.17	43,104.02	3 - 156
29	TELANGANA	5	15,405.53	17,658.07	14.62	3	12,870.01	15,122.55	3 - 180
30	MULTI STATE	37	2,80,185.47	3,85,651.81	37.64	28	1,82,893.28	2,12,220.21	4 - 202
Total		535	19,00,616.36	23,59,024.02	24.12	280	10,61,346.70	13,85,268.11	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,439.00	0.63	4	82,988.00	83,818.00	36 - 171
2	CIVIL AVIATION	5	7,613.90	9,612.71	26.25	4	6,208.90	8,207.71	26 - 48
3	COAL	35	1,27,847.29	1,35,583.93	6.05	10	48,471.28	53,125.15	17 - 96
4	MINES	2	6,436.00	6,436.00	0.00	2	6,436.00	6,436.00	5 - 47
5	STEEL	4	30,002.87	30,002.87	0.00	3	27,781.01	27,781.01	23 - 99
6	PETROLEUM	58	3,44,437.59	3,48,582.80	1.20	14	69,050.27	69,050.27	2 - 97
7	POWER	48	2,65,089.75	2,85,738.15	7.79	23	1,36,717.88	1,51,874.39	2 - 156
8	HEALTH AND FAMILY WELFARE	3	4,342.55	4,342.55	0.00	2	2,514.55	2,514.55	1 - 3
9	RAILWAYS	101	4,44,008.97	5,64,923.95	27.23	62	2,75,948.86	3,43,193.82	3 - 254
10	ROAD TRANSPORT AND HIGHWAYS	245	4,23,787.71	4,31,965.41	1.93	62	1,10,920.30	1,13,765.89	0 - 123
11	SHIPPING AND PORTS	1	4,633.10	5,362.27	15.74	1	4,633.10	5,362.27	45 - 45
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	1	13,334.00	13,334.00	98 - 98
13	URBAN DEVELOPMENT	22	2,82,496.46	3,05,681.47	8.21	10	1,36,669.15	1,53,441.90	3 - 60
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	48 - 48
15	DEPARTMENT OF HIGHER EDUCATION	1	1,085.04	1,085.04	0.00	0	0.00	0.00	-
16	HOME AFFAIRS	1	1,735.25	1,900.00	9.49	1	1,735.25	1,900.00	50 - 50
17	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45 - 45
Total		535	21,24,467.52	23,59,024.02	11.04	201	9,38,332.59	10,94,754.83	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,439.00	0.63	1	6,840.00	7,670.00	12.13
2	CIVIL AVIATION	5	7,613.90	9,612.71	26.25	2	2,525.00	4,523.81	79.16
3	COAL	35	1,27,847.29	1,35,583.93	6.05	3	25,805.84	33,542.60	29.98
4	MINES	2	6,436.00	6,436.00	0.00	0	0.00	0.00	0.00
5	STEEL	4	30,002.87	30,002.87	0.00	0	0.00	0.00	0.00
6	PETROLEUM	58	3,44,437.59	3,48,582.80	1.20	1	12,366.00	18,968.00	53.39
7	POWER	48	2,65,089.75	2,85,738.15	7.79	10	46,849.25	67,497.65	44.07
8	HEALTH AND FAMILY WELFARE	3	4,342.55	4,342.55	0.00	0	0.00	0.00	0.00
9	RAILWAYS	101	4,44,008.97	5,64,923.95	27.23	62	1,68,590.41	2,89,900.39	71.96
10	ROAD TRANSPORT AND HIGHWAYS	245	4,23,787.71	4,31,965.41	1.93	48	76,200.88	94,147.52	23.55
11	SHIPPING AND PORTS	1	4,633.10	5,362.27	15.74	1	4,633.10	5,362.27	15.74
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	22	2,82,496.46	3,05,681.47	8.21	6	1,05,641.56	1,28,905.77	22.02
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
15	DEPARTMENT OF HIGHER EDUCATION	1	1,085.04	1,085.04	0.00	0	0.00	0.00	0.00
16	HOME AFFAIRS	1	1,735.25	1,900.00	9.49	1	1,735.25	1,900.00	9.49
17	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	13.16
Total		535	21,24,467.52	23,59,024.02	11.04	137	4,66,111.33	7,13,367.88	53.05

[^] - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,439.00	0.63	1	6,840.00	7,670.00	171- 171
2	CIVIL AVIATION	5	7,613.90	9,612.71	26.25	2	2,525.00	4,523.81	39- 48
3	COAL	35	1,27,847.29	1,35,583.93	6.05	2	19,898.73	24,552.60	25- 60
4	MINES	2	6,436.00	6,436.00	0.00	0	0.00	0.00	0- 0
5	STEEL	4	30,002.87	30,002.87	0.00	0	0.00	0.00	0- 0
6	PETROLEUM	58	3,44,437.59	3,48,582.80	1.20	0	0.00	0.00	0- 0
7	POWER	48	2,65,089.75	2,85,738.15	7.79	9	46,317.25	61,473.76	20- 141
8	HEALTH AND FAMILY WELFARE	3	4,342.55	4,342.55	0.00	0	0.00	0.00	0- 0
9	RAILWAYS	101	4,44,008.97	5,64,923.95	27.23	41	84,934.41	1,52,574.37	3- 216
10	ROAD TRANSPORT AND HIGHWAYS	245	4,23,787.71	4,31,965.41	1.93	19	28,920.40	36,631.08	3- 123
11	SHIPPING AND PORTS	1	4,633.10	5,362.27	15.74	1	4,633.10	5,362.27	45- 45
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	22	2,82,496.46	3,05,681.47	8.21	3	47,274.77	64,126.72	3- 60
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	48- 48
15	DEPARTMENT OF HIGHER EDUCATION	1	1,085.04	1,085.04	0.00	0	0.00	0.00	0- 0
16	HOME AFFAIRS	1	1,735.25	1,900.00	9.49	1	1,735.25	1,900.00	50- 50
17	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45- 45
Total		535	21,24,467.52	23,59,024.02	11.04	81	2,58,002.95	4,19,764.48	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,439.00	14.30	3	27,271.00	43,969.00	84- 171
2	CIVIL AVIATION	5	7,613.90	9,612.71	26.25	2	2,525.00	4,523.81	39- 48
3	COAL	35	1,27,847.17	1,35,583.93	6.05	2	19,898.73	24,552.60	25- 60
4	MINES	2	5,540.00	6,436.00	16.17	1	4,103.00	5,055.00	47- 47
5	STEEL	4	21,558.98	30,002.87	39.17	1	15,525.00	23,840.00	99- 99
6	PETROLEUM	58	3,27,413.35	3,48,582.80	6.47	13	48,045.70	63,410.69	2- 143
7	POWER	48	2,30,995.67	2,85,738.15	23.70	13	64,817.82	1,19,028.30	20- 176
8	HEALTH AND FAMILY WELFARE	3	4,342.55	4,342.55	0.00	0	0.00	0.00	0- 0
9	RAILWAYS	101	3,22,502.64	5,64,923.95	75.17	59	1,14,334.81	2,51,699.88	3- 254
10	ROAD TRANSPORT AND HIGHWAYS	245	4,00,194.43	4,31,965.41	7.94	43	62,197.79	80,954.18	3- 123
11	SHIPPING AND PORTS	1	5,369.18	5,362.27	-0.13	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	22	2,80,260.24	3,05,681.47	9.07	4	58,694.77	77,782.94	3- 60
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	48- 48
15	DEPARTMENT OF HIGHER EDUCATION	1	676.00	1,085.04	60.51	1	676.00	1,085.04	8- 8
16	HOME AFFAIRS	1	1,219.21	1,900.00	55.84	1	1,219.21	1,900.00	50- 50
17	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	45- 45
Total		535	19,00,616.36	23,59,024.02	24.12	145	4,34,232.87	7,58,751.31	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>					Rs. 1000		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	<u>PETROLEUM</u>							
1	DHAMRA-ANGUL PIPELINE PROJECT	03/2017	1,933.00	12/2020	2,451.00	06/2023	2,103.90	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) PPP (BOT)	11/2013	1,916.79	11/2016	1,916.79	N.A.	1,660.92	
3	4L FROM KM 42.000 TO KM 80.00 OF DODABALLAPUR BYPASS TO HOSKOTE SECTION OF NH-648 (OLD NH- 207) ON H PPP BOT (Hybrid Annuity)	01/2020	1,278.00	02/2021	1,278.00	07/2023	950.43	
4	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	2,168.66	06/2019	2,168.66	12/2023	0.00	

TABLE-32

List of projects added Rs. 1000 Crore and above					(July 2023)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
1	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. HAM(Hybrid Annuity Mode)	12/2022	1,058.90	10/2025	1,058.90	10/2025
2	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 HAM(Hybrid Annuity Mode)	2/2023	1,253.24	10/2025	1,253.24	10/2025
3	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. HAM(Hybrid Annuity Mode)	2/2023	1,200.42	10/2025	1,200.42	10/2025
4	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 HAM(Hybrid Annuity Mode)	5/2022	1,063.72	7/2025	1,063.72	7/2025

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2637	
Achieved up to month	1658	

TABLE-34

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above							(July 2023)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI AAI	2,467.00	2,467.00	02/2022	07/2025	12/2025	5
	<u>COAL</u>						
2	JAYANT EXPANSION OCP 10 TO 20 MTPA NCL Central Sector Projects	1,783.09	1,783.09	03/2021	07/2023	10/2023	3
	<u>STEEL</u>						
3	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	23,840.00	05/2015	07/2023	08/2023	1
	<u>PETROLEUM</u>						
4	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT IOCL	1,636.00	1,636.00	08/2020	07/2023	11/2023	4
5	R and D CAMPUS II AT FARIDABAD IOCL	2,281.94	3,219.94	12/2022	11/2024	07/2025	8
6	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY IOCL Central Sector Projects	13,805.00	13,805.00	01/2024	01/2024	07/2025	18
	<u>POWER</u>						
7	BARH STPP(3X660MW) NTPC	8,692.97	21,312.11	10/2011	06/2024	07/2024	1
8	NAITWAR MORI HEP SJVN	648.33	1,272.29	12/2021	07/2023	08/2023	1
9	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C PGCIL PPP (BOT)	1,326.00	1,326.00	03/2023	08/2023	09/2023	1
10	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B PGCIL Central Sector Projects	4,546.26	4,546.26	06/2023	03/2024	06/2024	3
11	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) NTPC EPC	1,442.60	1,442.60	03/2024	03/2024	06/2024	3
12	TEHRI PUMPED STORAGE PLANT(1000MW) THDCIL	1,657.00	4,825.60	02/2016	02/2024	06/2024	4
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	6,285.33	21,247.54	09/2010	12/2024	05/2025	5

List of projects reporting additional delayed Rs. 1000 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
14	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	2,635.55	02/2020	09/2023	03/2024	6
15	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCIL	2,491.58	3,860.35	06/2013	06/2025	06/2026	12
	<u>RAILWAYS</u>						
16	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	37,012.26	11/2002	12/2023	01/2024	1
17	ROSA-SITAPUR CANTT-BURHWAL DOUBLING NER	1,295.42	2,560.00	03/2022	09/2023	10/2023	1
18	BONDAMUNDA RANCHI DOUBLING SER	1,724.20	3,029.04	03/2021	02/2024	03/2024	1
19	GADAG-WADI NL SWR	2,841.84	2,841.84	12/2018	06/2025	03/2026	9
20	PIRPAINTI-JASIDIH ER	915.98	2,137.81	03/2022	03/2024	03/2025	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
21	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] NHAI	1,587.49	3,063.99	04/2019	06/2023	07/2023	1
22	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA NHAI	1,094.97	1,094.97	02/2022	07/2023	08/2023	1
23	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE NHAI	1,047.00	1,047.00	05/2020	07/2023	08/2023	1
24	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE NHAI EPC	2,312.26	2,312.26	09/2021	07/2023	08/2023	1
25	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN NHAI EPC	2,252.75	2,252.75	09/2021	07/2023	08/2023	1
26	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA NHAI EPC	1,935.61	1,935.61	09/2021	07/2023	08/2023	1
27	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR NHAI	1,396.74	1,396.74	10/2019	05/2023	07/2023	2
28	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29 NHAI EPC	1,523.77	1,523.77	04/2023	05/2023	07/2023	2

List of projects reporting additional delayed Rs. 1000 Crore and above							(July 2023)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
29	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP NHAIPP BOT (Hybrid Annuity)	1,334.04	1,334.00	01/2024	01/2024	03/2024	2
30	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S NHAIPP BOT (Hybrid Annuity)	2,334.68	2,335.00	03/2023	09/2023	11/2023	2
31	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP NHAIPP BOT (Hybrid Annuity)	1,690.23	2,010.17	12/2023	12/2023	03/2024	3
32	6L ALURU - JAKKUA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) NHAIPP BOT (Hybrid Annuity)	922.50	1,128.68	03/2024	03/2024	06/2024	3
33	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 NHAIPP BOT (Hybrid Annuity)	1,408.00	1,659.12	07/2020	10/2023	02/2024	4
34	4-LANNING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) NHAIPP BOT (Hybrid Annuity)	1,518.53	1,518.53	10/2022	08/2023	12/2023	4
35	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN NHAIPP EPC	1,100.88	1,100.88	11/2021	11/2023	04/2024	5
36	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY NHAIPP EPC	2,919.96	2,919.96	02/2024	02/2024	08/2024	6
37	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V NHAIPP BOT (Hybrid Annuity)	1,060.29	1,060.29	01/2024	06/2023	12/2023	6
38	VARANASI-AURANGABAD KM.786 TO KM.978.40 NHAIPP BOT	2,848.00	3,379.45	03/2014	11/2023	06/2024	7
39	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD MoRTH EPC	1,948.25	1,948.25	02/2024	02/2024	09/2024	7
40	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N NHAIPP EPC	1,101.99	1,101.99	08/2023	02/2024	12/2024	10
41	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU MoRTH	1,979.00	2,036.90	N.A.	12/2021	05/2023	17
	HOME AFFAIRS						

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above (July 2023)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
42	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD FOR MHA	1,219.21	1,900.00	10/2019	09/2023	12/2023	3
	<u>DPIIT</u>						
43	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE IICC FOR DPIIT	4,773.00	5,401.00	12/2019	07/2023	09/2023	2

TABLE-35

Sector wise analysis of projects Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,326,09.00	1,33,439.00	92,937.75
CIVIL AVIATION	5	7,613.90	76,13.90	9,612.71	3,946.23
COAL	35	1,27,847.17	1,278,47.29	1,35,583.93	57,013.70
MINES	2	5,540.00	64,36.00	6,436.00	2,862.34
STEEL	4	21,558.98	300,02.87	30,002.87	26,042.15
PETROLEUM	58	3,27,413.35	3,444,37.59	3,48,582.80	1,50,492.84
POWER	48	2,30,995.67	2,650,89.75	2,85,738.15	1,56,412.52
HEALTH AND FAMILY WELFARE	3	4,342.55	43,42.55	4,342.55	1,104.85
RAILWAYS	101	3,22,502.64	4,440,08.97	5,64,923.95	3,51,539.38
ROAD TRANSPORT AND HIGHWAYS	245	4,00,194.43	4,237,87.71	4,31,965.41	1,78,285.19
SHIPPING AND PORTS	1	5,369.18	46,33.10	5,362.27	2,498.52
TELECOMMUNICATIONS	1	13,334.00	133,34.00	13,334.00	21,913.00
URBAN DEVELOPMENT	22	2,80,260.24	2,824,96.46	3,05,681.47	1,78,739.96
WATER RESOURCES	1	10,151.04	101,51.04	55,548.87	21,727.98
DEPARTMENT OF HIGHER EDUCATION	1	676.00	10,85.04	1,085.04	24.75
HOME AFFAIRS	1	1,219.21	17,35.25	1,900.00	1,583.95
DPIIT	2	24,857.00	248,57.00	25,485.00	13,754.67
Grand total	535	19,00,616.36	21,24,467.52	23,59,024.02	12,60,879.78


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	24	99,763.08	1,55,356.81	55.73	6	37,904.62	90,899.69	3 - 216
2	ARUNACHAL PRADESH	4	41,859.31	56,879.42	35.88	1	6,285.33	21,247.54	176 - 176
3	ASSAM	9	35,636.05	43,904.80	23.20	2	3,374.32	5,291.65	48 - 48
4	BIHAR	32	84,576.34	1,05,956.47	25.28	9	29,928.91	47,113.31	3 - 153
5	GOA	1	1,183.16	1,183.16	0.00	0	0.00	0.00	-
6	GUJARAT	29	1,02,865.77	1,16,420.21	13.18	8	30,203.90	43,758.34	6 - 144
7	HARYANA	16	60,027.49	61,983.50	3.26	2	3,972.17	5,230.11	3 - 31
8	HIMACHAL PRADESH	10	19,567.14	31,702.02	62.02	2	4,398.33	12,271.37	32 - 174
9	JAMMU AND KASHMIR	18	55,528.29	90,545.19	63.06	2	3,176.00	38,097.30	8 - 254
10	KARNATAKA	25	78,944.18	86,556.10	9.64	7	8,955.30	12,996.90	9 - 120
11	KERALA	22	59,086.61	64,242.19	8.73	4	6,880.35	8,587.01	13 - 68
12	MADHYA PRADESH	19	38,765.87	46,007.69	18.68	6	10,122.58	17,364.40	27 - 57
13	MAHARASHTRA	48	1,32,665.72	1,61,064.24	21.41	14	56,720.50	80,333.55	6 - 97
14	MANIPUR	1	4,454.17	14,322.79	221.56	1	4,454.17	14,322.79	168 - 168
15	MEGHALAYA	1	906.46	8,324.28	818.33	0	0.00	0.00	-
16	MIZORAM	2	3,036.43	10,501.91	245.86	2	3,036.43	10,501.91	7 - 119
17	NAGALAND	1	2,326.52	6,663.00	186.39	1	2,326.52	6,663.00	132 - 132
18	ODISHA	35	99,922.61	1,05,376.28	5.46	5	10,859.23	15,117.61	24 - 213
19	PUNJAB	14	19,388.00	19,388.00	0.00	0	0.00	0.00	-
20	RAJASTHAN	24	55,166.12	59,925.12	8.63	1	12,320.00	17,079.00	84 - 84
21	SIKKIM	2	7,087.52	13,624.96	92.24	1	1,339.48	7,876.92	96 - 96
22	TAMIL NADU	36	1,92,748.40	2,15,411.37	11.76	10	17,835.94	29,936.78	2 - 171
23	UTTAR PRADESH	44	1,16,260.95	1,31,262.10	12.90	12	31,639.31	41,960.26	5 - 60
24	WEST BENGAL	22	53,463.56	72,530.13	35.66	12	26,976.41	45,938.21	6 - 141
25	DELHI	13	85,717.78	89,159.34	4.02	4	10,566.88	12,491.73	15 - 50
26	CHHATTISGARH	16	64,197.44	73,481.32	14.46	4	21,713.00	30,853.73	43 - 99
27	JHARKHAND	16	60,507.53	66,840.03	10.47	3	16,914.05	21,173.83	12 - 60
28	UTTARAKHAND	9	29,372.86	47,101.71	60.36	5	23,991.39	41,720.24	3 - 156
29	TELANGANA	5	15,405.53	17,658.07	14.62	2	11,759.46	14,012.00	33 - 180
30	MULTI STATE	37	2,80,185.47	3,85,651.81	37.64	19	36,578.29	65,912.13	22 - 202
Total		535	19,00,616.36	23,59,024.02	24.12	145	4,34,232.87	7,58,751.31	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

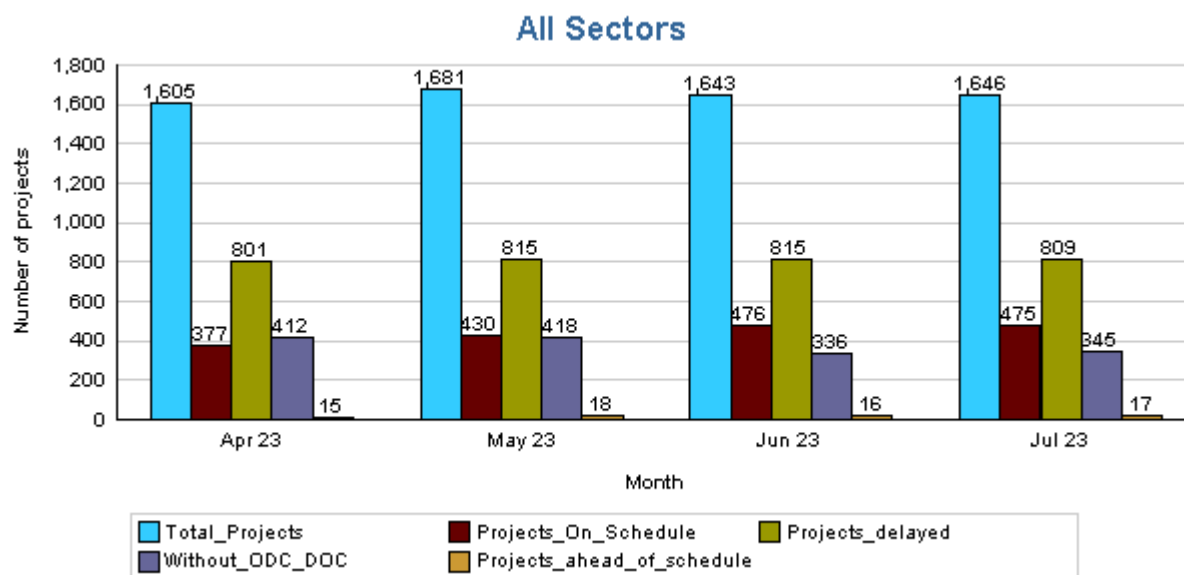

Break-up of 809 Delayed projects in July 2023

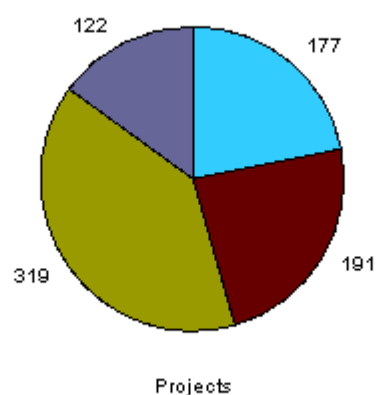


Delay in Months

Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of RENEWABLE ENERGY Sector

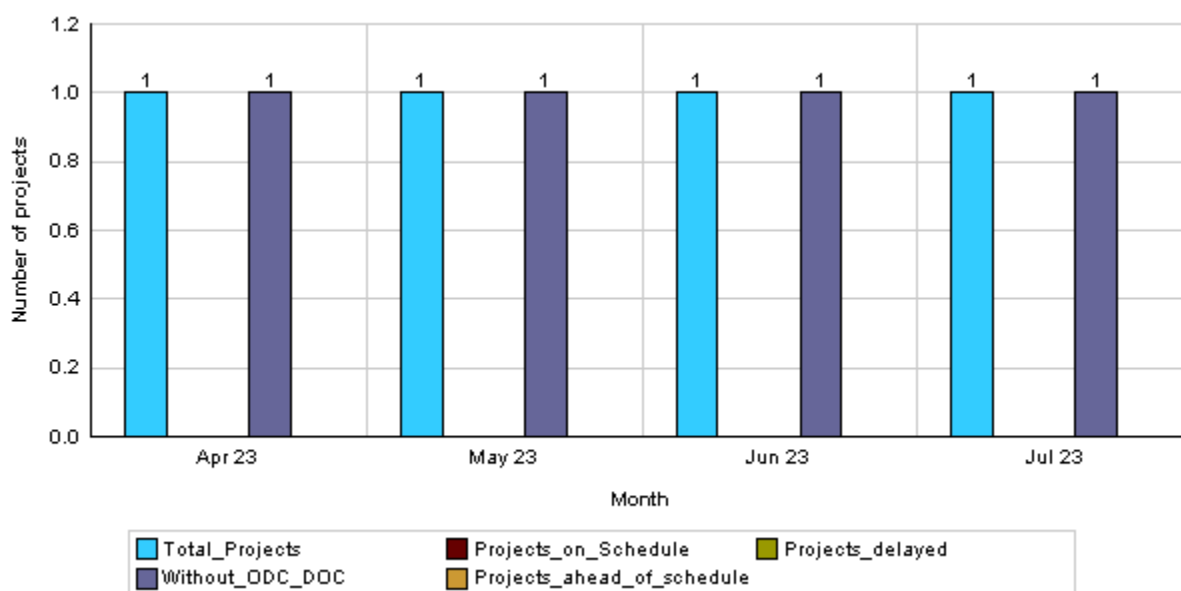


Break-up of 0 Delayed projects in July 2023

Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of DONER Sector

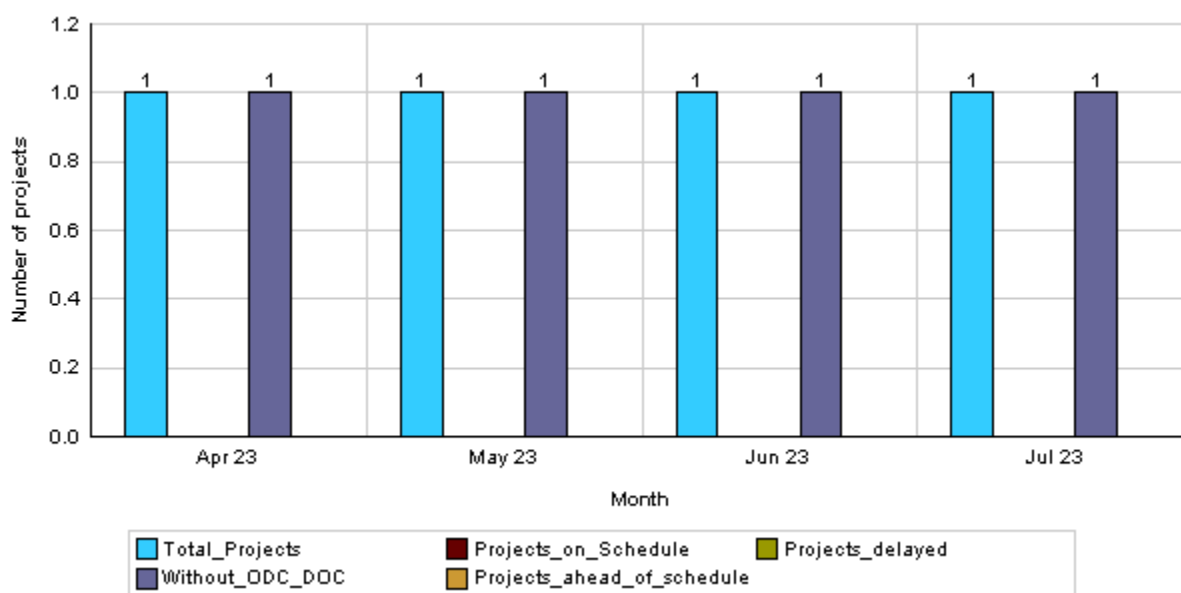


Break-up of 0 Delayed projects in July 2023


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12				
13-24				
25-60				
MORE THAN 60				

Graphical Presentation of DPIIT Sector

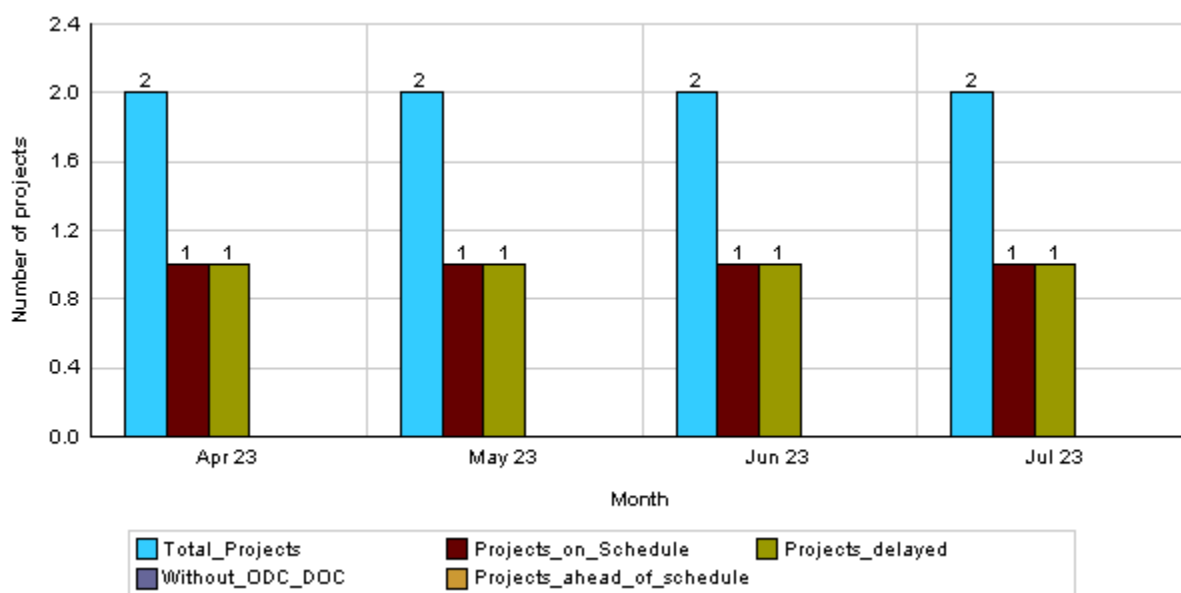


Break-up of 1 Delayed projects in July 2023

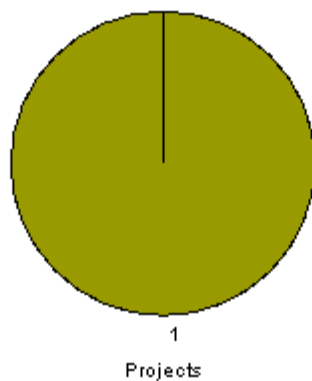


Delay in Months

Delay in Months	Count
1-12	0
13-24	0
25-60	1
MORE THAN 60	0

Graphical Presentation of HOME AFFAIRS Sector

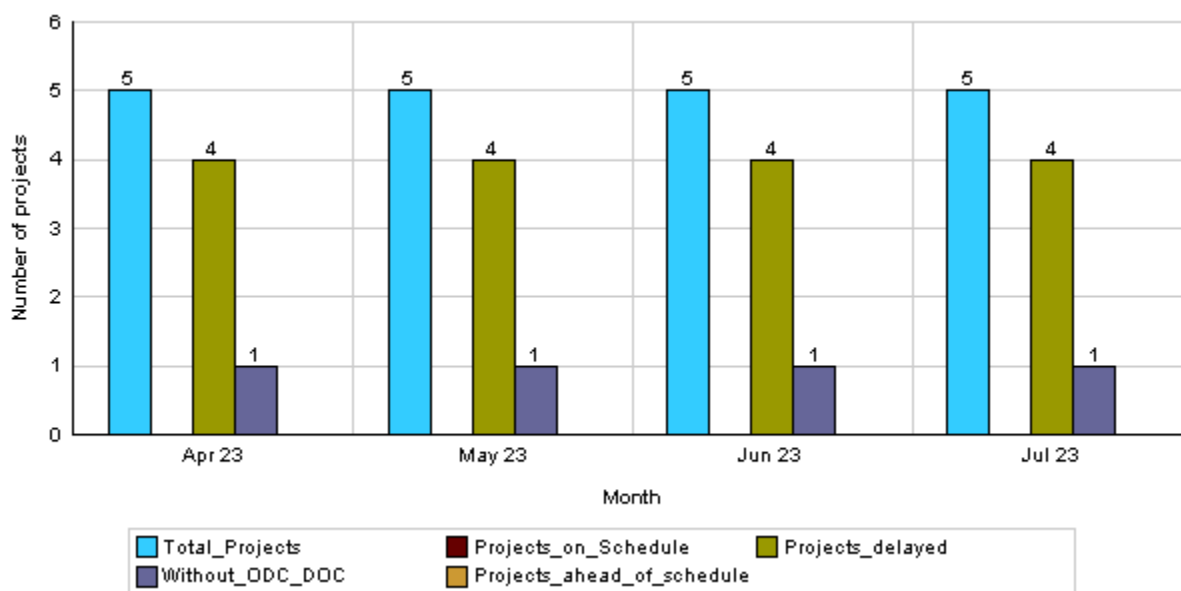


Break-up of 4 Delayed projects in July 2023

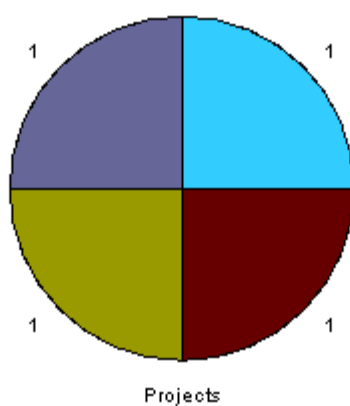


Delay in Months

Delay in Months	Count
1-12	1
13-24	1
25-60	1
MORE THAN 60	1

Graphical Presentation of DEPARTMENT OF HIGHER EDUCATION Sector

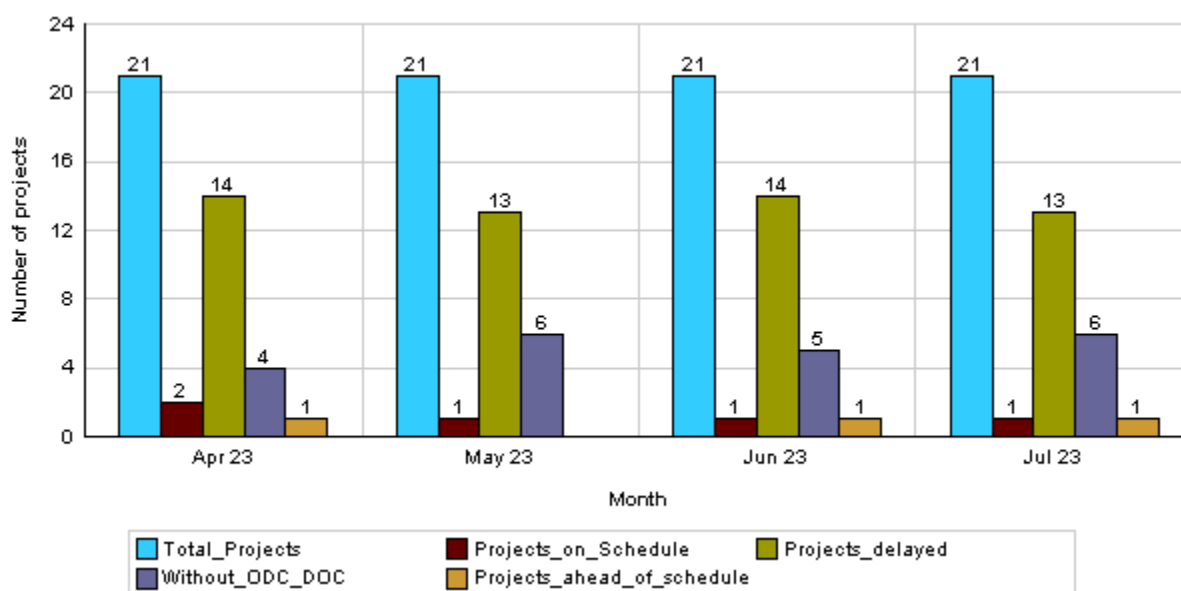


Break-up of 13 Delayed projects in July 2023

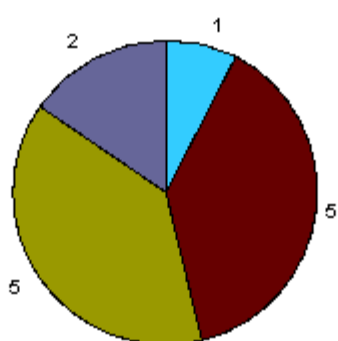

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	5	5	2

Graphical Presentation of COMMERCE Sector

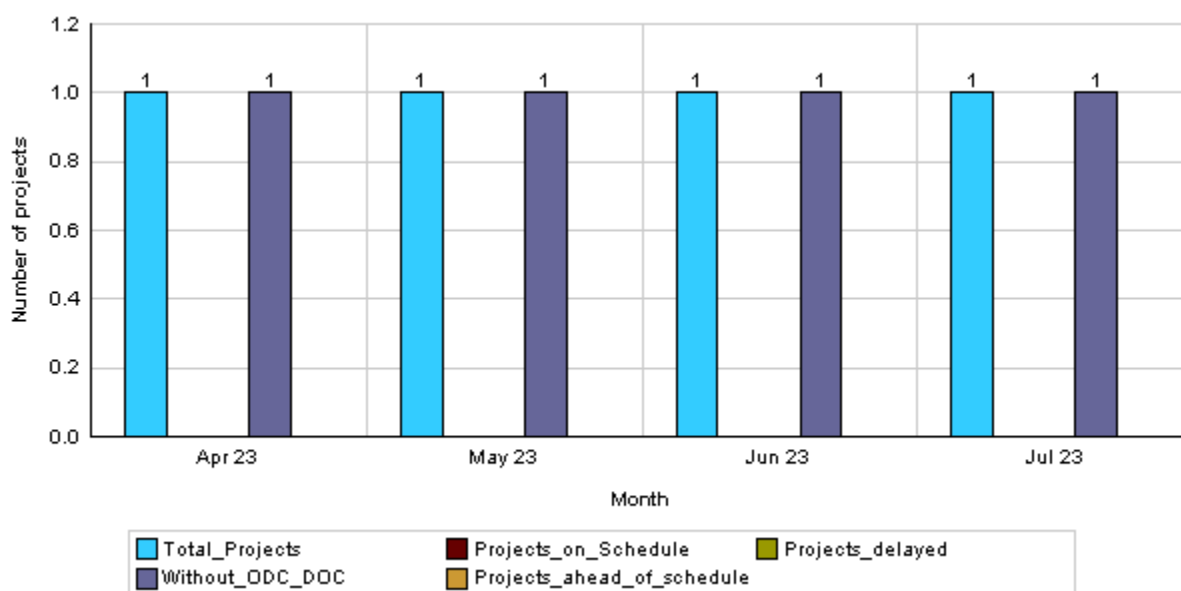


Break-up of 0 Delayed projects in July 2023

Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of DEFENCE PRODUCTION Sector

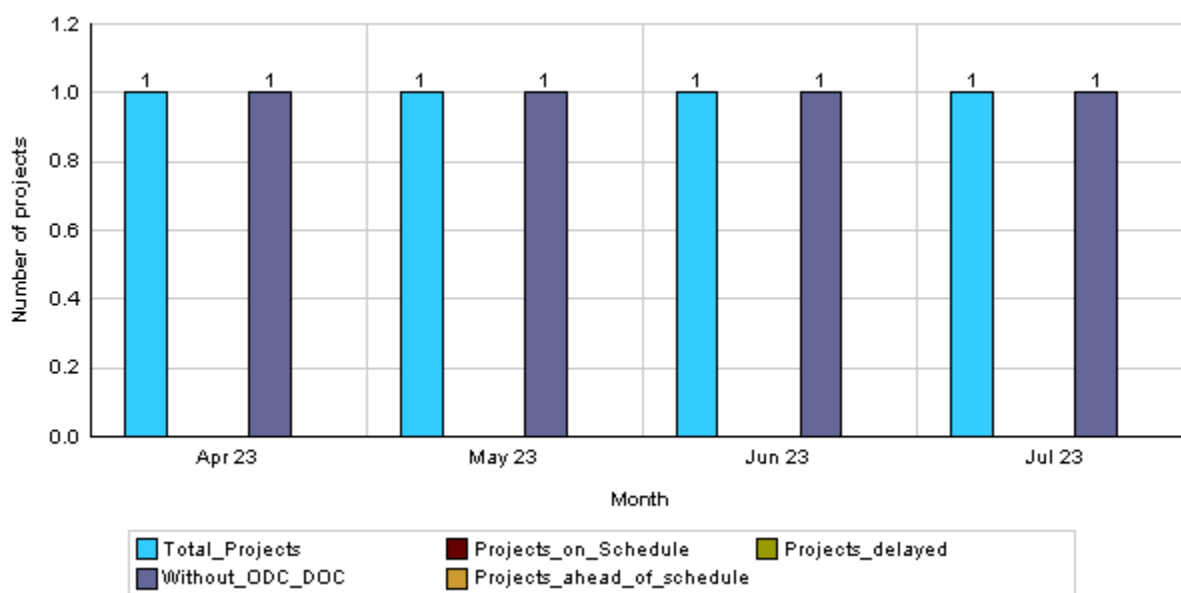


Break-up of 0 Delayed projects in July 2023


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

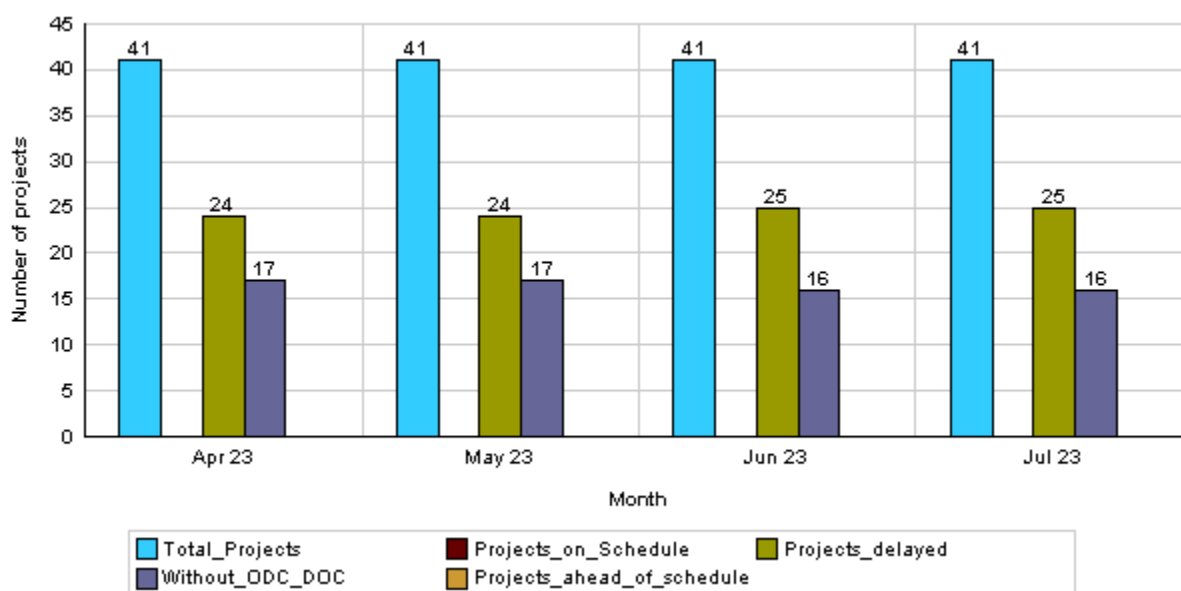


Break-up of 25 Delayed projects in July 2023

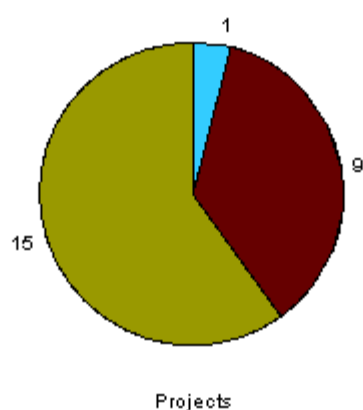


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	9	15	0

Graphical Presentation of URBAN DEVELOPMENT Sector

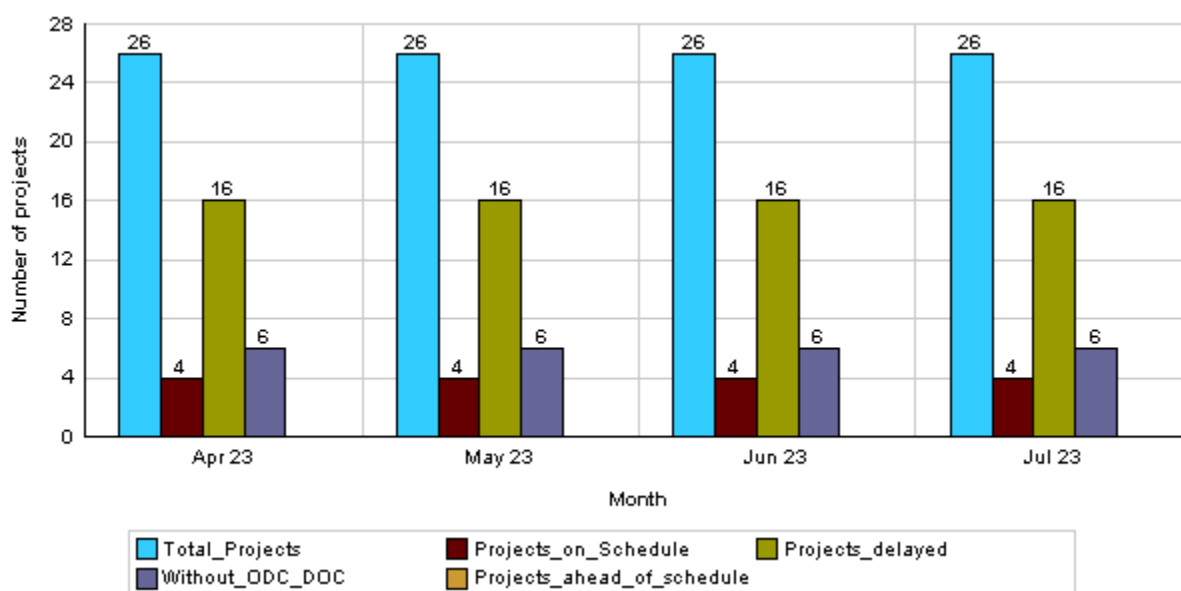


Break-up of 16 Delayed projects in July 2023

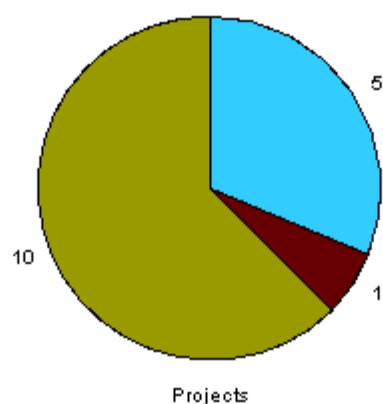


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of TELECOMMUNICATIONS Sector

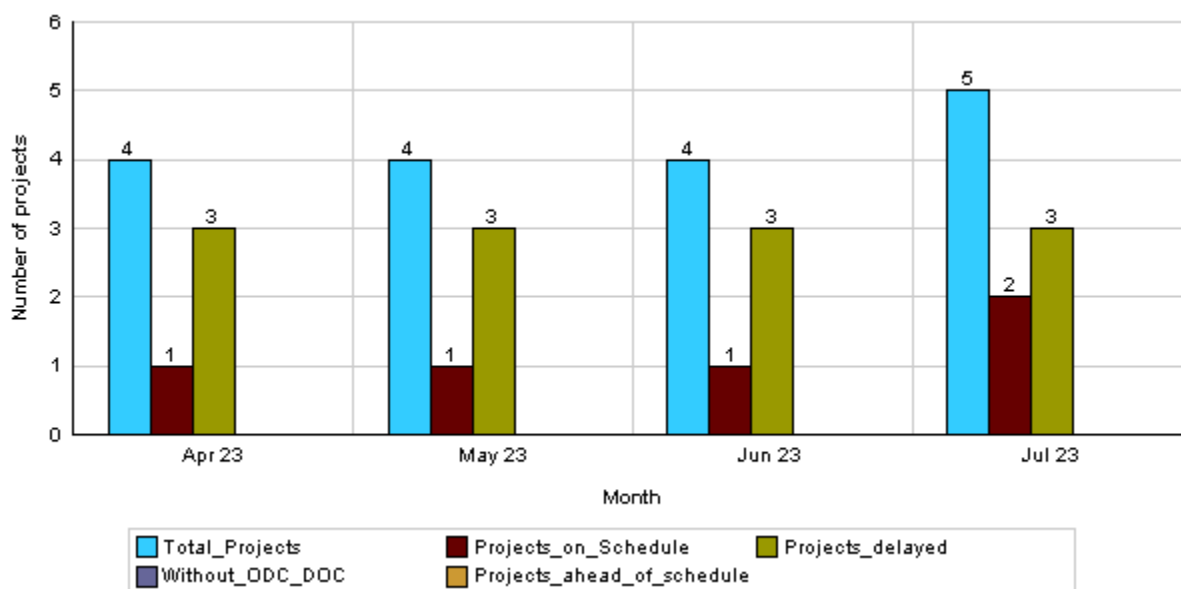


Break-up of 3 Delayed projects in July 2023

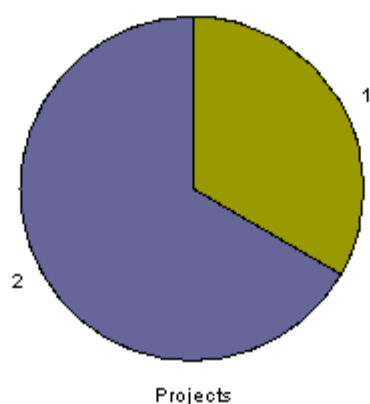


Delay in Months

Legend: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Dark Blue)

Graphical Presentation of SHIPPING AND PORTS Sector

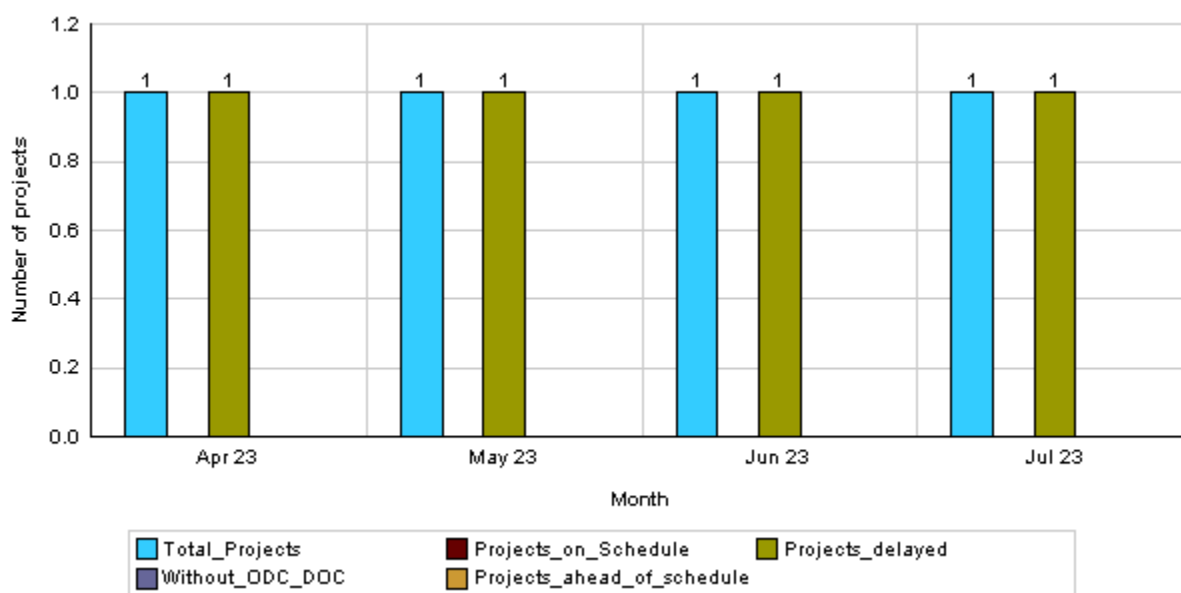


Break-up of 1 Delayed projects in July 2023

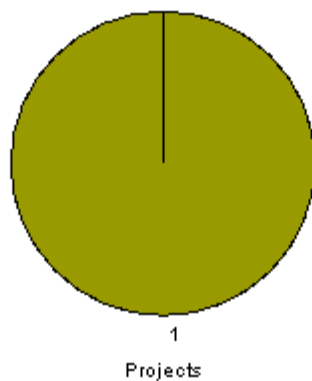


Delay in Months

Delay in Months	Count
1-12	1
13-24	0
25-60	0
MORE THAN 60	0

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

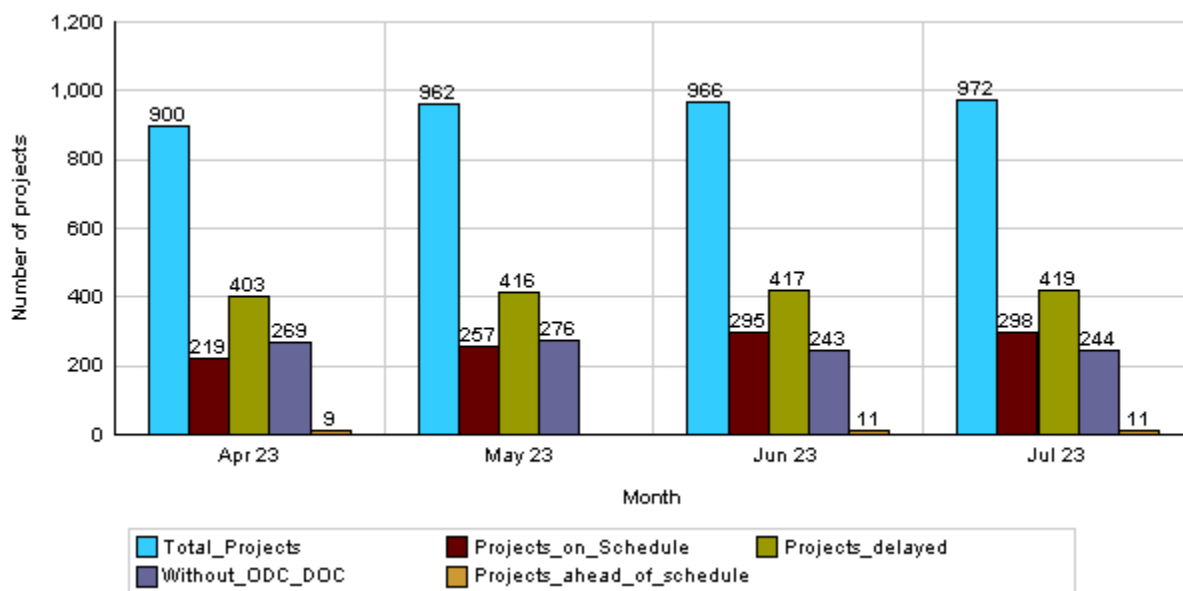


Break-up of 419 Delayed projects in July 2023

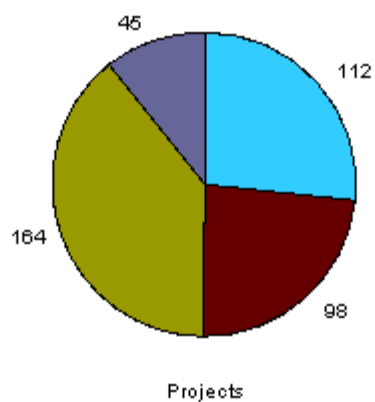


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

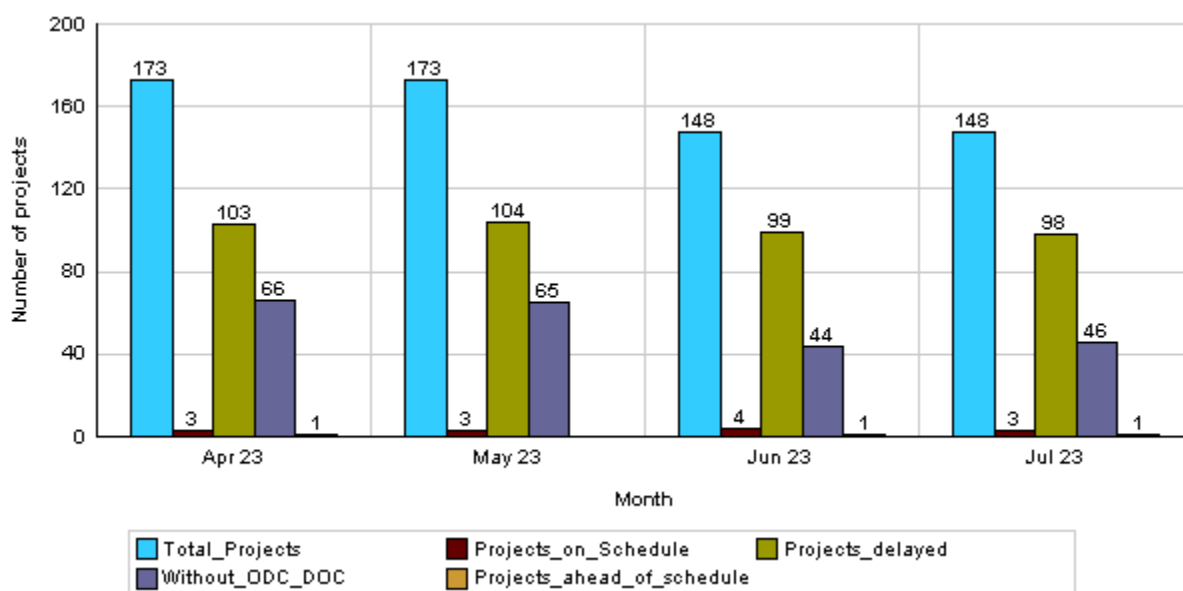


Break-up of 98 Delayed projects in July 2023

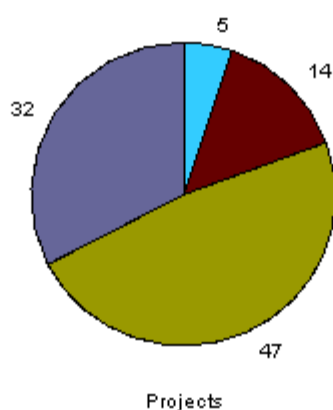


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	5	14	47	32

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

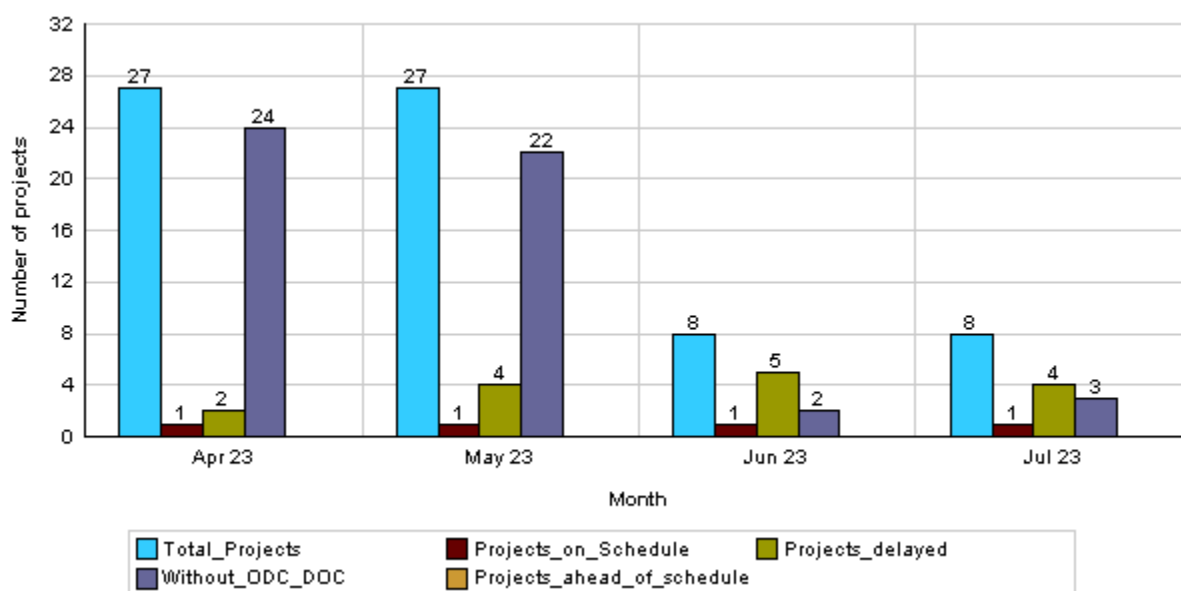


Break-up of 4 Delayed projects in July 2023

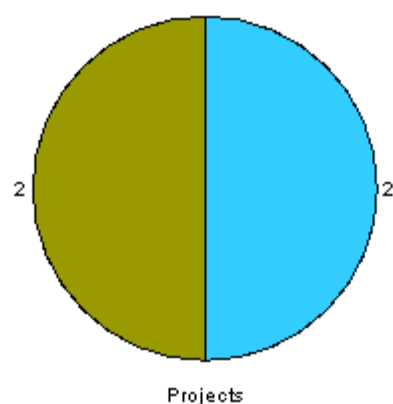


Delay in Months

Delay in Months	Count
1-12	2
13-24	0
25-60	2
MORE THAN 60	0

Graphical Presentation of POWER Sector

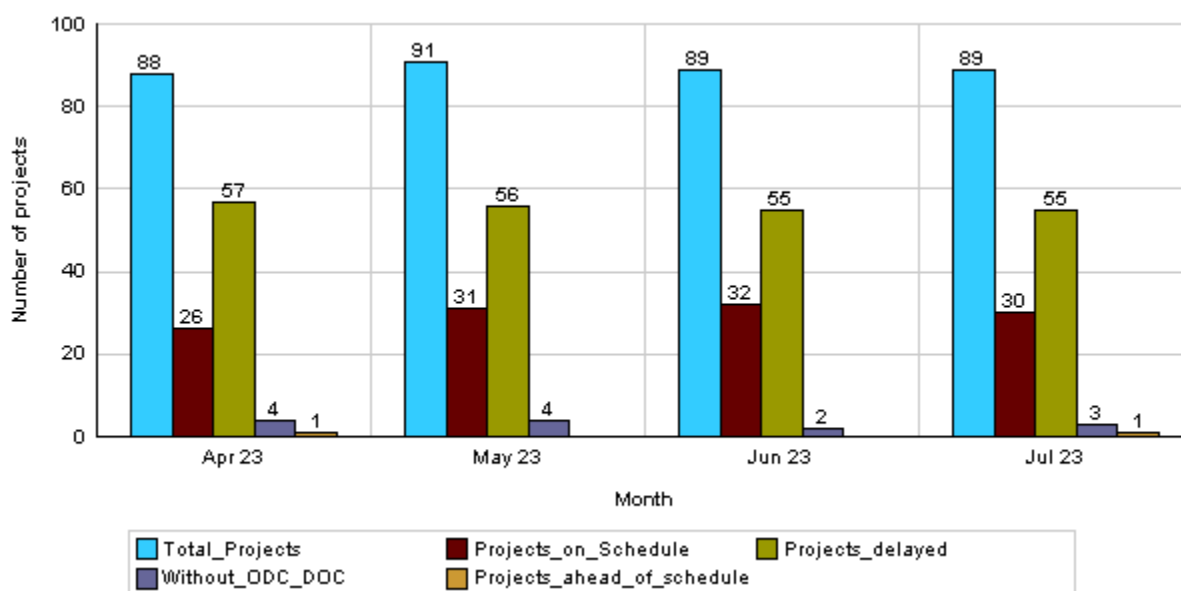


Break-up of 55 Delayed projects in July 2023

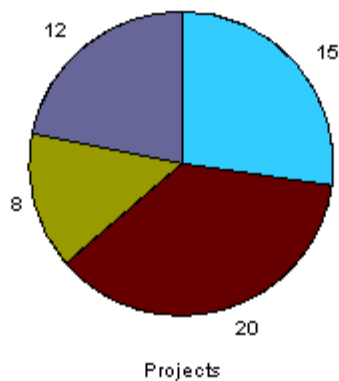

Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of PETROLEUM Sector

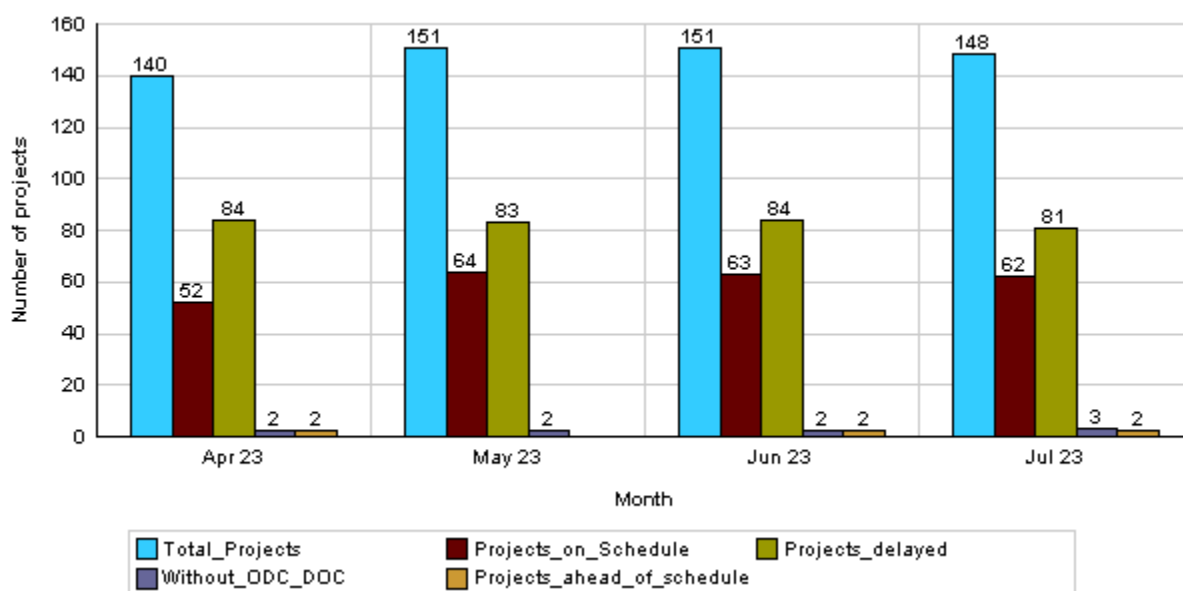


Break-up of 81 Delayed projects in July 2023




Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of STEEL Sector

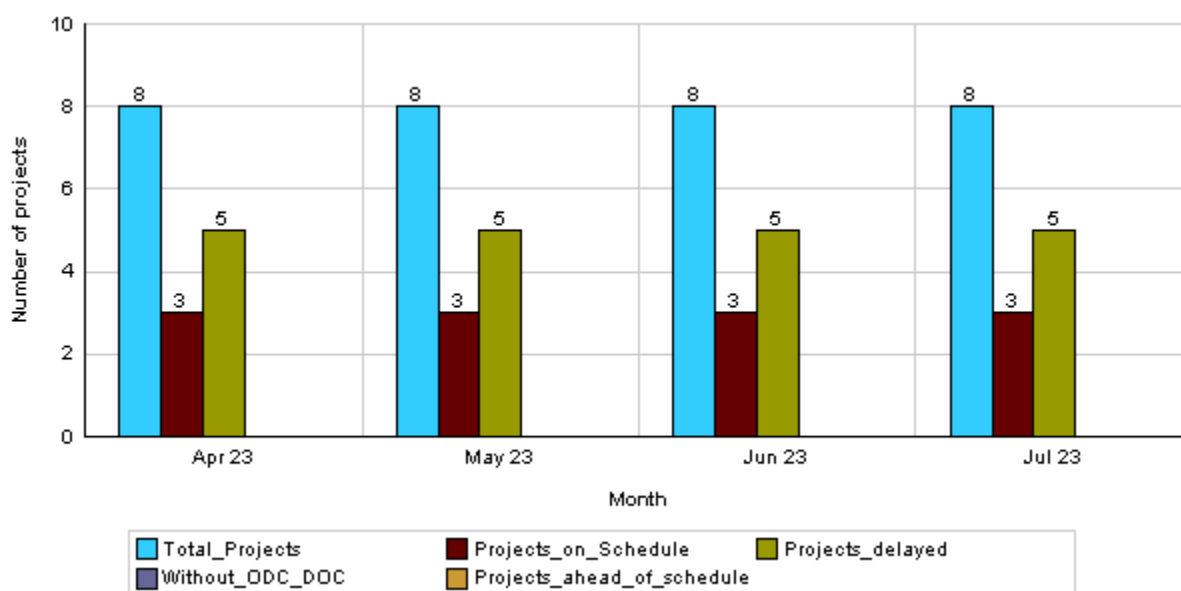


Break-up of 5 Delayed projects in July 2023

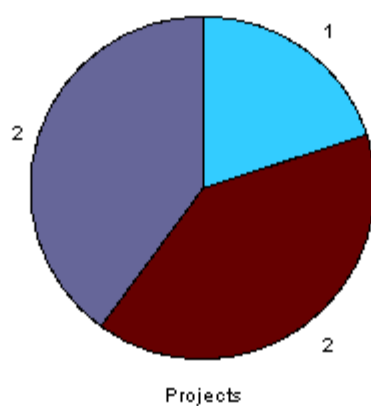


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	1	2	1	1

Graphical Presentation of MINES Sector

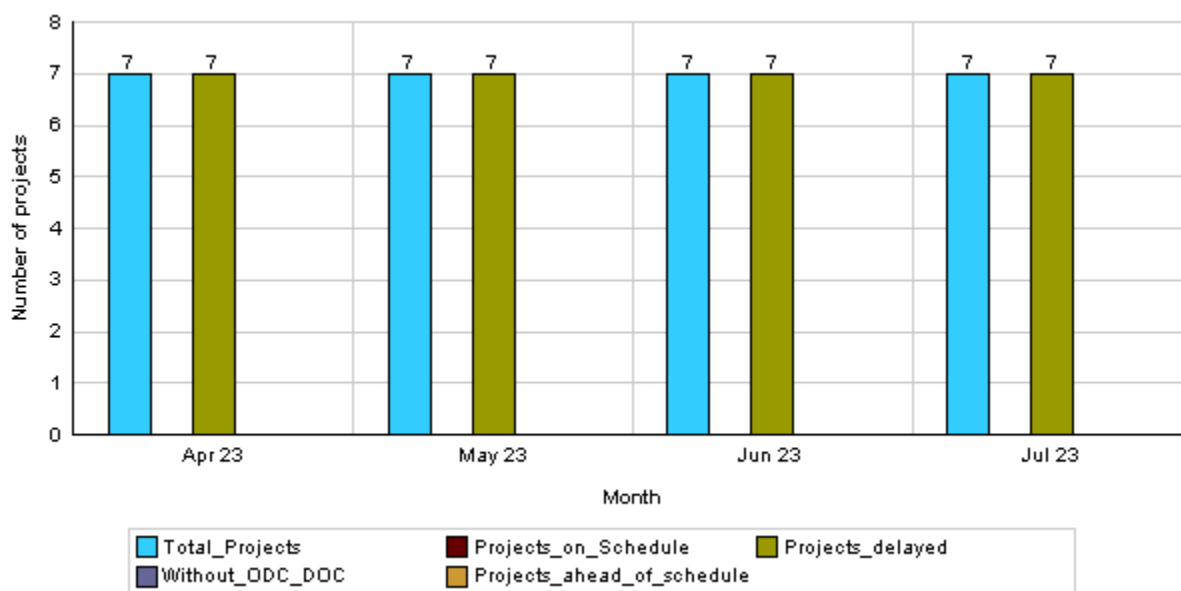


Break-up of 7 Delayed projects in July 2023

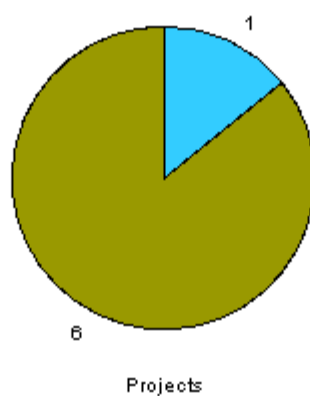

Delay in Months

Graphical Presentation of FERTILISERS Sector

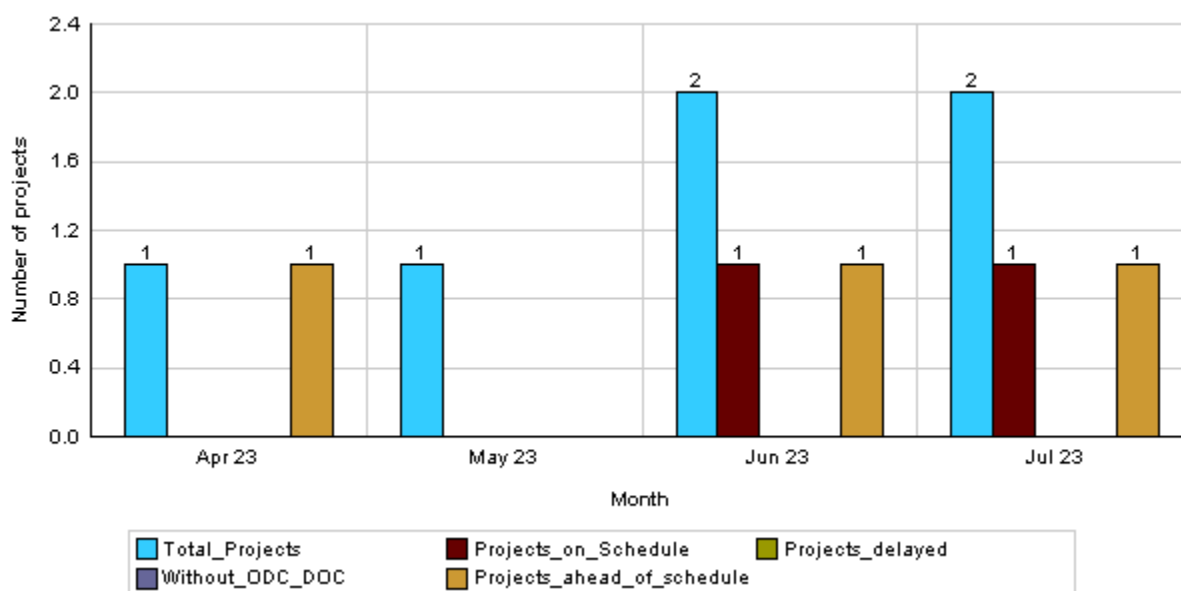


Break-up of 0 Delayed projects in July 2023

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	0	0
MORE THAN 60	0	0	0	0

Graphical Presentation of FINANCE Sector

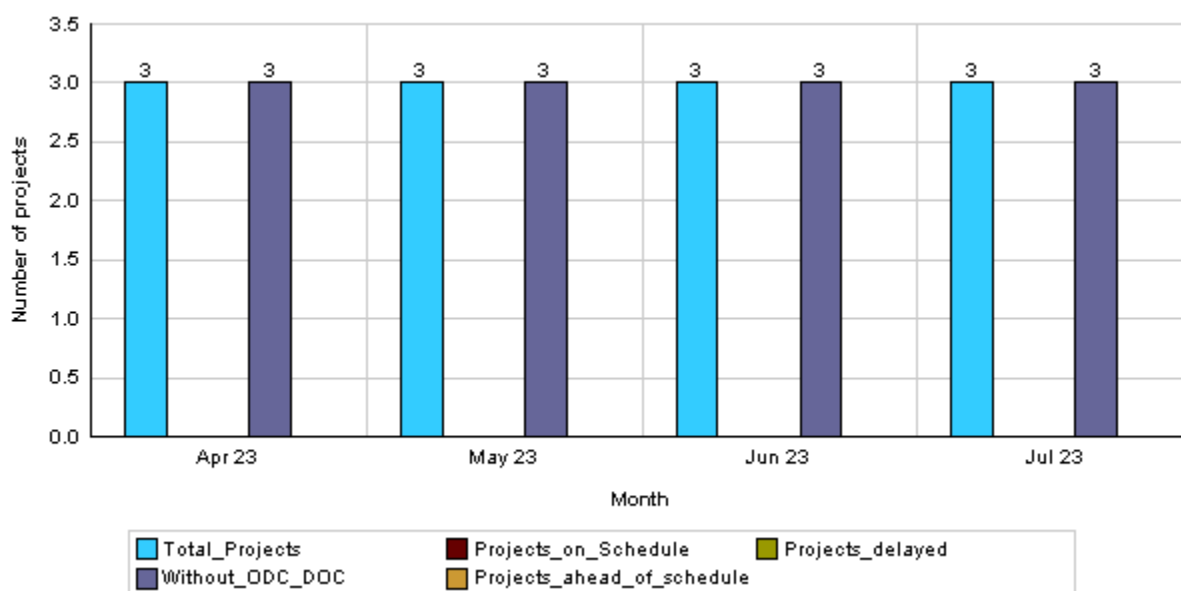


Break-up of 0 Delayed projects in July 2023


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of COAL Sector

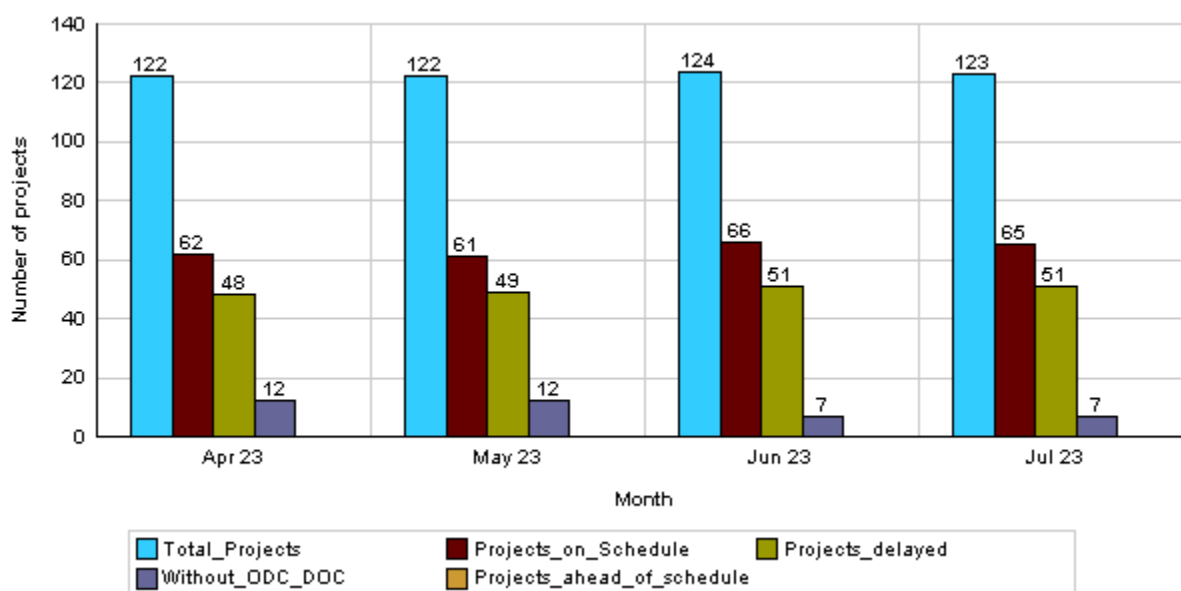


Break-up of 51 Delayed projects in July 2023

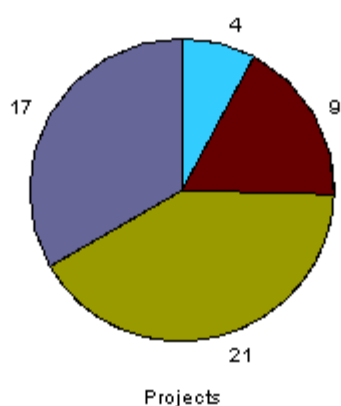


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)


Graphical Presentation of CIVIL AVIATION Sector

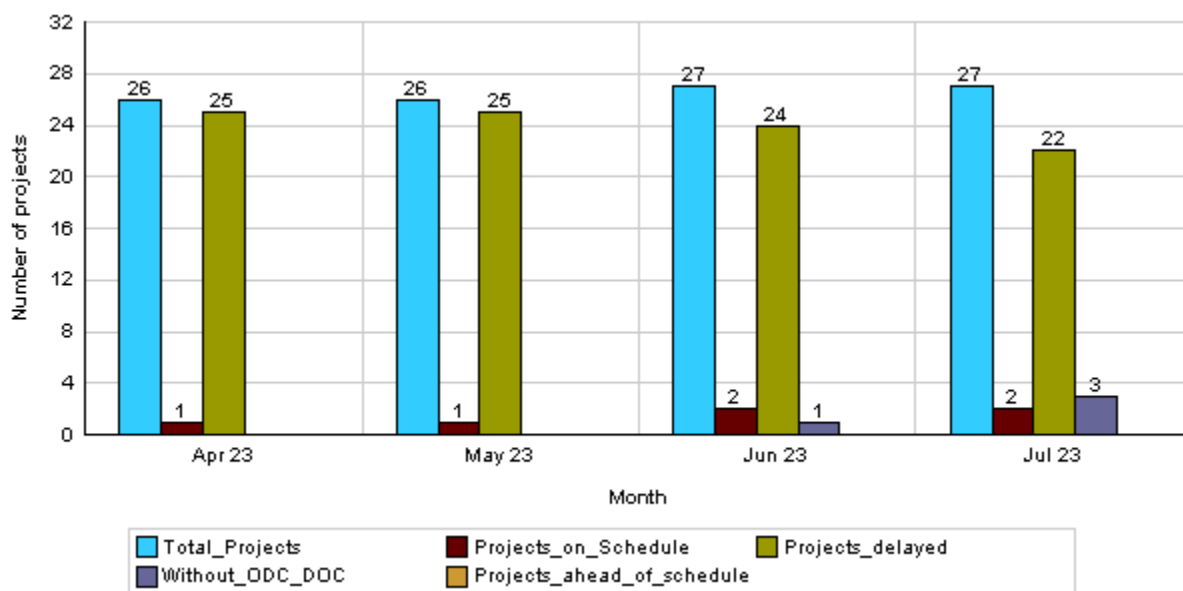


Break-up of 22 Delayed projects in July 2023

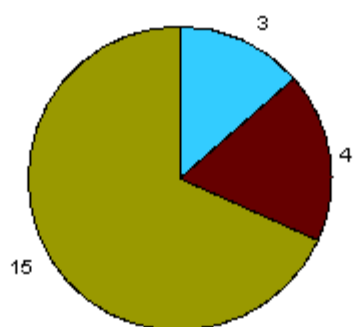

Graphical Presentation of ATOMIC ENERGY Sector

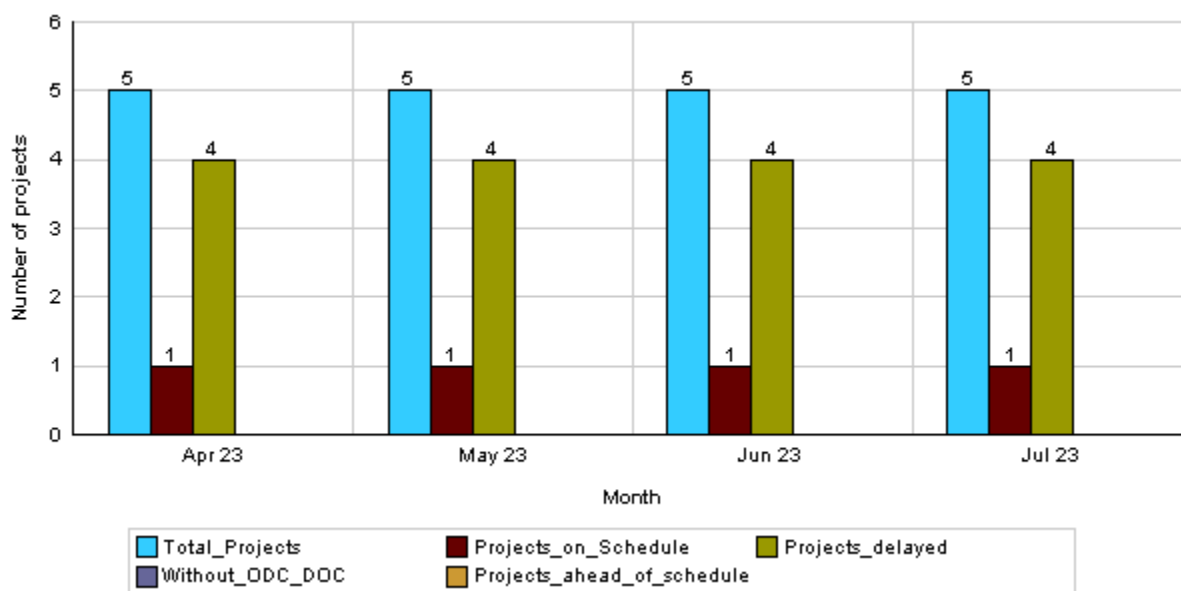

Break-up of 4 Delayed projects in July 2023

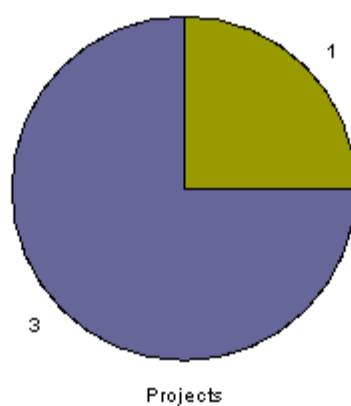

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	3

Detail of ongoing Projects Costing Rs		150	Crore and above.			(July 2023)
		(All Cost/ Expenditure in Rs. Crore)				
Sl.No	Project	Date of Approval (month / year)	Original / Revised / Anticipated Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]	Miles tones Achieved / Total
	ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044],BHAVNI,TAMIL NADU	9/2003	9/2010 (10/2022) [12/2024]	3,492.00 (6,840.00) [7,670.00]	6,569.75 (4,178.00) [171]	83/87
2	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029],NPCIL,TAMIL NADU	6/2017	9/2027 (-) [9/2027]	49,621.00 (-) [49,621.00]	10,592.00 (0.00) [0]	16/80
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028],NPCIL,TAMIL NADU	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	38,740.00 (0.00) [36]	35/76
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010],NPCIL,GUJARAT	10/2009	12/2015 (-) [3/2024]	11,459.00 (19,220.00) [19,220.00]	20,460.00 (7,761.00) [99]	66/70
5	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027],NPCIL,RAJASTHAN	10/2009	12/2016 (-) [12/2023]	12,320.00 (17,079.00) [17,079.00]	16,576.00 (4,759.00) [84]	55/68
	CIVIL AVIATION					
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076],AAI,DELHI	11/2016	4/2020 (-) [8/2023]	303.80 (351.21) [351.21]	304.71 (47.41) [40]	0/0
7	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 - [N04000098],AAI,MADHYA PRADESH	10/2021	8/2023 (9/2023) [9/2023]	446.12 (-) [446.12]	271.14 (0.00) [1]	2/9
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX - [N04000100],AAI,MANIPUR	11/2021	7/2024 (12/2024) [12/2024]	499.00 (-) [499.00]	83.88 (0.00) [5]	0/2
9	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085],AAI,UTTARAKHAND	7/2018	9/2020 (-) [9/2023]	456.86 (-) [456.86]	446.26 (0.00) [36]	1/7
10	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. - [N04000099],AAI,GUJARAT	6/2022	12/2025 (-) [12/2025]	1,305.00 (-) [636.45]	13.41 (-668.55) [0]	1/9
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079],AAI,MAHARASHTRA	3/2017	4/2021 (-) [9/2023]	475.39 (-) [475.39]	391.54 (0.00) [29]	4/10
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074],AAI,TAMIL NADU	6/2018	2/2022 (-) [12/2025]	2,467.00 (-) [2,467.00]	1,335.88 (0.00) [46]	12/13
13	CONSTRUCTION OF TERMINAL	7/2018	9/2028	480.33	245.19	2/9

	BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078],AAI,LADAKH		(12/2023) [3/2024]	(-) [640.00]	(159.67) [30]	
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083],AAI,ASSAM	12/2016	3/2021 (-) [3/2025]	1,142.00 (-) [1,232.00]	365.49 (90.00) [48]	0/1
15	UPGRADATION OF JABALPUR AIRPORT - [N04000087],AAI,MADHYA PRADESH	6/2016	6/2021 (-) [9/2023]	412.24 (-) [412.24]	354.98 (0.00) [27]	0/1
16	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092],AAI,ARUNACHAL PRADESH	2/2019	8/2022 (12/2023) [12/2023]	645.63 (-) [645.63]	636.43 (0.00) [16]	2/3
17	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075],AAI,TAMIL NADU	8/2018	10/2021 (-) [12/2023]	951.28 (-) [951.28]	867.64 (0.00) [26]	8/14
18	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080],AAI,WEST BENGAL	1/2016	3/2020 (6/2022) [8/2023]	458.00 (-) [458.00]	218.86 (0.00) [41]	0/2
19	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086],AAI,TELANGANA	5/2020	5/2022 (6/2023) [6/2023]	353.61 (-) [353.61]	296.11 (0.00) [0]	4/4
20	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 - [N04000094],AAI,UTTAR PRADESH	3/2021	12/2022 (9/2023) [9/2023]	242.14 (328.00) [328.00]	215.08 (85.86) [9]	0/14
21	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090],AAI,TAMIL NADU	6/2019	3/2022 (12/2023) [12/2023]	380.87 (-) [357.00]	168.32 (-23.87) [21]	13/28
22	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082],AAI,BIHAR	5/2018	10/2022 (-) [12/2024]	1,216.90 (-) [1,216.90]	466.96 (0.00) [26]	1/3
23	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073],AAI,ANDAMAN AND NICOBAR ISLANDS	10/2013	9/2018 (5/2023) [6/2023]	417.23 (707.73) [707.73]	674.47 (290.50) [0]	6/6
24	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088],AAI,GUJARAT	1/2018	8/2022 (12/2023) [12/2023]	1,405.00 (-) [1,405.00]	1,008.10 (0.00) [16]	6/16
25	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. - [N04000095],AAI,GOA	11/2017	9/2021 (-) [6/2024]	255.69 (-) [255.69]	45.34 (0.00) [33]	0/1
26	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089],AAI,ANDHRA PRADESH	8/2017	2/2020 (12/2021) [10/2023]	177.10 (-) [177.10]	142.52 (0.00) [44]	3/4
27	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM - [N04000096],AAI,MAHARASHTRA	6/2017	12/2020 (-) [9/2023]	255.68 (-) [255.68]	225.87 (0.00) [33]	0/1

28	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091],AAI,ANDHRA PRADESH	4/2020	3/2023 (-) [6/2024]	611.80 (-) [611.80]	217.58 (0.00) [15]	6/14
29	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. - [N04000093],AAI,GUJARAT	8/2018	2/2021 (-) [9/2023]	353.25 (-) [353.25]	254.94 (0.00) [31]	0/1
30	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT - [N04000101],AAI,RAJASTHAN	5/2022	11/2024 (-) [11/2024]	480.00 (-) [480.00]	0.19 (0.00) [0]	0/1
31	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077],AAI,UTTAR PRADESH	6/2018	9/2021 (-) [12/2024]	1,383.00 (-) [3,291.81]	769.80 (1,908.81) [39]	0/2
32	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081],AAI,WEST BENGAL	1/2019	11/2021 (-) [5/2023]	389.71 (-) [389.71]	391.78 (0.00) [0]	2/2
	<u>COAL</u>					
33	MURAI DIH UG TURN-KEY PROJECT - [N06000096],BCCL,JHARKHAND	2/2011	4/2014 (-) [10/2025]	339.88 (-) [339.88]	151.04 (0.00) [138]	6/7
34	MADHUBAND NLW WASHERY - [N06000126],BCCL,JHARKHAND	8/2010	5/2014 (-) [11/2023]	289.45 (-) [302.00]	297.18 (12.55) [114]	4/8
35	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195],BCCL,WEST BENGAL	12/2015	3/2017 (-) [12/2023]	304.13 (341.22) [341.22]	207.24 (37.09) [81]	0/0
36	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194],BCCL,JHARKHAND	10/2015	4/2018 (-) [3/2024]	243.00 (-) [334.27]	80.44 (91.27) [71]	0/0
37	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106],BCCL,JHARKHAND	2/2014	3/2021 (-) [3/2024]	555.52 (-) [555.52]	379.46 (0.00) [36]	1/2
38	MOONIDIH XV SEAM UG - [N06000098],BCCL,JHARKHAND	8/2011	3/2019 (-) [4/2025]	1,230.27 (-) [1,230.27]	582.15 (0.00) [73]	3/6
39	EPR PUNDI OCP - [N06000242],CCL,JHARKHAND	11/2020	3/2024 (-) [3/2024]	713.35 (-) [713.35]	235.72 (0.00) [0]	0/0
40	SIRKA OCP - [N06000239],CCL,JHARKHAND	5/2020	3/2025 (-) [3/2025]	222.82 (-) [222.82]	139.31 (0.00) [0]	0/0
41	EXPANSION PROJECT AMRAPALI OCP - [N06000217],CCL,JHARKHAND	8/2020	3/2028 (-) [3/2028]	5,136.15 (-) [5,136.15]	572.77 (0.00) [0]	0/0
42	EPR TAPIN SOUTH OCP - [N06000241],CCL,JHARKHAND	11/2020	3/2025 (-) [3/2025]	230.41 (-) [230.41]	17.20 (0.00) [0]	0/0
43	EXPANSION OF KARO OCP - [N06000246],CCL,JHARKHAND	1/2022	3/2026 (-) [3/2026]	908.47 (-) [908.47]	132.99 (0.00) [0]	0/0
44	EXPANSION OF KONAR OCP - [N06000245],CCL,JHARKHAND	1/2022	3/2032 (-) [3/2032]	799.34 (-) [799.34]	283.00 (0.00) [0]	0/0
45	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087],CCL,JHARKHAND	12/2009	3/2016 (-) [3/2025]	510.85 (-) [510.85]	487.68 (0.00) [108]	7/7
46	UCE OF EPR OF NORTH URIMARI OCP - [N06000218],CCL,JHARKHAND	7/2021	3/2026 (-) [3/2026]	778.80 (-) [778.80]	574.94 (0.00) [0]	0/0
47	CHANDRAGUPT OCP - [N06000238],CCL,JHARKHAND	8/2020	3/2032 (-)	973.50 (-)	5.95 (0.00)	0/0

			[3/2032]	[973.50]	[0]	
48	KOTRE BASANTPUR PACHMO OCP - [N06000237],CCL,JHARKHAND	8/2020	3/2032 (-) [3/2032]	861.06 (625.40) [861.06]	139.37 (0.00) [0]	0/0
49	EPR ROHINI KARKATA OCP - [N06000243],CCL,JHARKHAND	1/2021	3/2025 (-) [3/2025]	1,020.42 (-) [1,020.42]	79.34 (0.00) [0]	0/0
50	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216],CCL,JHARKHAND	8/2020	3/2028 (-) [3/2028]	7,254.37 (-) [7,254.37]	902.16 (0.00) [0]	0/0
51	EXPANSION OF ASHOK OCP - [N06000247],CCL,JHARKHAND	5/2021	3/2026 (-) [3/2026]	2,898.28 (-) [2,898.28]	173.90 (0.00) [0]	0/0
52	TETARIAKHAR EXPANSION OCP - [N06000186],CCL,JHARKHAND	11/2019	3/2023 (-) [3/2025]	243.52 (-) [243.52]	41.66 (0.00) [24]	1/1
53	CHURI BENTI UG (0.81 MTY) - [N06000083],CCL,JHARKHAND	8/2007	3/2011 (-) [3/2024]	163.51 (-) [163.51]	133.28 (0.00) [156]	7/7
54	JHARKHAND LAIYO OCP - [N06000240],CCL,JHARKHAND	8/2020	3/2031 (-) [3/2031]	764.57 (-) [764.57]	145.31 (0.00) [0]	0/0
55	KARMA OCP (1.0MTY) - [N06000088],CCL,JHARKHAND	6/2009	3/2014 (-) [3/2024]	162.46 (-) [162.46]	94.69 (0.00) [120]	7/7
56	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185],ECL, WEST BENGAL	7/2019	3/2027 (-) [3/2027]	826.42 (389.10) [389.10]	4.47 (-437.32) [0]	1/22
57	TILABONI UG MINE - [N06000172],ECL, WEST BENGAL	2/2019	3/2027 (-) [3/2027]	916.62 (749.08) [749.08]	9.72 (-167.54) [0]	3/27
58	SONEPUR BAZARI EXPANSION OC - [N06000220],ECL, WEST BENGAL	7/2021	3/2029 (-) [3/2029]	5,365.88 (5,366.00) [5,365.88]	316.12 (0.00) [0]	0/0
59	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223],ECL, WEST BENGAL	4/2020	3/2029 (-) [3/2029]	1,210.12 (-) [1,210.12]	259.91 (0.00) [0]	0/0
60	SIDULI MINE (OC AND UG) - [N06000165],ECL, WEST BENGAL	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	3.33 (0.00) [0]	4/22
61	MOHANPUR EXPANSION OC PHASE II - [N06000236],ECL, WEST BENGAL	11/2020	3/2025 (-) [3/2025]	888.99 (-) [888.99]	27.06 (0.00) [0]	0/0
62	HURA - C OC (3 MTY) - [N06000143],ECL,JHARKHAND	10/2015	3/2022 (3/2029) [3/2029]	359.69 (-) [859.41]	283.39 (499.72) [84]	4/22
63	CHITRA EAST (RCE) OCP - [N06000169],ECL,JHARKHAND	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.99]	139.51 (0.01) [0]	0/17
64	RANIGANJ MASTER PLAN - [N06000163],ECL, WEST BENGAL	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	713.53 (2,484.75) [60]	1/19
65	BONJEMEHARI EXPANSION OCP - [N06000244],ECL, WEST BENGAL	8/2021	3/2025 (-) [3/2025]	570.12 (-) [570.11]	14.55 (-0.01) [0]	0/0
66	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191],ECL, WEST BENGAL	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	21.68 (0.00) [0]	0/0
67	NAKRAKONDA KUMARDIH B OCP - [N06000170],ECL, WEST BENGAL	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	42.62 (0.00) [0]	4/22

68	BHUBANESWARI EXPANSION OCP - [N06000227],MCL,ODISHA	8/2020	3/2031 (-) [3/2031]	3,145.45 (-) [3,145.45]	941.66 (0.00) [0]	0/0
69	BALARAM EXPANSION OCP - [N06000230],MCL,ODISHA	8/2020	3/2029 (-) [3/2029]	3,504.21 (-) [3,504.21]	656.64 (0.00) [0]	0/0
70	RPR OF HINGULA -II EXPANSION PH-III - [N06000261],MCL,ODISHA	12/2022	3/2029 (-) [3/2029]	2,264.68 (-) [2,264.68]	934.65 (0.00) [0]	0/0
71	KULDA EXPANSION OCP- 15 MTY - [N06000248],MCL,ODISHA	6/2014	3/2018 (-) [3/2026]	348.16 (-) [348.16]	186.02 (0.00) [96]	0/0
72	ANANTA OCP EXPANSION PH III - [N06000225],MCL,ODISHA	8/2008	3/2012 (3/2022) [3/2022]	228.08 (-) [398.14]	398.14 (170.06) [0]	0/0
73	SIARMAL OCP (40.00MTY) - [N06000113],MCL,ODISHA	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	3,339.10 (0.00) [0]	13/15
74	GOPALJI-KANIHA OCP - [N06000229],MCL,ODISHA	8/2020	3/2028 (-) [3/2028]	8,416.19 (-) [8,416.19]	1,399.84 (0.00) [0]	0/0
75	SUBHADRA OCP - [N06000249],MCL,ODISHA	5/2021	3/2027 (3/2029) [3/2029]	1,693.81 (-) [1,693.81]	904.20 (0.00) [24]	0/0
76	GARJANBAHAL OCP - [N06000117],MCL,ODISHA	11/2014	3/2021 (-) [3/2026]	1,375.38 (-) [1,375.38]	779.83 (0.00) [60]	9/10
77	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112],MCL,ODISHA	5/2014	3/2019 (-) [3/2026]	479.15 (-) [479.15]	259.49 (0.00) [84]	4/9
78	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167],MCL,ODISHA	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	1,438.58 (0.00) [0]	5/12
79	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171],MCL,ODISHA	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,432.59 (0.00) [0]	3/9
80	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095],NLC,TAMIL NADU	6/2011	12/2015 (-) [2/2021]	5,907.11 (-) [8,990.00]	7,656.86 (3,082.89) [0]	35/35
81	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144],NLC,RAJASTHAN	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	9.88 (0.00) [0]	0/0
82	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188],NLC,RAJASTHAN	3/2015	9/2020 (-) [9/2020]	2,196.30 (-) [2,196.30]	106.24 (0.00) [0]	0/0
83	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138],NLC,TAMIL NADU	4/2013	6/2015 (-) [9/2027]	1,458.17 (-) [709.06]	541.79 (-749.11) [147]	5/7
84	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145],NLC,RAJASTHAN	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	175.30 (0.00) [0]	0/0
85	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187],NLC,RAJASTHAN	3/2015	9/2020 (-) [9/2020]	2,112.60 (-) [2,112.60]	85.90 (0.00) [0]	0/0
86	PACHWARA SOUTH COAL BLOCK - [N06000193],NLC,JHARKHAND	7/2013	9/2028 (-) [9/2028]	1,795.01 (-) [1,795.01]	45.19 (0.00) [0]	6/11
87	TALABIRA II AND III OCP - [N06000189],NLC,ODISHA	7/2017	1/2027 (-) [1/2027]	2,401.07 (-) [2,401.07]	1,051.59 (0.00) [0]	19/22

88	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152],NLC,UTTAR PRADESH	7/2016	11/2021 (-) [12/2023]	17,237.00 (-) [19,406.12]	15,652.81 (2,169.12) [25]	21/48
89	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159],NCL,MADHYA PRADESH	5/2017	3/2021 (-) [10/2023]	1,783.09 (-) [1,783.09]	1,447.90 (0.00) [31]	8/9
90	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162],NCL,MADHYA PRADESH	11/2017	3/2022 (-) [8/2023]	1,255.17 (-) [1,255.17]	1,011.43 (0.00) [17]	9/9
91	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192],NCL,MULTI STATE	8/2020	3/2024 (-) [3/2025]	836.42 (-) [836.42]	361.69 (0.00) [12]	4/6
92	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196],NCL,MADHYA PRADESH	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	285.78 (0.00) [0]	5/8
93	KHADIA EXPANSION OCP - [N06000208],NCL,UTTAR PRADESH	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	8.49 (0.00) [0]	3/5
94	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184],NCL,MADHYA PRADESH	7/2019	3/2023 (-) [3/2025]	998.71 (-) [998.71]	106.29 (0.00) [24]	4/7
95	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161],SCCL,TELANGANA	3/2017	3/2022 (-) [3/2024]	413.84 (-) [413.84]	409.48 (0.00) [24]	8/11
96	NAINI COAL MINE - [N06000203],SCCL,ODISHA	3/2020	3/2024 (-) [3/2025]	494.30 (-) [494.30]	397.67 (0.00) [12]	2/7
97	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210],SCCL,TELANGANA	11/2015	3/2023 (-) [3/2024]	489.62 (-) [489.62]	392.20 (0.00) [12]	1/3
98	SRP OC-II EXPANSION PROJECT - [N06000173],SCCL,TELANGANA	11/2016	3/2018 (-) [3/2024]	272.73 (-) [272.73]	153.75 (0.00) [72]	3/6
99	GOLETI OPENCAST MINE - [N06000258],SCCL,TELANGANA	7/2021	3/2026 (-) [3/2026]	345.60 (-) [345.60]	30.72 (0.00) [0]	0/5
100	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212],SCCL,TELANGANA	3/2019	3/2021 (-) [3/2023]	473.22 (-) [473.22]	446.35 (0.00) [0]	4/4
101	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213],SCCL,TELANGANA	3/2016	3/2020 (-) [3/2024]	384.32 (-) [384.32]	180.58 (0.00) [48]	0/3
102	VENKATESH KHANI COAL MINE - [N06000204],SCCL,TELANGANA	10/2020	3/2023 (-) [3/2025]	484.51 (-) [484.51]	64.04 (0.00) [24]	3/8
103	RCE OF INDARAM OPENCAST PROJECT - [N06000211],SCCL,TELANGANA	8/2017	3/2021 (-) [3/2024]	349.28 (-) [424.81]	335.24 (75.53) [36]	5/5
104	GODAVARIKHANI COAL MINE - [N06000202],SCCL,TELANGANA	7/2019	3/2023 (-) [3/2024]	438.98 (-) [438.98]	123.25 (0.00) [12]	8/11
105	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214],SCCL,TELANGANA	8/2017	3/2020 (-) [3/2024]	442.42 (-) [442.42]	222.33 (0.00) [48]	0/1
106	JAWAHAR KHANI OPENCAST (JK OC) MINE - [N06000259],SCCL,TAMIL NADU	12/2021	3/2025 (-) [3/2025]	297.88 (-) [297.88]	25.96 (0.00) [0]	0/5

107	RCE OF KISTARAM OPENCAS PROJECT - [N06000215],SCCL,TELANGANA	3/2017	3/2021 (-) [3/2024]	164.04 (-) [164.04]	143.08 (0.00) [36]	1/1
108	JHIRIA WEST OPENCAS PROJECT - [N06000166],SECL,CHHATTISGARH	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	15.69 (0.00) [0]	3/5
109	AMGAON OPENCAS PROJECT RCE - [N06000135],SECL,CHHATTISGARH	7/2015	3/2020 (-) [3/2025]	316.10 (-) [316.10]	156.33 (0.00) [60]	3/6
110	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199],SECL,CHHATTISGARH	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	39.19 (0.00) [0]	0/3
111	DIPKA OC EXPANSION 40 MTY - [N06000200],SECL,CHHATTISGARH	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	2,336.23 (0.00) [0]	0/5
112	AMERA OC RCE - [N06000123],SECL,CHHATTISGARH	2/2015	3/2018 (-) [3/2026]	335.97 (-) [335.97]	49.00 (0.00) [96]	1/7
113	KUSMUNDA EXPN.OCP(SECL)(15- 50)MTY - [N06000008],SECL,CHHATTISGARH	8/2013	3/2023 (-) [3/2025]	7,612.33 (-) [7,612.33]	4,109.56 (0.00) [24]	13/22
114	KARTALI (EAST) OCP (2.50 MTY) - [N06000076],SECL,CHHATTISGARH	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	9.22 (0.00) [144]	3/9
115	DURGAPUR OPENCAS PROJECT - [N06000136],SECL,CHHATTISGARH	2/2015	3/2023 (-) [3/2030]	916.24 (-) [916.24]	13.73 (0.00) [84]	2/12
116	AMADAND OPENCAS EXPANSION PROJECT - [N06000148],SECL,MADHYA PRADESH	3/2016	3/2021 (3/2025) [3/2025]	869.44 (-) [869.44]	201.12 (0.00) [48]	4/6
117	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232],SECL,CHHATTISGARH	7/2016	3/2020 (-) [3/2024]	459.49 (-) [459.49]	223.15 (0.00) [48]	0/0
118	KANCHAN OC EXPANSION - [N06000125],SECL,MADHYA PRADESH	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	100.88 (0.00) [36]	5/9
119	MAHAMAYA OPENCAS PROJECT - [N06000164],SECL,CHHATTISGARH	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	102.84 (0.00) [0]	2/4
120	RAMPUR BATURA OC (4.0 MTY) - [N06000233],SECL,MADHYA PRADESH	7/2019	3/2026 (-) [3/2026]	1,248.93 (-) [1,248.93]	408.00 (0.00) [0]	0/3
121	MADANNAGAR OPENCAS PROJECT - [N06000140],SECL,CHHATTISGARH	10/2015	3/2024 (-) [3/2027]	1,875.32 (-) [1,875.32]	0.00 (0.00) [36]	2/6
122	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207],SECL,MADHYA PRADESH	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]	0/0
123	AMRITDHARA OC PROJECT - [N06000122],SECL,MADHYA PRADESH	2/2015	3/2023 (-) [3/2027]	481.60 (-) [481.60]	1.08 (0.00) [48]	3/10
124	PELMA OCP(15.00MTY) - [N06000045],SECL,CHHATTISGARH	11/2014	3/2023 (-) [3/2031]	1,624.59 (-) [1,624.59]	49.60 (0.00) [96]	1/12
125	VIJAY WEST OPENCAS PROJECT - [N06000158],SECL,CHHATTISGARH	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	88.27 (0.00) [0]	2/2
126	JAMPALI OCP RCE - [N06000198],SECL,CHHATTISGARH	5/2020	3/2024 (-)	278.64 (-)	198.08 (0.00)	0/0

			[3/2024]	[278.64]	[0]	
127	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093],SECL,CHHATTISGARH	6/2010	3/2023 (-) [3/2025]	11,816.40 (-) [11,816.40]	5,887.31 (0.00) [24]	15/21
128	CHHAL OC SEAM -III (6.00 MTY) - [N06000104],SECL,CHHATTISGARH	12/2013	3/2022 (3/2025) [3/2025]	610.63 (-) [610.63]	482.80 (0.00) [36]	4/11
129	BATURA HIGHWALL PROJECT - [N06000134],SECL,MADHYA PRADESH	7/2015	3/2022 (-) [3/2024]	231.92 (-) [231.92]	2.26 (0.00) [24]	1/10
130	BAROUD OC EXPANSION (3-10 MTY) - [N06000197],SECL,CHHATTISGARH	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	721.14 (0.00) [0]	0/4
131	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124],SECL,MADHYA PRADESH	12/2014	3/2021 (-) [3/2024]	357.80 (-) [357.80]	86.99 (0.00) [36]	4/10
132	GOKUL EXPANSION OC - [N06000264],WCL,MAHARASHTRA	4/2021	3/2026 (-) [3/2026]	456.95 (-) [456.95]	147.37 (0.00) [0]	0/0
133	BHATADI EXPANSION OC - [N06000254],WCL,MAHARASHTRA	2/2020	3/2028 (-) [3/2028]	729.86 (-) [729.86]	158.48 (0.00) [0]	1/5
134	SAONER UG MINE I EXPANSION - [N06000251],WCL,MAHARASHTRA	1/2022	3/2028 (-) [3/2028]	253.51 (-) [253.51]	51.26 (0.00) [0]	0/5
135	GANDHIGRAM UG MINE - [N06000183],WCL,MADHYA PRADESH	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	24.41 (0.00) [0]	2/7
136	DHUPTALA OC(SASTI UG TO OC) - [N06000209],WCL,MAHARASHTRA	2/2019	3/2028 (-) [3/2028]	720.87 (-) [720.87]	171.31 (0.00) [0]	0/6
137	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222],WCL,MAHARASHTRA	2/2020	3/2027 (-) [3/2027]	1,184.33 (-) [1,184.33]	692.00 (0.00) [0]	2/8
138	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231],WCL,MAHARASHTRA	11/2020	3/2026 (-) [3/2026]	826.80 (-) [826.80]	340.53 (0.00) [0]	0/4
139	MAKARDHOKDA I EXPANSION OC - [N06000253],WCL,MAHARASHTRA	6/2022	3/2026 (-) [3/2026]	497.06 (-) [497.06]	140.99 (0.00) [0]	0/6
140	RPR PAUNI II EXPANSION OC - [N06000263],WCL,MAHARASHTRA	3/2023	3/2027 (-) [3/2027]	464.45 (-) [464.45]	177.30 (0.00) [0]	0/0
141	NEW MAJARI UG TO OC (3.0 MTY) - [N06000255],WCL,MAHARASHTRA	5/2019	3/2027 (-) [3/2027]	496.38 (-) [496.38]	105.47 (0.00) [0]	2/5
142	GHONSA EXPANSION DEEP OC - [N06000205],WCL,MAHARASHTRA	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	58.79 (0.00) [0]	0/7
143	BELLORA-NAIGAON DEEP OC - [N06000180],WCL,MAHARASHTRA	11/2018	3/2021 (3/2024) [3/2024]	252.71 (-) [252.71]	121.58 (0.00) [36]	1/3
144	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157],WCL,MULTI STATE	2/2017	3/2021 (3/2025) [3/2025]	328.00 (-) [328.00]	310.44 (0.00) [48]	5/6
145	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226],WCL,MAHARASHTRA	9/2018	3/2024 (-) [3/2024]	313.34 (-) [313.34]	192.55 (0.00) [0]	1/1
146	AMALGAMATED YEKONA-I YEKONA-II - [N06000132],WCL,MAHARASHTRA	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	505.75 (0.00) [0]	10/13

147	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) - [N06000257],WCL,MADHYA PRADESH	9/2022	3/2027 (-) [3/2027]	497.01 (-) [497.01]	136.72 (0.00) [0]	0/5
148	SINGHORI DEEP OC - [N06000252],WCL,MAHARASHTRA	5/2022	3/2029 (-) [3/2029]	421.84 (-) [421.84]	110.40 (0.00) [0]	0/6
149	ADASA UG TO OC (1.50 MTY) - [N06000219],WCL,MAHARASHTRA	11/2018	3/2024 (-) [3/2024]	333.43 (-) [333.43]	204.07 (0.00) [0]	0/4
150	BHANEGAON OC (1.15MTY) - [N06000256],WCL,MAHARASHTRA	9/2022	3/2028 (-) [3/2028]	494.60 (-) [494.60]	97.51 (0.00) [0]	1/6
151	SASTI EXPANSION OC - [N06000206],WCL,MAHARASHTRA	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	61.09 (0.00) [0]	2/7
152	VISHNUPURI UG TO OC - [N06000260],WCL,MADHYA PRADESH	11/2022	3/2029 (-) [3/2029]	227.65 (-) [227.65]	7.02 (0.00) [0]	0/6
153	UKNI DEEP OC - [N06000179],WCL,MAHARASHTRA	11/2018	3/2021 (3/2025) [3/2025]	318.14 (-) [318.14]	249.15 (0.00) [48]	1/4
154	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154],WCL,MULTI STATE	8/2016	3/2022 (3/2025) [3/2025]	319.76 (319.76) [319.76]	275.11 (0.00) [36]	0/3
155	TAWA III UG MINE - [N06000250],WCL,MADHYA PRADESH	12/2021	3/2027 (-) [3/2027]	324.25 (-) [324.25]	12.19 (0.00) [0]	0/5
	<u>COMMERCE</u>					
156	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003],NBCC FOR COMMER,DELHI	6/2018	10/2020 (-) [10/2020]	302.64 (-) [302.64]	30.00 (0.00) [0]	0/0
	<u>DEFENCE PRODUCTION</u>					
157	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103],CPWD FOR DEFENC,KARNATAKA	12/2016	2/2020 (3/2023) [3/2023]	246.31 (200.00) [195.00]	187.02 (-51.31) [0]	10/10
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
158	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL - [N42000010],CPWD,KARNATAKA	8/2021	2/2024 (-) [2/2024]	316.25 (-) [316.25]	246.36 (0.00) [0]	1/2
159	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100],CPWD EDUCATION,BIHAR	2/2016	6/2017 (10/2023) [10/2023]	496.18 (496.00) [460.00]	396.27 (-36.18) [76]	3/6
160	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075],CPWD EDUCATION,KERALA	1/2010	10/2012 (-) [10/2012]	165.23 (-) [165.23]	135.78 (0.00) [0]	8/8
161	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009],CPWD EDUCATION,BIHAR	9/2018	9/2020 (-) [8/2023]	375.00 (-) [375.00]	278.08 (0.00) [35]	6/7
162	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI,	1/2018	7/2020 (9/2023)	223.37 (275.00)	168.67 (6.63)	7/14

	MUMBAI [N28000117],CPWD EDUCATION,MAHARASHTRA		[9/2023]	[230.00]	[38]	
163	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067],CPWD EDUCATION,JHARKHAND	9/2012	3/2016 (-) [0/2016]	171.86 (-) [171.86]	169.69 (0.00) [0]	6/6
164	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007],CPWD EDUCATION,ANDHRA PRADESH	9/2019	9/2022 (-) [12/2023]	588.72 (-) [588.72]	457.26 (0.00) [15]	7/9
165	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140],CPWD EDUCATION,KERALA	7/2019	3/2021 (3/2023) [3/2024]	753.63 (-) [753.63]	346.00 (0.00) [36]	2/11
166	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142],CPWD EDUCATION,PUNJAB	10/2019	5/2022 (-) [3/2024]	348.24 (-) [348.24]	175.07 (0.00) [22]	1/8
167	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130],CPWD EDUCATION,JAMMU AND KASHMIR	3/2019	7/2022 (9/2023) [9/2023]	424.93 (-) [424.93]	363.19 (0.00) [14]	0/14
168	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131],CPWD EDUCATION,JAMMU AND KASHMIR	1/2018	4/2023 (12/2023) [12/2023]	676.00 (1,085.04) [1,085.04]	24.75 (409.04) [8]	0/1
169	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126],CPWD EDUCATION,ODISHA	1/2019	3/2022 (-) [3/2024]	790.79 (-) [790.79]	502.79 (0.00) [24]	2/5
170	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008],CPWD EDUCATION,HIMACHAL PRADESH	9/2018	6/2022 (1/2024) [1/2024]	392.51 (-) [446.43]	213.56 (53.92) [19]	0/2
171	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120],CPWD EDUCATION,PUNJAB	1/2018	5/2020 (-) [6/2023]	430.00 (-) [355.00]	357.89 (-75.00) [0]	4/5
172	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002],CPWD EDUCATION,GOA	5/2019	8/2021 (-) [11/2023]	303.90 (334.45) [364.00]	295.00 (60.10) [27]	6/8
173	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146],CPWD EDUCATION,WEST BENGAL	3/2020	6/2020 (-) [7/2023]	193.83 (-) [193.83]	150.97 (0.00) [37]	0/14
174	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006],CPWD EDUCATION,KARNATAKA	7/2019	3/2022 (10/2022) [3/2023]	851.00 (851.00) [851.00]	683.74 (0.00) [0]	8/12

175	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141],CPWD EDUCATION,CHHATTISGARH	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	640.70 (0.00) [0]	0/0
176	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005],CPWD EDUCATION,ANDHRA PRADESH	2/2019	6/2020 (-) [4/2023]	655.34 (-) [655.34]	366.21 (0.00) [0]	0/110
177	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001],RITES OF HIGHER,MEGHALAYA	9/2013	9/2014 (12/2023) [12/2023]	484.32 (429.70) [429.70]	262.25 (-54.62) [111]	0/0
178	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM - [N44000002],Sikkim Universi,SIKKIM	8/2020	1/2025 (-) [12/2024]	314.06 (-) [303.55]	15.70 (-10.51) [-1]	0/0
	<u>DONER</u>					
179	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103],HSCL FOR DONER,MEGHALAYA	4/2014	9/2017 (-) [9/2017]	151.33 (-) [151.33]	148.33 (0.00) [0]	12/15
	<u>DPIIT</u>					
180	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001],DMIC FOR DPIIT,MULTI STATE	9/2011	3/2027 (3/2027) [3/2027]	20,084.00 (20,084.00) [20,084.00]	9,682.86 (0.00) [0]	0/0
181	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002],IICC FOR DPIIT,DELHI	11/2017	12/2019 (-) [9/2023]	4,773.00 (-) [5,401.00]	4,071.81 (628.00) [45]	0/0
	<u>FERTILISERS</u>					
182	INSTALLATION OF NEW NANO UREA FERTILIZER PLANT AT RCF TROMBAY - [N08000020],RCF,MAHARASHTRA	5/2023	3/2024 (-) [3/2024]	238.30 (-) [238.30]	0.30 (0.00) [0]	0/0
183	AN MELT PROJECT AT RCF TROMBAY - [N08000019],RCF,MAHARASHTRA	5/2022	9/2024 (-) [7/2024]	187.27 (187.27) [187.27]	18.53 (0.00) [-2]	0/0
	<u>FINANCE</u>					
184	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109],CPWD FOR FINANC,TAMIL NADU	11/2017	11/2021 (-) [11/2022]	348.77 (-) [348.77]	296.23 (0.00) [0]	8/8
185	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089],CPWD FOR FINANC,TAMIL NADU	12/2015	10/2019 (10/2022) [10/2022]	209.00 (-) [262.00]	249.00 (53.00) [0]	6/6
186	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA - [N070000001],NPCC,DELHI	7/2018	4/2022 (-) [4/2022]	228.50 (-) [220.27]	176.28 (-8.23) [0]	6/15
	<u>HEALTH AND FAMILY WELFARE</u>					

187	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127],CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	6/2021 (-) [8/2025]	260.00 (-) [260.00]	0.00 (0.00) [50]	0/0
188	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112],CPWD FOR HEALTH,KERALA	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	121.00 (0.00) [0]	6/7
189	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098],CPWD FOR HEALTH,TELANGANA	10/2016	3/2020 (-) [3/2020]	209.84 (244.97) [273.00]	240.58 (63.16) [0]	1/5
190	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029],CPWD FOR HEALTH,JAMMU AND KASHMIR	3/2019	9/2023 (-) [10/2023]	1,404.00 (-) [1,404.00]	95.63 (0.00) [1]	0/0
191	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139],CPWD FOR HEALTH,PUDUCHERRY	3/2018	9/2020 (-) [9/2020]	195.00 (-) [195.00]	2.67 (0.00) [0]	0/33
192	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150],CPWD FOR HEALTH,JAMMU AND KASHMIR	3/2019	9/2025 (-) [9/2025]	1,828.00 (-) [1,828.00]	740.13 (0.00) [0]	0/0
193	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027],HITES,ASSAM	5/2017	5/2021 (12/2022) [10/2023]	875.00 (890.14) [860.00]	684.50 (-15.00) [29]	0/0
194	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR - [N21000031],HITES,TELANGANA	12/2018	7/2024 (-) [10/2024]	1,110.55 (-) [1,110.55]	269.09 (0.00) [3]	0/0
	HOME AFFAIRS					
195	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002],CPWD FOR MHA,DELHI	6/2019	7/2022 (-) [5/2024]	277.35 (-) [290.33]	90.12 (12.98) [22]	3/6
196	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071],CPWD FOR MHA,DELHI	10/2013	10/2019 (-) [12/2023]	1,219.21 (1,735.25) [1,900.00]	1,583.95 (680.79) [50]	1/7
197	NSG AT KOLKATA - [N28000104],CPWD FOR MHA,WEST BENGAL	10/2014	4/2018 (-) [12/2024]	162.88 (210.83) [210.83]	177.77 (47.95) [80]	6/7
198	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI - [N45000003],CPWD FOR MHA,UTTAR PRADESH	5/2019	1/2022 (3/2023) [3/2023]	199.31 (-) [199.31]	86.49 (0.00) [0]	3/6
199	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" - [N28000147],CPWD FOR	1/2020	10/2023 (3/2024) [3/2024]	166.98 (167.00) [166.98]	41.73 (0.00) [5]	2/13

	MHA,HARYANA					
	<u>MINES</u>					
200	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015],CPWD,WEST BENGAL	4/2019	4/2022 (-) [10/2025]	255.37 (-) [255.37]	37.77 (0.00) [42]	1/1
201	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012],NALCO,ODISHA	12/2015	11/2020 (9/2025) [9/2025]	355.00 (581.00) [581.00]	79.69 (226.00) [58]	3/3
202	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010],NALCO,ODISHA	12/2014	4/2021 (12/2022) [3/2025]	4,103.00 (5,055.00) [5,055.00]	2,259.22 (952.00) [47]	4/4
203	POTTANGI BAUXITE MINES - [N10000016],NALCO,ODISHA	5/2018	12/2024 (3/2025) [5/2025]	1,437.00 (1,381.00) [1,381.00]	603.12 (-56.00) [5]	0/0
204	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014],NALCO,TAMIL NADU	9/2017	6/2019 (12/2023) [12/2023]	166.62 (163.17) [163.17]	135.00 (-3.45) [54]	1/1
205	UTKAL D AND E COAL BLOCK - [N10000011],NALCO,ODISHA	5/2016	1/2020 (11/2023) [11/2023]	534.00 (667.23) [667.23]	605.95 (133.23) [46]	3/3
206	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013],NALCO,ODISHA	11/2017	4/2021 (5/2024) [5/2024]	483.00 (483.00) [483.00]	197.42 (0.00) [37]	2/2
	<u>PETROLEUM</u>					
207	CITY GAS DISTRIBUTION NETWORK PROJECT AT CHATRA AND PALAMU - [N16000474],BPCL,JHARKHAND	12/2019	3/2029 (-) [3/2029]	230.25 (-) [230.25]	42.85 (0.00) [0]	0/0
208	CITY GAS DISTRIBUTION NETWORK PROJECT AT JAJPUR AND KENDUJHAR - [N16000462],BPCL,ODISHA	4/2019	3/2030 (-) [3/2030]	741.29 (-) [741.29]	209.95 (0.00) [0]	0/0
209	CITY GAS DISTRIBUTION NETWORK PROJECT AT ANGUL AND DHENKANAL - [N16000463],BPCL,ODISHA	4/2019	3/2030 (-) [3/2030]	605.65 (-) [605.65]	158.42 (0.00) [0]	0/0
210	CITY GAS DISTRIBUTION NETWORK PROJECT AT JAGATSINGHPUR AND KENDRAPARA - [N16000465],BPCL,ODISHA	4/2019	3/2030 (-) [3/2030]	485.91 (-) [485.91]	121.66 (0.00) [0]	0/0
211	CITY GAS DISTRIBUTION NETWORK PROJECT AT AMETHI, RAEBARELI AND PRATAPGARH - [N16000466],BPCL,UTTAR PRADESH	4/2019	9/2028 (-) [9/2028]	432.06 (-) [432.06]	122.52 (0.00) [0]	0/0
212	CITY GAS DISTRIBUTION NETWORK PROJECT AT SANGLI AND SATARA - [N16000460],BPCL,MAHARASHTRA	4/2019	11/2028 (-) [11/2028]	2,337.98 (-) [2,337.98]	635.90 (0.00) [0]	0/0
213	CITY GAS DISTRIBUTION NETWORK PROJECT AT SATNA AND SHAHDOL - [N16000472],BPCL,MADHYA PRADESH	4/2019	9/2028 (-) [9/2028]	332.38 (-) [332.38]	86.74 (0.00) [0]	0/0
214	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373],BPCL,JHARKHAND	11/2018	6/2022 (3/2023) [5/2023]	248.55 (-) [248.55]	217.31 (0.00) [0]	7/16
215	KOCHI SALEM LPG PIPELINE	12/2015	6/2019	1,112.00	1,094.66	1/3

	PROJECT - [N16000314],BPCL,KERALA		(2/2024) [2/2025]	(1,507.24) [1,507.24]	(395.24) [68]	
216	CITY GAS DISTRIBUTION NETWORK PROJECT AT SIDHI AND SANGRAULI - [N16000468],BPCL,MADHYA PRADESH	12/2019	3/2029 (-) [3/2029]	350.35 (-) [350.35]	66.39 (0.00) [0]	0/0
217	CITY GAS DISTRIBUTION NETWORK PROJECT AT ROHTAK - [N16000473],BPCL,HARYANA	4/2018	6/2025 (-) [6/2025]	261.48 (-) [261.48]	137.28 (0.00) [0]	0/0
218	CITY GAS DISTRIBUTION NETWORK PROJECT AT BARGARH, DEBGARH AND SAMBALPUR - [N16000464],BPCL,ODISHA	4/2019	3/2030 (-) [3/2030]	599.19 (-) [599.19]	157.48 (0.00) [0]	0/0
219	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442],BPCL,MAHARASHTRA	4/2021	6/2024 (-) [7/2025]	1,164.69 (-) [1,164.69]	169.72 (0.00) [13]	0/0
220	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI - [N16000452],BPCL,MAHARASHTRA	5/2022	3/2024 (-) [9/2024]	423.39 (-) [423.39]	63.90 (0.00) [6]	0/0
221	CITY GAS DISTRIBUTION NETWORK PROJECT AT BALLARI AND GADAG - [N16000461],BPCL,KARNATAKA	4/2019	9/2028 (-) [9/2028]	897.62 (-) [897.62]	179.90 (0.00) [0]	0/0
222	Setting up of Integrated 2G and 1G Bio- Ethanol Refinery at Bargarh, Odisha - [N16000374],BPCL,ODISHA	8/2019	8/2022 (6/2023) [10/2024]	1,607.00 (-) [1,607.00]	867.50 (0.00) [26]	9/28
223	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234],BPCL,TAMIL NADU	11/2012	2/2017 (1/2026) [1/2026]	678.00 (1,732.00) [1,732.00]	30.71 (1,054.00) [107]	0/0
224	CITY GAS DISTRIBUTION NETWORK PROJECT AT AHMEDNAGAR AND AURANGABAD - [N16000459],BPCL,MAHARASHTRA	4/2019	9/2028 (-) [9/2028]	3,972.18 (-) [3,972.18]	1,233.81 (0.00) [0]	12/14
225	CITY GAS DISTRIBUTION NETWORK PROJECT AT BILASPUR, HAMIRPUR AND UNA - [N16000467],BPCL,HIMACHAL PRADESH	4/2019	9/2030 (-) [9/2030]	427.94 (-) [427.94]	71.16 (0.00) [0]	0/0
226	CBR 9 MMTPA PROJECT - [N16000434],CPCL,TAMIL NADU	1/2021	6/2025 (-) [0/0]	31,580.00 (31,580.00) [31,580.00]	906.79 (0.00) [0]	11/50
227	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II - [N16000285],GAIL,MULTI STATE	6/2009	12/2012 (11/2024) [11/2024]	2,915.00 (5,909.00) [5,909.00]	3,510.30 (2,994.00) [143]	41/42
228	DHAMRA HALDIA PIPELINE PROJECT - [N16000391],GAIL,MULTI STATE	3/2020	11/2022 (6/2024) [6/2024]	1,030.65 (-) [1,030.65]	625.20 (0.00) [19]	10/12
229	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398],GAIL,MULTI STATE	6/2020	5/2023 (10/2024) [10/2024]	7,844.25 (-) [7,844.25]	4,595.80 (0.00) [17]	24/29
230	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275],GAIL,WEST BENGAL	3/2017	12/2020 (6/2024) [6/2024]	1,740.00 (2,433.15) [2,433.15]	1,547.50 (693.15) [42]	19/24
231	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388],GAIL,MULTI STATE	9/2019	7/2022 (9/2024) [9/2024]	2,658.34 (-) [2,658.34]	1,553.40 (0.00) [26]	15/18
232	BARAUNI-GUWAHATI PIPELINE - [N16000334],GAIL,MULTI STATE	6/2018	12/2021 (10/2023) [10/2023]	3,308.00 (3,992.00) [3,992.00]	3,537.30 (684.00) [22]	18/20

233	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327],GAIL,BIHAR	10/2017	10/2022 (-) [10/2023]	359.25 (-) [359.25]	272.02 (0.00) [12]	10/10
234	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329],GAIL,JHARKHAND	10/2017	10/2022 (-) [10/2023]	226.45 (-) [226.45]	217.29 (0.00) [12]	19/19
235	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328],GAIL,ODISHA	7/2017	7/2022 (-) [12/2023]	182.20 (-) [182.20]	137.31 (0.00) [17]	9/9
236	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289],GAIL,ODISHA	7/2017	7/2022 (-) [12/2023]	243.53 (-) [243.53]	223.48 (0.00) [17]	10/10
237	60 KTA POLYPROPYLENE PROJECT - [N16000429],GAIL,UTTAR PRADESH	3/2019	4/2024 (-) [4/2024]	910.56 (1,299.02) [1,299.02]	430.40 (388.46) [0]	15/17
238	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349],GAIL,GUJARAT	9/2018	2/2021 (12/2023) [12/2023]	225.54 (-) [247.90]	219.43 (22.36) [34]	6/8
239	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430],GAIL,MAHARASHTRA	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	1,753.85 (0.00) [0]	15/20
240	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389],GAIL,JHARKHAND	10/2017	10/2022 (-) [12/2023]	221.45 (-) [221.45]	152.54 (0.00) [14]	9/9
241	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385],HPCL,HARYANA	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	353.70 (0.00) [5]	45/52
242	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413],HPCL,CHHATTISGARH	3/2021	3/2024 (3/2025) [3/2025]	456.00 (-) [456.00]	181.92 (0.00) [12]	30/62
243	BHATINDA SANGRUR PIPELINE - [N16000440],HPCL,PUNJAB	11/2021	4/2024 (-) [4/2024]	367.00 (-) [367.00]	142.19 (0.00) [0]	22/43
244	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM - [N16000494],HPCL,ASSAM	3/2023	12/2026 (-) [12/2026]	384.04 (-) [384.04]	0.35 (0.00) [0]	0/52
245	RUF PITCH LOADING GANTRY - [N16000406],HPCL,ANDHRA PRADESH	10/2020	11/2022 (-) [4/2024]	332.61 (332.61) [332.61]	214.55 (0.00) [17]	7/12
246	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392],HPCL,WEST BENGAL	3/2019	3/2031 (8/2031) [8/2031]	5,830.20 (-) [5,830.20]	414.68 (0.00) [5]	33/50
247	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM - [N16000484],HPCL,ASSAM	3/2023	3/2026 (3/2026) [3/2026]	156.36 (156.36) [156.36]	0.36 (0.00) [0]	0/0
248	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369],HPCL,KARNATAKA	12/2018	12/2022 (12/2023) [12/2023]	854.00 (854.00) [854.00]	384.42 (0.00) [12]	15/19
249	SWRO II WITH LLPH FACILITIES - [N16000378],HPCL,ANDHRA PRADESH	9/2019	7/2020 (7/2023) [10/2023]	196.26 (196.26) [196.26]	141.51 (0.00) [39]	1/5
250	LEASE OF MBPT RECLAIMED LAND AT JAWAHAR DWEET - [N16000493],HPCL,MAHARASHTRA	12/2022	12/2023 (-) [12/2023]	410.00 (-) [410.00]	40.71 (0.00) [0]	4/6
251	CITY GAS DISTRIBUTION IN UP AND	3/2019	3/2029	3,450.20	1,340.47	34/64

	UK - [N16000387],HPCL,UTTAR PRADESH		(8/2029) [8/2029]	(-) [3,450.20]	(0.00) [5]	
252	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432],HPCL,ANDHRA PRADESH	9/2021	6/2024 (-) [6/2024]	160.00 (-) [160.00]	0.43 (0.00) [0]	3/11
253	VISAKH REFINERY MODERNISATION PROJECT - [N16000235],HPCL,ANDHRA PRADESH	7/2016	7/2020 (7/2022) [4/2024]	20,928.00 (26,264.00) [26,264.00]	23,860.04 (5,336.00) [45]	106/111
254	NEW LPG PLANT AT VARANASI - [N16000447],HPCL,UTTAR PRADESH	8/2017	5/2024 (-) [5/2024]	194.62 (-) [194.62]	154.12 (0.00) [0]	0/20
255	HALDIA PANAGARH PIPELINE PROJECT - [N16000478],HPCL,WEST BENGAL	11/2022	11/2025 (-) [11/2025]	1,010.00 (-) [1,010.00]	5.55 (0.00) [0]	1/21
256	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402],HPCL,PUNJAB	5/2020	2/2023 (12/2023) [12/2023]	1,421.46 (-) [1,421.46]	735.28 (0.00) [10]	17/22
257	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421],IOCL,BIHAR	6/2019	12/2029 (3/2030) [3/2030]	988.00 (-) [988.00]	84.87 (0.00) [3]	0/0
258	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399],IOCL,BIHAR	6/2020	8/2022 (6/2023) [9/2023]	403.00 (-) [403.00]	250.14 (0.00) [13]	0/2
259	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362],IOCL,ODISHA	5/2019	8/2021 (3/2024) [3/2024]	3,361.00 (-) [3,361.00]	2,497.03 (0.00) [31]	9/11
260	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS - [N16000486],IOCL,TAMIL NADU	3/2022	3/2030 (-) [3/2030]	501.00 (-) [501.00]	41.04 (0.00) [0]	0/0
261	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427],IOCL,MULTI STATE	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	186.74 (0.00) [0]	0/0
262	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323],IOCL,UTTAR PRADESH	8/2017	8/2020 (11/2022) [8/2023]	255.40 (-) [255.40]	216.40 (0.00) [36]	3/3
263	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI - [N16000480],IOCL,JHARKHAND	3/2023	2/2026 (-) [2/2026]	202.07 (-) [202.07]	0.23 (0.00) [0]	0/0
264	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) - [N16000456],IOCL,MAHARASHTRA	9/2022	8/2025 (-) [8/2025]	165.00 (-) [165.00]	0.24 (0.00) [0]	0/0
265	EXTENSION OF ASANUR-SANKARI SECTION OF CHENNAI-TRICHY-MADURAI PIPELINE UPTO COIMBATORE (IRUGUR) - [N16000479],IOCL,TAMIL NADU	1/2023	1/2025 (-) [1/2025]	346.70 (-) [346.70]	0.13 (0.00) [0]	0/0
266	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383],IOCL,HARYANA	9/2019	7/2021 (3/2022) [12/2023]	164.69 (-) [164.69]	124.00 (0.00) [29]	7/9
267	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386],IOCL,BIHAR	1/2020	4/2023 (12/2024) [12/2024]	14,810.00 (-) [14,810.00]	6,350.87 (0.00) [20]	6/7

268	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361],IOCL,ODISHA	11/2018	9/2021 (7/2023) [4/2024]	462.30 (543.00) [543.00]	393.54 (80.70) [31]	4/5
269	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253],IOCL,TAMIL NADU	5/2016	12/2018 (11/2023) [3/2024]	4,497.00 (6,025.00) [6,025.00]	5,303.14 (1,528.00) [63]	5/5
270	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396],IOCL,ODISHA	7/2020	1/2024 (-) [7/2025]	13,805.00 (-) [13,805.00]	3,776.82 (0.00) [18]	7/12
271	LPG BP PROJECT CHITTOOR - [N16000381],IOCL,ANDHRA PRADESH	7/2019	7/2022 (6/2023) [2/2024]	167.00 (-) [167.00]	77.46 (0.00) [19]	0/5
272	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS - [N16000491],IOCL,WEST BENGAL	3/2022	3/2030 (-) [3/2030]	609.00 (-) [609.00]	6.56 (0.00) [0]	0/0
273	LPG BP PROJECT KHORDHA - [N16000283],IOCL,ODISHA	12/2016	12/2019 (1/2023) [9/2023]	161.59 (161.59) [161.59]	135.83 (0.00) [45]	18/26
274	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352],IOCL,HARYANA	1/2019	1/2021 (8/2022) [9/2023]	909.00 (-) [909.00]	810.76 (0.00) [32]	6/6
275	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY - [N16000446],IOCL,MAHARASHTRA	9/2021	10/2023 (5/2024) [5/2024]	378.00 (-) [378.00]	66.49 (0.00) [7]	0/0
276	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405],IOCL,TAMIL NADU	10/2020	12/2023 (-) [2/2024]	1,398.00 (1,587.00) [1,587.00]	726.79 (189.00) [2]	0/0
277	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS - [N16000487],IOCL,MAHARASHTRA	3/2022	3/2030 (-) [3/2030]	865.00 (-) [865.00]	13.28 (0.00) [0]	0/0
278	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435],IOCL,RAJASTHAN	12/2021	10/2024 (12/2024) [12/2024]	9,028.00 (-) [9,028.00]	4,088.75 (0.00) [2]	0/0
279	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT - [N16000495],IOCL,TRIPURA	6/2022	8/2025 (-) [8/2025]	656.00 (-) [656.00]	98.04 (0.00) [0]	0/0
280	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI - [N16000453],IOCL,BIHAR	1/2022	9/2024 (-) [9/2024]	389.00 (-) [389.00]	16.42 (0.00) [0]	0/0
281	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321],IOCL,HARYANA	4/2018	2/2020 (6/2023) [10/2023]	206.63 (340.76) [340.76]	274.27 (134.13) [44]	6/7
282	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340],IOCL,HARYANA	8/2018	8/2020 (7/2023) [11/2023]	1,636.00 (-) [1,636.00]	1,329.13 (0.00) [39]	6/7
283	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS - [N16000485],IOCL,ANDHRA PRADESH	3/2022	3/2030 (-) [3/2030]	1,420.00 (-) [1,420.00]	25.37 (0.00) [0]	0/0

284	CGD PROJECT AT SALEM DISTRICT - [N16000419],IOCL,TAMIL NADU	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	96.14 (0.00) [0]	0/0
285	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414],IOCL,ASSAM	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	236.12 (0.00) [0]	8/10
286	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403],IOCL,TAMIL NADU	10/2020	9/2023 (-) [12/2024]	921.00 (-) [921.00]	315.45 (0.00) [15]	0/0
287	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424],IOCL,BIHAR	6/2019	2/2028 (8/2029) [8/2029]	347.00 (-) [347.00]	147.32 (0.00) [18]	0/0
288	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW- II) AT HALDIA REFINERY - [N16000393],IOCL,WEST BENGAL	6/2020	1/2023 (11/2023) [11/2023]	1,019.00 (-) [1,019.00]	658.96 (0.00) [10]	5/6
289	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT - [N16000454],IOCL,GUJARAT	1/2022	9/2024 (-) [9/2024]	328.00 (-) [328.00]	12.15 (0.00) [0]	0/0
290	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423],IOCL,BIHAR	6/2019	12/2029 (3/2030) [3/2030]	163.00 (-) [163.00]	62.69 (0.00) [3]	0/0
291	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411],IOCL,GUJARAT	10/2020	8/2023 (-) [3/2024]	1,614.00 (-) [1,614.00]	513.56 (0.00) [7]	0/0
292	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351],IOCL,TELANGANA	12/2018	4/2022 (-) [10/2023]	611.00 (-) [611.00]	349.08 (0.00) [18]	0/0
293	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395],IOCL,ODISHA	1/2020	7/2022 (-) [8/2023]	202.16 (-) [202.16]	135.57 (0.00) [13]	3/4
294	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368],IOCL,ODISHA	6/2019	9/2022 (3/2024) [3/2024]	371.00 (427.10) [427.10]	204.58 (56.10) [18]	6/8
295	CGD PROJECT AT REWA DISTRICT - [N16000417],IOCL,MADHYA PRADESH	10/2018	2/2027 (9/2028) [9/2028]	177.00 (-) [177.00]	107.21 (0.00) [19]	0/0
296	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409],IOCL,GUJARAT	9/2020	9/2024 (-) [8/2024]	18,936.00 (-) [18,936.00]	4,182.86 (0.00) [-1]	10/15
297	POLY BUTADIENE RUBBER PLANT AT PANIPAT - [N16000458],IOCL,HARYANA	3/2022	3/2025 (-) [3/2025]	1,459.00 (2,102.79) [1,459.00]	69.74 (0.00) [0]	0/0
298	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343],IOCL,ANDHRA PRADESH	4/2018	4/2022 (-) [3/2025]	355.00 (-) [355.00]	198.26 (0.00) [35]	0/0
299	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM - [N16000441],IOCL,ASSAM	3/2022	7/2026 (-) [9/2026]	277.00 (-) [277.00]	35.19 (0.00) [2]	0/0

300	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS - [N16000490],IOCL,TAMIL NADU	3/2022	3/2030 (-) [3/2030]	1,328.00 (-) [1,328.00]	41.85 (0.00) [0]	0/0
301	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400],IOCL,GUJARAT	6/2020	12/2022 (2/2024) [12/2023]	1,378.00 (-) [1,378.00]	885.65 (0.00) [12]	0/0
302	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGOUR DISTRICTS - [N16000489],IOCL,RAJASTHAN	3/2022	3/2030 (-) [3/2030]	575.00 (-) [575.00]	22.91 (0.00) [0]	0/0
303	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418],IOCL,TAMIL NADU	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	288.06 (0.00) [0]	0/0
304	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416],IOCL,JHARKHAND	10/2018	12/2029 (3/2030) [3/2030]	613.00 (-) [613.00]	224.64 (0.00) [3]	0/0
305	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342],IOCL,ANDHRA PRADESH	8/2018	4/2021 (5/2023) [5/2023]	466.00 (-) [466.00]	415.73 (0.00) [0]	0/0
306	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412],IOCL,HARYANA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	4,702.23 (0.00) [0]	15/23
307	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363],IOCL,HARYANA	12/2018	6/2021 (7/2023) [9/2023]	278.60 (-) [278.60]	186.05 (0.00) [27]	5/5
308	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376],IOCL,HARYANA	8/2019	12/2021 (12/2023) [12/2023]	1,255.00 (-) [1,255.00]	776.69 (0.00) [24]	6/7
309	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI - [N16000438],IOCL,TAMIL NADU	1/2022	7/2024 (-) [12/2024]	827.00 (-) [827.00]	222.66 (0.00) [5]	0/0
310	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE - [N16000451],IOCL,TAMIL NADU	3/2022	11/2024 (-) [11/2024]	564.00 (-) [564.00]	96.53 (0.00) [0]	0/0
311	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415],IOCL,BIHAR	10/2018	8/2027 (2/2029) [2/2029]	176.00 (-) [176.00]	135.37 (0.00) [18]	0/0
312	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332],IOCL,WEST BENGAL	3/2018	9/2022 (6/2023) [12/2023]	3,712.00 (3,696.00) [3,696.00]	2,852.90 (-16.00) [15]	3/3
313	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA - [N16000457],IOCL,ASSAM	6/2022	10/2025 (-) [10/2025]	768.00 (-) [768.00]	1.39 (0.00) [0]	0/0
314	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS - [N16000492],IOCL,TAMIL NADU	3/2022	3/2030 (-) [3/2030]	1,295.00 (-) [1,295.00]	39.23 (0.00) [0]	0/0
315	CGD PROJECT AT PATHANKOT DISTRICT - [N16000488],IOCL,PUNJAB	3/2022	3/2030 (-) [3/2030]	151.00 (-) [151.00]	6.36 (0.00) [0]	0/0
316	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR	6/2019	2/2028 (8/2029)	2,996.00 (-)	517.47 (0.00)	0/0

	DISTRICTS [N16000425],IOCL,BIHAR		[8/2029]	[2,996.00]	[18]	
317	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) - [N16000455],IOCL,TAMIL NADU	1/2022	7/2024 (-) [7/2024]	829.00 (-) [829.00]	102.68 (0.00) [0]	0/0
318	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249],IOCL,MAHARASHTRA	5/2016	2/2022 (4/2023) [12/2023]	1,945.00 (2,251.00) [2,251.00]	2,005.03 (306.00) [22]	5/5
319	R and D CAMPUS II AT FARIDABAD - [N16000375],IOCL,HARYANA	6/2019	12/2022 (7/2023) [7/2025]	2,281.94 (3,219.94) [3,219.94]	1,122.50 (938.00) [31]	5/7
320	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324],IOCL,BIHAR	12/2017	10/2020 (6/2023) [12/2023]	199.36 (-) [199.36]	163.45 (0.00) [38]	2/2
321	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382],IOCL,GUJARAT	11/2019	5/2023 (11/2023) [11/2023]	5,251.00 (5,894.00) [5,251.00]	3,116.31 (0.00) [6]	10/11
322	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426],IOCL,MULTI STATE	6/2019	12/2029 (3/2030) [3/2030]	169.00 (-) [169.00]	64.99 (0.00) [3]	0/0
323	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420],IOCL,ANDHRA PRADESH	6/2019	8/2027 (3/2030) [3/2030]	2,880.00 (-) [2,880.00]	206.83 (0.00) [31]	0/0
324	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE - [N16000437],IOCL,KARNATAKA	1/2022	7/2025 (-) [7/2025]	463.00 (-) [463.00]	76.95 (0.00) [0]	0/0
325	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422],IOCL,BIHAR	6/2019	2/2028 (8/2029) [8/2029]	439.00 (-) [439.00]	195.43 (0.00) [18]	0/0
326	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345],IOCL,ODISHA	10/2018	10/2021 (4/2023) [7/2023]	1,297.50 (-) [1,297.50]	1,119.42 (0.00) [21]	1/1
327	NORTH EAST GAS GRID - [N16000439],IGGL,MULTI STATE	11/2020	3/2024 (-) [3/2024]	9,265.00 (9,265.00) [9,265.00]	4,481.56 (0.00) [0]	13/18
328	DEVANGONTHI MARKETING TERMINAL - [N16000401],MANGALORE REFIN,KARNATAKA	6/2020	6/2023 (1/2024) [1/2024]	200.00 (304.00) [304.00]	162.85 (104.00) [7]	3/6
329	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY - [N16000379],NRL,ASSAM	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	6,125.60 (6,602.00) [0]	8/14
330	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394],NRL,ASSAM	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	5,608.65 (-1,170.00) [0]	9/20
331	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433],ONGC,ASSAM	8/2021	2/2023 (-) [7/2024]	218.38 (-) [218.38]	66.27 (0.00) [17]	5/5
332	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD - [N16000444],ONGC,GUJARAT	1/2022	11/2024 (-) [11/2024]	621.40 (-) [621.40]	81.21 (0.00) [0]	1/2

333	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK - [N16000470],ONGC,MAHARASHTRA	6/2022	10/2025 (-) [10/2025]	4,144.41 (-) [4,144.41]	0.00 (0.00) [0]	6/6
334	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247],ONGC,ANDHRA PRADESH	3/2016	6/2020 (5/2024) [5/2024]	34,012.00 (-) [34,012.00]	25,464.83 (0.00) [47]	16/20
335	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213],ONGC,MAHARASHTRA	12/2015	4/2018 (12/2023) [5/2026]	3,190.69 (3,375.90) [3,375.90]	2,897.83 (185.21) [97]	14/15
336	CREATION OF GDU AND DPD FACILITIES AT RAJAHMUNDRY - [N16000471],ONGC,ANDHRA PRADESH	3/2022	5/2024 (-) [5/2024]	211.22 (-) [211.22]	6.03 (0.00) [0]	4/4
337	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A - [N16000483],ONGC,GUJARAT	7/2021	7/2025 (-) [7/2025]	173.03 (-) [173.03]	28.68 (0.00) [0]	5/5
338	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358],ONGC,MAHARASHTRA	4/2019	3/2022 (12/2023) [12/2023]	3,228.80 (3,976.67) [3,976.67]	3,793.93 (747.87) [21]	6/6
339	DEVELOPMENT OF NELP BLOCK KG-ONN-2003/1 NAGAYALANKA FIELD-PH II - [N16000469],ONGC,ANDHRA PRADESH	3/2022	6/2023 (-) [11/2023]	284.79 (-) [284.79]	201.63 (0.00) [5]	1/3
340	KALOL REDEVELOPMENT PROJECT - [N16000481],ONGC,GUJARAT	8/2022	3/2027 (-) [3/2027]	1,487.41 (-) [1,487.41]	374.18 (0.00) [0]	0/1
341	CONSTRUCTION OF TWO PRODUCED WATER TREATMENT PLANTS (PWTP) AT BECHARAJI AND SOBHASAN INSTALLATION OF - [N16000482],ONGC,GUJARAT	7/2021	7/2024 (-) [7/2024]	320.20 (-) [320.20]	22.53 (0.00) [0]	0/0
342	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239],ONGC,JHARKHAND	12/2015	3/2023 (3/2024) [3/2024]	823.27 (1,137.79) [1,137.79]	954.95 (314.52) [12]	9/11
343	CREATION OF GAS DEHYDRATION FACILITIES - [N16000443],ONGC,TRIPURA	3/2022	5/2024 (-) [5/2024]	209.33 (-) [209.33]	20.50 (0.00) [0]	1/2
344	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) - [N16000445],ONGC,JHARKHAND	11/2019	1/2024 (-) [12/2024]	431.00 (-) [431.00]	76.44 (0.00) [11]	1/3
345	REDEVELOPMENT OF LINCH FIELD - [N16000428],ONGC,GUJARAT	4/2021	3/2025 (-) [3/2025]	631.03 (-) [631.03]	214.83 (0.00) [0]	1/3
346	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241],ONGC,TAMIL NADU	11/2015	3/2019 (9/2021) [12/2024]	650.82 (-) [650.82]	469.54 (0.00) [69]	6/6
347	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431],ONGC,GUJARAT	8/2021	2/2026 (-) [2/2026]	885.63 (-) [885.63]	275.75 (0.00) [0]	1/3
348	PIPELINE REPLACEMENT PROJECT - VII - [N16000436],ONGC,MAHARASHTRA	1/2022	5/2024 (-) [5/2024]	3,183.58 (-) [3,183.58]	1,276.83 (0.00) [0]	5/5
349	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT - [N16000477],ONGC,GUJARAT	5/2022	2/2025 (-) [2/2025]	249.43 (-) [249.43]	5.95 (0.00) [0]	1/2
350	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-)	1,162.56 (-)	1,018.19 (0.00)	10/10

	- [N16000279],ONGC,GUJARAT		[3/2026]	[1,162.56]	[0]	
351	HEERA REDEVELOPMENT - PHASE III - [N16000360],ONGC,MAHARASHTRA	6/2019	3/2022 (12/2023) [12/2023]	2,494.68 (-) [2,494.68]	2,354.10 (0.00) [21]	6/6
352	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331],OIL,ASSAM	1/2018	2/2020 (3/2023) [9/2023]	543.91 (-) [661.21]	439.99 (117.30) [43]	1/14
353	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING - [N16000450],OIL,ASSAM	12/2020	7/2024 (-) [3/2024]	430.76 (-) [430.76]	118.55 (0.00) [-4]	0/0
354	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT - [N16000449],OIL,ASSAM	6/2021	12/2024 (-) [12/2024]	860.00 (-) [860.00]	101.03 (0.00) [0]	0/0
	POWER					
355	KWAR HE PROJECT - [N18000363],CVPPPL,JAMMU AND KASHMIR	5/2022	11/2026 (-) [11/2026]	4,526.12 (-) [4,526.12]	431.06 (0.00) [0]	0/0
356	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172],CVPPPL,JAMMU AND KASHMIR	10/2014	4/2020 (7/2025) [9/2026]	8,112.12 (-) [8,112.12]	3,194.18 (0.00) [77]	0/0
357	KIRU HYDRO ELECTRIC PROJECT - [N18000278],CVPPPL,JAMMU AND KASHMIR	3/2019	8/2024 (-) [3/2026]	4,287.59 (-) [4,287.59]	1,168.94 (0.00) [19]	0/0
358	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221],NHPC,ARUNACHAL PRADESH	9/2003	9/2010 (5/2025) [5/2025]	6,285.33 (21,247.54) [21,247.54]	18,903.19 (14,962.21) [176]	0/0
359	PARBATI HEP (4X200 MW) (NHPC) II - [180100210],NHPC,HIMACHAL PRADESH	9/2002	9/2009 (3/2024) [3/2024]	3,919.59 (11,134.54) [11,134.54]	10,807.99 (7,214.95) [174]	5/5
360	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH - [N18000362],NHPC,ARUNACHAL PRADESH	2/2023	2/2032 (-) [2/2032]	31,876.39 (-) [31,876.39]	2,177.22 (0.00) [0]	0/0
361	KALPI SOLAR POWER PROJECT - [N18000323],NHPC,UTTAR PRADESH	7/2020	3/2022 (3/2024) [3/2024]	314.64 (350.46) [350.46]	242.14 (35.82) [24]	0/0
362	RANGIT IV HE PROJECT - [N18000326],NHPC,SIKKIM	3/2021	5/2024 (8/2024) [8/2024]	938.29 (938.29) [938.29]	658.71 (0.00) [3]	0/0
363	TEESTA VI HE PROJECT - [N18000325],NHPC,SIKKIM	3/2019	3/2024 (8/2026) [8/2026]	5,748.04 (-) [5,748.04]	2,643.25 (0.00) [29]	0/0
364	RATLE HE PROJECT - [N18000324],NHPC,JAMMU AND KASHMIR	2/2021	2/2026 (5/2026) [5/2026]	5,281.94 (5,281.94) [5,281.94]	333.41 (0.00) [3]	0/0
365	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) - [N18000364],NTPC,ODISHA	8/2022	5/2027 (-) [5/2027]	11,844.00 (-) [11,844.00]	635.90 (0.00) [0]	0/0
366	BARH STPP(3X660MW) NTPC - [180100242],NTPC,BIHAR	2/2005	10/2011 (7/2023) [7/2024]	8,692.97 (21,312.11) [21,312.11]	21,304.21 (12,619.14) [153]	41/49
367	ANTA SOLAR 90 MW - [N18000292],NTPC,RAJASTHAN	1/2021	3/2022 (3/2024)	382.22 (-)	65.29 (0.00)	0/0

			[3/2024]	[382.22]	[24]	
368	GUJARAT 200 MW (GUVNL TENDER) - [N18000295],NTPC,GUJARAT	1/2021	7/2022 (3/2024) [3/2024]	842.27 (-) [842.27]	93.82 (0.00) [20]	0/0
369	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212],NTPC,TELANGANA	1/2016	11/2020 (7/2022) [8/2023]	10,598.98 (-) [10,998.00]	10,831.04 (399.02) [33]	36/39
370	RAMMAM-III HEPP (3X40 MW) - [N18000178],NTPC,WEST BENGAL	9/2014	9/2019 (12/2024) [9/2026]	1,381.84 (-) [1,803.00]	909.90 (421.16) [84]	7/10
371	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014],NTPC,UTTARAKHAND	11/2006	3/2013 (12/2021) [12/2024]	2,978.48 (5,867.38) [7,103.00]	5,911.37 (4,124.52) [141]	8/15
372	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321],NTPC,RAJASTHAN	3/2022	8/2023 (9/2024) [9/2024]	1,409.52 (-) [1,409.52]	160.80 (0.00) [13]	0/0
373	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320],NTPC,RAJASTHAN	3/2022	8/2023 (9/2024) [9/2024]	1,352.71 (-) [1,352.71]	91.14 (0.00) [13]	0/0
374	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142],NTPC,UTTARAKHAND	7/2012	8/2017 (-) [8/2017]	1,527.00 (-) [1,527.00]	149.93 (0.00) [0]	0/15
375	DAYAPAR WIND ENERGY PROJECT 200MW - [N18000345],NTPC,GUJARAT	7/2022	3/2025 (3/2025) [3/2025]	1,316.02 (-) [1,316.02]	92.02 (0.00) [0]	0/0
376	BHADLA-II 500MW SOLAR PV PROJECT - [N18000347],NTPC,RAJASTHAN	6/2022	3/2024 (3/2024) [3/2024]	2,598.92 (-) [2,598.92]	1.75 (0.00) [0]	0/0
377	SHAJAPUR 325MW SOLAR PV PROJECT - [N18000348],NTPC,MADHYA PRADESH	6/2022	3/2024 (3/2024) [2/2024]	1,530.49 (-) [1,530.49]	208.92 (0.00) [-1]	0/0
378	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277],NTPC,WEST BENGAL	12/2016	11/2018 (3/2023) [11/2023]	529.68 (633.80) [679.00]	560.81 (149.32) [60]	14/20
379	BHENSARA 320 MW - [N18000293],NTPC,RAJASTHAN	1/2021	7/2022 (3/2024) [3/2024]	1,221.73 (-) [1,221.73]	153.13 (0.00) [20]	0/0
380	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296],NTPC,GUJARAT	5/2021	9/2022 (3/2024) [3/2024]	674.92 (-) [674.92]	89.67 (0.00) [18]	0/0
381	DAYAPAR WIND ENERGY PROJECT 150MW - [N18000319],NTPC,GUJARAT	11/2021	5/2023 (6/2024) [6/2024]	937.80 (-) [937.80]	314.00 (0.00) [13]	0/0
382	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322],NTPC,RAJASTHAN	3/2022	8/2023 (9/2024) [9/2024]	1,426.94 (-) [1,426.94]	164.82 (0.00) [13]	0/0
383	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286],NTPC,RAJASTHAN	3/2020	9/2021 (9/2024) [9/2024]	1,782.00 (-) [1,782.00]	1,267.99 (0.00) [36]	0/0
384	CHHATTARGARH 150 MW - [N18000294],NTPC,RAJASTHAN	2/2021	7/2022 (3/2024) [3/2024]	599.99 (-) [599.99]	262.95 (0.00) [20]	0/0
385	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) - [N18000346],NTPC,GUJARAT	9/2022	9/2024 (9/2024) [9/2024]	7,179.54 (-) [7,179.54]	545.46 (0.00) [0]	0/0
386	PATRATU STPP-I (3X800MW) - [N18000275],NTPC,JHARKHAND	11/2017	3/2023 (-) [3/2025]	18,668.00 (-) [18,668.00]	11,484.39 (0.00) [24]	8/23
387	BHUJ SOLAR 300MW (TRANCHE-IV	11/2022	3/2024	1,442.60	80.60	0/0

	WIND SOLAR HYBRID) - [N18000349],NTPC,GUJARAT		(6/2024) [6/2024]	(-) [1,442.60]	(0.00) [3]	
388	NORTH KARANPURA STPP (3X660 MW) - [N18000177],NTPC,JHARKHAND	2/2014	6/2019 (10/2022) [6/2024]	14,366.58 (-) [17,007.00]	14,880.63 (2,640.42) [60]	38/46
389	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264],PGCIL,MULTI STATE	8/2017	2/2020 (-) [3/2024]	1,931.39 (-) [2,635.55]	1,952.75 (704.16) [49]	0/0
390	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION - [N18000339],PGCIL,MULTI STATE	11/2018	11/2021 (-) [6/2023]	173.94 (-) [173.94]	125.05 (0.00) [0]	0/0
391	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304],PGCIL,RAJASTHAN	3/2021	12/2022 (-) [7/2023]	1,340.81 (-) [1,340.81]	1,087.22 (0.00) [7]	0/0
392	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249],PGCIL,MULTI STATE	12/2014	12/2018 (-) [12/2024]	4,754.42 (-) [9,129.32]	5,600.77 (4,374.90) [72]	0/0
393	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD - [N18000314],PGCIL,RAJASTHAN	1/2020	1/2021 (-) [5/2023]	562.86 (545.88) [545.88]	394.19 (-16.98) [0]	0/0
394	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337],PGCIL,MULTI STATE	7/2022	6/2023 (-) [6/2024]	4,546.26 (-) [4,546.26]	633.23 (0.00) [12]	0/0
395	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327],PGCIL,ASSAM	3/2019	3/2023 (-) [9/2023]	1,326.00 (-) [1,326.00]	1,367.92 (0.00) [6]	0/0
396	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX - [N18000355],PGCIL,CHHATTISGARH	3/2023	3/2025 (-) [3/2025]	260.30 (-) [260.30]	0.00 (0.00) [0]	0/0
397	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317],PGCIL,MULTI STATE	11/2018	11/2021 (-) [9/2023]	241.38 (-) [241.38]	236.89 (0.00) [22]	0/0
398	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM - [N18000330],PGCIL,MULTI STATE	3/2022	12/2024 (-) [12/2024]	288.71 (-) [288.71]	0.00 (0.00) [0]	0/0
399	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000331],PGCIL,MULTI STATE	2/2022	9/2023 (-) [3/2024]	359.47 (-) [359.47]	54.26 (0.00) [6]	0/0
400	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B - [N18000352],PGCIL,MULTI STATE	3/2023	11/2024 (-) [11/2024]	3,546.94 (-) [3,546.94]	51.87 (0.00) [0]	0/0

401	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C - [N18000338],PGCIL,MULTI STATE	7/2022	3/2025 (-) [3/2025]	186.19 (-) [186.19]	16.84 (0.00) [0]	0/0
402	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM - [N18000328],PGCIL,MULTI STATE	2/2022	4/2025 (-) [4/2025]	318.12 (-) [318.12]	102.00 (0.00) [0]	0/0
403	POWERGRID NEEMUCH TRANSMISSION SYSTEM LIMITED - [N18000341],PGCIL,MULTI STATE	8/2022	2/2024 (-) [2/2024]	863.99 (-) [863.99]	118.49 (0.00) [0]	0/0
404	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT - [N18000358],PGCIL,GUJARAT	3/2023	3/2025 (-) [3/2025]	815.12 (-) [815.12]	0.00 (0.00) [0]	0/0
405	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305],PGCIL,RAJASTHAN	6/2021	12/2022 (-) [3/2024]	713.82 (-) [713.82]	433.26 (0.00) [15]	0/0
406	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299],PGCIL,BIHAR	5/2021	4/2023 (-) [8/2023]	179.29 (-) [179.29]	108.51 (0.00) [4]	0/0
407	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302],PGCIL,HARYANA	1/2019	3/2022 (-) [9/2023]	267.33 (-) [267.33]	109.36 (0.00) [18]	0/0
408	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307],PGCIL,RAJASTHAN	6/2021	12/2022 (-) [3/2024]	1,006.00 (-) [1,006.00]	791.18 (0.00) [15]	0/0
409	EASTERN REGION EXPANSION SCHEME XXIX - [N18000351],PGCIL,ODISHA	3/2023	11/2025 (-) [11/2025]	524.04 (-) [524.04]	15.25 (0.00) [0]	0/0
410	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK - [N18000357],PGCIL,GUJARAT	3/2023	12/2024 (-) [12/2024]	922.30 (-) [922.30]	0.00 (0.00) [0]	0/0
411	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332],PGCIL,MULTI STATE	5/2022	11/2023 (-) [3/2024]	1,666.00 (-) [1,666.00]	511.39 (0.00) [4]	0/0
412	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII - [N18000354],PGCIL,CHHATTISGARH	3/2023	9/2024 (-) [9/2024]	271.69 (-) [271.69]	0.00 (0.00) [0]	0/0
413	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303],PGCIL,RAJASTHAN	3/2021	12/2022 (-) [9/2023]	353.85 (-) [353.85]	239.56 (0.00) [9]	0/0
414	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR	3/2015	3/2018 (-)	197.40 (-)	159.47 (0.00)	0/0

	UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184],PGCIL,MULTI STATE		[9/2023]	[197.40]	[66]	
415	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK - [N18000359],PGCIL,GUJARAT	3/2023	12/2024 (-) [12/2024]	966.79 (-) [966.79]	0.00 (0.00) [0]	0/0
416	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000360],PGCIL,GUJARAT	3/2023	3/2025 (-) [3/2025]	1,167.55 (-) [1,167.55]	0.00 (0.00) [0]	0/0
417	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244],PGCIL,MULTI STATE	2/2017	6/2019 (-) [8/2023]	235.53 (-) [243.74]	168.69 (8.21) [50]	0/0
418	ER WR TRANSMISSION LIMITED - [N18000353],PGCIL,MULTI STATE	3/2023	3/2025 (-) [3/2025]	281.16 (-) [281.16]	0.00 (0.00) [0]	0/0
419	WESTERN REGION EXPANSION SCHEME XXV - [N18000350],PGCIL,CHHATTISGARH	2/2023	11/2023 (-) [3/2024]	385.84 (-) [385.84]	0.00 (0.00) [4]	0/0
420	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION - [N18000343],PGCIL,MULTI STATE	10/2022	10/2025 (-) [10/2025]	307.87 (-) [307.87]	7.34 (0.00) [0]	0/0
421	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316],PGCIL,MULTI STATE	5/2021	3/2023 (-) [2/2024]	576.42 (-) [576.42]	366.29 (0.00) [11]	0/0
422	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250],PGCIL,MULTI STATE	12/2014	12/2018 (-) [1/2024]	5,111.33 (-) [6,700.00]	4,578.01 (1,588.67) [61]	0/0
423	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262],PGCIL,TAMIL NADU	5/2017	7/2019 (-) [8/2023]	186.17 (-) [219.66]	178.40 (33.49) [49]	0/0
424	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000361],PGCIL,GUJARAT	3/2023	3/2025 (-) [3/2025]	2,820.99 (-) [2,820.99]	0.00 (0.00) [0]	0/0
425	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART - [N18000356],PGCIL,RAJASTHAN	3/2023	9/2024 (-) [9/2024]	1,433.28 (-) [1,433.28]	0.00 (0.00) [0]	0/0
426	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - [N18000329],PGCIL,MULTI STATE	3/2022	3/2023 (-) [10/2023]	176.22 (-) [176.22]	39.82 (0.00) [7]	0/0
427	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313],PGCIL,MULTI STATE	9/2015	12/2017 (-) [9/2023]	167.31 (-) [167.31]	129.77 (0.00) [69]	0/0
428	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306],PGCIL,RAJASTHAN	6/2021	12/2022 (-) [3/2024]	1,562.00 (-) [1,562.00]	805.08 (0.00) [15]	0/0

429	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300],PGCIL,RAJASTHAN	5/2021	9/2022 (-) [12/2023]	1,184.88 (-) [1,184.88]	712.85 (0.00) [15]	0/0
430	OMKARESHWAR FLOATING SOLAR POWER PROJECT (90 MW) - [N18000342],SJVN,MADHYA PRADESH	11/2022	4/2024 (-) [4/2024]	646.17 (-) [646.17]	255.95 (0.00) [0]	0/0
431	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194],SJVN,BIHAR	3/2019	1/2024 (-) [3/2024]	10,439.09 (-) [10,439.09]	8,067.59 (0.00) [2]	20/27
432	BIKANER SOLAR POWER PROJECT - [N18000335],SJVN,MAHARASHTRA	4/2022	5/2024 (-) [5/2024]	5,491.89 (532.00) [6,023.89]	2,211.03 (532.00) [0]	0/0
433	Bagodara Solar Power Project - [N18000297],SJVN,GUJARAT	5/2021	10/2022 (-) [12/2023]	339.35 (-) [339.35]	253.94 (0.00) [14]	0/5
434	NAITWAR MORI HEP - [N18000265],SJVN,UTTARAKHAND	10/2017	12/2021 (-) [8/2023]	648.33 (-) [1,272.29]	1,172.12 (623.96) [20]	18/32
435	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291],SJVN,HIMACHAL PRADESH	10/2020	11/2025 (-) [11/2025]	687.97 (-) [687.97]	433.34 (0.00) [0]	4/11
436	GURHAH SOLAR POWER PROJECT - [N18000334],SJVN,UTTAR PRADESH	5/2022	8/2023 (-) [8/2023]	466.82 (-) [466.82]	411.95 (0.00) [0]	0/0
437	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279],SJVN,HIMACHAL PRADESH	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	1,172.83 (0.00) [0]	2/10
438	RAGHANESDA SOLAR POWER PROJECT - [N18000340],SJVN,GUJARAT	6/2022	12/2023 (-) [12/2023]	642.15 (-) [642.15]	203.25 (0.00) [0]	0/0
439	GUJRAI SOLAR POWER PROJECT - [N18000336],SJVN,UTTAR PRADESH	6/2022	8/2023 (-) [8/2023]	279.94 (-) [279.94]	194.48 (0.00) [0]	0/3
440	SUNNI DAM HYDRO ELECTRIC PROJECT - [N18000344],SJVN,HIMACHAL PRADESH	1/2023	4/2028 (-) [4/2028]	2,614.51 (-) [2,614.51]	496.15 (0.00) [0]	0/0
441	KHURJA SUPER THERMAL POWER PROJECT - [N18000272],THDCIL,UTTAR PRADESH	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	7,902.37 (0.00) [11]	8/13
442	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010],THDCIL,UTTARAKHAND	7/2006	2/2016 (6/2022) [6/2024]	1,657.00 (-) [4,825.60]	5,601.35 (3,168.60) [100]	29/34
443	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042],THDCIL,UTTARAKHAND	8/2008	6/2013 (-) [6/2026]	2,491.58 (3,860.35) [3,860.35]	3,163.57 (1,368.77) [156]	11/25
RAILWAYS						
444	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181],CR,MAHARASHTRA	2/1997	3/2021 (3/2025) [3/2026]	2,271.50 (-) [4,805.17]	3,491.85 (2,533.67) [60]	0/0
445	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361],CR,MAHARASHTRA	2/2016	3/2022 (3/2025) [3/2024]	1,035.16 (-) [1,035.16]	830.46 (0.00) [24]	0/0
446	KALYAN-KASARA 3RD LINE	4/2011	3/2021	792.89	578.90	0/0

	- [N22000233],CR,MAHARASHTRA		(-) [3/2026]	(-) [792.89]	(0.00) [60]	
447	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356],CR,MAHARASHTRA	2/2015	3/2022 (3/2025) [12/2024]	1,272.19 (-) [1,384.72]	757.06 (112.53) [33]	0/0
448	WARDHA-NANDED MAHARASHTRA - [N22000231],CR,MAHARASHTRA	4/2008	3/2023 (-) [3/2024]	3,168.29 (-) [3,445.48]	1,666.35 (277.19) [12]	0/0
449	PUNE-MIRAJ-LONDA (467 KM) - [N22000359],CR,MAHARASHTRA	2/2015	3/2024 (3/2025) [3/2024]	3,627.47 (3,627.00) [6,409.38]	2,826.85 (2,781.91) [0]	0/0
450	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358],CR,MAHARASHTRA	2/2015	3/2023 (3/2025) [3/2024]	2,449.91 (-) [2,449.91]	928.90 (0.00) [12]	0/0
451	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250],CR,MAHARASHTRA	4/2012	3/2022 (-) [12/2024]	540.02 (-) [540.02]	410.94 (0.00) [33]	0/0
452	DAUND - MANMAD (236 KM) - [N22000360],CR,MAHARASHTRA	2/2016	3/2023 (3/2025) [3/2026]	1,876.00 (-) [2,081.27]	1,335.69 (205.27) [36]	0/0
453	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362],CR,MAHARASHTRA	2/2016	3/2023 (-) [12/2024]	637.95 (-) [637.95]	513.52 (0.00) [21]	0/0
454	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431],CCOI,ANDHRA PRADESH	8/2016	3/2019 (-) [3/2019]	234.50 (-) [235.00]	14.14 (0.50) [0]	0/0
455	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428],CCOI,GUJARAT	10/2013	3/2019 (-) [3/2019]	343.00 (-) [343.00]	222.83 (0.00) [0]	0/0
456	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464],DFCC,MULTI STATE	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	47,476.00 (34,509.00) [0]	0/0
457	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346],DFCC,MULTI STATE	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [51,219.00]	31,304.00 (39,630.00) [0]	0/0
458	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257],ECR,BIHAR	4/1997	/ (-) [3/2025]	162.87 (614.45) [614.45]	399.41 (451.58) [-]	0/0
459	KODERMA-TILAIYA (NL), ECR - [220100305],ECR,JHARKHAND	4/2002	/ (-) [3/2024]	459.91 (1,625.87) [1,625.87]	1,323.75 (1,165.96) [-]	0/0
460	SAKRI-HASANPUR ROAD (NL) - [N22000171],ECR,BIHAR	4/1999	/ (-) [12/2024]	325.00 (735.20) [735.20]	520.72 (410.20) [-]	0/0
461	JAYANAGAR-DARBHANGA- NARKATIA GANJ(GC),ECR - [220100240],ECR,BIHAR	4/1997	3/2012 (-) [6/2023]	324.73 (967.29) [1,110.00]	1,165.40 (785.27) [0]	0/0
462	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472],ECR,BIHAR	4/2016	3/2021 (-) [12/2024]	744.04 (1,215.54) [1,215.54]	950.34 (471.50) [45]	0/0
463	ARARIA-SUPAUL (NL) - [N22000177],ECR,BIHAR	4/2008	/ (-) [12/2025]	1,605.17 (1,605.17) [1,605.17]	834.76 (0.00) [-]	0/0
464	HAJIPUR-SAGAULI VIA VAISHALI (NL), ECR - [220100303],ECR,BIHAR	4/2003	/ (-) [12/2024]	528.65 (2,066.78) [2,066.78]	1,822.92 (1,538.13) [-]	0/0
465	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC - [N22000181],ECR,BIHAR	4/2009	3/2020 (-) [3/2025]	548.00 (548.00) [783.83]	543.54 (235.83) [60]	0/0

466	KIUL - GAYA DOUBLING PROJECT - [N22000349], ECR, BIHAR	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	1,346.62 (0.00) [0]	0/1
467	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476], ECR, BIHAR	4/1991	/ (-) [3/2024]	329.39 (1,483.14) [1,510.00]	2,102.69 (1,180.61) [-]	0/0
468	SAMASTIPUR-DARBANGHA - [N22000329], ECR, BIHAR	5/2015	/ (-) [12/2024]	380.00 (519.33) [519.33]	399.56 (139.33) [-]	0/0
469	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419], ECR, UTTAR PRADESH	8/2015	3/2019 (-) [3/2023]	528.57 (-) [528.57]	616.92 (0.00) [0]	0/0
470	RAMNA - SINGRAULI DOUBLING - [N22000417], ECR, UTTAR PRADESH	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	2,445.51 (0.00) [48]	0/0
471	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA- FORBESGANJ (GC) - [N22000180], ECR, BIHAR	4/2004	/ (-) [3/2024]	372.14 (1,470.50) [1,700.00]	2,044.95 (1,327.86) [-]	0/0
472	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350], ECR, BIHAR	12/2015	3/2020 (-) [12/2023]	1,491.47 (-) [1,491.47]	1,160.75 (0.00) [45]	1/1
473	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473], ECR, BIHAR	4/2016	3/2021 (-) [3/2024]	731.64 (1,185.73) [1,185.73]	965.84 (454.09) [36]	0/0
474	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328], ECR, ODISHA	4/2005	6/2021 (-) [3/2025]	810.78 (-) [1,928.07]	980.13 (1,117.29) [45]	0/0
475	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379], ECR, ODISHA	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	967.78 (0.00) [48]	0/0
476	SAMBALPUR-TALCHER DOUBLING - [N22000315], ECR, ODISHA	3/2011	2/2019 (2/2023) [2/2023]	1,111.99 (1,539.28) [1,539.28]	1,152.38 (427.29) [0]	0/0
477	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284], ECR, ODISHA	4/1994	3/2009 (-) [12/2026]	2,923.13 (3,791.66) [3,791.66]	2,904.31 (868.53) [213]	0/0
478	JAGDALPUR-KORAPUT DOUBLING - [N22000376], ECR, ODISHA	4/2015	3/2022 (-) [3/2024]	1,547.38 (-) [1,547.38]	790.93 (0.00) [24]	0/0
479	KOTTAVALSA - KORAPUT DOUBLING - [N22000377], ECR, ANDHRA PRADESH	4/2015	3/2022 (-) [9/2022]	2,499.71 (-) [2,499.71]	907.91 (0.00) [0]	0/0
480	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381], ECR, ODISHA	4/2015	12/2018 (-) [2/2025]	1,172.92 (-) [1,172.92]	1,052.09 (0.00) [74]	0/0
481	BHADRAK - NERGUNDI 3RD LINE - [N22000316], ECR, ODISHA	3/2013	10/2020 (-) [3/2024]	843.04 (1,284.39) [843.04]	723.04 (0.00) [41]	0/0
482	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380], ECR, ODISHA	4/2015	11/2018 (-) [3/2025]	701.61 (-) [810.02]	179.43 (108.41) [76]	0/0
483	KIRANDUL - JAGDALPUR DOUBLING - [N22000318], ECR, CHHATTISGARH	12/2012	3/2020 (-) [3/2024]	1,160.00 (-) [1,440.00]	1,058.66 (280.00) [48]	1/1
484	PIRPAINTI-JASIDIH - [N22000219], ER, MULTI STATE	4/2013	3/2022 (-)	915.98 (-)	980.46 (1,221.83)	0/0

			[3/2025]	[2,137.81]	[36]	
485	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI- SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229],ER,MULTI STATE	4/2010	3/2017 (-) [12/2022]	365.17 (-) [335.50]	794.67 (-29.67) [0]	0/0
486	MONIGRAM- NIMTITA - [N22000301],ER,MULTI STATE	4/2012	/ (-) [11/2023]	250.93 (-) [310.70]	753.91 (59.77) [-]	0/0
487	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272],ER, WEST BENGAL	4/2000	3/2019 (12/2009) [3/2024]	1,188.91 (-) [1,619.48]	1,141.34 (430.57) [60]	0/0
488	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489],IRCON,CHHATTISGARH	4/2013	9/2018 (-) [12/2023]	3,055.00 (-) [3,438.39]	2,976.72 (383.39) [63]	0/1
489	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418],IRCON,ODISHA	4/2016	3/2020 (-) [12/2025]	5,200.00 (-) [5,200.00]	0.00 (0.00) [69]	0/0
490	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108],KOMRCL, WEST BENGAL	4/2010	3/2016 (-) [3/2016]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]	0/0
491	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028],MRTP,TAMIL NADU	4/2006	6/2013 (-) [12/2023]	495.74 (-) [734.01]	576.39 (238.27) [126]	3/4
492	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135],MRTP, WEST BENGAL	3/2013	3/2016 (12/2023) [12/2023]	4,874.58 (8,574.98) [10,442.41]	8,008.94 (5,567.83) [93]	0/0
493	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092],MRTP,MAHARASHTRA	4/2008	3/2014 (-) [3/2014]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]	0/0
494	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158],NCR,MULTI STATE	4/2010	/ (5/2025) [12/2027]	2,030.50 (-) [746.83]	22.07 (-1,283.67) [-]	0/0
495	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148],NCR,MULTI STATE	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	1,024.32 (932.64) [33]	1/5
496	JHANSI BINA DOUBLING - [N22000496],NCR,UTTAR PRADESH	9/2016	3/2021 (-) [12/2023]	2,001.00 (2,001.00) [2,001.00]	1,118.80 (0.00) [33]	2/6
497	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495],NCR,UTTAR PRADESH	3/2018	3/2023 (-) [3/2026]	4,329.53 (-) [4,329.53]	60.37 (0.00) [36]	0/0
498	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206],NFR,MULTI STATE	4/2010	3/2020 (-) [12/2024]	242.22 (-) [632.63]	172.50 (390.41) [57]	0/0
499	AGARTALA-AKHAURA NL - [N22000195],NFR,TRIPURA	4/2012	3/2020 (6/2022) [9/2022]	569.63 (-) [708.73]	380.92 (139.10) [0]	2/3
500	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207],NFR,MULTI STATE	4/2010	/ (-) [3/2023]	241.52 (-) [401.65]	343.30 (160.13) [0]	0/0
501	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL	4/2006	3/2015 (-)	2,326.52 (-)	2,556.74 (4,336.48)	0/0

	PROJECT (NEFR) - [N22000124],NFR,NAGALAND		[3/2026]	[6,663.00]	[132]	
502	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086],NFR,ASSAM	9/2006	3/2019 (-) [0/0]	385.20 (-) [1,304.62]	1,104.78 (919.42) [0]	0/0
503	BHAIRABI SAIRONG, NL, NEFR - [N22000100],NFR,MIZORAM	4/2008	3/2014 (-) [2/2024]	2,393.47 (5,021.45) [9,362.06]	6,591.01 (6,968.59) [119]	0/0
504	BONGAIGAON-GOALPARA- GUWAHATI (176 KM) - [N22000388],NFR,ASSAM	4/2015	3/2022 (-) [3/2026]	2,232.32 (-) [4,059.65]	2,898.81 (1,827.33) [48]	0/0
505	SEVOK RANGPO, NEFR - [N22000102],NFR,SIKKIM	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [7,876.92]	3,290.96 (6,537.44) [96]	0/0
506	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087],NFR,BIHAR	9/2006	3/2019 (-) [3/2024]	532.87 (2,132.03) [2,650.00]	1,761.52 (2,117.13) [60]	0/0
507	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205],NFR,MEGHALAYA	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [8,324.28]	269.80 (7,417.82) [0]	0/0
508	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288],NFR,MANIPUR	4/2003	3/2011 (3/2025) [3/2025]	4,454.17 (12,264.15) [14,322.79]	13,763.33 (9,868.62) [168]	0/0
509	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING - [N22000183],NFR,MULTI STATE	4/2013	3/2019 (-) [1/2024]	1,798.00 (-) [2,647.51]	1,999.72 (849.51) [58]	0/0
510	MURKONGSELEK-PASIGHAT NL - [N22000208],NFR,MULTI STATE	4/2011	3/2020 (-) [10/2024]	414.84 (-) [1,187.49]	349.63 (772.65) [55]	0/0
511	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459],NER,UTTAR PRADESH	4/2017	4/2017 (-) [12/2024]	150.00 (-) [341.66]	1.20 (191.66) [92]	0/0
512	CHHAPRA-BALLIA UP - [N22000134],NER,MULTI STATE	3/2013	1/2019 (-) [2/2024]	295.00 (-) [830.00]	853.32 (535.00) [61]	0/0
513	SHAHGANJ-BHATNI-PHEPHNA- INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470],NER,UTTAR PRADESH	4/2016	12/2019 (-) [3/2024]	1,177.96 (-) [1,500.95]	1,119.47 (322.99) [51]	0/0
514	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347],NER,UTTAR PRADESH	3/2015	3/2022 (-) [10/2023]	1,295.42 (-) [2,560.00]	2,121.53 (1,264.58) [19]	0/0
515	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468],NER,UTTAR PRADESH	4/2016	/ (-) [5/2025]	602.50 (-) [800.00]	426.10 (197.50) [-]	0/0
516	DAUSA-GANGAPUR CITY(NL),NWR - [220100184],NWR,RAJASTHAN	2/1997	2/2019 (-) [9/2023]	410.08 (-) [970.00]	935.00 (559.92) [55]	0/0
517	PHULERA - DIGANA DOUBLING - [N22000326],NWR,MULTI STATE	5/2015	3/2020 (-) [2/2024]	600.00 (-) [701.81]	585.21 (101.81) [47]	0/0
518	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281],NR,DELHI	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	133.78 (123.32) [-]	0/0
519	ROHTAK-MEHAM HANSI - [N22000272],NR,HARYANA	4/2012	12/2011 (-) [12/2011]	287.00 (-) [893.45]	686.20 (606.45) [0]	0/0
520	CHANDIGARH-BADDI - [N22000467],NR,MULTI STATE	4/2007	3/2023 (6/2025) [6/2025]	328.14 (1,540.14) [1,540.14]	482.67 (1,212.00) [27]	0/0

521	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274],NR,MULTI STATE	4/2007	/ (-) [9/2023]	336.91 (-) [791.39]	572.99 (454.48) [-]	0/0
522	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133],NR,JAMMU AND KASHMIR	3/1995	11/2002 (12/2023) [1/2024]	2,500.00 (37,012.26) [37,012.26]	36,017.83 (34,512.26) [254]	0/0
523	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502],NR,PUNJAB	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]	0/0
524	NANGALDAM-TALWARA(NL),NR - [220100188],NR,MULTI STATE	3/1981	7/2012 (-) [11/2024]	450.00 (-) [2,017.96]	845.23 (1,567.96) [148]	0/0
525	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463],NHSRCL,MULTI STATE	12/2015	12/2023 (-) [8/2027]	1,08,000.00 (-) [1,08,000.00]	46,912.58 (0.00) [44]	1/2
526	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405],RVNL,UTTAR PRADESH	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,587.43 (0.00) [21]	0/0
527	BANASPANI- JAKHPURA - DOUBLING - [N22000412],RVNL,ODISHA	3/2009	3/2019 (10/2023) [5/2023]	942.95 (-) [1,552.26]	1,772.12 (609.31) [0]	0/0
528	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451],RVNL,TAMIL NADU	2/2015	3/2020 (-) [8/2023]	760.00 (-) [1,536.00]	1,846.81 (776.00) [41]	0/0
529	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501],RVNL,UTTAR PRADESH	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	4,306.50 (0.00) [0]	0/0
530	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449],RVNL,TAMIL NADU	2/2015	3/2022 (-) [10/2023]	1,700.00 (-) [1,305.00]	1,556.55 (-395.00) [19]	0/0
531	VARANASI-MODHOSINGH- ALLAHABAD DOUBLING - [N22000401],RVNL,UTTAR PRADESH	4/2015	3/2022 (-) [12/2023]	943.60 (-) [1,500.00]	1,251.40 (556.40) [21]	0/0
532	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404],RVNL,UTTAR PRADESH	4/2011	3/2019 (-) [3/2024]	927.01 (-) [1,457.79]	1,491.77 (530.78) [60]	0/0
533	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409],RVNL,ODISHA	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	3,674.36 (992.05) [24]	0/0
534	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406],RVNL,UTTARAKHAND	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [24,659.00]	14,020.06 (8,443.00) [3]	0/0
535	HOSPET-HUBLI-LONDA- VASCODAGAMA DL - [N22000297],RVNL,KARNATAKA	4/2010	3/2023 (-) [3/2024]	2,127.00 (-) [3,300.00]	3,204.74 (1,173.00) [12]	0/1
536	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213],RVNL,TELANGANA	4/2012	3/2016 (9/2023) [6/2023]	632.68 (-) [950.00]	973.99 (317.32) [0]	0/0
537	BHANUPALI-BILASPUR BERI NL - [N22000273],RVNL,HIMACHAL PRADESH	4/2008	12/2026 (-) [3/2025]	2,966.99 (-) [6,753.42]	3,955.01 (3,786.43) [-21]	0/0
538	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110],RVNL,WEST BENGAL	4/2010	3/2016 (-) [3/2026]	3,951.98 (-) [8,964.35]	5,943.37 (5,012.37) [120]	0/0
539	NEW WORK FOR CONSTRUCTION	4/2010	3/2014	2,298.42	355.80	0/0

	OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109],RVNL, WEST BENGAL		(-) [12/2025]	(-) [2,733.86]	(435.44) [141]	
540	VIJAYAWADA-GUDUR - [N22000369],RVNL,ANDHRA PRADESH	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	5,013.33 (302.42) [0]	0/0
541	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111],RVNL, WEST BENGAL	4/2010	3/2016 (-) [7/2025]	2,913.51 (-) [4,834.54]	3,020.54 (1,921.03) [112]	0/0
542	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327],RVNL,ODISHA	4/2000	3/2009 (3/2009) [7/2023]	133.41 (207.00) [433.00]	518.32 (299.59) [172]	1/1
543	MUNEERABAD- MAHABOBNAGAR(NL),SCR - [220100205],SCR,MULTI STATE	4/1997	3/2000 (-) [3/2000]	1,723.00 (1.00) [3,381.68]	2,532.11 (1,658.68) [0]	0/0
544	KAZIPET-BALHRSHA - [N22000367],SCR,MULTI STATE	4/2015	3/2021 (-) [1/2025]	2,063.03 (2,909.00) [2,909.00]	2,355.36 (845.97) [46]	0/0
545	GUNTUR-GUNTAKAL - [N22000368],SCR,ANDHRA PRADESH	4/2016	3/2022 (-) [12/2025]	3,631.00 (-) [3,887.48]	2,728.66 (256.48) [45]	0/0
546	MANMAD-PARBHANI-NANDED- SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432],SCR,TELANGANA	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [242.28]	54.15 (122.55) [0]	0/0
547	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032],SCR,TELANGANA	4/2006	3/2010 (-) [3/2025]	1,160.48 (-) [3,014.00]	1,071.53 (1,853.52) [180]	1/1
548	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261],SCR,MULTI STATE	4/2012	3/2023 (-) [3/2025]	1,856.95 (-) [1,952.68]	1,533.64 (95.73) [24]	0/0
549	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265],SCR,ANDHRA PRADESH	12/2001	3/2009 (-) [3/2027]	1,045.20 (-) [2,500.98]	1,129.92 (1,455.78) [216]	0/0
550	NADIKUDE-SRI KALAHASTI - [N22000286],SCR,ANDHRA PRADESH	4/2011	3/2021 (-) [3/2021]	2,288.70 (-) [3,122.35]	1,267.65 (833.65) [0]	0/1
551	BHADRACHALAM-KOVVUR - [N22000264],SCR,MULTI STATE	4/2012	/ (-) [0/0]	923.23 (-) [923.23]	2.46 (0.00) [0]	1/1
552	ANUPPUR-KATNI - [N22000485],SECR,MADHYA PRADESH	4/2015	12/2021 (12/2023) [12/2024]	1,370.00 (-) [1,680.00]	1,171.79 (310.00) [36]	0/0
553	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480],SECR,MAHARASHTRA	6/2018	12/2021 (-) [12/2025]	229.00 (-) [1,096.00]	230.25 (867.00) [48]	0/1
554	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420],SECR,MAHARASHTRA	9/2016	3/2023 (12/2023) [12/2024]	1,908.51 (2,753.05) [3,544.25]	2,238.21 (1,635.74) [21]	0/1
555	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484],SECR,CHHATTISGARH	4/2015	3/2021 (12/2023) [10/2024]	1,973.00 (2,135.34) [2,135.34]	1,488.70 (162.34) [43]	0/1
556	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506],SER,MULTI STATE	3/2019	5/2023 (-) [2/2025]	1,866.31 (-) [1,866.31]	1,148.32 (0.00) [21]	0/0
557	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509],SER,JHARKHAND	4/2018	12/2021 (-) [8/2023]	390.39 (-) [513.92]	429.26 (123.53) [20]	0/0

558	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510],SER, WEST BENGAL	4/2018	6/2022 (-) [2/2024]	338.00 (-) [393.83]	67.88 (55.83) [20]	0/0
559	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508],SER,JHARKHAND	4/2018	6/2022 (-) [3/2024]	428.65 (-) [472.50]	254.61 (43.85) [21]	0/0
560	BONDAMUNDA RANCHI DOUBLING - [N22000396],SER,JHARKHAND	3/2016	3/2021 (-) [3/2024]	1,724.20 (3,029.04) [3,029.04]	1,693.74 (1,304.84) [36]	0/0
561	MARIKUPPAM - KUPPAM - [N22000308],SWR,KARNATAKA	4/2012	3/2016 (-) [5/2025]	279.54 (-) [279.54]	38.69 (0.00) [110]	0/0
562	HOTGI-KUDGI-GADAG - [N22000333],SWR,MULTI STATE	3/2015	3/2019 (-) [12/2024]	1,614.59 (-) [1,960.00]	1,887.40 (345.41) [69]	0/0
563	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486],SWR,KARNATAKA	3/1996	3/2017 (-) [3/2026]	644.78 (889.00) [826.18]	500.25 (181.40) [108]	0/0
564	HUBLI-ANKOLA(NL),SWR - [220100193],SWR,KARNATAKA	4/1997	/ (-) [3/2030]	2,315.00 (-) [5,174.30]	159.49 (2,859.30) [-]	0/0
565	BAGALKOT-KUDACHI NL - [N22000258],SWR,KARNATAKA	4/2010	3/2016 (-) [3/2026]	986.30 (1,378.00) [1,649.31]	363.80 (663.01) [120]	1/1
566	GADAG-WADI NL - [N22000299],SWR,KARNATAKA	4/2013	12/2018 (-) [3/2026]	2,841.84 (-) [2,841.84]	722.55 (0.00) [87]	0/0
567	RAYADURGA-TUMKUR NL - [N22000279],SWR,MULTI STATE	4/2007	/ (-) [12/2025]	2,062.30 (2,404.03) [2,404.03]	1,161.58 (341.73) [-]	2/2
568	SHIMOGA-HARIHAR NL - [N22000278],SWR,KARNATAKA	4/2011	3/2016 (-) [12/2028]	832.47 (-) [832.47]	0.94 (0.00) [153]	0/0
569	TUMKUR-CHITRADURGA- DAVENGERE NL - [N22000256],SWR,KARNATAKA	4/2011	/ (-) [12/2026]	1,801.01 (-) [1,801.01]	126.80 (0.00) [-]	0/0
570	TIDIVANAM-NAGARI (NL) - [N22000085],SR,TAMIL NADU	9/2006	/ (12/2025) [12/2025]	582.83 (-) [3,620.28]	758.81 (3,037.45) [-]	0/0
571	MAYLADUTHURAI-THIRUVARUR- KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079],SR,TAMIL NADU	9/2007	2/2019 (-) [3/2025]	724.69 (-) [3,118.34]	1,877.71 (2,393.65) [73]	0/0
572	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215],SR,MULTI STATE	4/2011	3/2019 (12/2027) [12/2027]	120.70 (-) [2,053.39]	328.43 (1,932.69) [105]	0/0
573	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400],SR,KERALA	2/2015	/ (-) [3/2025]	1,000.00 (-) [1,339.00]	0.93 (339.00) [-]	0/0
574	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399],SR,KERALA	2/2015	/ (-) [3/2025]	1,431.90 (-) [1,431.90]	2,095.35 (0.00) [-]	0/0
575	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232],WCR,MULTI STATE	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,427.33 (8,000.84) [202]	1/9
576	KATNI-BINA 3RD LINE (263 KM) - [N22000415],WCR,MADHYA PRADESH	6/2016	3/2022 (-) [6/2024]	2,478.23 (2,938.00) [2,938.00]	1,279.35 (459.77) [27]	8/17
577	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-)	1,763.93 (2,445.30)	2,020.86 (681.37)	1/1

	- [N22000351],WCR,MADHYA PRADESH		[10/2024]	[2,445.30]	[55]	
578	KATNI GRADE SEPARATOR/BYE PASS - [N22000416],WCR,MADHYA PRADESH	8/2016	3/2022 (-) [9/2024]	582.13 (-) [1,247.64]	990.59 (665.51) [30]	1/1
579	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314],WCR,MADHYA PRADESH	4/2001	3/2021 (12/2025) [12/2025]	424.60 (2,909.99) [3,032.46]	2,080.00 (2,607.86) [57]	6/15
580	CHOTTAUDEPUR-DHAR(NL) - [N22000138],WR,MULTI STATE	4/2007	3/2022 (12/2026) [12/2026]	1,347.26 (1,793.63) [1,793.63]	1,222.16 (446.37) [57]	0/0
581	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436],WR,GUJARAT	3/2012	/ (-) [3/2024]	248.26 (-) [528.49]	116.25 (280.23) [-]	0/0
582	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142],WR,GUJARAT	4/2011	/ (-) [10/2025]	844.10 (844.10) [844.10]	457.93 (0.00) [-]	0/0
583	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120],WR,MADHYA PRADESH	4/2008	3/2022 (3/2026) [3/2026]	3,503.69 (5,677.80) [6,021.00]	2,919.74 (2,517.31) [48]	0/0
584	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503],WR,MADHYA PRADESH	4/2017	3/2022 (3/2026) [3/2026]	495.18 (495.18) [495.18]	0.83 (0.00) [48]	0/0
585	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435],WR,MAHARASHTRA	3/2012	/ (-) [3/2024]	217.38 (-) [393.62]	142.48 (176.24) [-]	0/0
586	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505],WR,GUJARAT	4/2018	3/2024 (12/2024) [12/2024]	537.31 (537.31) [537.31]	191.29 (0.00) [9]	0/0
587	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434],WR,MAHARASHTRA	3/2010	/ (-) [3/2024]	265.88 (-) [311.36]	0.00 (45.48) [-]	0/0
588	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123],WR,GUJARAT	4/2008	3/2012 (-) [3/2024]	318.24 (321.03) [1,095.12]	201.24 (776.88) [144]	0/0
589	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139],WR,MULTI STATE	4/2007	3/2022 (3/2026) [12/2025]	1,640.04 (1,873.10) [1,873.10]	1,136.95 (233.06) [45]	0/0
590	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504],WR,GUJARAT	4/2017	3/2020 (12/2024) [12/2024]	692.25 (692.26) [692.26]	116.70 (0.01) [57]	0/0
591	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493],WR,MADHYA PRADESH	4/2016	6/2020 (-) [10/2023]	700.00 (603.69) [603.69]	639.96 (-96.31) [40]	0/0
	RENEWABLE ENERGY					
592	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118],CPWD R ENERGY,DELHI	10/2017	11/2019 (4/2022) [4/2022]	271.90 (366.12) [366.12]	329.49 (94.22) [0]	0/0
	ROAD TRANSPORT AND HIGHWAYS					
593	4-LANING OF KASHIPUR-SITARGANJ SECTION - [N24000465],MEGA,UTTARAKHAND	11/2012	8/2016 (-) [8/2016]	605.84 (-) [605.84]	0.00 (0.00) [0]	0/0
594	MUL TO CHANDRAPUR - [N24001117],MoRTH,MAHARASHTRA	12/2016	7/2019 (-)	162.34 (-)	107.56 (0.00)	2/4

			[1/2023]	[162.34]	[0]	
595	SATARA MURVAD PILLOV PANDHARPUR - [N24001095],MoRTH,MAHARASHTRA	1/2017	/ (-) [6/2024]	388.44 (-) [388.44]	240.05 (0.00) [-]	0/0
596	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	486.70 (-) [486.70]	415.54 (0.00) [0]	0/0
597	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N - [N24001466],MoRTH,NAGALAND	3/2021	7/2024 (7/2024) [7/2024]	297.24 (-) [297.24]	44.41 (0.00) [0]	0/0
598	DIGRAS DARWAH KARANJA - [N24001013],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [12/2023]	391.06 (391.00) [391.06]	263.11 (0.00) [54]	0/0
599	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969],MoRTH,ANDHRA PRADESH	1/2017	9/2017 (5/2023) [5/2023]	263.45 (263.45) [263.45]	168.59 (0.00) [0]	1/4
600	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT - [N24001423],MoRTH,UTTAR PRADESH	4/2021	9/2023 (-) [12/2024]	309.48 (-) [309.48]	63.83 (0.00) [15]	0/0
601	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014- 15-775) - [N24001166],MoRTH,KARNATAKA	3/2015	1/2016 (7/2023) [7/2023]	159.12 (-) [159.12]	128.18 (0.00) [90]	0/0
602	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218],MoRTH,CHHATTISGARH	11/2015	6/2017 (-) [12/2023]	335.32 (-) [335.32]	321.06 (0.00) [78]	0/0
603	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374],MoRTH,ARUNACHAL PRADESH	6/2020	3/2027 (-) [3/2027]	437.60 (-) [437.60]	210.88 (0.00) [0]	0/0
604	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 - [N24000422],MoRTH,ANDHRA PRADESH	3/2015	9/2015 (8/2017) [5/2018]	309.01 (-) [309.01]	309.01 (0.00) [0]	0/0
605	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990],MoRTH,TELANGANA	2/2018	11/2019 (3/2022) [2/2023]	294.13 (-) [294.13]	193.20 (0.00) [0]	0/0
606	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157],MoRTH,KARNATAKA	8/2016	2/2017 (7/2023) [12/2023]	175.50 (-) [241.60]	178.73 (66.10) [82]	0/0
607	KARAD PATAN CHIPLUN GUHAGAR - [N24001057],MoRTH,MAHARASHTRA	2/2017	6/2019 (-)	407.19 (407.00)	323.02 (0.00)	2/4

			[6/2023]	[407.19]	[0]	
608	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874], MoRTH, WEST BENGAL	3/2016	11/2018 (12/2023) [12/2023]	271.17 (291.20) [291.20]	151.50 (20.03) [61]	0/0
609	SHEGAON TO DEORI PHATA - [N24001010], MoRTH, MAHARASHTRA	2/2017	5/2019 (-) [1/2023]	373.10 (373.00) [373.10]	320.45 (0.00) [0]	2/4
610	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887], MoRTH, WEST BENGAL	6/2016	9/2021 (2/2024) [2/2024]	236.78 (263.26) [263.26]	163.40 (26.48) [29]	0/0
611	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886], MoRTH, MADHYA PRADESH	1/2017	3/2017 (12/2021) [8/2023]	205.05 (-) [205.05]	140.29 (0.00) [77]	0/0
612	MANSAR TO SALAIKHURD - [N24001035], MoRTH, MAHARASHTRA	1/2018	12/2019 (-) [1/2023]	418.36 (-) [418.36]	263.13 (0.00) [0]	2/4
613	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914], MoRTH, ODISHA	12/2016	8/2018 (10/2023) [10/2023]	223.50 (-) [223.50]	139.44 (0.00) [62]	0/0
614	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP - [N24001462], MoRTH, UTTAR PRADESH	4/2020	7/2024 (-) [2/2024]	211.09 (-) [211.09]	31.61 (0.00) [-5]	0/0
615	SHAHPUR PATGAON SECTION I - [N24001027], MoRTH, MAHARASHTRA	1/2018	12/2019 (-) [3/2023]	150.79 (-) [150.79]	81.14 (0.00) [0]	2/4
616	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777], MoRTH, UTTARAKHAND	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	196.03 (0.00) [0]	0/0
617	SHIRUR TO KHARDA - [N24001123], MoRTH, MAHARASHTRA	2/2017	6/2019 (-) [3/2024]	381.77 (-) [381.77]	199.48 (0.00) [57]	2/4
618	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 - [N24001464], MoRTH, UTTAR PRADESH	3/2021	8/2023 (-) [11/2023]	264.86 (-) [264.86]	52.66 (0.00) [3]	0/0
619	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210], MoRTH, UTTAR PRADESH	3/2018	6/2021 (-) [9/2023]	306.59 (-) [306.59]	251.95 (0.00) [27]	0/0
620	INDAPUR TO VADPALE - [N24001114], MoRTH, MAHARASHTRA	1/2017	12/2019 (-) [6/2023]	1,202.52 (1,203.00) [1,202.52]	1,450.82 (0.00) [0]	2/4
621	LATUR TO PANGAON - [N24001066], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [8/2023]	336.47 (336.00) [336.47]	203.39 (0.00) [44]	2/4
622	REHABILITATION AND	11/2016	5/2017	290.15	204.32	3/4

	UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931],MoRTH,ANDHRA PRADESH		(11/2022) [11/2022]	(-) [236.16]	(-53.99) [0]	
623	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F - [N24001457],MoRTH,UTTAR PRADESH	4/2020	7/2024 (-) [7/2024]	172.50 (-) [172.50]	46.73 (0.00) [0]	0/0
624	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998],MoRTH,TELANGANA	1/2019	/ (1/2023) [6/2023]	193.19 (249.72) [249.72]	219.90 (56.53) [0]	0/0
625	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [12/2023]	406.51 (-) [406.51]	340.26 (0.00) [54]	0/0
626	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO - [N24001467],MoRTH,NAGALAND	3/2021	2/2024 (2/2024) [2/2024]	226.44 (-) [226.44]	50.91 (0.00) [0]	0/0
627	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	543.05 (-) [543.05]	414.11 (0.00) [0]	0/0
628	CHIMUR TO WARORA - [N24001105],MoRTH,MAHARASHTRA	11/2016	3/2019 (-) [2/2023]	467.70 (-) [467.70]	323.36 (0.00) [0]	2/4
629	JAHIRABAD TO LATUR - [N24001040],MoRTH,MAHARASHTRA	1/2017	11/2019 (-) [2/2023]	461.96 (-) [461.96]	329.59 (0.00) [0]	3/4
630	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963],MoRTH,ANDHRA PRADESH	1/2018	8/2018 (12/2021) [12/2021]	418.03 (386.99) [386.99]	365.73 (-31.04) [0]	4/4
631	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	394.27 (-) [394.27]	412.07 (0.00) [0]	0/0
632	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 - [N24001850],MoRTH,WEST BENGAL	3/2022	9/2025 (9/2025) [9/2025]	995.04 (995.04) [995.04]	18.84 (0.00) [0]	0/0
633	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584],MoRTH,MAHARASHTRA	3/2016	/ (-) [2/2023]	1,142.62 (1,907.03) [1,142.62]	1,056.08 (0.00) [0]	0/0
634	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 -	1/2016	5/2016 (10/2022) [10/2022]	386.09 (288.76) [288.76]	258.28 (-97.33) [0]	3/4

	[N24000965],MoRTH,ANDHRA PRADESH					
635	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388],MoRTH,KARNATAKA	3/2019	12/2019 (11/2024) [11/2024]	423.15 (-) [423.15]	308.74 (0.00) [59]	0/0
636	KHAMGAON TO DEULGAON SAKARSHA - [N24001074],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [1/2023]	249.29 (-) [249.29]	146.41 (0.00) [0]	0/0
637	PANCHARAL TO MANDANGHAR - [N24001107],MoRTH,MAHARASHTRA	7/2018	5/2020 (-) [12/2023]	381.08 (302.00) [381.08]	45.66 (0.00) [43]	2/4
638	REPANPALLI TO SIRONCHA - [N24001468],MoRTH,MAHARASHTRA	3/2022	6/2022 (-) [6/2024]	282.07 (-) [282.07]	34.65 (0.00) [24]	0/0
639	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422],MoRTH,HIMACHAL PRADESH	2/2021	9/2021 (-) [9/2021]	345.89 (-) [345.89]	193.34 (0.00) [0]	0/0
640	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216],MoRTH,JHARKHAND	12/2016	9/2021 (-) [3/2023]	196.00 (-) [196.00]	150.41 (0.00) [0]	3/4
641	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928],MoRTH,ANDHRA PRADESH	10/2015	12/2015 (12/2019) [1/2021]	333.21 (-) [353.43]	342.71 (20.22) [0]	3/3
642	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307],MoRTH,TRIPURA	1/2017	12/2022 (5/2023) [5/2023]	197.67 (236.18) [236.18]	211.12 (38.51) [0]	0/0
643	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228],MoRTH,CHHATTISGARH	11/2017	5/2019 (-) [8/2023]	188.80 (-) [188.80]	131.38 (0.00) [51]	0/0
644	MALEWADA TO CHIMUR - [N24001104],MoRTH,MAHARASHTRA	10/2016	6/2019 (-) [9/2023]	322.55 (-) [322.55]	242.09 (0.00) [51]	3/4
645	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883],MoRTH,WEST BENGAL	3/2018	10/2020 (3/2024) [3/2024]	254.30 (254.30) [254.30]	171.67 (0.00) [41]	0/0
646	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156],MoRTH,KARNATAKA	1/2017	9/2017 (5/2023) [5/2023]	166.67 (-) [264.34]	193.04 (97.67) [0]	0/0
647	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064],MoRTH,MAHARASHTRA	3/2018	2/2020 (-) [8/2023]	217.14 (217.00) [217.14]	157.89 (0.00) [42]	2/4
648	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS	10/2015	/	936.40 (-)	708.69 (0.00)	0/0

	RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444],MoRTH,GOA		[0/0]	[936.40]	[0]	
649	WAKAN PALI KHOPOLI - [N24001026],MoRTH,MAHARASHTRA	1/2017	5/2019 (-) [10/2023]	376.19 (-) [376.19]	113.66 (0.00) [53]	2/4
650	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO - [N24001469],MoRTH,UTTAR PRADESH	11/2021	5/2024 (-) [5/2024]	307.11 (-) [307.11]	21.55 (0.00) [0]	0/0
651	PARLI PIMPLA DAHIGUDA - [N24001138],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [8/2023]	205.72 (206.00) [205.72]	85.71 (0.00) [50]	2/4
652	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161],MoRTH,KARNATAKA	12/2017	1/2019 (4/2022) [4/2022]	297.30 (-) [318.28]	279.03 (20.98) [0]	0/0
653	SAKOLI TO BHANDARA - [N24001118],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [9/2023]	362.96 (-) [362.96]	273.57 (0.00) [51]	2/4
654	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415],MoRTH,MIZORAM	8/2010	10/2010 (6/2023) [6/2023]	195.04 (434.65) [377.99]	415.11 (182.95) [0]	0/0
655	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 - [N24001463],MoRTH,UTTAR PRADESH	4/2020	7/2024 (-) [7/2024]	294.84 (-) [294.84]	160.63 (0.00) [0]	0/0
656	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881],MoRTH,MADHYA PRADESH	11/2017	2/2018 (9/2021) [4/2023]	184.62 (-) [184.62]	145.45 (0.00) [0]	0/0
657	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870],MoRTH,MADHYA PRADESH	3/2018	3/2018 (10/2021) [4/2023]	162.56 (-) [162.56]	137.52 (0.00) [0]	0/0
658	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888],MoRTH,MADHYA PRADESH	3/2018	3/2018 (12/2023) [12/2023]	214.69 (-) [214.69]	101.84 (0.00) [69]	0/0
659	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885],MoRTH,WEST BENGAL	3/2016	9/2023 (3/2024) [6/2024]	160.27 (213.97) [213.97]	70.95 (53.70) [9]	0/0
660	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421],MoRTH,UTTAR PRADESH	7/2018	2/2024 (-) [9/2024]	1,948.25 (-) [1,948.25]	640.55 (0.00) [7]	0/0
661	MAHAD TO RAIGAD FORT - [N24001038],MoRTH,MAHARASHTRA	7/2018	5/2020 (-) [12/2023]	237.40 (-) [237.40]	73.12 (0.00) [43]	2/4
662	TALEGAON TO GONAPUR - [N24001096],MoRTH,MAHARASHTRA	1/2018	3/2019 (-) [2/2023]	264.41 (264.00) [264.41]	200.42 (0.00) [0]	0/0

663	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247],MoRTH,TELANGANA	10/2014	2/2017 (12/2022) [10/2023]	295.47 (-) [295.47]	221.36 (0.00) [80]	0/1
664	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933],MoRTH,ANDHRA PRADESH	2/2017	11/2017 (11/2022) [11/2022]	429.43 (-) [373.05]	376.80 (-56.38) [0]	3/4
665	KOLHA TO NASRATPUR - [N24001111],MoRTH,MAHARASHTRA	4/2016	4/2019 (-) [12/2023]	281.78 (282.00) [281.78]	77.83 (0.00) [56]	2/4
666	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988],MoRTH,TELANGANA	1/2018	12/2019 (11/2020) [11/2020]	230.03 (-) [230.03]	229.41 (0.00) [0]	0/0
667	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782],MoRTH,UTTARAKHAND	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]	0/0
668	BHANDARA TO GHOTITOK - [N24001018],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [1/2023]	392.83 (393.00) [392.83]	274.75 (0.00) [0]	0/0
669	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876],MoRTH,WEST BENGAL	1/2017	9/2019 (3/2023) [3/2023]	396.86 (-) [396.86]	325.22 (0.00) [0]	0/0
670	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894],MoRTH,MADHYA PRADESH	2/2018	3/2018 (11/2021) [5/2022]	279.44 (-) [279.44]	234.24 (0.00) [0]	0/0
671	PARTUR TO MAJALGAON - [N24001034],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [2/2023]	420.57 (-) [420.57]	270.28 (0.00) [0]	3/4
672	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W - [N24001424],MoRTH,UTTAR PRADESH	3/2021	9/2023 (-) [3/2024]	185.09 (-) [185.09]	92.62 (0.00) [6]	0/0
673	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932],MoRTH,ANDHRA PRADESH	1/2017	8/2017 (7/2022) [7/2022]	319.28 (-) [319.28]	245.47 (0.00) [0]	4/4
674	KARASWADA TO BAMBOLIM - [N24001005],MoRTH,GOA	3/2017	12/2019 (-) [1/2023]	852.67 (-) [852.67]	300.98 (0.00) [0]	2/4
675	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198],MoRTH,MADHYA PRADESH	1/2019	3/2021 (11/2022) [3/2023]	264.50 (-) [264.50]	215.21 (0.00) [0]	0/0
676	JALKOT TO TOGRI	7/2018	8/2020	299.92	188.96	2/4

	- [N24001071],MoRTH,MAHARASHTRA		(-) [12/2023]	(300.00) [299.92]	(0.00) [40]	
677	SARSAM TO KOTHARI - [N24001002],MoRTH,MAHARASHTRA	2/2016	7/2019 (-) [9/2022]	545.64 (-) [545.64]	232.64 (0.00) [0]	2/4
678	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [8/2023]	256.15 (-) [256.15]	126.62 (0.00) [44]	0/0
679	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282],MoRTH,ANDHRA PRADESH	1/2014	11/2014 (5/2024) [5/2024]	195.45 (385.97) [385.97]	187.74 (190.52) [114]	2/4
680	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) - [N24001479],MoRTH,UTTAR PRADESH	3/2021	5/2024 (-) [5/2024]	395.62 (-) [395.62]	62.63 (0.00) [0]	0/0
681	SILLOD TO FARDAPUR - [N24001125],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [10/2023]	337.46 (-) [337.46]	335.30 (0.00) [52]	2/4
682	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA- GOH) OF NH - [N24001000],MoRTH,BIHAR	3/2018	/ (3/2022) [3/2022]	153.24 (-) [153.24]	122.60 (0.00) [0]	0/0
683	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514],MoRTH,GOA	12/2015	/ (-) [1/2023]	773.98 (-) [773.98]	464.36 (0.00) [0]	0/0
684	WAKED TO TALEGAON - [N24001135],MoRTH,MAHARASHTRA	2/2016	2/2019 (-) [2/2023]	1,244.75 (1,245.00) [1,244.75]	1,025.72 (0.00) [0]	0/0
685	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909],MoRTH,PUNJAB	10/2017	10/2019 (-) [12/2023]	1,069.59 (-) [1,069.59]	739.08 (0.00) [50]	0/1
686	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258],MoRTH,GOA	3/2015	/ (-) [12/2022]	184.05 (-) [184.05]	136.74 (0.00) [0]	2/4
687	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR- ASIND SECTION (K - [N24001242],MoRTH,RAJASTHAN	8/2020	11/2022 (-) [9/2023]	196.23 (-) [196.00]	144.86 (-0.23) [10]	3/4
688	PIMPLA TO MANJARUMBHA - [N24001030],MoRTH,MAHARASHTRA	1/2017	8/2019 (-) [1/2023]	595.77 (-) [595.77]	357.73 (0.00) [0]	3/4
689	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197],MoRTH,GUJARAT	3/2018	6/2021 (7/2023) [7/2023]	351.00 (270.00) [270.00]	215.52 (-81.00) [25]	3/4
690	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820],MoRTH,ANDAMAN AND	11/2017	11/2019 (4/2023) [4/2023]	237.80 (-) [238.00]	109.61 (0.20) [0]	0/0

	NICOBAR ISLANDS					
691	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475],MoRTH,MADHYA PRADESH	11/2015	1/2020 (6/2021) [4/2023]	628.45 (-) [628.45]	480.18 (0.00) [0]	0/0
692	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773],MoRTH,UTTARAKHAND	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	141.39 (0.00) [0]	0/0
693	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907],MoRTH,PUNJAB	3/2018	8/2020 (-) [6/2023]	293.10 (341.84) [293.10]	302.40 (0.00) [0]	0/1
694	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776],MoRTH,UTTARAKHAND	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	151.70 (0.00) [0]	0/0
695	GADCHIROLI TO MUL - [N24001116],MoRTH,MAHARASHTRA	12/2016	6/2019 (-) [1/2023]	484.15 (-) [484.15]	456.25 (0.00) [0]	3/4
696	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF - [N24001587],MoRTH,UTTAR PRADESH	3/2020	9/2024 (-) [9/2024]	262.37 (-) [343.77]	72.28 (81.40) [0]	0/0
697	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383],MoRTH,HIMACHAL PRADESH	8/2020	4/2021 (-) [4/2021]	349.20 (-) [349.20]	316.84 (0.00) [0]	0/0
698	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236],MoRTH,TAMIL NADU	3/2019	11/2019 (-) [9/2023]	297.55 (320.00) [320.00]	296.73 (22.45) [46]	3/4
699	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 - [N24001455],MoRTH,TAMIL NADU	2/2022	8/2022 (-) [10/2024]	191.33 (-) [191.33]	28.48 (0.00) [26]	0/4
700	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	421.48 (-) [421.48]	349.87 (0.00) [0]	0/0
701	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779],MoRTH,UTTARAKHAND	2/2018	2/2020 (3/2023) [3/2023]	418.88 (-) [418.88]	264.67 (0.00) [0]	0/0
702	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982],MoRTH,TELANGANA	1/2017	5/2019 (8/2019) [8/2019]	244.54 (-) [244.54]	174.50 (0.00) [0]	0/0

703	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA - [N24001840],MoRTH,ASSAM	3/2022	4/2025 (-) [4/2025]	535.03 (-) [535.03]	0.00 (0.00) [0]	0/0
704	SARAD VANI PIMPALGAON - [N24001103],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [2/2023]	250.46 (-) [250.46]	198.32 (0.00) [0]	2/4
705	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219],MoRTH,CHHATTISGARH	1/2016	9/2016 (-) [12/2023]	476.20 (543.73) [543.73]	476.08 (67.53) [87]	0/0
706	VITA TO NAGAJ - [N24001050],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [12/2023]	304.58 (305.00) [304.58]	150.26 (0.00) [48]	2/4
707	WADI TO ASOLA - [N24001022],MoRTH,MAHARASHTRA	1/2017	9/2019 (-) [8/2023]	363.82 (364.00) [363.82]	154.65 (0.00) [47]	2/4
708	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958],MoRTH,RAJASTHAN	2/2018	12/2019 (-) [8/2021]	370.30 (-) [370.30]	336.24 (0.00) [0]	3/4
709	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056],MoRTH,MAHARASHTRA	2/2017	7/2019 (-) [2/2023]	422.02 (422.00) [422.02]	302.13 (0.00) [0]	0/0
710	MORSHI TO MAH/MP BORDER - [N24001016],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [2/2023]	471.61 (472.00) [471.61]	321.02 (0.00) [0]	0/0
711	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241],MoRTH,RAJASTHAN	3/2020	10/2022 (-) [12/2023]	255.23 (-) [255.23]	179.27 (0.00) [14]	3/4
712	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780],MoRTH,UTTARAKHAND	2/2018	/ (4/2023) [4/2023]	293.68 (-) [293.68]	201.20 (0.00) [0]	0/0
713	AKOT TO ANJANGAON - [N24001006],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [1/2023]	245.77 (246.00) [245.77]	221.84 (0.00) [0]	2/4
714	NAGAJ TO VAJJAPUR - [N24001023],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [1/2023]	376.72 (377.00) [376.72]	273.87 (0.00) [0]	2/4
715	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164],MoRTH,KARNATAKA	10/2016	3/2017 (7/2022) [7/2022]	396.96 (-) [396.96]	332.58 (0.00) [0]	0/0
716	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981],MoRTH,TELANGANA	10/2016	3/2019 (4/2023) [4/2023]	248.83 (-) [248.83]	164.28 (0.00) [0]	0/0
717	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSA GAR DAM SECT - [N24000245],MoRTH,TELANGANA	1/2014	3/2016 (9/2019) [9/2019]	270.00 (-) [270.00]	0.00 (0.00) [0]	1/4

718	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) - [N24001442],MoRTH,SIKKIM	10/2021	5/2024 (5/2024) [5/2024]	385.15 (-) [385.15]	81.83 (0.00) [0]	0/0
719	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513],MoRTH,MADHYA PRADESH	3/2015	8/2017 (12/2023) [12/2023]	511.83 (-) [511.83]	455.78 (0.00) [76]	0/0
720	BARASGAON TO RAHATEE - [N24001113],MoRTH,MAHARASHTRA	7/2016	9/2018 (-) [9/2023]	289.11 (290.00) [289.11]	232.56 (0.00) [60]	2/4
721	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173],MoRTH,KARNATAKA	2/2017	5/2019 (-) [11/2024]	157.32 (188.00) [187.61]	43.16 (30.29) [66]	0/0
722	KANTE TO WAKED - [N24001134],MoRTH,MAHARASHTRA	3/2016	11/2019 (-) [12/2023]	1,230.02 (1,230.00) [1,230.02]	791.80 (0.00) [49]	2/4
723	CONSTRUCTION OF RING ROAD FOR RAEARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331],MoRTH,UTTAR PRADESH	12/2019	4/2022 (-) [2/2024]	282.41 (-) [319.96]	248.23 (37.55) [22]	0/0
724	REHABILITATION AND UP- GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875],MoRTH,MADHYA PRADESH	2/2018	3/2018 (12/2022) [12/2023]	169.63 (-) [169.63]	103.61 (0.00) [69]	0/0
725	BALANCE WORK OF 2-LANING OF LONGDING– TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373],MoRTH,ARUNACHAL PRADESH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	334.89 (0.00) [0]	0/0
726	PATGAON KHOPOLI SECTION I - [N24001028],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [3/2023]	170.00 (-) [170.00]	125.80 (0.00) [0]	2/4
727	HIMAYATNAGAR TO PHULSAWANGI - [N24001081],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [9/2023]	294.87 (295.00) [294.87]	183.17 (0.00) [45]	2/4
728	REHABILITATION AND UPGRADATION OF LOSARI- MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967],MoRTH,ANDHRA PRADESH	3/2016	9/2016 (10/2022) [10/2022]	444.84 (459.37) [459.37]	419.80 (14.53) [0]	3/4
729	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375],MoRTH,ARUNACHAL PRADESH	6/2020	3/2027 (-) [3/2027]	496.47 (-) [496.47]	103.90 (0.00) [0]	0/0
730	BARELA-MANDLA SECTION OF NH- 12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378],MoRTH,MADHYA PRADESH	6/2015	/ (-) [3/2021]	390.51 (-) [390.51]	306.63 (0.00) [0]	0/0

731	JALGAON TO NANDURA - [N24001088],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [9/2023]	177.84 (177.00) [177.84]	110.20 (0.00) [45]	0/0
732	MANTHA TALUKAS BORDER TO PARTUR - [N24001033],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2023]	486.19 (-) [486.19]	315.19 (0.00) [0]	3/4
733	NASRATPUR TO BARASGAON - [N24001112],MoRTH,MAHARASHTRA	7/2016	9/2019 (-) [12/2023]	406.54 (407.00) [406.54]	274.30 (0.00) [51]	3/4
734	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940],MoRTH,ANDHRA PRADESH	3/2016	5/2016 (2/2023) [2/2023]	995.09 (995.00) [995.09]	643.54 (0.00) [0]	3/4
735	ARNI TO NAIGAINBANDI - [N24001093],MoRTH,MAHARASHTRA	12/2017	12/2019 (-) [2/2023]	309.94 (310.00) [309.94]	207.17 (0.00) [0]	0/0
736	AHMADPUR TO PIMPLA - [N24001029],MoRTH,MAHARASHTRA	1/2017	8/2019 (-) [3/2023]	422.38 (-) [422.38]	256.59 (0.00) [0]	3/4
737	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	450.65 (-) [450.65]	272.11 (0.00) [0]	0/0
738	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	560.39 (-) [560.39]	531.18 (0.00) [0]	0/0
739	KARWANDI TO RAJURI - [N24001058],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [11/2023]	276.95 (277.00) [276.95]	160.17 (0.00) [47]	2/4
740	ANJANGAON TO MAH/MP BORDER - [N24001007],MoRTH,MADHYA PRADESH	1/2017	6/2019 (-) [1/2023]	359.00 (359.00) [359.00]	326.56 (0.00) [0]	2/4
741	KOTHARI TO DHANORA - [N24001073],MoRTH,MAHARASHTRA	9/2018	8/2020 (-) [9/2023]	301.38 (301.00) [301.38]	240.32 (0.00) [37]	0/0
742	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370],MoRTH,KERALA	2/2017	9/2017 (1/2023) [6/2023]	380.76 (372.87) [372.87]	313.19 (-7.89) [0]	0/0
743	CONSTRUCTION OF 4 LANE ELEVATED VIADUCT AT KM. 7.500 MUNSHI PULIA OF NH-24A - [N24001460],MoRTH,UTTAR PRADESH	12/2021	9/2024 (-) [9/2024]	170.60 (-) [170.60]	40.08 (0.00) [0]	0/0
744	WIDENING OF PACHPADRA- BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE - [N24001528],MoRTH,RAJASTHAN	1/2022	12/2024 (-) [12/2024]	194.88 (-) [194.88]	13.40 (0.00) [0]	0/0
745	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU - [N24001829],MoRTH,TAMIL NADU	10/2022	11/2024 (-) [11/2024]	172.15 (-) [172.15]	0.00 (0.00) [0]	0/4

746	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]),MoRTH,PUNJAB	3/2018	11/2020 (-) [11/2023]	170.57 (192.48) [192.48]	94.84 (21.91) [36]	0/1
747	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172],MoRTH,KARNATAKA	1/2017	8/2017 (6/2022) [6/2022]	291.49 (-) [291.49]	238.77 (0.00) [0]	0/0
748	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980],MoRTH,TELANGANA	10/2016	2/2019 (6/2022) [6/2023]	298.32 (-) [298.32]	171.24 (0.00) [0]	0/0
749	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257],MoRTH,GOA	3/2015	/ (12/2021) [12/2022]	298.33 (354.43) [298.33]	399.84 (0.00) [0]	0/4
750	BHOKAR TO SARSAM - [N24001128],MoRTH,MAHARASHTRA	2/2017	7/2019 (-) [11/2020]	295.09 (-) [295.99]	186.27 (0.90) [0]	2/4
751	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201],MoRTH,BIHAR	2/2019	/ (9/2024) [0/0]	2,926.42 (-) [2,926.42]	787.79 (0.00) [0]	0/0
752	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159],MoRTH,KARNATAKA	1/2018	7/2018 (3/2022) [3/2022]	159.70 (-) [159.70]	155.15 (0.00) [0]	0/0
753	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369],MoRTH,KERALA	2/2017	8/2017 (3/2022) [8/2023]	294.28 (296.53) [296.53]	274.50 (2.25) [72]	0/0
754	NANDGAON TO MORSHI - [N24001014],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [3/2023]	385.87 (386.00) [385.87]	258.29 (0.00) [0]	0/0
755	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983],MoRTH,TELANGANA	1/2017	10/2019 (10/2019) [10/2019]	196.52 (-) [196.52]	123.68 (0.00) [0]	0/0
756	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. - [N24001227],MoRTH,CHHATTISGARH	3/2018	1/2019 (-) [12/2023]	349.03 (-) [349.03]	277.34 (0.00) [59]	0/0
757	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 - [N24001470],MoRTH,HIMACHAL PRADESH	8/2020	4/2025 (-) [4/2025]	314.32 (-) [314.32]	24.78 (0.00) [0]	0/0
758	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410],MoRTH,RAJASTHAN	8/2020	12/2022 (-) [9/2023]	216.72 (-) [216.72]	151.46 (0.00) [9]	3/4
759	RALEGAON TO RAMTIRTH	1/2017	7/2019	210.81	210.81	2/4

	- [N24001046],MoRTH,MAHARASHTRA		(-) [8/2023]	(-) [210.81]	(0.00) [49]	
760	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934],MoRTH,ANDHRA PRADESH	3/2018	8/2018 (5/2022) [5/2022]	228.32 (-) [202.83]	175.29 (-25.49) [0]	3/4
761	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [8/2022]	223.46 (-) [223.46]	123.46 (0.00) [0]	0/0
762	PARBHANI TO GANGKHED - [N24001065],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [8/2023]	238.19 (238.00) [238.19]	194.54 (0.00) [44]	2/4
763	DEORI TO AMGAON - [N24001032],MoRTH,MAHARASHTRA	1/2017	5/2019 (-) [2/2023]	409.62 (410.00) [409.62]	290.44 (0.00) [0]	2/4
764	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386],MoRTH,ANDHRA PRADESH	8/2020	3/2021 (3/2024) [3/2024]	222.61 (-) [222.61]	75.90 (0.00) [36]	2/4
765	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778],MoRTH,UTTARAKHAND	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	153.44 (0.00) [0]	0/0
766	CONSTRUCTION OF FOUR LANE PINJORE BYPASS FROM KM 0.00 TO 7.70 ON EPC MODE. - [N24001513],MoRTH,HARYANA	12/2016	12/2017 (-) [9/2023]	170.27 (-) [170.27]	98.77 (0.00) [69]	0/0
767	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [12/2023]	336.21 (336.00) [336.21]	236.11 (0.00) [48]	2/4
768	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDA-SAGWARA) SECTION OF NH-927A. PKG - - [N24001413],MoRTH,RAJASTHAN	2/2021	1/2024 (-) [1/2024]	240.99 (-) [240.99]	110.30 (0.00) [0]	0/0
769	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880],MoRTH,WEST BENGAL	2/2018	9/2020 (12/2023) [12/2023]	426.18 (426.18) [426.18]	339.05 (0.00) [39]	0/0
770	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301],MoRTH,ANDHRA PRADESH	3/2015	10/2015 (5/2021) [5/2021]	271.45 (-) [271.45]	240.72 (0.00) [0]	4/4
771	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158],MoRTH,KARNATAKA	3/2018	6/2019 (12/2023) [12/2023]	159.97 (-) [242.61]	135.31 (82.64) [54]	0/0
772	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994],MoRTH,TELANGANA	3/2018	7/2020 (6/2024) [6/2024]	626.76 (-) [626.76]	255.13 (0.00) [47]	0/0

773	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409],MoRTH,RAJASTHAN	7/2020	3/2024 (-) [7/2024]	319.09 (-) [319.09]	77.04 (0.00) [4]	1/4
774	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891],MoRTH,MADHYA PRADESH	3/2018	3/2018 (10/2021) [6/2023]	233.04 (-) [233.04]	187.88 (0.00) [0]	0/0
775	PUNE TO MALE VILLAGE - [N24001078],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [8/2023]	228.31 (-) [228.31]	100.97 (0.00) [44]	0/0
776	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194],MoRTH,ARUNACHAL PRADESH	9/2011	/ (12/2021) [5/2023]	1,979.00 (-) [2,036.90]	1,253.04 (57.90) [0]	0/0
777	MORSHI TO ACHALPUR - [N24001015],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [12/2023]	341.16 (341.00) [341.16]	247.86 (0.00) [54]	0/0
778	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH - [N24001448],MoRTH,MAHARASHTRA	11/2021	2/2022 (-) [12/2023]	223.35 (-) [223.35]	114.32 (0.00) [22]	0/0
779	NANDED TO JALKOT - [N24001069],MoRTH,MAHARASHTRA	12/2017	9/2019 (-) [3/2023]	456.93 (457.00) [456.93]	278.22 (0.00) [0]	2/4
780	OSMANNAGAR TO KUNDRAJ - [N24001075],MoRTH,MAHARASHTRA	9/2017	8/2020 (-) [12/2023]	344.25 (344.00) [344.25]	188.48 (0.00) [40]	2/4
781	AURANGABAD TO SILLOD - [N24001124],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [2/2023]	456.32 (-) [456.32]	342.78 (0.00) [0]	2/4
782	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941],MoRTH,PUNJAB	3/2018	8/2020 (-) [3/2023]	293.64 (326.84) [293.64]	295.46 (0.00) [0]	0/0
783	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926],MoRTH,GUJARAT	8/2017	9/2020 (10/2023) [10/2023]	962.43 (978.93) [978.93]	818.30 (16.50) [37]	3/4
784	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917],MoRTH,ODISHA	3/2018	8/2018 (9/2023) [9/2023]	199.16 (-) [199.16]	101.34 (0.00) [61]	0/0
785	BHOGAN KHURD TO KASHEDI - [N24001132],MoRTH,MAHARASHTRA	9/2017	6/2021 (-) [6/2023]	743.21 (743.00) [743.21]	911.64 (0.00) [0]	2/4
786	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM - [N24001456],MoRTH,UTTAR PRADESH	4/2020	2/2024 (-) [2/2024]	199.39 (206.59) [199.39]	65.98 (0.00) [0]	0/0
787	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION -	12/2014	3/2015 (-) [3/2015]	496.02 (-) [496.02]	240.11 (0.00) [0]	0/0

	[N24001226],MoRTH,CHHATTISGARH					
788	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	403.68 (-) [403.68]	346.74 (0.00) [0]	0/0
789	WIDENING AND STRENGTHENING FROM KM.15.000 TO KM, 58.600 (BHADEWARA -DRAMANDGANJ SECTION) OF NATIONAL - [N24001478],MoRTH,UTTAR PRADESH	12/2021	5/2024 (-) [5/2024]	257.97 (-) [257.97]	68.81 (0.00) [0]	0/0
790	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382],MoRTH,BIHAR	1/1991	/ (12/2023) [12/2023]	675.00 (780.77) [780.77]	485.28 (105.77) [-]	0/0
791	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130],MoRTH,UTTARAKHAND	8/2016	12/2017 (-) [12/2017]	234.88 (-) [234.88]	174.51 (0.00) [0]	0/0
792	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168],MoRTH,KARNATAKA	5/2018	5/2018 (10/2023) [10/2023]	171.60 (-) [171.60]	138.16 (0.00) [65]	0/0
793	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160],MoRTH,KARNATAKA	9/2017	10/2018 (4/2022) [4/2022]	191.60 (-) [191.60]	112.05 (0.00) [0]	0/0
794	MEHKAR TO AJISPUR - [N24001048],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [8/2023]	232.77 (-) [232.77]	151.60 (0.00) [49]	0/0
795	KARAD TO VITA - [N24001049],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [10/2023]	344.85 (245.00) [344.85]	281.41 (0.00) [46]	2/4
796	VADPALE TO BHOGAN KHURD - [N24001115],MoRTH,MAHARASHTRA	1/2017	11/2019 (-) [2/2023]	1,598.47 (1,560.00) [1,598.47]	1,277.25 (0.00) [0]	2/4
797	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387],MoRTH,KARNATAKA	1/2017	9/2017 (6/2023) [6/2023]	264.34 (-) [264.34]	193.05 (0.00) [0]	0/0
798	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411],MoRTH,RAJASTHAN	12/2020	10/2023 (-) [6/2024]	379.23 (-) [379.23]	143.30 (0.00) [8]	0/0
799	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968],MoRTH,ANDHRA PRADESH	11/2016	8/2017 (10/2022) [10/2022]	376.25 (414.44) [414.44]	399.50 (38.19) [0]	3/4
800	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222],MoRTH,CHHATTISGARH	3/2016	7/2016 (-) [12/2023]	452.94 (-) [435.61]	205.99 (-17.33) [89]	0/0

801	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408], MoRTH, ASSAM	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	76.97 (0.00) [0]	0/0
802	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412], MoRTH, RAJASTHAN	12/2020	10/2023 (-) [6/2024]	339.65 (-) [339.65]	170.39 (0.00) [8]	0/0
803	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939], MoRTH, ANDHRA PRADESH	3/2018	11/2018 (-) [11/2018]	504.19 (504.00) [504.19]	517.57 (0.00) [0]	4/4
804	KALMATH TO ZARAP - [N24001137], MoRTH, MAHARASHTRA	9/2016	3/2020 (-) [1/2023]	1,338.13 (2,617.44) [1,338.13]	1,346.39 (0.00) [0]	5/5
805	NALDURG TO AKKALKOT - [N24001051], MoRTH, MAHARASHTRA	2/2018	12/2019 (-) [12/2023]	274.50 (275.00) [274.50]	143.39 (0.00) [48]	2/4
806	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING REHABILITATION AND - [N24000943], MoRTH, BIHAR	9/2018	/ (-) [6/2024]	1,478.40 (-) [1,478.40]	621.30 (0.00) [-]	0/0
807	SHIVUR TO YEOLA - [N24001059], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [3/2022]	181.08 (-) [181.08]	97.86 (0.00) [0]	2/4
808	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937], MoRTH, ANDHRA PRADESH	3/2018	8/2018 (10/2022) [10/2022]	289.67 (285.29) [285.29]	254.19 (-4.38) [0]	3/4
809	PATRADEVI TO KARASWADA 4L - [N24001004], MoRTH, GOA	3/2017	5/2020 (-) [3/2023]	634.32 (-) [634.32]	496.44 (0.00) [0]	2/4
810	SELDOH TO PANVAR - [N24001097], MoRTH, MAHARASHTRA	7/2018	5/2020 (-) [3/2024]	404.33 (404.00) [404.33]	140.65 (0.00) [46]	2/4
811	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380], MoRTH, TAMIL NADU	8/2020	2/2021 (-) [8/2023]	302.62 (306.14) [306.14]	293.37 (3.52) [30]	3/4
812	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912], MoRTH, ODISHA	8/2016	2/2017 (10/2023) [10/2023]	287.70 (-) [287.70]	196.92 (0.00) [80]	0/0
813	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M - [N24001529], MoRTH, RAJASTHAN	12/2021	8/2024 (-) [8/2024]	451.66 (-) [451.66]	186.59 (0.00) [0]	0/0
814	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181], MoRTH, MIZORAM	8/2010	9/2014 (6/2023) [6/2023]	186.96 (-) [322.24]	312.50 (135.28) [0]	0/0

815	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574],MoRTH,BIHAR	11/2013	7/2016 (5/2022) [5/2022]	683.83 (828.45) [828.45]	768.65 (144.62) [0]	0/0
816	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 - [N24001441],MoRTH,MEGHALAYA	8/2020	2/2022 (1/2024) [1/2024]	302.88 (-) [302.88]	91.62 (0.00) [23]	0/0
817	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR - [N24001454],MoRTH,TAMIL NADU	2/2022	8/2022 (-) [8/2024]	184.15 (-) [184.15]	82.06 (0.00) [24]	2/4
818	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987],MoRTH,TELANGANA	1/2018	5/2020 (12/2022) [8/2023]	283.15 (-) [283.15]	250.50 (0.00) [39]	0/0
819	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970],MoRTH,ANDHRA PRADESH	1/2017	1/2018 (2/2023) [2/2023]	576.48 (686.13) [686.13]	635.78 (109.65) [0]	3/4
820	NAIGAONBANDI TO MANGRULPIR - [N24001094],MoRTH,MAHARASHTRA	12/2017	3/2019 (-) [1/2023]	244.04 (244.00) [244.04]	177.94 (0.00) [0]	0/0
821	KARAD TO TAGAON - [N24001053],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [6/2023]	537.81 (538.00) [537.81]	245.41 (0.00) [0]	2/4
822	PARSHURAM GHAT TO ARAWALI - [N24001133],MoRTH,MAHARASHTRA	4/2016	12/2019 (-) [6/2023]	983.14 (2,226.11) [983.14]	1,108.30 (0.00) [0]	2/4
823	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925],MoRTH,GUJARAT	10/2018	11/2020 (9/2023) [9/2023]	400.76 (394.44) [394.44]	276.30 (-6.32) [34]	3/4
824	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989],MoRTH,TELANGANA	2/2018	6/2020 (1/2021) [1/2021]	206.13 (-) [206.13]	187.55 (0.00) [0]	0/0
825	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531],MoRTH,BIHAR	1/1991	/ (5/2023) [5/2023]	319.68 (404.10) [404.10]	401.17 (84.42) [0]	0/0
826	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385],MoRTH,ANDHRA PRADESH	6/2020	5/2021 (11/2022) [12/2022]	221.40 (-) [221.40]	166.34 (0.00) [0]	2/4
827	KOLDE TO KHETIYA - [N24001090],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2023]	509.18 (-) [509.18]	283.13 (0.00) [0]	2/4
828	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	263.61 (0.00) [0]	0/0

	THE STATE OF ARUNACHAL PRADESH [N24001372], MoRTH, ARUNACHAL PRADESH					
829	KATOL TO WARUD - [N24001019], MoRTH, MAHARASHTRA	1/2017	6/2019 (-) [3/2023]	463.62 (664.00) [463.62]	265.78 (0.00) [0]	2/4
830	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585], MoRTH, MAHARASHTRA	3/2016	/ (-) [12/2023]	1,101.58 (-) [1,101.58]	608.53 (0.00) [-]	0/0
831	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334], MoRTH, KARNATAKA	3/2015	11/2015 (6/2023) [9/2023]	165.67 (-) [165.67]	126.47 (0.00) [94]	0/0
832	RISOD TO HINGOLI - [N24001149], MoRTH, MAHARASHTRA	2/2018	12/2019 (-) [1/2023]	355.99 (-) [355.99]	247.60 (0.00) [0]	0/0
833	CHIKALI TO DHAD - [N24001061], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [3/2024]	189.46 (189.00) [189.46]	111.73 (0.00) [51]	2/4
834	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872], MoRTH, MADHYA PRADESH	3/2018	8/2018 (8/2021) [4/2023]	166.21 (-) [174.90]	155.10 (8.69) [0]	0/0
835	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252], MoRTH, MAHARASHTRA	3/2015	/ (-) [6/2019]	168.30 (-) [168.30]	100.56 (0.00) [0]	0/4
836	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376], MoRTH, ARUNACHAL PRADESH	3/2021	3/2027 (-) [3/2027]	182.55 (-) [182.55]	72.99 (0.00) [0]	0/0
837	SATARA TO MHASWAD - [N24001092], MoRTH, MAHARASHTRA	1/2017	7/2019 (-) [6/2023]	653.46 (-) [653.46]	369.62 (0.00) [0]	2/4
838	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772], MoRTH, UTTARAKHAND	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	156.63 (0.00) [0]	0/0
839	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I - [N24001465], MoRTH, NAGALAND	6/2020	9/2024 (9/2024) [9/2024]	252.19 (-) [252.19]	0.28 (0.00) [0]	0/0
840	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516], MoRTH, GOA	12/2015	/ (-) [1/2023]	819.95 (-) [819.95]	709.30 (0.00) [0]	0/0
841	SANGOLA TO JATH - [N24001052], MoRTH, MAHARASHTRA	1/2018	12/2019 (-) [2/2023]	257.38 (257.00) [257.38]	166.31 (0.00) [0]	2/4
842	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916], MoRTH, ODISHA	3/2018	8/2018 (9/2023) [9/2023]	214.23 (-) [214.23]	179.48 (0.00) [61]	0/0

843	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151],MoRTH,MADHYA PRADESH	11/2017	3/2018 (3/2022) [8/2023]	392.33 (470.72) [470.72]	431.91 (78.39) [65]	0/0
844	INDAPUR TO AGARDANDA - [N24001025],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [2/2023]	355.17 (-) [355.17]	318.68 (0.00) [0]	4/4
845	PANDHARPUR TO SANGOLA - [N24001102],MoRTH,MAHARASHTRA	7/2017	7/2019 (-) [9/2023]	218.38 (-) [218.38]	182.63 (0.00) [50]	2/4
846	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775],MoRTH,UTTARAKHAND	6/2017	6/2019 (3/2023) [3/2023]	282.08 (-) [282.08]	206.46 (0.00) [0]	0/0
847	JINTUR TO PARBHANI - [N24001039],MoRTH,MAHARASHTRA	1/2017	/ (-) [8/2023]	356.66 (-) [356.66]	209.48 (0.00) [-]	2/4
848	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT - [N24001427],MoRTH,GUJARAT	6/2020	4/2023 (8/2023) [8/2023]	166.21 (-) [166.21]	89.45 (0.00) [4]	3/4
849	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929],MoRTH,ANDHRA PRADESH	9/2016	2/2017 (1/2022) [2/2022]	372.68 (-) [309.37]	274.76 (-63.31) [0]	4/4
850	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576],MoRTH,BIHAR	2/2016	5/2016 (7/2023) [7/2023]	178.85 (225.06) [225.06]	227.48 (46.21) [86]	0/0
851	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217],MoRTH,CHHATTISGARH	1/2016	8/2016 (-) [3/2024]	497.14 (-) [572.66]	309.49 (75.52) [91]	0/0
852	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179],MoRTH,NAGALAND	3/2017	11/2020 (2/2023) [2/2023]	217.35 (-) [217.35]	197.79 (0.00) [0]	0/0
853	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM.0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579],MoRTH,BIHAR	1/2014	10/2016 (-) [11/2023]	1,408.85 (2,138.16) [2,138.16]	1,560.46 (729.31) [85]	0/0
854	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180],MoRTH,NAGALAND	3/2019	12/2022 (5/2023) [5/2023]	237.51 (-) [237.51]	200.01 (0.00) [0]	0/0
855	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993],MoRTH,TELANGANA	3/2018	9/2020 (6/2022) [4/2023]	322.81 (-) [322.81]	307.95 (0.00) [0]	0/0

856	WARDHA TO HINGAGHAT - [N24001098], MoRTH, MAHARASHTRA	1/2018	12/2019 (-) [8/2023]	216.90 (217.00) [216.90]	164.00 (0.00) [44]	2/4
857	PALPHATA TO PHULAMBARI - [N24001060], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [9/2023]	227.19 (227.00) [227.19]	141.92 (0.00) [45]	2/4
858	CONSTRUCTION OF 1 ROB CUM FLYOVER FROM KM 136.200 TO 137.800 AND 2 FLYOVERS - [N24001459], MoRTH, UTTAR PRADESH	1/2022	4/2024 (-) [4/2024]	297.06 (-) [297.06]	184.94 (0.00) [0]	0/0
859	KHAMGAON TO SHEGAON - [N24001009], MoRTH, MAHARASHTRA	2/2017	5/2019 (-) [9/2019]	203.21 (203.00) [203.21]	163.81 (0.00) [0]	0/0
860	MOPA AIRPORT - [N24001458], MoRTH, GOA	12/2021	4/2022 (-) [10/2023]	1,183.16 (-) [1,183.16]	485.75 (0.00) [18]	0/0
861	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD - [N24000964], MoRTH, ANDHRA PRADESH	8/2016	1/2017 (6/2023) [6/2023]	350.61 (411.18) [411.18]	340.08 (60.57) [0]	3/4
862	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578], MoRTH, BIHAR	2/2016	5/2016 (6/2023) [6/2023]	553.30 (587.41) [587.41]	583.48 (34.11) [0]	0/0
863	WADIGODRI TO DHANGRIPIMPRI - [N24001063], MoRTH, MAHARASHTRA	3/2018	2/2020 (-) [9/2023]	194.23 (194.00) [194.23]	136.55 (0.00) [43]	2/4
864	PEN TO KHOPOLI - [N24001106], MoRTH, MAHARASHTRA	3/2018	3/2018 (-) [1/2024]	301.39 (302.00) [301.39]	170.12 (0.00) [70]	2/4
865	BODHWAD TO STATE BORDER - [N24001086], MoRTH, MAHARASHTRA	1/2017	7/2019 (-) [11/2020]	178.26 (-) [178.26]	159.96 (0.00) [0]	2/4
866	WIDENING TO 2 LANE, RE- ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306], MoRTH, MIZORAM	11/2010	3/2011 (6/2023) [6/2023]	624.41 (1,109.88) [992.67]	1,021.46 (368.26) [0]	0/0
867	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781], MoRTH, UTTARAKHAND	5/2018	5/2020 (12/2023) [12/2023]	248.00 (-) [248.00]	111.85 (0.00) [43]	0/0
868	MHASWAD TO TEMBHURNI - [N24001099], MoRTH, MAHARASHTRA	1/2017	7/2019 (-) [12/2023]	488.60 (-) [488.60]	279.42 (0.00) [53]	2/4
869	FARDAPUR TO JALGAON - [N24001126], MoRTH, MAHARASHTRA	2/2017	6/2019 (-) [2/2023]	456.45 (-) [456.45]	427.43 (0.00) [0]	2/4
870	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332], MoRTH, MAHARASHTRA	1/2015	/ (-) [6/2023]	225.81 (-) [225.81]	167.96 (0.00) [0]	0/0
871	ARDHAPUR TO HIMAYATNAGAR - [N24001079], MoRTH, MAHARASHTRA	12/2017	6/2020 (-)	426.06 (426.00)	271.40 (0.00)	2/4

			[1/2023]	[426.06]	[0]	
872	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW - [N24001480],MoRTH,UTTAR PRADESH	10/2021	4/2024 (-) [4/2024]	227.06 (-) [227.06]	42.18 (0.00) [0]	0/0
873	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412],MoRTH,MADHYA PRADESH	1/2012	4/2015 (-) [6/2023]	410.72 (-) [410.72]	392.45 (0.00) [0]	0/0
874	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308],MoRTH,MIZORAM	8/2010	10/2010 (6/2023) [6/2023]	193.69 (374.59) [327.92]	364.32 (134.23) [0]	0/0
875	AKOLA TO AKOT - [N24001003],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [8/2023]	313.95 (-) [313.95]	270.26 (0.00) [50]	2/4
876	CHIKLI TO TAKARKHED - [N24001083],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [1/2023]	393.10 (393.00) [393.10]	255.24 (0.00) [0]	3/4
877	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950],MoRTH,RAJASTHAN	11/2017	10/2019 (-) [4/2021]	187.82 (-) [187.82]	151.49 (0.00) [0]	4/4
878	MANGAON TO DIGHI PORT - [N24001024],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [2/2023]	457.52 (-) [457.52]	426.61 (0.00) [0]	3/4
879	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K - [N24001447],MoRTH,HIMACHAL PRADESH	8/2020	12/2024 (-) [12/2024]	371.93 (-) [371.93]	63.42 (0.00) [0]	0/0
880	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984],MoRTH,TELANGANA	1/2017	12/2019 (12/2019) [12/2019]	283.00 (-) [283.00]	253.40 (0.00) [0]	0/0
881	SALAIKHURD TO TIRORA - [N24001042],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [1/2023]	415.25 (415.25) [415.25]	274.02 (0.00) [0]	2/4
882	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892],MoRTH,MADHYA PRADESH	11/2017	7/2018 (8/2021) [8/2023]	249.05 (-) [249.05]	221.19 (0.00) [61]	0/0
883	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913],MoRTH,ODISHA	9/2016	2/2017 (9/2023) [9/2023]	295.67 (-) [295.67]	203.61 (0.00) [79]	0/0
884	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384],MoRTH,ANDHRA PRADESH	3/2020	3/2021 (11/2022) [11/2022]	207.79 (-) [207.79]	171.92 (0.00) [0]	3/4
885	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO	3/2018	7/2019 (6/2022)	192.67 (-)	171.11 (0.00)	0/0

	154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997],MoRTH,TELANGANA		[7/2023]	[192.67]	[48]	
886	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN- LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH - [N24001530],MoRTH,RAJASTHAN	12/2021	9/2024 (-) [9/2024]	150.11 (-) [150.11]	24.18 (0.00) [0]	0/0
887	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP - [N24001461],MoRTH,UTTAR PRADESH	4/2020	3/2024 (-) [3/2024]	236.47 (-) [236.47]	46.55 (0.00) [0]	0/0
888	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915],MoRTH,ODISHA	12/2016	4/2018 (9/2023) [9/2023]	206.88 (-) [206.88]	123.50 (0.00) [65]	0/0
889	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966],MoRTH,ANDHRA PRADESH	1/2016	8/2016 (11/2022) [11/2022]	348.95 (355.69) [355.69]	300.51 (6.74) [0]	3/4
890	DAHEGAON TO KUHI - [N24001017],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [9/2023]	228.89 (229.00) [228.89]	154.82 (0.00) [51]	4/4
891	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224],MoRTH,CHHATTISGARH	3/2017	1/2018 (-) [8/2023]	423.79 (-) [423.79]	324.86 (0.00) [67]	0/0
892	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221],MoRTH,CHHATTISGARH	1/2016	10/2016 (-) [12/2023]	624.98 (731.50) [731.50]	539.88 (106.52) [86]	0/0
893	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF BARMER GHAGARIYA SECTION FROM KM 0 - [N24001531],MoRTH,RAJASTHAN	3/2022	8/2024 (-) [8/2024]	304.87 (-) [304.87]	94.33 (0.00) [0]	0/0
894	NILAJPHATA TO BHANDARA - [N24001043],MoRTH,MAHARASHTRA	1/2018	5/2020 (-) [6/2023]	420.63 (421.00) [420.63]	219.40 (0.00) [0]	2/4
895	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382],MoRTH,HIMACHAL PRADESH	8/2020	3/2021 (-) [3/2021]	242.80 (-) [242.80]	115.62 (0.00) [0]	0/0
896	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH- 730C FROM KM.0.00 TO 52.770 UNDER GNHCP - [N24001471],MoRTH,UTTAR PRADESH	4/2020	11/2024 (-) [11/2024]	325.24 (-) [325.24]	24.98 (0.00) [0]	0/0
897	HELWAK TO KARAD - [N24001055],MoRTH,MAHARASHTRA	2/2017	7/2019 (-) [1/2023]	416.99 (-) [416.99]	225.83 (0.00) [0]	2/4
898	MALEGAON TO RISOD	2/2018	12/2019	303.24	199.08	2/4

	- [N24001089],MoRTH,MAHARASHTRA		(-) [3/2023]	(303.00) [303.24]	(0.00) [0]	
899	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774],MoRTH,UTTARAKHAND	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	146.17 (0.00) [0]	0/0
900	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248],MoRTH,TELANGANA	3/2015	1/2017 (-) [0/2017]	153.21 (-) [153.21]	100.96 (0.00) [0]	0/0
901	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986],MoRTH,TELANGANA	1/2017	5/2019 (7/2021) [7/2021]	300.00 (-) [300.00]	224.70 (0.00) [0]	0/0
902	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR - [N24001527],MoRTH,RAJASTHAN	12/2021	5/2024 (-) [5/2024]	411.40 (-) [411.40]	57.30 (0.00) [0]	0/0
903	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381],MoRTH,HIMACHAL PRADESH	8/2020	4/2021 (-) [4/2021]	272.98 (-) [272.98]	168.27 (0.00) [0]	0/0
904	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165],MoRTH,KARNATAKA	11/2016	3/2017 (7/2023) [7/2023]	314.90 (-) [314.90]	234.09 (0.00) [76]	0/0
905	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162],MoRTH,KARNATAKA	3/2018	10/2018 (-) [8/2022]	325.86 (-) [386.41]	356.78 (60.55) [0]	0/0
906	AMD I TO SAONER - [N24001021],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [8/2023]	396.91 (397.00) [396.91]	289.79 (0.00) [50]	4/4
907	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922],MoRTH,GUJARAT	12/2017	11/2020 (12/2023) [12/2023]	867.97 (913.49) [913.49]	778.14 (45.52) [37]	3/4
908	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 – 29/250 INCLUDING LA AND SHIFTING OF NH-234 - [N24001828],MoRTH,TAMIL NADU	1/2022	11/2024 (-) [11/2024]	221.03 (243.95) [243.95]	0.00 (22.92) [0]	0/4
909	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996],MoRTH,TELANGANA	1/2017	10/2019 (10/2019) [6/2021]	605.08 (-) [605.08]	412.60 (0.00) [0]	0/0
910	KURUDWADI TO PANDHARPUR - [N24001101],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [9/2023]	307.63 (-) [307.63]	232.57 (0.00) [50]	2/4
911	PAITHAN TO SHIRUR - [N24001122],MoRTH,MAHARASHTRA	3/2017	6/2019 (-) [3/2024]	341.80 (-) [341.80]	203.09 (0.00) [57]	2/4

912	SHIROD SHAHPURER TO NANDED - [N24001041],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [8/2023]	211.34 (-) [211.34]	136.33 (0.00) [49]	3/4
913	WARDHA TO ARVI - [N24001150],MoRTH,MAHARASHTRA	2/2018	4/2020 (-) [8/2023]	313.58 (-) [313.58]	230.41 (0.00) [40]	2/4
914	4-LANING OF DERGAON TOWN - [N24001435],NHIDCL,ASSAM	3/2020	6/2022 (-) [6/2023]	287.63 (-) [287.63]	383.88 (0.00) [0]	0/4
915	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748],NHIDCL,ANDAMAN AND NICOBAR ISLANDS	2/2018	9/2020 (1/2023) [6/2024]	391.00 (-) [391.00]	170.37 (0.00) [45]	2/4
916	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865],NHIDCL,MIZORAM	4/2017	9/2023 (5/2024) [5/2024]	428.11 (777.50) [777.50]	437.46 (349.39) [8]	3/4
917	IMPROVEMENT/WIDENING TO 2- LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903],NHIDCL,MEGHALAYA	3/2019	3/2022 (-) [10/2023]	306.28 (-) [306.28]	196.84 (0.00) [19]	3/4
918	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389],NHIDCL,NAGALAND	3/2020	6/2022 (9/2022) [0/0]	206.53 (-) [206.53]	98.69 (0.00) [0]	3/4
919	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284],NHIDCL,NAGALAND	3/2020	6/2022 (6/2023) [12/2023]	361.53 (-) [361.53]	112.55 (0.00) [18]	2/4
920	IMPHAL – MOREH (PACKAGE 4) - [N24001399],NHIDCL,MANIPUR	3/2021	1/2023 (-) [5/2023]	277.99 (-) [277.99]	123.86 (0.00) [0]	3/4
921	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH- 102A FROM - [N24001473],NHIDCL,MANIPUR	9/2021	2/2024 (-) [2/2024]	310.76 (-) [310.76]	66.01 (0.00) [0]	0/0
922	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763],NHIDCL,NAGALAND	3/2018	12/2021 (8/2022) [12/2023]	215.79 (-) [215.79]	97.45 (0.00) [24]	1/4
923	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332],NHIDCL,ASSAM	3/2020	6/2022 (-) [6/2023]	217.50 (-) [217.50]	48.14 (0.00) [0]	1/4
924	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331],NHIDCL,ASSAM	3/2020	6/2022 (-) [3/2024]	261.13 (-) [261.13]	51.90 (0.00) [21]	1/4
925	PEREN-DIMAPUR PKG-5 - [N24001407],NHIDCL,NAGALAND	2/2021	3/2023 (-) [0/0]	207.33 (-) [207.33]	0.00 (0.00) [0]	0/0
926	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333],NHIDCL,ASSAM	9/2019	5/2023 (-) [5/2023]	761.54 (820.56) [761.54]	425.77 (0.00) [0]	3/4
927	KHELLANI-KHANABAL PKG-4 - [N24001395],NHIDCL,JAMMU AND KASHMIR	7/2021	8/2023 (-) [9/2024]	859.67 (-) [859.67]	66.85 (0.00) [13]	1/4

928	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (5/2024) [5/2024]	301.06 (-) [301.06]	96.33 (0.00) [25]	2/4
929	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742],NHIDCL,UTTARAKHAND	3/2018	11/2020 (12/2022) [4/2024]	403.36 (-) [403.36]	328.94 (0.00) [41]	3/4
930	KARGIL-ZANSKR PACKAGE-1 - [N24001343],NHIDCL,LADAKH	3/2021	1/2023 (11/2023) [11/2023]	384.23 (-) [384.23]	48.09 (0.00) [10]	2/4
931	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768],NHIDCL,SIKKIM	11/2017	10/2020 (8/2023) [8/2023]	290.05 (-) [290.05]	218.36 (0.00) [34]	3/4
932	IMPHAL - KHONGSANG PKG-3 - [N24001401],NHIDCL,MANIPUR	7/2021	3/2023 (-) [9/2023]	467.00 (-) [467.00]	139.15 (0.00) [6]	2/4
933	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG-IB) - [N24001269],NHIDCL,ASSAM	3/2020	3/2022 (-) [6/2023]	216.49 (241.52) [216.49]	101.02 (0.00) [0]	2/4
934	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688],NHIDCL,NAGALAND	3/2016	8/2022 (8/2022) [1/2023]	429.52 (562.98) [429.52]	267.69 (0.00) [0]	3/4
935	TAMENGLONG - MAHUR PKG-5 - [N24001436],NHIDCL,MANIPUR	8/2021	5/2023 (-) [5/2023]	477.86 (-) [477.86]	68.12 (0.00) [0]	1/4
936	KHELLANI-KHANABAL PKG-1 - [N24001323],NHIDCL,JAMMU AND KASHMIR	3/2021	9/2022 (6/2023) [10/2023]	486.45 (-) [486.45]	92.05 (0.00) [13]	3/4
937	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285],NHIDCL,NAGALAND	3/2020	12/2021 (3/2023) [3/2023]	330.78 (-) [330.78]	199.02 (0.00) [0]	4/4
938	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326],NHIDCL,ASSAM	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	1,340.72 (0.00) [0]	1/4
939	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268],NHIDCL,MANIPUR	3/2019	7/2022 (-) [3/2023]	471.00 (-) [471.00]	319.81 (0.00) [0]	4/4
940	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276],NHIDCL,MANIPUR	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]	0/4
941	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308],NHIDCL,TRIPURA	11/2020	7/2022 (4/2023) [4/2023]	332.14 (-) [332.14]	148.07 (0.00) [0]	3/4
942	KARGIL-ZANSKR PACKAGE-7 - [N24001347],NHIDCL,LADAKH	1/2021	6/2024 (-) [6/2024]	308.86 (328.60) [308.86]	185.10 (0.00) [0]	2/4
943	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS	1/2016	12/2021 (12/2019)	252.00 (330.30)	146.28 (78.30)	2/4

	TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583],NHIDCL,ASSAM		[8/2023]	[330.30]	[20]	
944	KARGIL-ZANSKR PACKAGE-6 - [N24001346],NHIDCL,LADAKH	1/2021	5/2024 (-) [5/2024]	239.81 (265.41) [239.81]	171.38 (0.00) [0]	2/4
945	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B - [N24001833],NHIDCL,JAMMU AND KASHMIR	7/2022	3/2025 (-) [3/2025]	198.28 (-) [198.28]	1.79 (0.00) [0]	0/0
946	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328],NHIDCL,ASSAM	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	508.56 (0.00) [0]	2/4
947	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758],NHIDCL,NAGALAND	3/2018	12/2021 (3/2023) [4/2023]	240.64 (255.58) [240.64]	172.36 (0.00) [0]	0/4
948	KHELLANI-KHANABAL PKG-5 - [N24001396],NHIDCL,JAMMU AND KASHMIR	7/2021	2/2023 (-) [1/2024]	497.09 (-) [497.09]	74.15 (0.00) [11]	2/4
949	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262],NHIDCL,SIKKIM	7/2020	4/2023 (-) [10/2023]	345.38 (395.59) [395.59]	300.58 (50.21) [6]	3/4
950	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327],NHIDCL,SIKKIM	8/2020	5/2022 (10/2023) [11/2024]	292.80 (-) [292.80]	94.56 (0.00) [30]	1/4
951	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 - [N24001832],NHIDCL,ASSAM	1/2023	5/2025 (-) [5/2025]	458.59 (-) [458.59]	0.00 (0.00) [0]	0/0
952	DABOKA KATHKATI PACKAGE-2 - [N24001364],NHIDCL,ASSAM	3/2021	1/2024 (-) [5/2023]	335.88 (-) [335.88]	211.73 (0.00) [0]	2/4
953	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 - [N24001541],NHIDCL,MEGHALAYA	11/2021	6/2024 (-) [6/2024]	283.50 (261.40) [283.50]	96.86 (0.00) [0]	0/0
954	KARGIL-ZANSKR PACKAGE-8 - [N24001348],NHIDCL,LADAKH	3/2021	1/2023 (8/2023) [8/2023]	398.37 (-) [398.37]	93.05 (0.00) [7]	1/4
955	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355],NHIDCL,MIZORAM	3/2021	12/2022 (11/2023) [11/2023]	374.39 (374.39) [374.39]	267.81 (0.00) [11]	3/4
956	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 - [N24001451],NHIDCL,ASSAM	3/2022	7/2024 (-) [7/2024]	215.27 (-) [215.27]	50.37 (0.00) [0]	0/4
957	AKASH BRIDGE - JESSAMI SECTION PKG-2 - [N24001540],NHIDCL,MANIPUR	3/2022	2/2025 (-) [2/2025]	152.11 (-) [152.11]	0.00 (0.00) [0]	0/0
958	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (7/2023) [7/2023]	199.03 (-) [199.03]	101.66 (0.00) [15]	3/4
959	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH- 144A FROM GANESH VIHA -	3/2018	7/2021 (3/2023) [8/2023]	253.44 (-) [253.44]	167.30 (0.00) [25]	2/4

	[N24000868],NHIDCL,JAMMU AND KASHMIR					
960	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282],NHIDCL,NAGALAND	3/2020	6/2022 (2/2023) [12/2023]	355.79 (-) [355.79]	109.24 (0.00) [18]	2/4
961	KARGIL-ZANSKR PACKAGE-2 - [N24001344],NHIDCL,LADAKH	3/2021	1/2023 (11/2023) [11/2023]	404.89 (-) [404.89]	40.59 (0.00) [10]	1/4
962	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749],NHIDCL,ANDAMAN AND NICOBAR ISLANDS	3/2018	9/2020 (11/2022) [1/2024]	234.27 (-) [234.27]	124.29 (0.00) [40]	3/4
963	2-LANING FROM JOLAIBARI - BELONIA - [N24001317],NHIDCL,TRIPURA	6/2020	1/2022 (6/2023) [12/2023]	201.99 (-) [201.99]	117.12 (0.00) [23]	2/4
964	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255],NHIDCL,NAGALAND	9/2020	10/2022 (-) [7/2024]	277.44 (-) [277.44]	134.18 (0.00) [21]	2/4
965	KEIFANG - TUVAI PKG-1 - [N24001440],NHIDCL,MIZORAM	9/2021	5/2023 (2/2024) [4/2024]	492.94 (492.94) [492.94]	230.26 (0.00) [11]	0/4
966	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309],NHIDCL,TRIPURA	11/2020	6/2022 (6/2023) [10/2023]	159.13 (171.50) [171.50]	67.62 (12.37) [16]	3/4
967	LADDA - BASAI - [N24001316],NHIDCL,ARUNACHAL PRADESH	2/2021	4/2023 (-) [2/2024]	445.96 (-) [445.96]	75.67 (0.00) [10]	1/4
968	CHURACHANPUR TUIVAI PKG-3 - [N24001405],NHIDCL,MANIPUR	7/2021	10/2023 (-) [8/2023]	673.27 (-) [673.27]	281.57 (0.00) [-2]	1/4
969	MARIAM - PEREN (PKG 1B) - [N24001350],NHIDCL,MANIPUR	2/2021	12/2022 (-) [10/2023]	188.36 (-) [188.36]	81.38 (0.00) [10]	2/4
970	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338],NHIDCL,SIKKIM	10/2020	12/2023 (9/2024) [9/2024]	816.79 (786.60) [786.60]	204.88 (-30.19) [9]	1/4
971	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336],NHIDCL,SIKKIM	8/2020	4/2023 (9/2023) [9/2023]	230.45 (244.91) [244.91]	190.66 (14.46) [5]	3/4
972	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821],NHIDCL,ANDAMAN AND NICOBAR ISLANDS	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	214.90 (-19.34) [0]	0/0
973	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864],NHIDCL,MIZORAM	4/2017	4/2024 (7/2024) [7/2024]	404.29 (723.80) [723.80]	452.54 (319.51) [3]	2/4
974	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION	3/2017	3/2022 (12/2023) [3/2024]	1,718.59 (1,718.59) [1,718.59]	656.26 (0.00) [24]	2/4

	TO KM 21.500 OF - [N24000946],NHIDCL,ARUNACHAL PRADESH					
975	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431],NHIDCL,ASSAM	1/1991	6/2019 (6/2019) [4/2023]	520.01 (-) [520.01]	277.79 (0.00) [0]	3/4
976	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329],NHIDCL,TRIPURA	3/2020	7/2022 (3/2023) [4/2023]	165.54 (-) [210.54]	85.02 (45.00) [0]	3/4
977	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855],NHIDCL,UTTARAKHAND	3/2018	7/2022 (7/2022) [5/2024]	1,383.78 (-) [1,383.78]	542.67 (0.00) [22]	3/5
978	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361],NHIDCL,SIKKIM	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	117.90 (0.00) [0]	1/4
979	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248],NHIDCL,ASSAM	8/2020	4/2022 (-) [7/2024]	208.84 (-) [208.84]	90.92 (0.00) [27]	1/4
980	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752],NHIDCL,NAGALAND	2/2017	9/2020 (8/2022) [9/2023]	387.00 (-) [387.00]	384.58 (0.00) [36]	3/4
981	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582],NHIDCL,ASSAM	1/2016	1/2016 (-) [7/2024]	294.17 (-) [294.17]	248.08 (0.00) [102]	3/4
982	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764],NHIDCL,NAGALAND	3/2018	10/2022 (10/2022) [10/2023]	272.89 (-) [272.89]	145.48 (0.00) [12]	0/4
983	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325],NHIDCL,SIKKIM	9/2020	5/2023 (-) [8/2024]	262.84 (414.20) [414.20]	185.56 (151.36) [15]	1/4
984	KHELLANI-KHANABAL PKG-6 - [N24001324],NHIDCL,JAMMU AND KASHMIR	2/2021	9/2022 (-) [8/2023]	285.28 (-) [285.28]	218.89 (0.00) [11]	3/4
985	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266],NHIDCL,JAMMU AND KASHMIR	7/2020	4/2022 (5/2023) [1/2024]	210.79 (-) [210.79]	46.44 (0.00) [21]	2/4
986	MARIAM - PEREN (PKG 2A) - [N24001398],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	126.78 (0.00) [0]	3/4
987	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318],NHIDCL,TRIPURA	9/2020	4/2022 (10/2022) [6/2023]	173.17 (-) [173.17]	64.05 (0.00) [0]	1/4
988	WIDENING AND UP-GRADATION TO	4/2017	7/2023	640.07	965.74	3/4

	2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858],NHIDCL,MIZORAM		(2/2024) [2/2024]	(1,134.72) [640.07]	(0.00) [7]	
989	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685],NHIDCL,ARUNACHAL PRADESH	2/2017	4/2022 (7/2023) [7/2023]	167.28 (229.70) [167.28]	138.66 (0.00) [15]	3/4
990	DABOKA KATHKATI PACKAGE-5 - [N24001366],NHIDCL,ASSAM	3/2021	1/2023 (-) [10/2023]	288.85 (-) [288.85]	110.33 (0.00) [9]	0/4
991	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245],NHIDCL,ARUNACHAL PRADESH	9/2020	5/2022 (10/2022) [3/2024]	353.90 (-) [353.90]	41.82 (0.00) [22]	1/4
992	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-3 - [N24001360],NHIDCL,MEGHALAYA	3/2021	12/2022 (-) [11/2023]	260.21 (-) [260.21]	149.15 (0.00) [11]	2/4
993	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356],NHIDCL,MIZORAM	3/2021	12/2022 (7/2023) [1/2024]	233.25 (233.25) [233.25]	153.10 (0.00) [13]	3/4
994	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438],NHIDCL,ASSAM	12/2015	12/2018 (7/2021) [5/2023]	289.99 (-) [289.99]	216.08 (0.00) [0]	2/4
995	DEMBUEN - BRUNI - [N24001321],NHIDCL,ARUNACHAL PRADESH	12/2020	3/2023 (-) [11/2023]	606.63 (606.63) [606.63]	270.03 (0.00) [8]	3/4
996	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196],NHIDCL,ASSAM	3/2017	8/2023 (-) [8/2023]	1,049.51 (-) [1,049.51]	293.67 (0.00) [0]	2/4
997	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745],NHIDCL,ANDAMAN AND NICOBAR ISLANDS	3/2017	12/2019 (3/2023) [1/2024]	409.85 (-) [409.85]	207.65 (0.00) [49]	3/4
998	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310],NHIDCL,TRIPURA	11/2020	7/2022 (4/2023) [5/2023]	280.91 (296.48) [296.48]	202.06 (15.57) [0]	3/4
999	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260],NHIDCL,NAGALAND	9/2020	4/2022 (2/2023) [7/2023]	257.15 (-) [257.15]	124.52 (0.00) [15]	2/4
1000	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261],NHIDCL,SIKKIM	8/2020	4/2023 (-) [1/2024]	311.00 (273.78) [273.78]	200.01 (-37.22) [9]	2/4
1001	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259],NHIDCL,NAGALAND	9/2020	4/2022 (-) [8/2023]	315.63 (-) [315.63]	42.64 (0.00) [16]	1/4

1002	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	181.82 (0.00) [0]	0/4
1003	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274],NHIDCL,MANIPUR	8/2020	4/2022 (-) [8/2023]	379.39 (-) [379.39]	186.51 (0.00) [16]	1/4
1004	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322],NHIDCL,SIKKIM	9/2020	5/2022 (-) [4/2024]	183.31 (439.56) [439.56]	322.34 (256.25) [23]	1/4
1005	IMPHAL - KHONGSANG PKG-4 - [N24001453],NHIDCL,MANIPUR	8/2021	12/2023 (-) [12/2023]	579.63 (-) [579.63]	53.90 (0.00) [0]	1/4
1006	TAMENGLONG - MAHUR PKG-3 - [N24001354],NHIDCL,MANIPUR	3/2021	12/2022 (-) [4/2023]	234.08 (-) [234.08]	111.25 (0.00) [0]	2/4
1007	DABOKA KATHKATI PACKAGE-4 - [N24001365],NHIDCL,ASSAM	2/2021	12/2023 (-) [6/2023]	260.07 (-) [260.07]	284.93 (0.00) [0]	3/4
1008	TLABUNG - LUNGLEI PKG-A - [N24001358],NHIDCL,MIZORAM	3/2021	12/2022 (10/2023) [12/2024]	698.44 (698.45) [698.45]	227.20 (0.01) [24]	1/4
1009	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247],NHIDCL,TRIPURA	3/2020	1/2022 (10/2022) [8/2023]	247.76 (251.89) [251.89]	137.58 (4.13) [19]	3/4
1010	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863],NHIDCL,MIZORAM	4/2017	6/2023 (2/2024) [2/2024]	518.53 (902.20) [902.20]	623.42 (383.67) [8]	3/4
1011	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948],NHIDCL,ARUNACHAL PRADESH	9/2016	12/2019 (3/2023) [9/2023]	568.92 (568.92) [568.92]	493.58 (0.00) [45]	3/4
1012	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683],NHIDCL,ARUNACHAL PRADESH	2/2017	11/2023 (11/2023) [11/2023]	180.57 (244.10) [180.57]	96.11 (0.00) [0]	2/4
1013	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253],NHIDCL,JAMMU AND KASHMIR	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	0.00 (0.00) [0]	2/4
1014	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271],NHIDCL,MANIPUR	6/2020	8/2022 (-) [5/2023]	365.53 (-) [365.53]	142.51 (0.00) [0]	2/4
1015	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368],NHIDCL,ASSAM	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	36.36 (0.00) [0]	0/4
1016	JOGIGHOPA BRIDGE	8/2021	11/2024	746.76	144.33	0/4

	- [N24001434],NHIDCL,ASSAM		(-) [11/2024]	(-) [746.76]	(0.00) [0]	
1017	MARIAM - PEREN PKG-2B - [N24001351],NHIDCL,MANIPUR	2/2021	12/2022 (-) [8/2023]	232.26 (-) [232.26]	147.43 (0.00) [8]	3/4
1018	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 - [N24001544],NHIDCL,ASSAM	3/2022	1/2025 (-) [1/2025]	909.02 (-) [909.02]	72.25 (0.00) [0]	0/0
1019	DABOKA KATHKATI PACKAGE-7 - [N24001537],NHIDCL,ASSAM	11/2021	7/2024 (-) [7/2024]	204.10 (-) [204.10]	54.66 (0.00) [0]	0/0
1020	KHELLANI-KHANABAL PKG-3 - [N24001341],NHIDCL,JAMMU AND KASHMIR	3/2021	12/2022 (-) [11/2023]	398.51 (-) [398.51]	53.04 (0.00) [11]	2/4
1021	IMPHAL – MOREH PACKAGE- 3 - [N24001352],NHIDCL,MANIPUR	3/2021	12/2022 (-) [8/2023]	259.31 (-) [259.31]	136.05 (0.00) [8]	3/4
1022	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362],NHIDCL,SIKKIM	12/2020	2/2024 (2/2024) [2/2024]	410.60 (379.30) [379.30]	147.62 (-31.30) [0]	1/4
1023	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256],NHIDCL,JAMMU AND KASHMIR	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	2,199.36 (0.00) [0]	3/7
1024	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312],NHIDCL,MANIPUR	3/2020	6/2022 (-) [5/2023]	167.95 (-) [167.95]	84.16 (0.00) [0]	4/4
1025	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319],NHIDCL,ASSAM	6/2015	8/2023 (-) [11/2023]	437.39 (-) [437.39]	224.61 (0.00) [3]	1/4
1026	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305],NHIDCL,ASSAM	5/2015	5/2018 (-) [6/2023]	454.89 (814.56) [814.56]	498.86 (359.67) [0]	3/4
1027	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771],NHIDCL,MEGHALAYA	4/2017	9/2021 (9/2021) [7/2023]	553.51 (610.09) [553.51]	290.35 (0.00) [22]	2/4
1028	IMPHAL - KHONGSANG PKG-5 - [N24001538],NHIDCL,MANIPUR	12/2021	5/2024 (-) [5/2024]	410.68 (-) [410.68]	40.52 (0.00) [0]	0/0
1029	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 - [N24001452],NHIDCL,ASSAM	4/2022	7/2024 (-) [1/2024]	170.95 (-) [170.95]	22.38 (0.00) [-6]	0/4
1030	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272],NHIDCL,MANIPUR	3/2020	6/2022 (-) [5/2023]	167.95 (204.12) [167.95]	77.72 (0.00) [0]	2/4
1031	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756],NHIDCL,NAGALAND	3/2018	9/2022 (1/2023) [8/2023]	285.68 (-) [285.68]	155.93 (0.00) [11]	2/4
1032	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF	3/2018	12/2021 (3/2023)	315.03 (-)	212.85 (0.00)	0/4

	CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757],NHIDCL,NAGALAND		[3/2023]	[315.03]	[0]	
1033	MERANGKONG-TAMLU-MON (MTM) PKG-5 - [N24001438],NHIDCL,NAGALAND	7/2021	12/2023 (-) [3/2024]	161.73 (-) [161.73]	32.41 (0.00) [3]	1/4
1034	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337],NHIDCL,SIKKIM	10/2020	11/2023 (-) [5/2024]	493.42 (478.79) [478.79]	230.22 (-14.63) [6]	1/4
1035	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765],NHIDCL,NAGALAND	3/2018	9/2018 (6/2023) [3/2024]	323.98 (-) [323.98]	70.01 (0.00) [66]	0/4
1036	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267],NHIDCL,TRIPURA	3/2020	7/2022 (8/2023) [8/2023]	178.43 (-) [208.74]	77.89 (30.31) [13]	3/4
1037	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (7/2023) [7/2023]	294.04 (-) [294.04]	129.38 (0.00) [15]	3/4
1038	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323],NHIDCL,ASSAM	10/2014	11/2018 (2/2022) [6/2023]	588.95 (811.28) [873.91]	647.07 (284.96) [0]	3/4
1039	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753],NHIDCL,NAGALAND	3/2018	11/2022 (6/2023) [12/2023]	500.09 (583.31) [500.09]	299.49 (0.00) [13]	2/4
1040	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357],NHIDCL,MIZORAM	3/2021	6/2023 (1/2024) [1/2024]	674.71 (674.71) [674.71]	521.28 (0.00) [7]	3/4
1041	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265],NHIDCL,TRIPURA	3/2020	7/2022 (3/2023) [7/2023]	154.51 (-) [154.51]	73.74 (0.00) [12]	3/4
1042	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286],NHIDCL,NAGALAND	3/2020	6/2022 (10/2022) [6/2023]	278.95 (-) [278.95]	161.69 (0.00) [0]	3/4
1043	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342],NHIDCL,JAMMU AND KASHMIR	3/2021	12/2022 (-) [4/2023]	260.40 (-) [260.40]	152.09 (0.00) [0]	1/4
1044	TAMENGLONG - MAHUR PKG-2 - [N24001403],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	197.54 (0.00) [0]	2/4
1045	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	45.46 (0.00) [0]	0/4
1046	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER	11/2020	12/2023 (-)	445.51 (-)	191.35 (0.00)	1/4

	FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334],NHIDCL,MEGHALAYA		[7/2023]	[445.51]	[-5]	
1047	RANIKOR-MAHESHKOLA- BAGHMARA (RMB) PKG-4 (KANAI- RONGARA) - [N24001339],NHIDCL,MEGHALAYA	10/2020	4/2022 (-) [1/2024]	157.86 (-) [157.86]	102.41 (0.00) [21]	2/4
1048	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252],NHIDCL,SIKKIM	8/2020	4/2023 (8/2023) [12/2023]	295.97 (-) [295.97]	190.56 (0.00) [8]	2/4
1049	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251],NHIDCL,SIKKIM	3/2019	4/2022 (-) [1/2024]	402.94 (-) [402.94]	188.53 (0.00) [21]	2/4
1050	MANU-SIMLUNG (PKG 4) - [N24001363],NHIDCL,TRIPURA	3/2021	12/2022 (6/2023) [11/2023]	354.79 (-) [354.79]	33.27 (0.00) [11]	1/4
1051	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249],NHIDCL,TRIPURA	6/2020	1/2022 (4/2023) [7/2023]	347.36 (-) [347.36]	224.48 (0.00) [18]	3/4
1052	GOHA-KHELLANI PKG-3 - [N24001397],NHIDCL,JAMMU AND KASHMIR	2/2021	3/2023 (5/2023) [10/2023]	431.28 (-) [431.28]	173.60 (0.00) [7]	2/4
1053	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861],NHIDCL,MIZORAM	4/2017	4/2023 (11/2023) [1/2024]	473.18 (667.06) [667.06]	465.49 (193.88) [9]	3/4
1054	DABOKA KATHKATI PACKAGE-6 - [N24001450],NHIDCL,ASSAM	9/2021	7/2024 (-) [7/2024]	625.64 (-) [625.64]	265.02 (0.00) [0]	0/4
1055	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH- 54 - [N24001277],NHIDCL,MIZORAM	9/2020	10/2022 (7/2023) [10/2023]	275.02 (-) [275.02]	166.23 (0.00) [12]	1/4
1056	FOUR LANING OF BALACHERA- HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902],NHIDCL,ASSAM	10/2017	6/2020 (6/2020) [12/2023]	818.00 (887.68) [818.00]	659.65 (0.00) [42]	2/4
1057	SENAPATI- IMPHAL PKG-5B - [N24001400],NHIDCL,MANIPUR	3/2021	1/2023 (-) [5/2024]	211.70 (-) [211.70]	1.64 (0.00) [16]	0/4
1058	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686],NHIDCL,NAGALAND	3/2016	9/2019 (9/2019) [9/2023]	373.07 (489.01) [387.00]	377.90 (13.93) [48]	3/4
1059	KHELLANI-KHANABAL PKG-2 - [N24001394],NHIDCL,JAMMU AND KASHMIR	7/2021	2/2023 (-) [10/2024]	512.43 (-) [512.43]	38.94 (0.00) [20]	1/4
1060	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280],NHIDCL,NAGALAND	3/2020	6/2022 (3/2023) [8/2023]	320.97 (-) [320.97]	168.47 (0.00) [14]	3/4
1061	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM	12/2016	1/2020 (1/2022) [8/2023]	200.44 (200.44) [200.44]	146.43 (0.00) [43]	3/4

	106.200 TO KM 120. - [N24000944],NHIDCL,ARUNACHAL PRADESH					
1062	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254],NHIDCL,SIKKIM	3/2020	6/2022 (-) [12/2023]	242.97 (-) [242.97]	204.16 (0.00) [18]	2/4
1063	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979],NHIDCL,ARUNACHAL PRADESH	1/2017	5/2023 (5/2023) [5/2023]	256.66 (-) [256.66]	0.00 (0.00) [0]	1/4
1064	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862],NHIDCL,MIZORAM	4/2017	4/2023 (10/2023) [1/2024]	537.82 (820.42) [820.42]	619.87 (282.60) [9]	3/4
1065	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281],NHIDCL,MIZORAM	3/2020	7/2022 (8/2023) [12/2023]	292.24 (331.17) [331.17]	235.26 (38.93) [17]	2/4
1066	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT- KAILASHAHAR SECTION - [N24001263],NHIDCL,TRIPURA	6/2020	1/2022 (6/2023) [1/2024]	277.50 (302.02) [302.02]	201.23 (24.52) [24]	2/4
1067	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287],NHIDCL,NAGALAND	4/2020	12/2021 (12/2022) [3/2024]	330.80 (-) [330.80]	83.11 (0.00) [27]	2/4
1068	2 LANING FROM MANU-SIMLUNG PKG-2 - [N24001542],NHIDCL,TRIPURA	2/2022	1/2025 (-) [1/2025]	456.88 (-) [456.88]	11.22 (0.00) [0]	0/0
1069	MARIAM - PEREN PKG-1A - [N24001349],NHIDCL,MANIPUR	2/2021	12/2022 (-) [10/2023]	226.32 (-) [226.32]	47.15 (0.00) [10]	1/4
1070	SRIRAMPUR - DHUBRI PKG-1 - [N24001831],NHIDCL,ASSAM	3/2022	2/2025 (-) [2/2025]	613.89 (-) [613.89]	0.00 (0.00) [0]	0/0
1071	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283],NHIDCL,MIZORAM	3/2020	7/2022 (7/2023) [10/2023]	281.78 (253.41) [253.41]	228.20 (-28.37) [15]	3/4
1072	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367],NHIDCL,ASSAM	3/2021	12/2022 (-) [10/2023]	636.42 (-) [418.49]	544.79 (-217.93) [10]	1/4
1073	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J - [N24001475],NHIDCL,NAGALAND	3/2022	12/2024 (-) [12/2024]	605.36 (-) [605.36]	82.51 (0.00) [0]	0/0
1074	TAMENGLONG - MAHUR PKG-6 - [N24001437],NHIDCL,MANIPUR	9/2021	5/2023 (-) [5/2023]	311.18 (-) [311.18]	121.73 (0.00) [0]	2/4
1075	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO -	4/2017	4/2023 (1/2024) [1/2024]	519.09 (775.47) [775.47]	532.37 (256.38) [9]	3/4

	[N24000857],NHIDCL,MIZORAM					
1076	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823],NHIDCL,ASSAM	3/2015	1/2016 (-) [6/2023]	829.00 (-) [829.00]	819.58 (0.00) [0]	2/3
1077	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744],NHIDCL,ANDAMAN AND NICOBAR ISLANDS	3/2015	1/2022 (-) [3/2024]	262.97 (-) [262.97]	92.73 (0.00) [26]	2/4
1078	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258],NHIDCL,NAGALAND	8/2020	4/2022 (-) [3/2024]	202.36 (-) [202.36]	62.66 (0.00) [23]	1/4
1079	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859],NHIDCL,MIZORAM	4/2017	6/2023 (12/2023) [1/2024]	642.96 (1,139.85) [1,139.85]	528.71 (496.89) [7]	3/4
1080	TADADEGE - HENKAR - [N24001315],NHIDCL,ARUNACHAL PRADESH	2/2021	3/2023 (-) [6/2024]	550.45 (-) [550.45]	61.12 (0.00) [15]	1/4
1081	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG-4B) - [N24001273],NHIDCL,MANIPUR	7/2020	8/2022 (-) [5/2023]	177.76 (-) [177.76]	70.23 (0.00) [0]	2/4
1082	KARGIL-ZANSKR PACKAGE-5 - [N24001330],NHIDCL,LADAKH	8/2020	12/2023 (-) [12/2023]	169.79 (217.99) [169.79]	196.67 (0.00) [0]	3/4
1083	TLABUNG - LUNGLEI PKG-B - [N24001359],NHIDCL,MIZORAM	3/2021	1/2023 (11/2023) [12/2024]	740.58 (740.58) [740.58]	104.66 (0.00) [23]	0/4
1084	DOGINALA - GAU - [N24001320],NHIDCL,ARUNACHAL PRADESH	12/2020	9/2022 (-) [8/2023]	242.30 (-) [242.30]	21.47 (0.00) [11]	1/4
1085	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM - [N24001474],NHIDCL,MEGHALAYA	9/2021	5/2024 (-) [5/2024]	359.86 (-) [359.86]	169.42 (0.00) [0]	0/0
1086	PEREN-DIMAPUR SECTION PKG-2 - [N24001406],NHIDCL,NAGALAND	7/2021	3/2023 (2/2023) [6/2023]	258.52 (-) [258.52]	57.58 (0.00) [0]	0/4
1087	FOUR LANING OF JAMMU-AKHNOOR PKG-1 - [N24001543],NHIDCL,JAMMU AND KASHMIR	7/2022	1/2025 (-) [1/2025]	245.34 (-) [245.34]	3.94 (0.00) [0]	0/0
1088	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275],NHIDCL,MANIPUR	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	22.08 (0.00) [0]	0/4
1089	TAMENGLONG - MAHUR PKG-1 - [N24001402],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	52.65 (0.00) [0]	2/4
1090	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL -	7/2020	4/2022 (6/2023) [3/2024]	228.39 (-) [228.39]	36.59 (0.00) [23]	2/4

	[N24001264],NHIDCL,JAMMU AND KASHMIR					
1091	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278],NHIDCL,MIZORAM	3/2020	7/2022 (8/2023) [12/2023]	206.88 (219.33) [278.98]	227.33 (72.10) [17]	2/4
1092	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [9/2023]	525.68 (-) [525.68]	357.03 (0.00) [-3]	3/4
1093	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320],NHIDCL,ASSAM	6/2015	3/2024 (-) [3/2024]	463.49 (-) [463.49]	284.31 (0.00) [0]	2/4
1094	IMPHAL - KHONGSANG PKG-2 - [N24001353],NHIDCL,MANIPUR	3/2021	12/2022 (-) [11/2023]	195.14 (-) [195.14]	34.94 (0.00) [11]	1/4
1095	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (11/2023) [11/2023]	184.88 (-) [184.88]	71.91 (0.00) [19]	2/4
1096	IMPHAL - KHONGSANG PKG-6 - [N24001539],NHIDCL,MANIPUR	12/2021	2/2025 (-) [2/2025]	504.76 (-) [504.76]	16.43 (0.00) [0]	0/0
1097	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG-2A) - [N24001270],NHIDCL,MANIPUR	3/2020	6/2022 (-) [5/2023]	292.24 (-) [292.24]	127.86 (0.00) [0]	3/4
1098	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741],NHIDCL,UTTARAKHAND	3/2018	11/2020 (12/2022) [12/2023]	274.31 (-) [274.31]	240.98 (0.00) [37]	3/4
1099	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (7/2023) [7/2023]	228.71 (-) [228.71]	90.14 (0.00) [15]	3/4
1100	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743],NHIDCL,UTTARAKHAND	3/2018	11/2020 (12/2022) [4/2024]	417.24 (-) [417.24]	337.20 (0.00) [41]	3/4
1101	MARAM - PEREN PKG-3 - [N24001439],NHIDCL,MANIPUR	8/2021	5/2023 (-) [11/2023]	467.41 (-) [467.41]	126.80 (0.00) [6]	2/4
1102	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767],NHIDCL,SIKKIM	3/2017	4/2022 (5/2022) [12/2023]	375.80 (-) [375.80]	270.63 (0.00) [20]	3/4
1103	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246],NHIDCL,ASSAM	3/2020	12/2022 (-) [8/2023]	220.20 (-) [220.20]	168.60 (0.00) [8]	2/4
1104	TAMENGLONG - MAHUR PKG-4 - [N24001404],NHIDCL,MANIPUR	7/2021	3/2023 (-) [4/2023]	198.77 (-) [198.77]	53.84 (0.00) [0]	2/4

1105	KARGIL-ZANSKR PACKAGE-3 - [N24001345],NHIDCL,LADAKH	8/2020	1/2023 (10/2023) [10/2023]	381.01 (-) [381.01]	83.24 (0.00) [9]	1/4
1106	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687],NHIDCL,NAGALAND	3/2016	8/2019 (8/2019) [9/2023]	396.52 (519.72) [396.52]	330.51 (0.00) [49]	3/4
1107	AJANTHA TO BULDHANA - [N24001008],NHIDCL,ANDAMAN AND NICOBAR ISLANDS	2/2017	7/2019 (-) [9/2023]	401.00 (401.00) [401.00]	260.08 (0.00) [50]	2/4
1108	PATAS-VASUNDE PHATA - BARAMATI BYPASS - [N24001501],NHAI,MAHARASHTRA	9/2021	9/2023 (9/2023) [9/2023]	531.86 (532.41) [532.41]	489.85 (0.55) [0]	0/0
1109	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V - [N24001483],NHAI,TELANGANA	2/2022	9/2024 (-) [9/2024]	637.11 (-) [637.11]	162.16 (0.00) [0]	0/0
1110	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K - [N24001736],NHAI,UTTAR PRADESH	1/2022	8/2024 (-) [8/2024]	1,159.96 (-) [1,159.96]	268.31 (0.00) [0]	0/0
1111	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO - [N24001609],NHAI,MAHARASHTRA	1/2023	12/2023 (-) [12/2023]	151.26 (-) [151.26]	15.85 (0.00) [0]	0/0
1112	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 - [N24001625],NHAI,TELANGANA	1/2022	1/2025 (-) [1/2025]	1,227.57 (-) [1,227.57]	4.98 (0.00) [0]	0/0
1113	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214],NHAI,MADHYA PRADESH	12/2017	12/2022 (-) [8/2023]	217.96 (-) [884.00]	2,298.00 (666.04) [8]	3/4
1114	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182],NHAI,MULTI STATE	9/2011	3/2014 (-) [6/2024]	2,848.00 (-) [3,379.45]	3,656.21 (531.45) [123]	0/0
1115	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725],NHAI,JHARKHAND	1/2018	11/2021 (-) [6/2023]	273.46 (-) [276.17]	219.58 (2.71) [0]	0/0
1116	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A - [N24001823],NHAI,ANDHRA PRADESH	1/2022	1/2025 (1/2023) [1/2025]	1,852.12 (-) [1,787.00]	255.61 (-65.12) [0]	0/4
1117	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) - [N24001792],NHAI,GUJARAT	3/2021	9/2022 (-) [12/2023]	536.03 (-) [536.03]	350.00 (0.00) [15]	0/0
1118	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825],NHAI,TELANGANA	3/2018	2/2023 (6/2023) [8/2023]	828.29 (1,140.50) [828.29]	448.81 (0.00) [6]	0/0

1119	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 - [N24001519],NHAI,GUJARAT	9/2020	11/2023 (-) [11/2023]	1,198.55 (-) [1,198.55]	431.31 (0.00) [0]	0/0
1120	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559],NHAI,UTTARAKHAND	3/2016	10/2019 (3/2024) [3/2024]	720.00 (810.60) [810.60]	348.45 (90.60) [53]	2/4
1121	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS - [N24001692],NHAI,TAMIL NADU	1/2022	9/2024 (-) [9/2024]	467.99 (-) [468.00]	18.83 (0.01) [0]	0/0
1122	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) - [N24001546],NHAI,MAHARASHTRA	1/2023	1/2025 (-) [1/2025]	1,025.20 (-) [1,025.20]	80.27 (0.00) [0]	0/4
1123	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298],NHAI,ANDHRA PRADESH	9/2018	1/2020 (7/2024) [7/2024]	597.67 (641.90) [641.90]	610.69 (44.23) [54]	0/0
1124	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) - [N24001507],NHAI,MAHARASHTRA	11/2022	5/2024 (-) [5/2024]	1,124.00 (-) [1,124.00]	116.71 (0.00) [0]	0/0
1125	4L PS OF MEERUT TO AFTER BRIDGE OVER RIVER YAMUNA, HARYANA VIA SHAMLI-FROM KM. 0.00 TO KM. 88.476 OF - [N24001741],NHAI,UTTAR PRADESH	9/2020	1/2023 (-) [6/2023]	798.96 (-) [798.96]	585.30 (0.00) [0]	0/0
1126	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) - [N24001553],NHAI,UTTARAKHAND	3/2022	2/2025 (-) [2/2025]	1,092.90 (1,092.90) [1,092.90]	0.03 (0.00) [0]	0/0
1127	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] - [N24001761],NHAI,MADHYA PRADESH	2/2023	2/2025 (-) [2/2025]	520.28 (-) [520.28]	75.46 (0.00) [0]	0/0
1128	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-4) - [N24001575],NHAI,RAJASTHAN	10/2019	11/2022 (9/2023) [5/2023]	598.01 (-) [598.01]	405.20 (0.00) [0]	0/0
1129	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739],NHAI,UTTAR PRADESH	10/2019	11/2023 (-) [11/2023]	1,779.83 (-) [2,200.00]	708.00 (420.17) [0]	0/0
1130	TUNNEL AT KHAMBATAKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 - [N24001486],NHAI,MAHARASHTRA	2/2019	2/2022 (3/2023) [12/2023]	493.00 (-) [493.00]	374.15 (0.00) [22]	0/0
1131	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) - [N24001600],NHAI,TAMIL NADU	10/2020	5/2023 (10/2023) [10/2023]	434.12 (-) [434.12]	161.17 (0.00) [5]	0/0
1132	6 LANING OF EXISTING 4-LANE	3/2022	1/2025	955.49	84.06	0/0

	STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, - [N24001555],NHAI,TELANGANA		(-) [1/2025]	(-) [955.49]	(0.00) [0]	
1133	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828],NHAI,TAMIL NADU	3/2018	9/2023 (8/2023) [8/2023]	633.55 (736.33) [736.33]	194.97 (102.78) [-1]	0/0
1134	6L OF BADA KUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE – OD-3) - [N24001668],NHAI,ODISHA	3/2021	4/2024 (-) [4/2024]	1,249.00 (-) [1,249.00]	0.00 (0.00) [0]	0/0
1135	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 - [N24001696],NHAI,TAMIL NADU	2/2019	8/2023 (-) [8/2023]	1,291.37 (-) [1,291.37]	215.02 (0.00) [0]	0/0
1136	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K - [N24001717],NHAI,TAMIL NADU	11/2020	8/2024 (-) [8/2024]	1,155.49 (-) [1,155.49]	227.66 (0.00) [0]	0/0
1137	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556],NHAI,UTTAR PRADESH	3/2016	4/2019 (2/2024) [2/2024]	899.00 (1,381.45) [1,381.45]	939.15 (482.45) [58]	3/4
1138	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH - [N24001722],NHAI,TAMIL NADU	11/2021	2/2023 (-) [5/2023]	463.44 (-) [464.00]	0.00 (0.56) [0]	0/0
1139	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M - [N24001689],NHAI,KARNATAKA	12/2020	9/2023 (-) [9/2023]	1,745.00 (-) [1,279.00]	822.13 (-466.00) [0]	0/0
1140	BALANCE WORK UNDER PHASE-I FOR 4L OF KHED SINER SECTION COMPRISING OF THE STRETCHES (I) KHED BYPASS - [N24001487],NHAI,MAHARASHTRA	10/2020	10/2022 (6/2023) [6/2023]	169.83 (-) [169.83]	201.04 (0.00) [0]	0/0
1141	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 - [N24001616],NHAI,MADHYA PRADESH	1/2021	10/2023 (-) [10/2023]	428.04 (-) [328.77]	291.27 (-99.27) [0]	0/0
1142	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 - [N24001443],NHAI,GUJARAT	5/2020	3/2024 (-) [3/2024]	690.30 (-) [690.30]	422.62 (0.00) [0]	2/4
1143	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA - [N24001682],NHAI,KARNATAKA	3/2022	3/2024 (3/2024) [3/2024]	294.62 (-) [294.62]	5.40 (0.00) [0]	0/4
1144	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR	12/2021	7/2025 (7/2025) [7/2025]	1,972.10 (-) [1,936.00]	158.30 (-36.10) [0]	0/0

	LUCKNOW EXPRESSWAY (N - [N24001745],NHAI,UTTAR PRADESH					
1145	8L OF GUDUVANCHERY (KM 38.00) - MARAIMALAI NAGAR (KM 42.00) - SINGAPERUMAL KOIL (47.00) - CHETTIPU - [N24001695],NHAI,TAMIL NADU	12/2020	2/2022 (-) [8/2023]	230.69 (-) [230.69]	174.08 (0.00) [18]	0/0
1146	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 - [N24001676],NHAI,KARNATAKA	12/2022	6/2025 (-) [6/2025]	2,718.46 (-) [2,718.46]	0.00 (0.00) [0]	0/4
1147	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629],NHAI,MAHARASHTRA	11/2016	3/2019 (7/2023) [7/2023]	400.25 (-) [304.07]	299.26 (-96.18) [52]	0/0
1148	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233],NHAI,MADHYA PRADESH	3/2019	5/2020 (3/2023) [8/2023]	1,047.00 (-) [1,047.00]	1,169.00 (0.00) [39]	2/3
1149	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 - [N24001628],NHAI,MULTI STATE	11/2021	2/2025 (-) [2/2025]	2,155.95 (-) [2,155.95]	793.18 (0.00) [0]	0/0
1150	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR - [N24001772],NHAI,UTTAR PRADESH	8/2021	3/2024 (-) [3/2024]	1,147.26 (-) [1,147.26]	49.00 (0.00) [0]	0/0
1151	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA - [N24001593],NHAI,CHHATTISGARH	11/2021	9/2024 (-) [9/2024]	1,368.19 (-) [1,368.19]	595.79 (0.00) [0]	0/0
1152	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR - [N24001557],NHAI,RAJASTHAN	3/2022	11/2024 (-) [11/2024]	1,636.15 (-) [1,636.15]	281.01 (0.00) [0]	0/0
1153	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415],NHAI,PUNJAB	12/2020	4/2024 (7/2024) [7/2024]	881.00 (-) [881.00]	546.76 (0.00) [3]	1/1
1154	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S - [N24001610],NHAI,MAHARASHTRA	1/2022	5/2024 (5/2024) [5/2024]	1,833.73 (-) [1,833.73]	126.16 (0.00) [0]	0/0
1155	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] - [N24001590],NHAI,JHARKHAND	9/2020	10/2023 (-) [10/2023]	748.99 (-) [903.00]	675.22 (154.01) [0]	0/0
1156	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK - [N24001559],NHAI,RAJASTHAN	9/2021	6/2024 (-) [6/2024]	672.35 (-) [672.35]	224.87 (0.00) [0]	0/0
1157	VARANASI RING ROAD (PKG-II)	2/2019	2/2022	927.77	1,104.18	0/1

	CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826],NHAI,UTTAR PRADESH		(-) [10/2023]	(-) [1,603.00]	(675.23) [20]	
1158	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721],NHAI,TAMIL NADU	2/2019	5/2024 (-) [5/2024]	1,008.99 (-) [1,361.00]	12.42 (352.01) [0]	0/0
1159	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755],NHAI,UTTAR PRADESH	10/2019	3/2023 (-) [8/2023]	1,936.68 (-) [2,458.03]	1,380.90 (521.35) [5]	0/0
1160	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213],NHAI,MADHYA PRADESH	12/2017	2/2022 (11/2022) [8/2023]	1,094.97 (-) [1,094.97]	1,188.00 (0.00) [18]	3/4
1161	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI - [N24001624],NHAI,JAMMU AND KASHMIR	7/2019	10/2020 (4/2023) [8/2023]	157.05 (-) [157.05]	109.95 (0.00) [34]	3/4
1162	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0 - [N24001645],NHAI,PUNJAB	12/2020	6/2023 (8/2023) [8/2023]	366.85 (366.85) [366.85]	252.03 (0.00) [2]	0/0
1163	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP - [N24001824],NHAI,ANDHRA PRADESH	3/2020	1/2024 (1/2022) [1/2024]	1,863.09 (-) [2,238.00]	894.15 (374.91) [0]	0/4
1164	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N - [N24001568],NHAI,RAJASTHAN	11/2019	5/2023 (10/2023) [7/2023]	1,119.35 (-) [1,119.35]	1,108.34 (0.00) [2]	0/0
1165	6 L OF AURANGABAD TO BIHAR-JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N - [N24001703],NHAI,BIHAR	2/2022	5/2025 (-) [5/2025]	786.81 (787.00) [787.00]	0.00 (0.19) [0]	0/0
1166	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR - [N24001652],NHAI,KERALA	3/2020	6/2022 (1/2023) [12/2023]	210.37 (213.06) [213.06]	171.75 (2.69) [18]	0/0
1167	FOUR LANING OF AURANGABAD-PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . - [N24001795],NHAI,MAHARASHTRA	10/2022	7/2024 (-) [7/2024]	490.40 (-) [289.00]	13.29 (-201.40) [0]	0/0
1168	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF - [N24001526],NHAI,UTTARAKHAND	8/2021	10/2024 (10/2024) [10/2024]	1,377.79 (1,384.11) [1,377.79]	678.86 (0.00) [0]	0/0
1169	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE -	8/2021	8/2023 (-) [12/2023]	557.55 (-) [557.55]	393.31 (0.00) [4]	0/0

	[N24001749],NHAI,WEST BENGAL					
1170	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE -- - [N24001678],NHAI,ODISHA	8/2021	6/2024 (-) [6/2024]	1,460.00 (1,460.00) [1,460.00]	0.00 (0.00) [0]	0/0
1171	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649],NHAI,GUJARAT	1/2017	12/2020 (10/2023) [10/2023]	1,251.11 (-) [1,361.00]	563.93 (109.89) [34]	3/4
1172	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. - [N24001734],NHAI,UTTAR PRADESH	3/2022	8/2024 (-) [8/2024]	1,335.45 (-) [1,335.45]	173.11 (0.00) [0]	0/0
1173	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812],NHAI,HIMACHAL PRADESH	3/2021	5/2024 (-) [5/2024]	1,002.11 (1,247.93) [1,358.00]	28.69 (355.89) [0]	0/0
1174	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212],NHAI,MADHYA PRADESH	12/2017	11/2022 (-) [8/2023]	656.98 (-) [840.00]	1,103.00 (183.02) [9]	2/4
1175	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) - [N24001558],NHAI,RAJASTHAN	11/2021	8/2024 (-) [8/2024]	736.75 (-) [736.75]	61.63 (0.00) [0]	0/0
1176	4L MISSING LINK (OF REWA BYPASS) FROM JN. WITH NH 30 NEAR BELA TO JN. WITH MPRDC RING ROAD (NEAR SIL - [N24001617],NHAI,MADHYA PRADESH	2/2021	1/2023 (-) [12/2023]	197.87 (-) [197.87]	35.62 (0.00) [11]	0/0
1177	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: - [N24001702],NHAI,BIHAR	12/2021	9/2024 (-) [9/2024]	184.90 (185.00) [185.00]	79.79 (0.10) [0]	0/0
1178	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 - [N24001638],NHAI,PUNJAB	11/2021	7/2024 (7/2024) [7/2024]	646.42 (646.42) [646.42]	158.90 (0.00) [0]	0/0
1179	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699],NHAI,ODISHA	7/2017	11/2020 (6/2021) [5/2023]	476.56 (780.37) [780.37]	311.77 (303.81) [0]	0/0
1180	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798],NHAI,UTTAR PRADESH	3/2018	11/2021 (-) [3/2024]	2,140.93 (-) [2,140.93]	1,912.14 (0.00) [28]	0/0
1181	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603],NHAI,KARNATAKA	8/2016	3/2019 (5/2025) [5/2025]	1,167.42 (-) [870.00]	408.72 (-297.42) [74]	2/4
1182	NAGPUR RING ROAD PACKAGE-1 - [N24000558],NHAI,MAHARASHTRA	3/2016	7/2019 (7/2023) [12/2023]	546.00 (-) [546.00]	450.68 (0.00) [53]	3/3

1183	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 - [N24001551],NHAI,JAMMU AND KASHMIR	10/2021	9/2024 (-) [9/2024]	3,044.02 (3,044.02) [3,044.02]	214.97 (0.00) [0]	0/0
1184	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY - [N24001511],NHAI,JAMMU AND KASHMIR	3/2021	2/2024 (8/2024) [8/2024]	2,919.96 (-) [2,919.96]	1,659.64 (0.00) [6]	1/4
1185	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE OF - [N24001635],NHAI,HARYANA	3/2022	2/2025 (-) [2/2025]	1,269.50 (-) [1,269.50]	35.00 (0.00) [0]	0/0
1186	6L OF HATIBENA - BADAUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE – OD-2) - [N24001671],NHAI,ODISHA	2/2021	3/2024 (-) [3/2024]	925.00 (-) [925.00]	0.00 (0.00) [0]	0/0
1187	ALIGARH-KANPUR SECTION PACKAGEV FROM MITRASEN-KANPUR - [N24001740],NHAI,UTTAR PRADESH	10/2019	9/2023 (-) [10/2023]	2,325.28 (-) [2,325.28]	1,836.49 (0.00) [1]	0/0
1188	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) - [N24001503],NHAI,MAHARASHTRA	9/2021	9/2023 (9/2023) [3/2024]	667.66 (666.21) [666.21]	329.65 (-1.45) [6]	0/0
1189	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630],NHAI,MAHARASHTRA	11/2016	3/2019 (-) [12/2023]	446.17 (-) [356.62]	318.13 (-89.55) [57]	0/0
1190	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718],NHAI,ANDHRA PRADESH	12/2017	6/2019 (5/2023) [8/2023]	328.67 (416.07) [416.07]	333.18 (87.40) [50]	0/0
1191	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 - [N24001842],NHAI,ANDHRA PRADESH	12/2022	11/2025 (-) [11/2025]	750.81 (-) [750.81]	22.03 (0.00) [0]	0/0
1192	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI - [N24001642],NHAI,PUNJAB	2/2021	8/2024 (-) [8/2024]	1,474.77 (-) [1,474.77]	146.71 (0.00) [0]	0/0
1193	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG – II) - [N24001834],NHAI,MAHARASHTRA	5/2023	5/2025 (-) [5/2025]	839.00 (-) [839.00]	4.51 (0.00) [0]	0/4
1194	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 - [N24001679],NHAI,KARNATAKA	10/2022	4/2025 (4/2025) [4/2025]	1,479.30 (-) [1,479.30]	86.76 (0.00) [0]	1/4
1195	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) - [N24001504],NHAI,MAHARASHTRA	5/2022	5/2024 (-) [5/2024]	1,260.00 (-) [1,260.00]	295.36 (0.00) [0]	0/0
1196	4L OF KODAD (DESIGN KM	1/2021	1/2024	1,307.95	420.17	0/0

	0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 - [N24001522],NHAI,TELANGANA		(-) [1/2024]	(-) [1,307.95]	(0.00) [0]	
1197	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835],NHAI,HARYANA	3/2018	12/2020 (8/2023) [5/2023]	1,484.30 (-) [2,182.41]	1,219.02 (698.11) [0]	0/0
1198	AURAD - BIDAR KM 0.00 TO KM 45.878 - [N24001683],NHAI,KARNATAKA	9/2021	4/2023 (-) [9/2023]	912.37 (-) [912.37]	222.63 (0.00) [5]	0/4
1199	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT - [N24001785],NHAI,GUJARAT	3/2022	6/2025 (-) [6/2025]	1,373.06 (1,085.00) [1,373.06]	202.38 (0.00) [0]	0/0
1200	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377],NHAI,MAHARASHTRA	2/2019	1/2022 (5/2023) [8/2023]	731.89 (731.99) [731.99]	626.45 (0.10) [19]	3/3
1201	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 - [N24001778],NHAI,DELHI	7/2020	10/2023 (-) [10/2023]	801.46 (-) [801.46]	382.03 (0.00) [0]	0/0
1202	BALANCE WORKS OF 4L AMRAVATI CHIKHLI (PKG IV) [NANDURA TO CHIKHLI FROM KM. 315.00 TO KM. 360.00] - [N24001802],NHAI,MAHARASHTRA	11/2019	5/2023 (-) [8/2023]	583.61 (-) [583.61]	237.57 (0.00) [3]	0/0
1203	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199],NHAI,MADHYA PRADESH	10/2019	12/2021 (11/2022) [8/2023]	743.88 (-) [743.89]	832.00 (0.01) [20]	2/3
1204	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501],NHAI,BIHAR	8/2015	4/2018 (8/2023) [8/2023]	322.09 (-) [322.09]	282.54 (0.00) [64]	0/0
1205	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655],NHAI,MAHARASHTRA	3/2017	3/2020 (-) [6/2023]	247.02 (-) [157.49]	70.50 (-89.53) [0]	0/0
1206	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF - [N24001808],NHAI,HIMACHAL PRADESH	3/2021	12/2024 (12/2024) [12/2024]	1,322.95 (1,442.47) [1,442.47]	498.17 (119.52) [0]	0/0
1207	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416],NHAI,PUNJAB	12/2020	1/2024 (3/2025) [3/2025]	989.66 (-) [989.66]	46.35 (0.00) [14]	0/0
1208	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-16) (CH. 427.300 TO CH.452.420) [MAJOR BRIDGE OVE - [N24001572],NHAI,RAJASTHAN	11/2019	1/2023 (10/2023) [6/2023]	952.57 (-) [952.57]	791.27 (0.00) [0]	0/0
1209	VADODARA MUMBAI EXPRESSWAY	9/2021	7/2025	2,208.68	56.93	0/0

	(PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) - [N24001608],NHAI,MAHARASHTRA		(-) [7/2025]	(-) [2,208.68]	(0.00) [0]	
1210	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 (-) [N24001495],NHAI,MAHARASHTRA	11/2022	11/2024 (-) [11/2024]	930.00 (-) [930.00]	104.34 (0.00) [0]	0/4
1211	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) - [N24001697],NHAI,BIHAR	2/2023	2/2025 (-) [2/2025]	1,358.00 (-) [1,358.00]	0.65 (0.00) [0]	0/0
1212	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N - [N24001640],NHAI,PUNJAB	3/2021	11/2024 (-) [11/2024]	1,229.38 (-) [1,229.38]	499.62 (0.00) [0]	0/0
1213	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 - [N24001515],NHAI,GUJARAT	9/2020	2/2024 (-) [2/2024]	1,542.02 (-) [1,542.02]	363.32 (0.00) [0]	0/0
1214	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834],NHAI,GUJARAT	3/2018	10/2021 (3/2024) [3/2024]	1,161.39 (1,404.00) [1,404.00]	396.76 (242.61) [29]	0/0
1215	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA - [N24001630],NHAI,PUNJAB	7/2021	2/2025 (-) [2/2025]	1,501.02 (-) [1,501.02]	33.00 (0.00) [0]	0/0
1216	4L OF ADDAHOLE TO BANTWAL CROSS SECTION - [N24001426],NHAI,KARNATAKA	3/2021	10/2021 (9/2023) [9/2023]	317.90 (317.90) [317.90]	214.13 (0.00) [23]	3/4
1217	CONSTRUCTION OF 4 LANE BANGALORE -CHENNAI EXPRESSWAY FROM KM 53.500 TO KM 71.000 SECTION OF NE-7 (BA - [N24001685],NHAI,KARNATAKA	1/2021	1/2024 (-) [1/2024]	1,069.00 (-) [863.00]	508.94 (-206.00) [0]	0/0
1218	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 - [N24001845],NHAI,ANDHRA PRADESH	2/2023	10/2025 (-) [10/2025]	1,253.24 (-) [1,253.24]	68.47 (0.00) [0]	0/0
1219	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205],NHAI,ODISHA	12/2011	6/2014 (12/2023) [12/2023]	1,047.00 (-) [1,047.00]	1,855.00 (0.00) [114]	0/0
1220	MEDSHI (KM 47.700) TO WASHIM (KM 92.200) OF NH-161 IN MAHARASHTRA - [N24001807],NHAI,MAHARASHTRA	2/2018	10/2021 (5/2023) [5/2023]	1,061.29 (1,061.29) [683.10]	685.97 (-378.19) [0]	0/0
1221	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507],NHAI,BIHAR	12/2015	12/2019 (-) [12/2023]	1,167.45 (-) [1,182.94]	589.65 (15.49) [48]	0/0
1222	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. - [N24001846],NHAI,ANDHRA PRADESH	2/2023	10/2025 (-) [10/2025]	1,200.42 (-) [1,200.42]	56.79 (0.00) [0]	0/0
1223	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN	11/2019	2/2021 (8/2023)	1,226.88 (1,569.68)	1,054.39 (342.80)	0/0

	CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300],NHAI,ANDHRA PRADESH		[8/2023]	[1,569.68]	[30]	
1224	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234],NHAI,MADHYA PRADESH	2/2019	3/2022 (11/2022) [8/2023]	996.27 (-) [996.27]	1,079.00 (0.00) [17]	3/3
1225	DWARKA EXPRESSWAY FROM KM - 0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779],NHAI,DELHI	3/2018	9/2022 (-) [12/2023]	2,507.00 (-) [3,030.73]	1,155.70 (523.73) [15]	0/0
1226	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-5) - [N24001613],NHAI,RAJASTHAN	10/2019	3/2023 (9/2023) [5/2023]	584.37 (-) [584.37]	429.13 (0.00) [0]	0/0
1227	SANGARIYA (NEAR CHAUTALA)- RASISAR (NEAR BIKANER) (AJ/SR-PACKAGE-9) - [N24001586],NHAI,RAJASTHAN	2/2019	6/2022 (9/2023) [6/2023]	656.57 (-) [656.57]	559.31 (0.00) [0]	0/0
1228	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) - [N24001820],NHAI,ANDHRA PRADESH	2/2021	12/2024 (-) [12/2024]	1,484.83 (-) [1,768.00]	383.07 (283.17) [0]	0/4
1229	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION - [N24001444],NHAI,GUJARAT	5/2020	1/2024 (-) [3/2024]	882.00 (-) [882.00]	319.15 (0.00) [2]	2/4
1230	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION - [N24001488],NHAI,MAHARASHTRA	9/2021	9/2023 (-) [9/2023]	618.45 (-) [618.45]	353.77 (0.00) [0]	0/0
1231	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711],NHAI,RAJASTHAN	12/2017	12/2020 (-) [2/2024]	1,308.73 (-) [1,308.73]	309.04 (0.00) [38]	0/0
1232	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-3) - [N24001574],NHAI,RAJASTHAN	2/2019	12/2022 (9/2023) [5/2023]	820.19 (-) [820.19]	7.37 (0.00) [0]	0/0
1233	INTEGRATED STRUCTURE WITH DEVELOPMENT OF OTHER ALLIED STRUCTURES ON BOTH SIDES OF CHANDNI CHOWK JUNC - [N24001485],NHAI,MAHARASHTRA	2/2019	2/2022 (-) [8/2023]	397.60 (-) [397.60]	335.38 (0.00) [18]	0/0
1234	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE - [N24001648],NHAI,KERALA	8/2022	1/2026 (-) [1/2026]	2,429.52 (-) [2,429.52]	0.00 (0.00) [0]	0/0
1235	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781],NHAI,DELHI	1/2018	10/2021 (-) [11/2023]	2,067.67 (-) [2,160.00]	1,496.49 (92.33) [25]	0/0
1236	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH.	11/2019	5/2023 (8/2023)	1,640.10 (-)	1,099.00 (0.00)	0/0

	319.400 TO CH. 331.030) [HARDEOGANJ VILL - [N24001566],NHAI,RAJASTHAN		[5/2023]	[1,640.10]	[0]	
1237	4-LANNING OF WARANGA- MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659],NHAI,MAHARASHTRA	3/2017	3/2017 (5/2021) [6/2023]	1,059.73 (1,071.00) [1,071.00]	837.73 (11.27) [0]	0/0
1238	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 - [N24001770],NHAI,MADHYA PRADESH	2/2022	3/2024 (-) [3/2024]	417.51 (-) [417.51]	52.14 (0.00) [0]	0/0
1239	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K - [N24001637],NHAI,PUNJAB	3/2021	1/2025 (-) [1/2025]	1,754.84 (-) [1,754.84]	758.50 (0.00) [0]	0/0
1240	4L OF HARDA - BETUL (PKG-I) FROM KM.0 TO KM.30 [HARDA - TEMAGAON] - [N24001763],NHAI,MADHYA PRADESH	9/2021	9/2023 (-) [9/2023]	774.16 (-) [774.16]	336.63 (0.00) [0]	0/0
1241	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692],NHAI,HIMACHAL PRADESH	6/2017	6/2020 (-) [3/2024]	2,485.93 (-) [2,485.93]	1,433.11 (0.00) [45]	0/0
1242	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231],NHAI,MADHYA PRADESH	2/2019	12/2021 (9/2022) [8/2023]	990.97 (-) [990.97]	1,092.00 (0.00) [20]	3/3
1243	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658],NHAI,KERALA	1/2021	7/2024 (-) [7/2024]	4,265.42 (-) [4,708.42]	2,751.50 (443.00) [0]	0/0
1244	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A - [N24001690],NHAI,KARNATAKA	1/2021	1/2023 (12/2023) [6/2023]	1,167.52 (1,157.00) [1,167.52]	802.91 (0.00) [0]	0/0
1245	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II - [N24001744],NHAI,UTTAR PRADESH	5/2019	11/2022 (-) [12/2023]	779.17 (-) [779.17]	0.00 (0.00) [13]	0/0
1246	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 - [N24001720],NHAI,TAMIL NADU	10/2020	5/2024 (-) [5/2024]	1,023.91 (-) [1,285.00]	318.78 (261.09) [0]	0/0
1247	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726],NHAI,JHARKHAND	1/2018	11/2021 (-) [11/2023]	1,155.16 (-) [950.49]	564.62 (-204.67) [24]	0/0
1248	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379],NHAI,MAHARASHTRA	2/2019	1/2022 (5/2023) [8/2023]	594.75 (594.75) [613.75]	532.55 (19.00) [19]	4/4
1249	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO	3/2021	3/2024 (-) [12/2024]	1,259.00 (-) [1,910.00]	60.25 (651.00) [9]	0/0

	KM 128.000 OF VADODARA MU - [N24001786],NHAI,GUJARAT					
1250	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303],NHAI,BIHAR	10/2013	12/2020 (-) [12/2023]	649.90 (-) [649.90]	456.06 (0.00) [36]	0/0
1251	FOUR LANING OF SOLAN- KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852],NHAI,HIMACHAL PRADESH	3/2018	5/2021 (11/2022) [1/2024]	478.74 (-) [1,136.83]	1,016.30 (658.09) [32]	0/0
1252	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340],NHAI,MADHYA PRADESH	11/2019	7/2021 (11/2023) [7/2023]	716.00 (-) [716.00]	334.38 (0.00) [24]	0/0
1253	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595],NHAI,JHARKHAND	8/2020	3/2024 (-) [3/2024]	1,034.00 (-) [1,589.00]	41.50 (555.00) [0]	0/0
1254	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG- IV - [N24000691],NHAI,RAJASTHAN	4/2017	4/2020 (9/2023) [9/2023]	894.00 (-) [929.32]	880.00 (35.32) [41]	0/0
1255	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO - [N24001634],NHAI,HARYANA	1/2021	12/2023 (-) [12/2023]	1,306.95 (-) [1,306.95]	761.02 (0.00) [0]	0/0
1256	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417],NHAI,PUNJAB	12/2020	4/2024 (7/2024) [7/2024]	1,234.40 (-) [1,234.40]	344.12 (0.00) [3]	0/1
1257	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA - [N24001472],NHAI,JAMMU AND KASHMIR	9/2021	12/2023 (1/2024) [1/2024]	811.19 (-) [811.19]	593.45 (0.00) [1]	0/0
1258	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI - [N24001548],NHAI,ASSAM	3/2022	6/2024 (-) [6/2024]	457.72 (-) [457.72]	33.65 (0.00) [0]	0/0
1259	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844],NHAI,ODISHA	3/2018	4/2021 (9/2023) [9/2023]	806.11 (767.45) [767.45]	737.93 (-38.66) [29]	0/0
1260	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR - DEHRADUN SECTION FROM KM. - [N24001525],NHAI,UTTARAKHAND	3/2021	3/2024 (3/2024) [3/2024]	169.08 (-) [169.08]	60.65 (0.00) [0]	0/0
1261	4-LANNING OF CHAPRA-HAJIPUR - [N24000187],NHAI,BIHAR	1/2011	7/2013 (6/2023) [6/2023]	575.00 (-) [575.00]	519.82 (0.00) [0]	2/3
1262	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND	3/2018	12/2021 (12/2023) [12/2023]	1,117.84 (-) [1,117.84]	699.89 (0.00) [24]	0/0

	TERMINATING AT SITAPUR RO - [N24000796],NHAI,UTTAR PRADESH					
1263	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714],NHAI,BIHAR	12/2017	10/2024 (10/2024) [10/2024]	2,598.00 (-) [1,962.50]	1,012.87 (-635.50) [0]	0/0
1264	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480],NHAI,BIHAR	12/2015	4/2019 (7/2022) [3/2024]	1,041.10 (567.00) [639.58]	530.28 (-401.52) [59]	0/0
1265	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG-III) - [N24001835],NHAI,MAHARASHTRA	5/2023	5/2025 (-) [5/2025]	986.00 (-) [986.00]	0.00 (0.00) [0]	0/4
1266	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813],NHAI,BIHAR	3/2018	11/2021 (-) [6/2023]	496.20 (-) [537.17]	282.48 (40.97) [0]	0/0
1267	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 - [N24001797],NHAI,MAHARASHTRA	10/2021	1/2024 (-) [1/2024]	815.77 (-) [815.77]	227.75 (0.00) [0]	0/0
1268	4 LANING OF PATHRAPALI TO KATGHORA FROM KM.53.300 TO KM.92.600 - [N24001592],NHAI,CHHATTISGARH	11/2019	12/2022 (3/2023) [8/2023]	865.10 (-) [865.10]	655.41 (0.00) [8]	0/0
1269	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP - [N24001534],NHAI,HARYANA	12/2020	1/2024 (3/2024) [3/2024]	1,334.04 (-) [1,334.00]	717.42 (-0.04) [2]	0/0
1270	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656],NHAI,KERALA	6/2021	3/2025 (-) [3/2025]	2,595.00 (-) [3,994.60]	2,696.56 (1,399.60) [0]	0/0
1271	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-1) - [N24001562],NHAI,RAJASTHAN	2/2019	10/2023 (-) [10/2023]	738.90 (-) [738.90]	778.02 (0.00) [0]	0/0
1272	6L KORLAM-KANTAKAPALLE SECTION OF NH-130CD ROAD FROM KM 421.100 TO KM 445.100 (PKG-3) - [N24001839],NHAI,ANDHRA PRADESH	2/2021	2/2024 (-) [2/2024]	772.70 (-) [980.51]	321.87 (207.81) [0]	0/4
1273	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA - [N24001567],NHAI,RAJASTHAN	11/2019	10/2022 (9/2023) [7/2023]	1,272.97 (-) [1,272.97]	330.25 (0.00) [9]	0/0
1274	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT-GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 - [N24001699],NHAI,BIHAR	3/2022	12/2024 (-) [12/2024]	312.58 (-) [312.58]	37.38 (0.00) [0]	0/0
1275	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 - [N24001432],NHAI,ASSAM	12/2021	8/2024 (-) [8/2024]	300.00 (-) [300.00]	223.00 (0.00) [0]	0/0

1276	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418],NHAI,PUNJAB	12/2020	4/2024 (7/2024) [7/2024]	1,094.46 (-) [1,094.46]	357.25 (0.00) [3]	0/1
1277	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723],NHAI,BIHAR	1/2018	12/2021 (12/2019) [3/2024]	573.70 (644.50) [726.99]	371.11 (153.29) [27]	0/0
1278	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO - [N24001712],NHAI,BIHAR	8/2020	7/2023 (-) [7/2023]	690.00 (-) [690.00]	594.41 (0.00) [0]	0/0
1279	PATNA-MUZZAFFARPUR - [N24000165],NHAI,BIHAR	8/2010	2/2013 (6/2023) [6/2023]	671.30 (-) [671.30]	1,591.71 (0.00) [0]	3/4
1280	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN - [N24001783],NHAI,HARYANA	11/2018	9/2021 (-) [8/2023]	2,252.75 (-) [2,252.75]	1,223.07 (0.00) [23]	0/0
1281	4L OF KHEDEKHAJURIYA TO SUHAGADI FROM KM. 41.400 TO KM. 89.200 OF NH-148NG (PKG-II) - [N24001757],NHAI,MADHYA PRADESH	1/2020	10/2024 (-) [6/2024]	876.37 (-) [876.37]	177.45 (0.00) [-4]	0/0
1282	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 - [N24001798],NHAI,MAHARASHTRA	2/2021	11/2023 (-) [11/2023]	540.21 (-) [540.21]	164.19 (0.00) [0]	0/0
1283	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI - [N24001704],NHAI,BIHAR	3/2021	3/2024 (-) [3/2024]	1,020.84 (-) [1,020.84]	84.78 (0.00) [0]	0/0
1284	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZZAFARNAGAR) AND NH-58 (MEERUT - [N24001726],NHAI,UTTAR PRADESH	1/2023	8/2024 (-) [8/2024]	391.26 (-) [391.26]	14.12 (0.00) [0]	0/0
1285	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] - [N24001762],NHAI,MADHYA PRADESH	10/2021	1/2024 (-) [1/2024]	1,146.22 (-) [1,146.22]	444.64 (0.00) [0]	0/0
1286	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462],NHAI,KARNATAKA	5/2014	8/2016 (6/2023) [7/2023]	1,655.01 (2,639.00) [2,639.00]	1,771.52 (983.99) [83]	4/4
1287	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S - [N24001571],NHAI,RAJASTHAN	11/2019	12/2023 (-) [12/2023]	1,341.36 (-) [1,341.36]	806.97 (0.00) [0]	0/0
1288	BANGALORE/TN BORDER TO HOSKOTE - [N24001674],NHAI,KARNATAKA	2/2023	2/2025 (-) [2/2025]	1,240.60 (-) [1,240.60]	403.45 (0.00) [0]	0/0
1289	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED	8/2022	10/2024 (-)	772.11 (-)	234.08 (0.00)	0/0

	(GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM - [N24001482],NHAI,TELANGANA		[10/2024]	[772.11]	[0]	
1290	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736],NHAI,ODISHA	1/2018	9/2020 (-) [12/2023]	686.65 (504.09) [1,015.16]	355.84 (328.51) [39]	0/0
1291	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) - [N24001506],NHAI,MAHARASHTRA	2/2022	2/2024 (-) [2/2024]	2,747.00 (-) [2,747.00]	544.65 (0.00) [0]	0/0
1292	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) - [N24001598],NHAI,KARNATAKA	1/2022	4/2025 (-) [4/2025]	1,388.70 (-) [1,388.70]	73.09 (0.00) [0]	0/4
1293	4L OF AHMEDNAGAR - MIRAJGAON - KARMALA - TEMBHURNI (PKG-I) [AHMEDNAGAR TO GHOGARGAON] FROM KM. 0.00 - [N24001498],NHAI,MAHARASHTRA	12/2021	12/2023 (-) [12/2023]	605.00 (605.00) [605.00]	415.21 (0.00) [0]	0/4
1294	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE - [N24001827],NHAI,GUJARAT	3/2022	3/2023 (-) [10/2023]	162.73 (-) [162.73]	54.00 (0.00) [7]	0/0
1295	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 - [N24001849],NHAI,ANDHRA PRADESH	5/2022	7/2025 (-) [7/2025]	1,063.72 (-) [1,063.72]	170.67 (0.00) [0]	0/0
1296	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656],NHAI,MAHARASHTRA	3/2017	3/2020 (7/2022) [7/2024]	744.64 (-) [1,007.00]	257.01 (262.36) [52]	0/0
1297	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH - [N24001660],NHAI,KERALA	8/2020	2/2024 (11/2021) [2/2024]	2,714.60 (3,319.41) [2,714.60]	1,414.01 (0.00) [0]	0/0
1298	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724],NHAI,BIHAR	1/2018	4/2024 (-) [3/2024]	895.39 (-) [895.39]	1,632.71 (0.00) [-1]	0/0
1299	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) - [N24001521],NHAI,MAHARASHTRA	11/2022	10/2024 (5/2024) [5/2024]	990.00 (-) [990.00]	153.78 (0.00) [-5]	0/0
1300	AHMEDNAGAR BYPASS - [N24001497],NHAI,MAHARASHTRA	7/2021	7/2023 (-) [7/2023]	715.00 (715.00) [715.00]	398.42 (0.00) [0]	3/4
1301	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 - [N24001693],NHAI,TAMIL NADU	9/2021	10/2024 (-) [10/2024]	1,751.18 (-) [1,751.18]	308.26 (0.00) [0]	0/0
1302	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA - [N24001784],NHAI,HARYANA	11/2018	9/2021 (-) [8/2023]	1,935.61 (-) [1,935.61]	856.41 (0.00) [23]	0/0
1303	6L KANTAKAPALLE – SABBAVARAM SECTION OF NH-130CD ROAD FROM	2/2021	10/2024 (-)	824.29 (-)	306.38 (99.71)	0/4

	KM 445.100 TO KM 464.662 (PKG-4) - [N24001836],NHAI,ANDHRA PRADESH		[10/2024]	[924.00]	[0]	
1304	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] - [N24001766],NHAI,MADHYA PRADESH	1/2022	10/2024 (-) [10/2024]	1,011.29 (-) [1,011.29]	0.00 (0.00) [0]	0/0
1305	REHABILITATION AND UP- GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734],NHAI,ODISHA	1/2018	8/2021 (-) [10/2023]	614.48 (503.30) [757.12]	641.00 (142.64) [26]	0/0
1306	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND - [N24001767],NHAI,MADHYA PRADESH	1/2021	4/2024 (-) [4/2024]	1,001.69 (-) [1,001.69]	29.75 (0.00) [0]	0/0
1307	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 - [N24001665],NHAI,ODISHA	12/2021	10/2024 (-) [10/2024]	1,592.00 (1,592.00) [1,592.00]	0.00 (0.00) [0]	0/0
1308	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM - [N24001632],NHAI,PUNJAB	1/2021	5/2024 (-) [5/2024]	1,741.86 (-) [1,741.86]	849.17 (0.00) [0]	0/0
1309	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM - [N24001694],NHAI,TAMIL NADU	2/2019	12/2023 (-) [12/2023]	1,243.57 (-) [1,243.57]	171.63 (0.00) [0]	0/0
1310	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)- KUNJWANI SECTION OF NH-4 - [N24001550],NHAI,JAMMU AND KASHMIR	9/2021	9/2024 (-) [9/2024]	1,821.72 (1,917.32) [1,917.32]	248.20 (95.60) [0]	0/0
1311	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463],NHAI,WEST BENGAL	12/2015	6/2018 (8/2023) [8/2023]	1,083.00 (1,414.01) [1,414.01]	1,059.61 (331.01) [62]	0/0
1312	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704],NHAI,KERALA	9/2017	5/2020 (11/2023) [11/2023]	1,124.11 (1,503.86) [1,503.86]	1,405.49 (379.75) [42]	0/0
1313	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 (- [N24001607],NHAI,MAHARASHTRA	10/2022	5/2024 (-) [5/2024]	332.00 (-) [332.00]	0.00 (0.00) [0]	0/0
1314	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493],NHAI,UTTAR PRADESH	1/2016	6/2018 (7/2023) [6/2023]	1,027.53 (2,950.04) [2,628.31]	2,615.85 (1,600.78) [0]	0/1
1315	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) - [N24001561],NHAI,RAJASTHAN	10/2019	10/2023 (-) [10/2023]	839.63 (-) [839.63]	38.16 (0.00) [0]	0/0
1316	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 -	9/2020	4/2023 (-) [4/2023]	897.45 (-) [897.45]	1,030.28 (0.00) [0]	0/0

	[N24001709],NHAI,BIHAR					
1317	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739],NHAI,ODISHA	1/2018	6/2021 (6/2022) [12/2023]	503.88 (609.03) [609.03]	221.76 (105.15) [30]	0/0
1318	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC - [N24001657],NHAI,KERALA	6/2021	10/2024 (10/2024) [10/2024]	2,842.14 (-) [2,842.14]	117.96 (0.00) [0]	0/0
1319	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378],NHAI,MAHARASHTRA	2/2019	1/2022 (6/2023) [6/2023]	362.46 (372.46) [372.46]	346.15 (10.00) [0]	4/4
1320	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 - [N24001718],NHAI,TAMIL NADU	12/2020	7/2024 (-) [7/2024]	843.48 (-) [966.00]	203.01 (122.52) [0]	0/0
1321	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799],NHAI,MAHARASHTRA	2/2021	10/2023 (-) [4/2024]	1,166.96 (-) [1,251.00]	755.96 (84.04) [6]	0/0
1322	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE-7(ALONG WITH 0.700 - [N24001688],NHAI,KARNATAKA	10/2020	9/2023 (-) [9/2023]	3,184.00 (-) [3,184.00]	799.94 (0.00) [0]	0/0
1323	4L OF DHROL-BHADRA-PATIYA SECTION FROM 0.000 TO KM 13.600 AND BHADRA PATIYA - PIPALIYA SECTION FROM - [N24001787],NHAI,GUJARAT	5/2020	10/2023 (10/2023) [10/2023]	971.03 (-) [971.03]	411.77 (0.00) [0]	0/0
1324	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR - [N24001746],NHAI,UTTAR PRADESH	3/2021	4/2024 (-) [4/2024]	364.47 (-) [364.47]	28.87 (0.00) [0]	0/0
1325	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) - [N24001502],NHAI,MAHARASHTRA	9/2021	9/2023 (9/2023) [3/2024]	624.45 (627.79) [627.79]	309.89 (3.34) [6]	0/0
1326	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662],NHAI,PUNJAB	3/2017	3/2020 (8/2023) [8/2023]	754.54 (668.74) [668.74]	677.74 (-85.80) [41]	3/4
1327	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796],NHAI,MAHARASHTRA	3/2022	10/2024 (10/2024) [10/2024]	1,013.33 (-) [1,111.33]	202.73 (98.00) [0]	0/0
1328	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - [N24001710],NHAI,BIHAR	9/2020	3/2023 (11/2023) [11/2023]	2,334.68 (2,335.00) [2,335.00]	714.12 (0.32) [8]	0/0
1329	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG I) [AMRAVATI TO KURANKHED FROM KM. 166.00 TO KM. 220.00] - [N24001800],NHAI,MAHARASHTRA	11/2019	7/2023 (-) [10/2023]	713.07 (-) [713.07]	281.00 (0.00) [3]	0/0

1330	4L OF KM 0.00 TO KM 42.00 OF OFDOBBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALO - [N24001509],NHAI,KARNATAKA	1/2020	4/2021 (12/2023) [12/2023]	1,307.00 (-) [1,307.00]	701.00 (0.00) [32]	0/0
1331	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 - [N24001686],NHAI,KARNATAKA	3/2021	3/2023 (12/2023) [12/2023]	1,065.06 (1,577.92) [1,577.92]	26.31 (512.86) [9]	0/0
1332	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON - [N24001569],NHAI,RAJASTHAN	11/2019	3/2023 (11/2023) [8/2023]	1,425.02 (-) [1,425.02]	1,026.56 (0.00) [5]	0/0
1333	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF - [N24001596],NHAI,JHARKHAND	11/2021	7/2023 (-) [3/2024]	1,302.72 (-) [1,302.72]	521.32 (0.00) [8]	0/0
1334	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622],NHAI,KARNATAKA	9/2016	8/2019 (5/2024) [5/2024]	950.69 (-) [1,108.00]	1,679.45 (157.31) [57]	0/0
1335	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) - [N24001794],NHAI,GUJARAT	2/2020	3/2023 (-) [8/2023]	778.15 (-) [785.67]	429.03 (7.52) [5]	0/0
1336	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-6) - [N24001579],NHAI,RAJASTHAN	2/2019	10/2022 (9/2023) [5/2023]	635.84 (-) [635.84]	445.96 (0.00) [0]	0/0
1337	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652],NHAI,TAMIL NADU	3/2017	3/2020 (5/2024) [5/2024]	848.45 (-) [848.45]	296.66 (0.00) [50]	0/0
1338	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29 - [N24001517],NHAI,GUJARAT	9/2020	4/2023 (-) [7/2023]	1,523.77 (-) [1,523.77]	963.02 (0.00) [3]	0/0
1339	6L OF KARKI - KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE - OD-4) - [N24001670],NHAI,ODISHA	2/2021	3/2024 (-) [3/2024]	593.00 (-) [593.00]	0.00 (0.00) [0]	0/0
1340	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795],NHAI,RAJASTHAN	2/2018	4/2021 (8/2023) [8/2023]	741.86 (649.00) [649.00]	634.53 (-92.86) [28]	0/0
1341	SIX / FOUR LANING OF NH 5 (NEW NH 16) FROM PUINTOLA TO TANGI (KM. 284.000 TO KM. 355.000) - [N24000845],NHAI,ODISHA	3/2018	12/2020 (-) [10/2023]	538.41 (478.32) [478.32]	415.11 (-60.09) [34]	0/0
1342	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B - [N24001727],NHAI,UTTAR PRADESH	3/2022	2/2025 (-) [2/2025]	762.62 (-) [762.62]	170.66 (0.00) [0]	0/0
1343	4L FROM GAJU VILLAGE AT KM	12/2021	1/2025	1,384.79	398.01	0/0

	32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) - [N24001730],NHAI,UTTAR PRADESH		(-) [1/2025]	(-) [1,384.79]	(0.00) [0]	
1344	4 LANE OF BILASPUR TO URGU PROJECT (KM 0.00 TO KM 70.2) OF NH-130A - [N24001611],NHAI,CHHATTISGARH	4/2020	3/2024 (-) [3/2024]	1,855.59 (1,869.85) [1,869.85]	187.36 (14.26) [0]	0/0
1345	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA - [N24001815],NHAI,UTTAR PRADESH	12/2022	11/2024 (-) [11/2024]	1,699.00 (-) [1,699.00]	13.76 (0.00) [0]	0/1
1346	CONSTRUCTION OF 8 LANE OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851],NHAI,MAHARASHTRA	3/2018	7/2021 (-) [9/2024]	1,162.92 (1,182.87) [1,182.87]	160.20 (19.95) [38]	0/0
1347	FOUR LANE OF MADURAI- CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827],NHAI,TAMIL NADU	3/2018	11/2020 (7/2023) [7/2023]	628.71 (-) [628.71]	583.02 (0.00) [32]	0/0
1348	FOUR LANE OF JAGDISHPUR- FAIZABAD SECTION FROM KM 47.930 TO KM 107.680 OF NH-330A - [N24001816],NHAI,UTTAR PRADESH	3/2021	3/2023 (-) [7/2023]	1,980.00 (-) [1,980.00]	1,043.39 (0.00) [4]	0/1
1349	4 LANE OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 - [N24001753],NHAI,UTTAR PRADESH	2/2022	6/2024 (-) [6/2024]	570.98 (-) [570.98]	186.06 (0.00) [0]	0/0
1350	TWO-LANE WITH PAVED SHOULDER OF MAHSHKUNT- SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665],NHAI,BIHAR	3/2017	3/2020 (3/2024) [3/2024]	672.89 (736.01) [830.31]	347.17 (157.42) [48]	0/0
1351	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419],NHAI,PUNJAB	2/2021	4/2024 (11/2024) [11/2024]	1,269.96 (-) [1,269.96]	241.67 (0.00) [7]	0/1
1352	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533],NHAI,HARYANA	11/2020	12/2023 (-) [3/2024]	1,690.23 (-) [2,010.17]	1,067.66 (319.94) [3]	0/0
1353	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 - [N24001618],NHAI,MADHYA PRADESH	9/2019	9/2022 (-) [6/2023]	194.40 (-) [194.40]	134.69 (0.00) [0]	0/0
1354	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 - [N24001518],NHAI,GUJARAT	11/2019	9/2023 (-) [9/2023]	1,669.56 (-) [1,669.56]	575.33 (0.00) [0]	0/0
1355	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719],NHAI,TAMIL NADU	2/2021	7/2024 (-) [7/2024]	2,948.31 (-) [3,392.00]	506.57 (443.69) [0]	0/0
1356	DHANGAON - BORGAON SECTION (KM 81.000 TO KM 139.000) [INDORE -	11/2018	8/2023 (-)	831.00 (-)	608.00 (0.00)	0/0

	EDLABAD PKG IV] [N24001769],NHAI,MADHYA PRADESH		[12/2023]	[831.00]	[4]	
1357	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A - [N24001813],NHAI,HIMACHAL PRADESH	7/2021	9/2024 (-) [9/2024]	1,692.05 (-) [1,692.05]	598.25 (0.00) [0]	0/0
1358	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 - [N24001777],NHAI,DELHI	7/2020	10/2023 (-) [10/2023]	2,171.80 (-) [2,171.80]	958.13 (0.00) [0]	0/0
1359	4-LANNING OF STHIYATHOPU- CHOLOPURAM - [N24000708],NHAI,TAMIL NADU	9/2017	8/2020 (6/2024) [6/2024]	1,227.87 (-) [1,227.87]	1,097.03 (0.00) [46]	0/0
1360	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743],NHAI,UTTAR PRADESH	1/2018	2/2023 (8/2023) [8/2023]	1,916.38 (-) [2,078.00]	1,158.54 (161.62) [6]	0/0
1361	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549],NHAI,UTTAR PRADESH	3/2016	10/2019 (5/2023) [7/2023]	1,396.74 (4,041.80) [1,396.74]	3,738.01 (0.00) [45]	0/1
1362	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 - [N24001731],NHAI,UTTAR PRADESH	12/2021	5/2025 (5/2025) [5/2025]	2,470.64 (-) [2,335.00]	139.84 (-135.64) [0]	0/0
1363	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP - [N24001810],NHAI,HIMACHAL PRADESH	2/2022	6/2024 (-) [6/2024]	190.60 (-) [163.00]	51.65 (-27.60) [0]	0/0
1364	4L OF AHMEDNAGAR - MIRAJGAON - KARMALA - TEMBHURNI (PKG-II) [GHOGARGAON TO AHMEDNAGAR- SOLPAUR DISTR - [N24001499],NHAI,MAHARASHTRA	1/2022	1/2024 (-) [1/2024]	629.00 (629.00) [629.00]	426.44 (0.00) [0]	3/4
1365	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR - [N24001641],NHAI,PUNJAB	3/2021	10/2024 (-) [10/2024]	1,641.75 (-) [1,641.75]	69.48 (0.00) [0]	0/0
1366	BALANCE WORK OF RANCHI- MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG- - [N24001597],NHAI,JHARKHAND	1/2019	12/2020 (-) [12/2023]	466.55 (518.00) [466.55]	0.00 (0.00) [36]	0/0
1367	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B - [N24001552],NHAI,JAMMU AND KASHMIR	10/2021	9/2024 (-) [9/2024]	2,714.95 (2,714.95) [2,714.95]	276.91 (0.00) [0]	0/0
1368	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) - [N24001804],NHAI,MAHARASHTRA	12/2019	9/2022 (-) [11/2023]	1,654.07 (-) [980.00]	724.63 (-674.07) [14]	0/0
1369	BANGALORE CHENNAI	11/2020	10/2024	1,137.74	321.70	0/4

	EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP - [N24001821],NHAI,ANDHRA PRADESH		(-) [10/2024]	(-) [1,289.00]	(151.26) [0]	
1370	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305],NHAI,BIHAR	10/2013	11/2020 (-) [12/2023]	464.09 (-) [464.09]	461.45 (0.00) [37]	0/0
1371	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430],NHAI,TAMIL NADU	3/2018	1/2022 (-) [1/2024]	2,120.40 (2,565.63) [2,565.63]	1,147.79 (445.23) [24]	0/0
1372	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH -66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 (- [N24001653],NHAI,KERALA	11/2021	4/2025 (-) [4/2025]	3,565.82 (-) [3,064.11]	1,570.57 (-501.71) [0]	0/0
1373	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442],NHAI,MAHARASHTRA	12/2015	3/2019 (11/2023) [11/2023]	649.50 (-) [649.50]	303.15 (0.00) [56]	2/4
1374	4L OF AKOLA - MEDSHI FROM KM. 0.00 TO KM. 47.70 OF NH-161 INCLUDING BYPASSES AT PATUR AND MEDSHI - [N24001803],NHAI,MAHARASHTRA	12/2019	11/2022 (9/2023) [9/2023]	1,393.95 (1,393.95) [576.00]	527.13 (-817.95) [10]	0/0
1375	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. - [N24001706],NHAI,BIHAR	3/2021	1/2024 (-) [1/2024]	1,097.18 (1,097.00) [1,097.00]	329.35 (-0.18) [0]	0/0
1376	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 - [N24001535],NHAI,HARYANA	7/2020	7/2022 (11/2023) [11/2023]	899.00 (-) [947.00]	920.51 (48.00) [16]	0/0
1377	2L PS OF UJJAIN - JHALAWAR (UPTO RJ BORDER) FROM KM. (-)0.650 TO KM. 132.955 OF NH-552G - [N24001760],NHAI,MADHYA PRADESH	10/2020	6/2023 (11/2023) [6/2023]	506.56 (498.00) [506.56]	345.36 (0.00) [0]	0/0
1378	RASISAR (NEAR BIKANER)- DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-2) - [N24001584],NHAI,RAJASTHAN	2/2019	1/2022 (9/2023) [4/2023]	676.19 (-) [676.19]	534.35 (0.00) [0]	0/0
1379	4L OF BAL WORKS OF MAHUA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) - [N24001793],NHAI,GUJARAT	3/2021	9/2022 (-) [12/2023]	485.75 (-) [485.75]	207.82 (0.00) [15]	0/0
1380	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185],NHAI,UTTAR PRADESH	11/2017	7/2021 (4/2023) [5/2023]	2,159.00 (2,262.00) [2,262.00]	2,212.19 (103.00) [0]	0/0
1381	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 - [N24001677],NHAI,KARNATAKA	11/2022	5/2024 (5/2024) [5/2024]	226.76 (-) [226.76]	39.80 (0.00) [0]	1/4

1382	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) - [N24001780],NHAI,HARYANA	1/2018	11/2020 (8/2023) [5/2023]	2,228.00 (-) [2,228.00]	1,411.27 (0.00) [0]	0/4
1383	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH - [N24001843],NHAI,ANDHRA PRADESH	12/2022	11/2025 (-) [11/2025]	992.89 (-) [992.89]	28.26 (0.00) [0]	0/0
1384	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) - [N24001493],NHAI,MAHARASHTRA	12/2022	12/2024 (-) [12/2024]	1,749.86 (-) [1,749.86]	228.15 (0.00) [0]	1/4
1385	2ND FLYOVER (LCW) PARALLEL TO EXISTING FLYOVER IN KISHANGANJ TOWN. - [N24001713],NHAI,BIHAR	3/2018	6/2020 (8/2023) [8/2023]	150.21 (150.00) [150.00]	148.40 (-0.21) [38]	0/0
1386	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 - [N24001723],NHAI,TAMIL NADU	10/2018	2/2021 (-) [12/2023]	707.90 (-) [717.00]	343.05 (9.10) [34]	0/0
1387	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) - [N24001606],NHAI,TAMIL NADU	12/2018	3/2022 (7/2024) [7/2024]	854.94 (-) [854.94]	169.70 (0.00) [28]	0/0
1388	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431],NHAI,TAMIL NADU	3/2018	10/2020 (-) [9/2024]	1,872.68 (2,661.51) [2,756.09]	848.82 (883.41) [47]	0/0
1389	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM - [N24001825],NHAI,DELHI	7/2020	10/2023 (-) [10/2023]	1,894.96 (-) [1,894.96]	741.88 (0.00) [0]	0/0
1390	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR - [N24001771],NHAI,DELHI	6/2020	12/2024 (-) [12/2024]	1,479.22 (-) [1,479.22]	667.80 (0.00) [0]	0/0
1391	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III - [N24001737],NHAI,UTTAR PRADESH	11/2021	4/2024 (-) [4/2024]	923.15 (-) [923.15]	455.61 (0.00) [0]	0/0
1392	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M - [N24001573],NHAI,RAJASTHAN	11/2019	12/2022 (8/2023) [6/2023]	1,658.06 (-) [1,658.06]	153.69 (0.00) [0]	0/0
1393	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. - [N24001621],NHAI,JAMMU AND KASHMIR	7/2021	8/2024 (8/2024) [8/2024]	614.48 (-) [614.48]	58.21 (0.00) [0]	0/0
1394	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 - [N24001650],NHAI,KERALA	12/2021	1/2025 (1/2025) [1/2025]	3,635.64 (-) [3,635.64]	75.12 (0.00) [0]	0/0
1395	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD	3/2021	10/2024 (-)	1,525.31 (-)	132.46 (0.00)	0/0

	- [N24001631],NHAI,PUNJAB		[10/2024]	[1,525.31]	[0]	
1396	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.- MAVIKALAN) TO VILL.-LOHADDA FROM K - [N24001733],NHAI,UTTAR PRADESH	3/2022	8/2024 (-) [8/2024]	1,602.48 (-) [1,602.48]	162.20 (0.00) [0]	0/0
1397	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM - [N24001626],NHAI,TELANGANA	2/2022	1/2025 (-) [1/2025]	972.06 (-) [972.06]	8.38 (0.00) [0]	0/0
1398	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR – DEHRADUN SECTION FROM - [N24001524],NHAI,UTTAR PRADESH	3/2021	10/2023 (10/2023) [10/2023]	990.28 (-) [990.28]	671.82 (0.00) [0]	0/0
1399	4 LANING OF CHAMPA-KORBA-CHHURI-KATGHORA SECTION OF NH 149B FROM KM.0.000 TO KM.38.200 - [N24001591],NHAI,CHHATTISGARH	2/2021	1/2024 (-) [1/2024]	999.97 (-) [999.97]	831.22 (0.00) [0]	0/0
1400	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306],NHAI,UTTAR PRADESH	10/2020	3/2023 (-) [1/2024]	724.60 (-) [724.60]	464.18 (0.00) [10]	0/1
1401	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) - [N24001603],NHAI,TAMIL NADU	1/2019	10/2022 (-) [12/2023]	1,518.53 (-) [1,518.53]	844.56 (0.00) [14]	0/0
1402	6L ALURU - JAKKUBA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838],NHAI,ANDHRA PRADESH	2/2021	3/2024 (-) [6/2024]	922.50 (-) [1,128.68]	435.46 (206.18) [3]	0/4
1403	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK - [N24001848],NHAI,ANDHRA PRADESH	2/2023	10/2025 (-) [10/2025]	909.02 (-) [909.02]	27.25 (0.00) [0]	0/0
1404	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) - [N24001818],NHAI,ANDHRA PRADESH	2/2021	1/2025 (-) [1/2025]	818.73 (-) [1,105.00]	73.20 (286.27) [0]	0/4
1405	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN - [N24001691],NHAI,KARNATAKA	10/2019	10/2021 (1/2024) [1/2024]	1,225.24 (1,676.11) [1,676.11]	14.76 (450.87) [27]	0/0
1406	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. - [N24001620],NHAI,JAMMU AND KASHMIR	9/2021	10/2023 (10/2023) [10/2023]	442.14 (-) [442.14]	107.84 (0.00) [0]	0/0
1407	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI - [N24001536],NHAI,HARYANA	7/2020	7/2022 (-) [11/2023]	817.00 (-) [817.00]	851.73 (0.00) [16]	0/0
1408	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM.	1/2020	1/2024 (1/2024)	336.01 (-)	91.52 (0.00)	0/0

	187.00 TO KM. 189.350 [N24001623],NHAI,JAMMU AND KASHMIR		[1/2024]	[336.01]	[0]	
1409	4L OF CHANDESARA TO KHEDEKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D - [N24001759],NHAI,MADHYA PRADESH	1/2020	6/2024 (-) [6/2024]	909.84 (-) [909.84]	130.08 (0.00) [0]	0/0
1410	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566],NHAI,KERALA	4/2016	6/2018 (7/2023) [7/2023]	804.97 (571.45) [571.45]	648.26 (-233.52) [61]	0/0
1411	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA – RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR - [N24001636],NHAI,PUNJAB	5/2021	12/2024 (12/2024) [12/2024]	1,368.91 (1,368.91) [1,368.91]	63.88 (0.00) [0]	0/4
1412	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 - [N24001725],NHAI,TAMIL NADU	1/2019	5/2021 (-) [2/2024]	654.26 (-) [821.00]	295.75 (166.74) [33]	0/0
1413	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) - [N24001564],NHAI,RAJASTHAN	10/2019	7/2023 (11/2023) [7/2023]	662.08 (-) [662.08]	32.02 (0.00) [0]	0/0
1414	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S - [N24001489],NHAI,MAHARASHTRA	5/2022	5/2024 (-) [5/2024]	519.93 (-) [519.93]	126.16 (0.00) [0]	0/0
1415	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU - [N24001774],NHAI,HARYANA	12/2020	11/2023 (-) [11/2023]	1,524.03 (-) [1,524.03]	890.82 (0.00) [0]	0/0
1416	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K - [N24001627],NHAI,JAMMU AND KASHMIR	7/2021	2/2025 (2/2025) [2/2025]	1,912.17 (-) [1,912.17]	0.26 (0.00) [0]	0/0
1417	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS - [N24001732],NHAI,UTTAR PRADESH	12/2021	10/2024 (-) [10/2024]	540.97 (-) [540.97]	50.31 (0.00) [0]	0/0
1418	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 - [N24001649],NHAI,KERALA	12/2021	2/2025 (2/2025) [2/2025]	3,273.61 (-) [3,273.61]	75.26 (0.00) [0]	0/0
1419	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619],NHAI,ODISHA	9/2016	8/2019 (-) [12/2023]	2,510.04 (-) [2,510.04]	783.15 (0.00) [52]	0/0
1420	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570],NHAI,GUJARAT	5/2016	8/2019 (-) [10/2023]	763.08 (-) [763.08]	408.37 (0.00) [50]	2/2

1421	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709],NHAI,MADHYA PRADESH	12/2017	2/2020 (-) [10/2023]	950.27 (-) [950.27]	521.56 (0.00) [44]	4/4
1422	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 - [N24001817],NHAI,ANDHRA PRADESH	2/2019	3/2023 (-) [3/2024]	757.45 (-) [757.45]	261.31 (0.00) [12]	0/4
1423	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) - [N24001811],NHAI,HIMACHAL PRADESH	4/2021	6/2024 (-) [6/2024]	583.93 (-) [583.93]	33.42 (0.00) [0]	0/0
1424	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697],NHAI,TAMIL NADU	8/2017	9/2020 (6/2024) [6/2024]	1,176.37 (-) [1,176.37]	970.43 (0.00) [45]	0/0
1425	6L GREENFIELD KALIAGURA – BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG - [N24001667],NHAI,ODISHA	9/2021	5/2024 (-) [5/2024]	1,734.00 (1,734.00) [1,734.00]	6.94 (0.00) [0]	0/0
1426	JUNAGADH BYPASS - [N24000701],NHAI,GUJARAT	10/2017	4/2021 (6/2023) [8/2023]	232.49 (375.78) [290.69]	319.53 (58.20) [28]	0/0
1427	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G - [N24001711],NHAI,BIHAR	9/2020	3/2023 (-) [12/2023]	939.43 (-) [939.43]	40.02 (0.00) [9]	0/0
1428	4L OF SHAMLI TO MUZAFFARNAGAR SECTION OF NH-709AD, PKG-II - [N24001742],NHAI,UTTAR PRADESH	6/2020	10/2022 (-) [7/2023]	1,621.07 (-) [1,621.07]	977.49 (0.00) [9]	0/0
1429	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569],NHAI,GUJARAT	5/2016	9/2019 (-) [10/2023]	723.64 (-) [723.64]	551.69 (0.00) [49]	2/2
1430	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 - [N24001830],NHAI,UTTAR PRADESH	6/2020	11/2023 (-) [11/2023]	2,002.79 (-) [2,002.79]	753.29 (0.00) [0]	0/0
1431	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU - [N24001701],NHAI,BIHAR	4/2022	4/2024 (-) [4/2024]	1,769.50 (-) [1,769.50]	0.00 (0.00) [0]	0/0
1432	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP - [N24001477],NHAI,ANDHRA PRADESH	9/2021	9/2022 (9/2024) [9/2024]	622.00 (-) [817.91]	116.11 (195.91) [24]	0/0
1433	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 - [N24001520],NHAI,GUJARAT	11/2019	5/2024 (-) [5/2024]	1,604.06 (-) [1,604.06]	1,057.90 (0.00) [0]	0/0
1434	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738],NHAI,ODISHA	1/2018	9/2021 (-) [6/2023]	999.00 (1,152.70) [1,152.70]	339.23 (153.70) [0]	0/0

1435	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) - [N24001508],NHAI,MAHARASHTRA	11/2022	10/2024 (-) [10/2024]	1,450.00 (-) [1,450.00]	153.30 (0.00) [0]	0/0
1436	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429],NHAI,TAMIL NADU	3/2018	11/2021 (-) [11/2023]	1,294.47 (1,588.40) [1,588.40]	605.20 (293.93) [24]	0/0
1437	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 - [N24001654],NHAI,KERALA	6/2021	3/2025 (3/2025) [3/2025]	2,641.37 (-) [2,641.37]	138.53 (0.00) [0]	0/0
1438	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) - [N24001615],NHAI,MADHYA PRADESH	3/2021	4/2024 (-) [4/2024]	790.78 (-) [790.78]	133.42 (0.00) [0]	0/0
1439	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU - [N24000788],NHAI,WEST BENGAL	3/2018	9/2022 (12/2022) [3/2024]	841.57 (1,619.48) [1,619.48]	1,368.06 (777.91) [18]	0/0
1440	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA - [N24001847],NHAI,ANDHRA PRADESH	1/2023	11/2025 (-) [11/2025]	956.14 (-) [956.14]	18.72 (0.00) [0]	0/0
1441	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 - [N24001556],NHAI,TELANGANA	12/2021	7/2024 (-) [7/2024]	521.53 (-) [521.53]	126.88 (0.00) [0]	0/0
1442	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O - [N24001651],NHAI,KERALA	9/2021	9/2024 (9/2024) [9/2024]	2,878.97 (-) [2,878.97]	154.45 (0.00) [0]	0/0
1443	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO - [N24001700],NHAI,BIHAR	12/2021	3/2024 (-) [3/2024]	552.55 (553.00) [553.00]	292.70 (0.45) [0]	0/0
1444	BALANCE 4 LANING WORK OF RAIGANJ DALKHOLA SECTION OF NH34 FROM KM 398.000 TO KM 452.750 (PACKAGE V) - [N24001751],NHAI,WEST BENGAL	12/2018	9/2021 (-) [12/2023]	1,548.07 (-) [1,548.07]	1,086.32 (0.00) [27]	0/0
1445	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 - [N24000564],NHAI,UTTAR PRADESH	3/2016	7/2020 (2/2024) [2/2024]	1,408.00 (1,659.12) [1,659.12]	1,115.46 (251.12) [43]	1/4
1446	REMAINING WORK OF 2L+PS OF TRICHY - KARAUKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS - [N24001604],NHAI,TAMIL NADU	2/2019	3/2021 (-) [9/2023]	166.90 (-) [166.90]	118.82 (0.00) [30]	0/0
1447	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ - [N24001663],NHAI,KERALA	6/2020	4/2024 (10/2021) [4/2024]	3,041.65 (3,799.76) [3,041.65]	1,795.19 (0.00) [0]	0/0
1448	HARIHARGANJ TO PARWA MODE	9/2020	3/2024	755.26	385.01	0/0

	SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - [N24001589],NHAI,JHARKHAND		(-) [3/2024]	(-) [1,039.00]	(283.74) [0]	
1449	RASISAR (NEAR BIKANER)- DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-3) - [N24001582],NHAI,RAJASTHAN	2/2019	1/2022 (9/2023) [4/2023]	732.84 (-) [732.84]	558.75 (0.00) [0]	0/0
1450	4-LANNING OF TARSOD- FAGNE(FROM KM 422.700-510.00) - [N24000628],NHAI,MAHARASHTRA	11/2016	7/2021 (12/2023) [12/2023]	1,064.88 (-) [1,021.00]	800.70 (-43.88) [29]	3/4
1451	DEVELOPMENT OF 6L UER II [PACKAGE - III] (NANGLOI - NAJAFGARH ROAD TILL SECTOR 24 DWARKA) FROM KM. 2 - [N24001776],NHAI,DELHI	7/2020	10/2023 (-) [10/2023]	1,069.27 (-) [1,069.27]	748.48 (0.00) [0]	0/0
1452	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) - [N24001602],NHAI,TAMIL NADU	1/2019	12/2022 (-) [2/2024]	1,409.38 (-) [1,409.38]	520.63 (0.00) [14]	0/0
1453	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) - [N24001505],NHAI,MAHARASHTRA	3/2022	3/2024 (-) [3/2024]	1,549.02 (-) [1,549.02]	290.04 (0.00) [0]	0/0
1454	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 - [N24001687],NHAI,KARNATAKA	10/2021	10/2023 (10/2024) [10/2023]	1,331.77 (2,508.79) [2,508.79]	60.90 (1,177.02) [0]	0/0
1455	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV - [N24001644],NHAI,PUNJAB	12/2020	9/2023 (-) [9/2023]	524.88 (-) [524.88]	122.22 (0.00) [0]	0/0
1456	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE - [N24001822],NHAI,ANDHRA PRADESH	12/2020	10/2024 (-) [10/2024]	1,075.27 (-) [1,307.00]	384.53 (231.73) [0]	0/4
1457	4L OF HARDA - BETUL (PKG-III) FROM KM. 81.00 TO KM.121.248 [CHICHOLI - BETUL] - [N24001764],NHAI,MADHYA PRADESH	9/2021	9/2023 (-) [9/2023]	814.04 (-) [814.04]	391.67 (0.00) [0]	0/0
1458	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784],NHAI,KERALA	2/2018	2/2023 (-) [9/2024]	1,424.77 (1,862.77) [1,862.77]	465.92 (438.00) [19]	0/0
1459	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL-LATIFPUR AT SAHARANPUR BYPASS FROM KM - [N24001735],NHAI,UTTAR PRADESH	3/2022	8/2024 (-) [8/2024]	1,428.19 (-) [1,428.19]	211.90 (0.00) [0]	0/0
1460	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301],NHAI,ANDHRA PRADESH	11/2019	1/2024 (-) [7/2024]	1,601.10 (-) [1,601.10]	738.85 (0.00) [6]	0/4
1461	SANGARIYA (NEAR CHAUTALA)- RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-2) - [N24001560],NHAI,RAJASTHAN	2/2019	10/2023 (11/2023) [10/2023]	755.16 (-) [755.16]	723.96 (0.00) [0]	0/0

1462	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551],NHAI,UTTAR PRADESH	3/2016	4/2019 (12/2022) [7/2023]	1,587.49 (3,150.00) [3,063.99]	2,938.25 (1,476.50) [51]	0/1
1463	BALANCE WORK OF 2L PS OF TINDIVANAM KRISHNAGIRI FROM KM 37.600 TO 219.782 - [N24001724],NHAI,TAMIL NADU	5/2019	7/2021 (5/2023) [8/2023]	602.57 (621.38) [548.89]	313.44 (-53.68) [25]	0/0
1464	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE - [N24001775],NHAI,HARYANA	2/2020	1/2023 (-) [6/2023]	808.31 (-) [958.00]	734.96 (149.69) [0]	0/0
1465	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826],NHAI,TAMIL NADU	3/2018	10/2022 (7/2023) [7/2023]	505.35 (-) [505.35]	354.35 (0.00) [9]	0/0
1466	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 - [N24001601],NHAI,TAMIL NADU	1/2019	1/2023 (2/2024) [2/2024]	1,051.69 (-) [1,051.69]	349.20 (0.00) [13]	0/0
1467	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 - [N24001675],NHAI,KARNATAKA	11/2022	5/2025 (-) [5/2025]	1,732.73 (-) [1,732.73]	214.41 (0.00) [0]	0/0
1468	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI - HASSAN SECTION - [N24001684],NHAI,KARNATAKA	9/2020	1/2023 (-) [3/2025]	688.00 (-) [688.00]	399.88 (0.00) [26]	3/4
1469	6L JAKKUVA – KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) - [N24001837],NHAI,ANDHRA PRADESH	2/2021	3/2024 (-) [6/2024]	663.60 (-) [768.00]	241.99 (104.40) [3]	0/4
1470	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM - [N24001594],NHAI,JHARKHAND	2/2022	1/2025 (-) [1/2025]	534.73 (-) [534.73]	0.00 (0.00) [0]	0/0
1471	4-LANING OF BRAHAMPORE-FARAKA - [N24000203],NHAI,WEST BENGAL	2/2011	8/2013 (-) [12/2023]	998.79 (-) [998.79]	2,170.28 (0.00) [124]	3/4
1472	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. - [N24001599],NHAI,KARNATAKA	3/2018	12/2022 (12/2023) [2/2024]	440.16 (-) [440.16]	126.80 (0.00) [14]	1/4
1473	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232],NHAI,MADHYA PRADESH	2/2019	3/2022 (11/2022) [8/2023]	847.00 (-) [847.00]	920.50 (0.00) [17]	3/3
1474	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-3) - [N24001580],NHAI,RAJASTHAN	2/2019	10/2022 (9/2023) [5/2023]	672.72 (-) [672.72]	579.29 (0.00) [0]	0/0
1475	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM.	3/2020	3/2023 (-)	510.97 (-)	506.37 (0.00)	0/0

	347+800 OF NH-71 AND CONNECTING LINK FROM K - [N24001673],NHAI,HARYANA		[10/2023]	[510.97]	[7]	
1476	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA - [N24001748],NHAI,WEST BENGAL	3/2021	9/2024 (-) [9/2024]	2,200.93 (-) [2,200.93]	1,255.60 (0.00) [0]	0/0
1477	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N - [N24001765],NHAI,MADHYA PRADESH	8/2022	7/2024 (-) [7/2024]	207.77 (-) [207.77]	0.00 (0.00) [0]	0/0
1478	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA - [N24001841],NHAI,ANDHRA PRADESH	12/2022	9/2025 (-) [9/2025]	912.94 (-) [912.94]	59.28 (0.00) [0]	0/0
1479	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O - [N24001629],NHAI,MULTI STATE	4/2022	11/2024 (-) [11/2024]	796.65 (-) [796.65]	26.55 (0.00) [0]	0/0
1480	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION-HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 - [N24001547],NHAI,ASSAM	3/2022	1/2026 (-) [1/2026]	1,909.98 (-) [1,909.98]	22.90 (0.00) [0]	0/0
1481	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A - [N24001782],NHAI,HARYANA	11/2018	9/2021 (-) [8/2023]	2,312.26 (-) [2,312.26]	1,361.51 (0.00) [23]	0/0
1482	SIX LANNING OF MANDI DABWALI (PUNJAB/HARYANA BORDER)-CHAUTALA ROAD SECTION FROM PROPOSED MANDI DABW - [N24001672],NHAI,HARYANA	1/2021	1/2024 (1/2024) [1/2024]	864.27 (864.00) [864.27]	327.36 (0.00) [0]	0/0
1483	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613],NHAI,HIMACHAL PRADESH	9/2016	7/2020 (-) [6/2024]	1,273.71 (-) [1,273.71]	1,264.66 (0.00) [47]	0/0
1484	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567],NHAI,GUJARAT	5/2016	8/2019 (-) [8/2023]	998.18 (-) [998.18]	802.04 (0.00) [48]	2/2
1485	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811],NHAI,ANDHRA PRADESH	3/2018	12/2020 (12/2022) [12/2024]	314.43 (-) [348.72]	85.61 (34.29) [48]	0/0
1486	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA - [N24001588],NHAI,CHHATTISGARH	12/2021	1/2025 (-) [1/2025]	1,470.73 (-) [1,470.73]	179.31 (0.00) [0]	0/0
1487	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV	9/2021	10/2023 (-)	300.79 (-)	122.56 (0.00)	0/0

	- [N24001738],NHAI,UTTAR PRADESH		[10/2023]	[300.79]	[0]	
1488	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH-383 - [N24001605],NHAI,TAMIL NADU	6/2018	3/2022 (-) [4/2024]	1,103.86 (-) [1,103.86]	295.97 (0.00) [25]	0/0
1489	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655],NHAI,KERALA	6/2021	2/2025 (-) [2/2025]	3,606.00 (-) [3,923.82]	2,789.91 (317.82) [0]	0/0
1490	REHABILITATION AND UP- GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731],NHAI,ODISHA	1/2018	5/2020 (-) [5/2023]	953.09 (1,014.08) [1,014.08]	731.39 (60.99) [0]	0/0
1491	SIX-LANING OF BARWA ADDA- PANAGARH - [N24000515],NHAI,WEST BENGAL	4/2014	9/2016 (-) [12/2023]	1,665.00 (-) [2,360.65]	4,657.47 (695.65) [87]	0/0
1492	SIX LANNING OF AUNTA- SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696],NHAI,BIHAR	8/2017	2/2022 (8/2023) [10/2024]	950.64 (1,161.00) [1,168.33]	729.78 (217.69) [32]	0/0
1493	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488],NHAI,JAMMU AND KASHMIR	12/2015	12/2018 (7/2023) [7/2023]	2,136.97 (2,288.97) [2,136.97]	2,362.99 (0.00) [55]	3/4
1494	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX - [N24001622],NHAI,JAMMU AND KASHMIR	7/2021	6/2024 (6/2024) [6/2024]	1,401.87 (-) [1,401.87]	138.72 (0.00) [0]	0/0
1495	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) - [N24001563],NHAI,RAJASTHAN	10/2019	8/2023 (9/2023) [8/2023]	846.59 (-) [846.59]	37.29 (0.00) [0]	0/0
1496	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH - [N24001545],NHAI,ASSAM	8/2022	12/2022 (-) [6/2024]	175.00 (-) [175.00]	66.50 (0.00) [18]	0/0
1497	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE - [N24001639],NHAI,PUNJAB	5/2020	12/2024 (12/2024) [12/2024]	864.23 (864.23) [864.23]	342.25 (0.00) [0]	0/0
1498	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI-MOTIHARI- RAXAUL SECTION OF NH-28A FRO - [N24001715],NHAI,BIHAR	12/2018	10/2020 (-) [9/2023]	333.60 (459.89) [461.41]	399.69 (127.81) [35]	0/0
1499	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH - [N24001662],NHAI,KERALA	5/2020	5/2024 (11/2021) [5/2024]	1,981.07 (2,430.53) [1,981.07]	1,121.13 (0.00) [0]	0/0
1500	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806],NHAI,MAHARASHTRA	3/2018	3/2023 (-) [6/2023]	1,241.38 (-) [2,122.64]	1,577.64 (881.26) [0]	0/0
1501	SANCHORE - SANTALPUR FROM KM	2/2020	8/2023	752.30	392.85	0/0

	67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) - [N24001790],NHAI,GUJARAT		(12/2023) [8/2023]	(-) [766.20]	(13.90) [0]	
1502	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU - [N24001809],NHAI,HIMACHAL PRADESH	5/2022	3/2024 (-) [3/2024]	469.95 (-) [280.00]	188.16 (-189.95) [0]	0/0
1503	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414],NHAI,PUNJAB	12/2020	1/2024 (5/2024) [5/2024]	733.00 (-) [733.00]	522.95 (0.00) [4]	1/1
1504	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 - [N24001516],NHAI,GUJARAT	9/2020	2/2024 (-) [2/2024]	1,185.69 (-) [1,185.69]	432.47 (0.00) [0]	0/0
1505	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592],NHAI,GUJARAT	7/2016	7/2020 (-) [12/2023]	829.97 (-) [829.97]	329.71 (0.00) [41]	1/1
1506	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D - [N24001756],NHAI,MADHYA PRADESH	10/2020	10/2024 (-) [10/2024]	1,352.56 (-) [1,352.56]	178.51 (0.00) [0]	0/0
1507	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854],NHAI,JHARKHAND	3/2018	3/2021 (6/2023) [6/2023]	1,005.08 (1,073.10) [1,073.10]	699.05 (68.02) [0]	0/0
1508	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428],NHAI,TAMIL NADU	3/2018	11/2021 (-) [11/2023]	998.70 (1,358.32) [1,358.32]	785.96 (359.62) [24]	0/0
1509	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III) - [N24001758],NHAI,MADHYA PRADESH	1/2020	10/2024 (-) [6/2024]	823.05 (-) [823.05]	120.24 (0.00) [-4]	0/0
1510	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE – OD-1) - [N24001669],NHAI,ODISHA	2/2021	3/2024 (-) [3/2024]	586.00 (-) [586.00]	0.00 (0.00) [0]	0/0
1511	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788],NHAI,GUJARAT	7/2020	12/2023 (-) [6/2024]	2,271.86 (-) [3,916.00]	426.80 (1,644.14) [6]	0/0
1512	NAGPUR RING ROAD PACKAGE-2 - [N24000560],NHAI,MAHARASHTRA	3/2016	7/2019 (3/2024) [3/2024]	591.66 (-) [591.66]	429.66 (0.00) [56]	0/0
1513	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. - [N24001844],NHAI,ANDHRA PRADESH	12/2022	10/2025 (-) [10/2025]	1,058.90 (-) [1,058.90]	28.23 (0.00) [0]	0/0
1514	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III)	3/2021	1/2025 (-) [1/2025]	1,102.63 (-) [1,303.00]	212.43 (200.37) [0]	0/4

	- [N24001819],NHAI,ANDHRA PRADESH					
1515	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH - [N24001549],NHAI,ASSAM	7/2017	4/2020 (-) [6/2023]	442.23 (-) [442.23]	192.31 (0.00) [0]	0/0
1516	TUMKUR - NELAMANGALA(6L) - [N24001681],NHAI,KARNATAKA	8/2022	8/2025 (-) [8/2025]	2,032.15 (1,351.00) [2,032.15]	29.46 (0.00) [0]	0/0
1517	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- - [N24001619],NHAI,JAMMU AND KASHMIR	8/2022	6/2024 (-) [6/2024]	200.05 (200.05) [200.05]	5.75 (0.00) [0]	0/0
1518	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 - [N24001647],NHAI,ODISHA	8/2020	3/2022 (-) [8/2023]	200.00 (154.73) [154.73]	137.04 (-45.27) [17]	0/0
1519	RASISAR (NEAR BIKANER)-DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-1) - [N24001576],NHAI,RAJASTHAN	2/2019	10/2022 (9/2023) [4/2023]	621.82 (-) [621.82]	479.50 (0.00) [0]	0/0
1520	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304],NHAI,BIHAR	10/2013	11/2020 (-) [12/2023]	446.97 (-) [446.97]	384.28 (0.00) [37]	0/0
1521	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH - [N24001612],NHAI,RAJASTHAN	7/2020	1/2024 (9/2024) [1/2024]	1,788.69 (-) [1,788.69]	411.07 (0.00) [0]	0/0
1522	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH - [N24001698],NHAI,BIHAR	8/2022	8/2024 (-) [8/2024]	1,198.02 (-) [1,198.02]	0.00 (0.00) [0]	0/0
1523	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA - [N24001484],NHAI,TELANGANA	9/2022	2/2024 (-) [2/2024]	804.69 (-) [804.69]	257.86 (0.00) [0]	0/0
1524	4LBERKHEDI TO GODPEHRA NH-44 - [N24001614],NHAI,MADHYA PRADESH	2/2022	11/2024 (-) [11/2024]	524.84 (-) [524.84]	1,600.30 (0.00) [0]	0/0
1525	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF - [N24001768],NHAI,MADHYA PRADESH	8/2019	4/2023 (-) [11/2023]	323.51 (-) [323.51]	2.46 (0.00) [7]	0/0
1526	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE - [N24001680],NHAI,KARNATAKA	3/2021	10/2024 (-) [10/2024]	1,409.68 (-) [1,409.68]	512.39 (0.00) [0]	1/4
1527	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715],NHAI,ODISHA	12/2017	7/2020 (-) [12/2023]	686.65 (565.00) [686.65]	461.14 (0.00) [41]	0/0

1528	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 - [N24001747],NHAI, WEST BENGAL	3/2020	9/2024 (-) [9/2024]	2,193.23 (2,314.00) [2,314.00]	1,191.60 (120.77) [0]	0/0
1529	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) - [N24001791],NHAI, GUJARAT	2/2020	6/2023 (-) [8/2023]	606.51 (-) [657.00]	446.88 (50.49) [2]	0/0
1530	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499],NHAI, UTTAR PRADESH	12/2015	6/2018 (7/2023) [6/2023]	667.00 (3,192.10) [3,006.53]	3,022.15 (2,339.53) [0]	0/1
1531	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659],NHAI, KERALA	2/2021	7/2024 (-) [7/2024]	3,375.31 (-) [3,790.17]	1,745.63 (414.86) [0]	0/0
1532	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM - [N24001716],NHAI, TAMIL NADU	7/2022	8/2023 (-) [8/2023]	186.50 (-) [201.00]	0.00 (14.50) [0]	0/0
1533	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO - [N24001728],NHAI, UTTAR PRADESH	12/2021	7/2025 (-) [7/2025]	1,138.81 (-) [1,138.81]	122.05 (0.00) [0]	0/0
1534	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAGE - [N24001446],NHAI, GUJARAT	5/2020	12/2023 (-) [12/2023]	894.00 (-) [894.00]	437.91 (0.00) [0]	2/4
1535	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN - [N24001754],NHAI, UTTAR PRADESH	1/2022	10/2024 (-) [10/2024]	953.79 (-) [953.79]	384.66 (0.00) [0]	0/0
1536	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717],NHAI, JAMMU AND KASHMIR	12/2017	7/2021 (7/2023) [8/2023]	1,471.75 (1,471.75) [1,471.75]	1,439.30 (0.00) [25]	3/3
1537	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E - [N24001707],NHAI, BIHAR	3/2021	1/2024 (-) [1/2024]	1,143.46 (1,143.00) [1,143.00]	268.70 (-0.46) [0]	0/0
1538	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT – SHAMLI – MUZAFFARNAGAR) AND NH-709A (KARN - [N24001729],NHAI, UTTAR PRADESH	8/2022	4/2024 (-) [4/2024]	326.79 (-) [329.79]	18.75 (3.00) [0]	0/0
1539	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ - [N24001664],NHAI, KERALA	6/2020	4/2024 (10/2021) [4/2024]	1,746.45 (2,377.88) [1,746.45]	879.34 (0.00) [0]	0/0
1540	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR – DEHRADUN SECTION FROM K - [N24001523],NHAI, UTTAR PRADESH	3/2021	10/2023 (10/2023) [10/2023]	836.24 (-) [836.24]	489.16 (0.00) [0]	0/0
1541	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD	9/2021	9/2022 (9/2024)	517.05 (-)	174.28 (138.01)	0/0

	HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI - [N24001476],NHAI,ANDHRA PRADESH		[9/2024]	[655.06]	[24]	
1542	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD - [N24001666],NHAI,ODISHA	12/2021	9/2024 (-) [9/2024]	714.00 (714.00) [714.00]	0.00 (0.00) [0]	0/0
1543	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C - [N24001705],NHAI,BIHAR	3/2022	3/2024 (-) [3/2024]	1,485.66 (-) [1,485.66]	0.00 (0.00) [0]	0/0
1544	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371],NHAI,BIHAR	10/2019	8/2023 (12/2024) [12/2024]	1,101.99 (-) [1,101.99]	563.96 (0.00) [16]	2/4
1545	CONSTRUCTION OF 4-LANE NH- 344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA - [N24001532],NHAI,HARYANA	11/2021	11/2023 (11/2023) [11/2023]	694.00 (-) [694.00]	1,212.57 (0.00) [0]	0/0
1546	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I - [N24001643],NHAI,PUNJAB	12/2020	6/2024 (-) [6/2024]	857.91 (-) [857.91]	73.50 (0.00) [0]	0/0
1547	SANGARIYA (NEAR CHAUTALA)- RASISAR (NEAR BIKANER) SECTION OF NH-754K (PHASE-I) (AJ/SR- PACKAGE-7) - [N24001565],NHAI,RAJASTHAN	2/2019	5/2023 (9/2023) [6/2023]	520.63 (-) [520.63]	423.98 (0.00) [0]	0/0
1548	SANGARIYA (NEAR CHAUTALA)- RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-5) - [N24001581],NHAI,RAJASTHAN	2/2019	10/2022 (-) [8/2022]	515.45 (-) [515.45]	0.12 (0.00) [0]	0/0
1549	REHABILITATION AND UP- GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733],NHAI,ODISHA	1/2018	8/2022 (-) [3/2024]	633.68 (492.83) [633.68]	560.38 (0.00) [19]	0/1
1550	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR- MEHTA-SRIHARGOBINDPUR- - [N24001420],NHAI,PUNJAB	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]	0/0
1551	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805],NHAI,MAHARASHTRA	3/2018	3/2021 (-) [6/2023]	1,169.04 (-) [1,693.95]	1,010.33 (524.91) [0]	0/0
1552	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789],NHAI,GUJARAT	7/2020	8/2023 (-) [6/2024]	1,710.30 (-) [1,927.00]	265.19 (216.70) [10]	0/0
1553	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F - [N24001633],NHAI,HARYANA	12/2020	12/2023 (-) [12/2023]	1,430.88 (-) [1,430.88]	872.76 (0.00) [0]	0/0
1554	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520	9/2020	6/2024 (-)	2,156.22 (-)	1,585.58 (0.00)	0/0

	NH20 [N24001708],NHAI,BIHAR		[6/2024]	[2,156.22]	[0]	
1555	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN - [N24001425],NHAI,KARNATAKA	3/2021	11/2021 (4/2024) [4/2024]	1,100.88 (1,100.88) [1,100.88]	561.13 (0.00) [29]	3/4
1556	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 - [N24001752],NHAI,WEST BENGAL	12/2018	2/2023 (8/2023) [8/2023]	2,375.87 (2,566.80) [2,566.80]	2,299.14 (190.93) [6]	0/0
1557	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA - [N24001750],NHAI,WEST BENGAL	8/2018	12/2021 (-) [12/2024]	622.04 (-) [622.04]	295.81 (0.00) [36]	0/0
1558	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH- 66 - [N24001661],NHAI,KERALA	10/2020	4/2024 (5/2025) [5/2025]	3,219.47 (3,713.14) [3,713.14]	1,911.28 (493.67) [13]	0/0
1559	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138],NHAI,KARNATAKA	9/2010	6/2018 (8/2023) [8/2023]	946.00 (1,046.56) [1,046.56]	827.99 (100.56) [62]	4/4
1560	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB - [N24001445],NHAI,GUJARAT	5/2020	7/2023 (-) [9/2023]	691.52 (-) [691.52]	342.22 (0.00) [2]	2/4
1561	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V - [N24001514],NHAI,PUNJAB	1/2021	1/2024 (12/2023) [12/2023]	1,060.29 (-) [1,060.29]	745.17 (0.00) [-1]	0/0
1562	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552],NHAI,KARNATAKA	3/2016	3/2019 (12/2023) [12/2024]	701.40 (-) [701.40]	282.96 (0.00) [69]	4/4
1563	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG II) [KURANKHED TO SHELAD FROM KM. 220.00 TO KM. 270.00] - [N24001801],NHAI,MAHARASHTRA	11/2019	2/2023 (-) [9/2023]	633.70 (-) [633.70]	244.30 (0.00) [7]	0/0
1564	4L OF HARIDWAR NAGINA SECTION DESIGN CH. LME FROM KM 13.829 TO KM 17.110 AND KM 26.077 TO KM 27.508 - [N24001554],NHAI,UTTARAKHAND	6/2020	2/2024 (-) [2/2024]	183.92 (-) [183.92]	20.62 (0.00) [0]	0/0
	<u>SHIPPING AND PORTS</u>					
1565	JAL MARG VIKAS PROJECT - [N25000072],IWAI,MULTI STATE	1/2018	3/2023 (-) [12/2026]	5,369.18 (4,633.10) [5,362.27]	2,498.52 (-6.91) [45]	3/7
	<u>SOCIAL JUSTICE</u>					
1566	CENTRE FOR DISABILITY SPORTS - [N38000001],CPWD,MADHYA PRADESH	2/2019	3/2024 (-) [3/2024]	170.99 (-) [170.99]	73.80 (0.00) [0]	1/5
	<u>STEEL</u>					
1567	SCREENING PLANT-III AT KIRANDUL - [N12000127],NMDC,CHHATTISGARH	3/2021	8/2024 (-) [8/2024]	2,092.97 (2,221.86) [2,221.86]	704.51 (128.89) [0]	2/5
1568	NMDC INTEGRATED STEEL PLANT - [N12000086],NMDC,CHHATTISGARH	1/2010	5/2015 (6/2023) [8/2023]	15,525.00 (23,840.00) [23,840.00]	23,131.35 (8,315.00) [99]	81/86
1569	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (7/2024)	2,907.00 (-)	1,362.32 (0.00)	3/8

	- [N12000124],NMDC,CHHATTISGARH		[5/2025]	[2,907.00]	[23]	
1570	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123],SAIL,CHHATTISGARH	11/2020	12/2023 (-) [4/2025]	542.24 (-) [542.24]	160.15 (0.00) [16]	0/0
1571	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122],SAIL,ODISHA	11/2020	5/2023 (-) [2/2024]	377.18 (-) [377.18]	299.73 (0.00) [9]	0/1
1572	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125],SAIL,ODISHA	1/2022	5/2025 (-) [5/2025]	970.18 (-) [970.18]	168.95 (0.00) [0]	0/1
1573	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095],SAIL,JHARKHAND	3/2015	10/2017 (12/2021) [9/2025]	1,034.01 (-) [1,034.01]	843.97 (0.00) [95]	0/2
1574	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT - [N12000126],SAIL,JHARKHAND	2/2022	6/2024 (-) [6/2024]	207.74 (-) [207.74]	104.27 (0.00) [0]	0/0
	TELECOMMUNICATIONS					
1575	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114],BSNL,MULTI STATE	3/2020	6/2021 (11/2021) [12/2023]	461.42 (461.42) [461.42]	134.92 (0.00) [30]	0/0
1576	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and - [N26000115],BSNL,MULTI STATE	3/2023	3/2024 (-) [3/2024]	185.27 (-) [185.27]	0.00 (0.00) [0]	0/0
1577	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT - [N26000116],BSNL,MULTI STATE	5/2023	8/2024 (-) [8/2024]	645.13 (-) [645.13]	0.00 (0.00) [0]	0/0
1578	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115],CPWD FOR TELECO,DELHI	10/2014	3/2018 (-) [12/2023]	248.20 (-) [248.20]	187.88 (0.00) [69]	3/5
1579	NETWORK FOR SPECTRUM - [N26000101],DOT,MULTI STATE	3/2012	7/2015 (12/2022) [9/2023]	13,334.00 (-) [13,334.00]	21,913.00 (0.00) [98]	0/0
	URBAN DEVELOPMENT					
1580	SURAT METRO RAIL PROJECT - [N28000138],MEGA,GUJARAT	3/2019	3/2024 (-) [3/2025]	12,020.32 (-) [12,020.32]	2,396.13 (0.00) [12]	0/1
1581	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137],MEGA,GUJARAT	3/2019	3/2024 (-) [12/2024]	5,384.17 (-) [5,384.17]	1,428.76 (0.00) [9]	0/1
1582	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122],MEGA,GUJARAT	11/2014	12/2018 (-) [12/2023]	10,773.00 (-) [12,925.22]	11,786.54 (2,152.22) [60]	0/1
1583	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151],BMRCL,KARNATAKA	6/2021	6/2026 (-) [6/2026]	14,788.10 (-) [14,788.10]	2,424.04 (0.00) [0]	0/76
1584	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2021 (-)	26,405.14 (-)	20,936.29 (0.00)	164/249

	- [N28000058],BMRCL,KARNATAKA		[3/2025]	[26,405.14]	[49]	
1585	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149],CPWD,CHHATTISGARH	5/2019	9/2020 (2/2024) [2/2024]	299.97 (299.97) [299.97]	150.93 (0.00) [41]	3/6
1586	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128],CPWD,DELHI	10/2016	7/2021 (-) [6/2024]	1,180.00 (-) [1,100.80]	36.69 (-79.20) [35]	0/6
1587	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI - [N28000153],CPWD,DELHI	1/2022	11/2024 (5/2025) [5/2025]	646.52 (-) [646.52]	38.46 (0.00) [6]	1/6
1588	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D - [N28000154],CPWD,HIMACHAL PRADESH	4/2022	11/2024 (-) [11/2024]	512.34 (-) [512.34]	0.00 (0.00) [0]	0/0
1589	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129],CPWD,DELHI	10/2016	3/2022 (6/2024) [6/2024]	1,128.00 (-) [1,128.00]	166.06 (0.00) [27]	0/0
1590	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097],CMRL,TAMIL NADU	6/2016	3/2018 (2/2021) [2/2021]	3,770.00 (-) [3,770.00]	2,527.73 (0.00) [0]	21/21
1591	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084],CMRL,TAMIL NADU	2/2009	12/2015 (-) [12/2015]	14,600.00 (-) [18,380.00]	17,619.68 (3,780.00) [0]	24/24
1592	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135],DMRC,DELHI	7/2019	3/2025 (-) [3/2026]	24,948.65 (-) [24,948.65]	7,812.66 (0.00) [12]	0/1
1593	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136],DMRC,DELHI	5/2017	12/2020 (9/2021) [9/2021]	565.00 (-) [565.00]	520.56 (0.00) [0]	1/1
1594	DELHI MRTS PHASE-III - [N28000056],DMRC,DELHI	9/2011	3/2016 (8/2021) [8/2021]	38,585.00 (-) [40,180.91]	40,217.45 (1,595.91) [0]	1/1
1595	KOCHI METRO RAIL PROJECT - [N28000081],KMRCL,KERALA	7/2012	7/2017 (9/2020) [9/2020]	5,181.79 (-) [6,218.14]	6,059.17 (1,036.35) [0]	0/0
1596	AGRA METRO RAIL PROJECT - [N28000145],LMRCL,UTTAR PRADESH	5/2019	3/2024 (-) [12/2025]	8,379.62 (-) [8,379.62]	2,611.47 (0.00) [21]	0/0
1597	KANPUR METRO RAIL PROJECT - [N28000144],LMRCL,UTTAR PRADESH	5/2019	3/2024 (-) [6/2026]	11,076.48 (-) [11,076.48]	5,323.53 (0.00) [27]	0/0
1598	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121],MMRC,MAHARASHTRA	12/2016	11/2021 (12/2023) [12/2023]	11,420.00 (13,656.22) [13,656.22]	10,829.00 (2,236.22) [25]	0/0
1599	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) - [N28000086],MMRCL,MAHARASHTRA	7/2013	3/2020 (-) [12/2023]	23,136.00 (-) [37,276.00]	24,123.86 (14,140.00) [45]	0/0
1600	INDORE METRO RAIL - [N28000125],MPMRCL,MADHYA PRADESH	11/2018	2/2023 (12/2026) [12/2026]	7,500.80 (-) [7,500.80]	1,615.18 (0.00) [46]	0/0
1601	BHOPAL METRO RAIL - [N28000124],MPMRCL,MADHYA PRADESH	11/2018	2/2023 (12/2026) [12/2026]	6,941.40 (-) [6,941.40]	1,271.31 (0.00) [46]	0/0

1602	NAGPUR METRO RAIL PROJECT PHASE II - [N28000155],NMRCL,MAHARASHTRA	12/2022	12/2027 (-) [12/2027]	6,708.00 (-) [6,708.00]	0.00 (0.00) [0]	0/0
1603	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105],NBCC,DELHI	7/2016	/ (-) [9/2023]	2,694.00 (-) [2,694.00]	1,832.74 (0.00) [-]	2/9
1604	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134],NCRTC,MULTI STATE	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	16,368.35 (0.00) [0]	1/8
1605	PATNA METRO RAIL CORPORATION LIMITED - [N28000148],PATNA METRO RAI,BIHAR	2/2019	6/2024 (-) [9/2024]	13,365.77 (-) [13,925.50]	1,353.32 (559.73) [3]	0/0
	WATER RESOURCES					
1606	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001],BPB,MAHARASHTRA	3/2017	12/2019 (9/2023) [12/2023]	233.57 (-) [233.57]	209.79 (0.00) [48]	0/0
1607	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036],BUIDCO,BIHAR	3/2018	10/2021 (3/2018) [12/2023]	294.02 (350.79) [294.02]	212.03 (0.00) [26]	0/0
1608	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027],BUIDCO,BIHAR	10/2017	9/2020 (11/2020) [3/2024]	254.13 (413.29) [413.29]	59.00 (159.16) [42]	0/0
1609	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051],BUIDCO,BIHAR	8/2017	6/2022 (-) [3/2024]	824.00 (734.09) [824.00]	198.83 (0.00) [21]	0/0
1610	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050],BUIDCO,BIHAR	8/2017	6/2022 (-) [3/2024]	578.89 (453.83) [578.89]	45.41 (0.00) [21]	0/0
1611	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043],BUIDCO,BIHAR	5/2017	11/2020 (5/2017) [11/2020]	191.62 (-) [191.62]	117.30 (0.00) [0]	0/0
1612	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026],BUIDCO,BIHAR	3/2018	7/2021 (12/2019) [12/2019]	230.06 (-) [230.06]	188.78 (0.00) [0]	0/0
1613	SAIDPUR SEWER NETWORK PATNA - [N30000039],BUIDCO,BIHAR	4/2015	1/2021 (-) [1/2021]	268.63 (-) [431.21]	478.03 (162.58) [0]	0/0
1614	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035],BUIDCO,BIHAR	3/2018	8/2021 (-) [8/2023]	305.19 (-) [305.19]	282.74 (0.00) [24]	0/0
1615	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044],BUIDCO,BIHAR	3/2017	5/2021 (3/2017) [5/2021]	277.42 (253.98) [277.42]	328.54 (0.00) [0]	0/0
1616	I AND D AND STP AT CHAPPRA - [N30000028],BUIDCO,BIHAR	11/2018	12/2020 (-) [8/2023]	236.15 (-) [236.15]	110.63 (0.00) [32]	0/0
1617	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040],BUIDCO,BIHAR	5/2017	4/2021 (5/2017) [4/2021]	356.37 (364.00) [356.37]	290.70 (0.00) [0]	0/0
1618	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037],BUIDCO,BIHAR	12/2014	3/2020 (-) [6/2020]	225.77 (-) [398.90]	360.57 (173.13) [0]	0/0
1619	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018],DJB,DELHI	5/2017	5/2020 (-) [5/2020]	344.81 (-) [344.81]	0.00 (0.00) [0]	0/0
1620	REHABILITATION AND	5/2016	2/2022	239.11	252.01	0/0

	UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016],DJB,DELHI		(9/2023) [9/2023]	(314.71) [239.11]	(0.00) [19]	
1621	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017],DJB,DELHI	12/2018	1/2021 (-) [3/2022]	515.07 (-) [515.07]	388.08 (0.00) [0]	0/0
1622	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014],DJB,DELHI	3/2017	12/2022 (-) [9/2023]	665.78 (-) [665.78]	522.28 (0.00) [9]	0/0
1623	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015],DJB,DELHI	5/2016	12/2021 (-) [6/2023]	211.79 (223.70) [211.79]	167.48 (0.00) [0]	0/0
1624	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048],KMDA, WEST BENGAL	1/2018	12/2021 (2/2021) [9/2023]	172.10 (-) [172.10]	47.20 (0.00) [21]	0/0
1625	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047],KMDA, WEST BENGAL	12/2014	4/2020 (-) [4/2020]	272.32 (341.68) [272.32]	298.49 (0.00) [0]	0/0
1626	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031],KMDA, WEST BENGAL	12/2018	4/2022 (-) [12/2024]	234.31 (-) [234.31]	0.00 (0.00) [32]	0/0
1627	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033],KMDA, WEST BENGAL	3/2018	6/2022 (-) [3/2024]	165.16 (-) [165.16]	0.00 (0.00) [21]	0/0
1628	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049],KMDA, WEST BENGAL	10/2017	12/2021 (2/2021) [3/2024]	164.93 (-) [164.93]	45.45 (0.00) [27]	0/0
1629	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046],KMDA, WEST BENGAL	2/2014	12/2019 (1/2023) [6/2022]	274.76 (332.56) [274.76]	267.15 (0.00) [0]	0/0
1630	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030],KMDA, WEST BENGAL	3/2019	4/2022 (-) [12/2024]	287.53 (-) [287.53]	0.00 (0.00) [32]	0/0
1631	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034],KMDA, WEST BENGAL	8/2017	9/2022 (-) [12/2026]	307.12 (-) [653.67]	0.00 (346.55) [51]	0/0
1632	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042],KMDA, WEST BENGAL	5/2018	2/2022 (9/2020) [6/2024]	160.00 (154.73) [154.73]	56.61 (-5.27) [28]	0/0
1633	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029],KMDA, WEST BENGAL	1/2019	4/2022 (-) [12/2024]	384.96 (-) [384.96]	0.00 (0.00) [32]	0/0
1634	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045],KMDA, WEST BENGAL	8/2017	12/2021 (2/2021) [8/2023]	185.22 (-) [185.22]	49.99 (0.00) [20]	0/0
1635	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032],KMDA, WEST BENGAL	5/2018	2/2022 (-) [3/2024]	198.43 (224.69) [224.69]	32.86 (26.26) [25]	0/0
1636	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020	10,151.04	21,727.98	8/19

	- [N30000002],PPA,ANDHRA PRADESH		(-) [3/2024]	(-) [55,548.87]	(45,397.83) [48]	
1637	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021],UPJalNigam,UTTAR PRADESH	1/2019	12/2021 (1/2020) [6/2023]	231.79 (234.03) [234.03]	94.19 (2.24) [0]	0/0
1638	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008],UPJalNigam,UTTAR PRADESH	10/2017	3/2022 (2/2021) [4/2024]	213.62 (261.12) [261.12]	69.96 (47.50) [25]	0/0
1639	MATHURA SEWERAGE SCHEME - [N30000019],UPJalNigam,UTTAR PRADESH	12/2017	12/2020 (6/2018) [12/2020]	460.45 (-) [460.45]	295.23 (0.00) [0]	0/0
1640	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010],UPJalNigam,UTTAR PRADESH	3/2018	9/2021 (-) [9/2023]	967.23 (708.70) [967.23]	220.73 (0.00) [24]	0/0
1641	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006],UPJalNigam,UTTAR PRADESH	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	276.97 (0.00) [0]	0/0
1642	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022],UPJalNigam,UTTAR PRADESH	1/2019	10/2021 (-) [3/2023]	206.05 (-) [206.05]	137.58 (0.00) [0]	0/0
1643	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013],UPJalNigam,UTTAR PRADESH	3/2019	8/2021 (-) [3/2024]	271.39 (-) [271.39]	59.32 (0.00) [31]	0/0
1644	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025],UPJalNigam,UTTAR PRADESH	3/2019	7/2021 (5/2020) [4/2024]	298.12 (-) [213.91]	36.94 (-84.21) [33]	0/0
1645	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024],UPJalNigam,UTTAR PRADESH	2/2019	6/2022 (-) [4/2024]	681.78 (-) [690.71]	0.00 (8.93) [22]	0/0
1646	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004],UKJalNigam,UTTARAKHAND	3/2017	11/2019 (-) [2/2022]	158.00 (-) [158.00]	98.88 (0.00) [0]	0/0
	Total			23,92,837.89 (7,62,556.44) [28,58,394.39]	15,21,550.38 (4,65,556.50)	3054/5590


Summary of projects in the Flash Report for the month of July, 2023

Project Implementation - Current Status:

Number of Projects in Previous Month	1643
Number of Projects completed/dropped/frozen in Current Month	34
	0
Number of Projects Added in Current Month	12
Number of Projects in Current Month	1646

Brief Analysis

Project Status with respect to Original Schedule: Out of 1646 projects, 17 projects are ahead of schedule, 475 projects are on schedule 809 projects are delayed. 315 projects do not have fixed dates of commissioning. 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

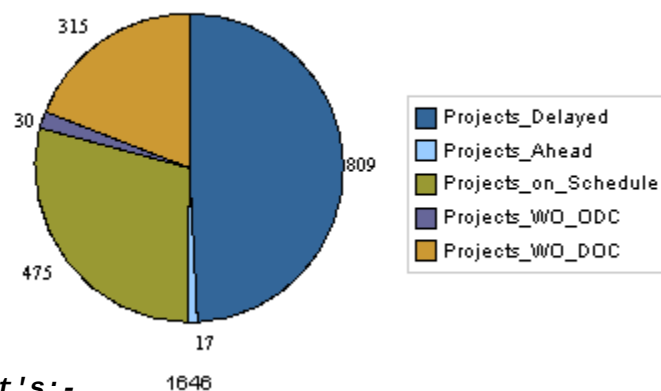


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1646 projects when sanctioned, was of the order of Rs. 2392837.89 crore but this was subsequently revised to Rs. 2858394.39 crore implying a cost overrun of 19.5%. The expenditure incurred on these projects till July, 2023 is Rs. 1521550.38 crore, which is 53.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

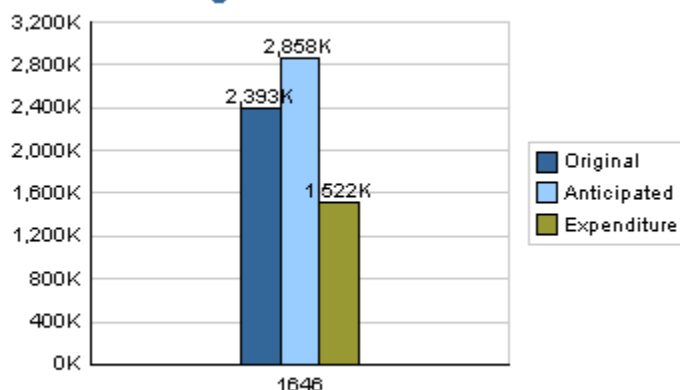

Sector wise current status of projects on the Flash Report

RENEWABLE ENERGY


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

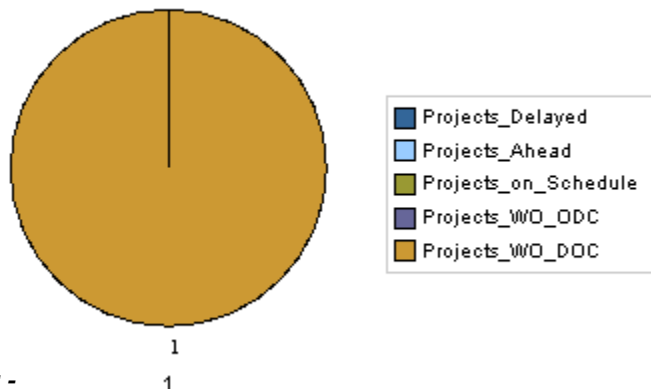


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 271.9 crore but this was subsequently anticipated to Rs. 366.12 crore implying a cost overrun of 34.7%. The expenditure incurred on these projects till July, 2023 is Rs. 329.49 crore, which is 90% of the anticipated cost of the projects.

Figures are in Rs. Crore

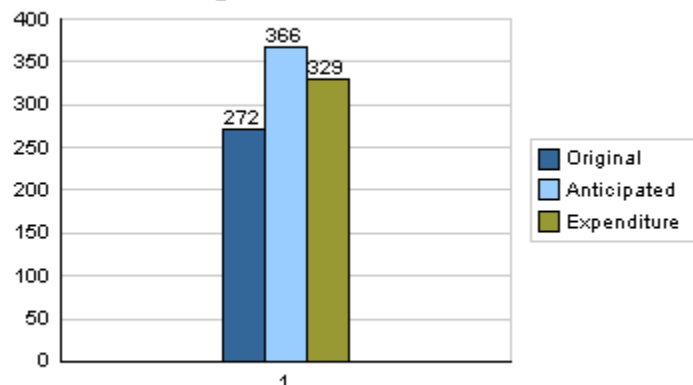

Sector wise current status of projects on the Flash Report

DONER


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

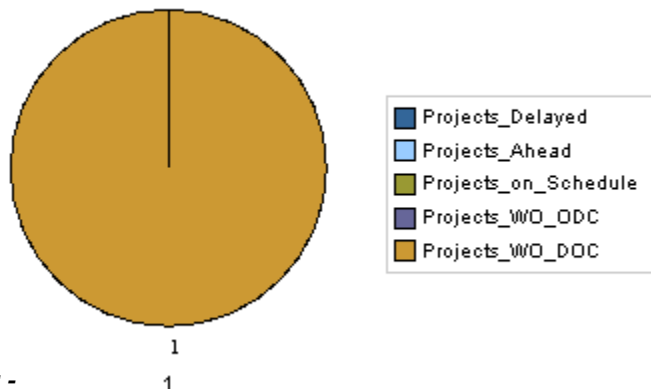

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 151.33 crore but this was subsequently anticipated to Rs. 151.33 crore. The expenditure incurred on these projects till July, 2023 is Rs. 148.33 crore, which is 98% of the anticipated cost of the projects.

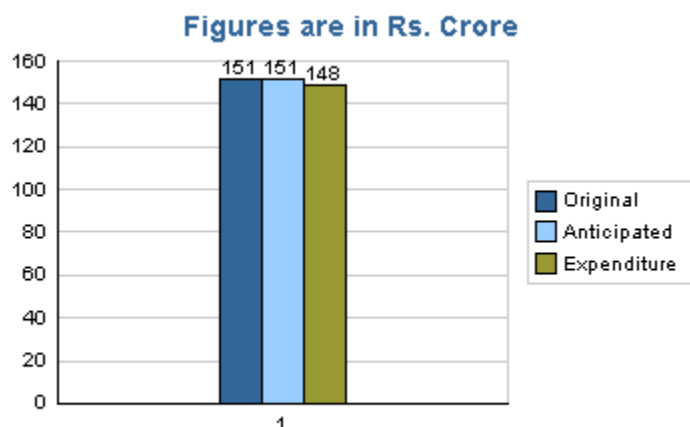

Sector wise current status of projects on the Flash Report


DPIIT

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

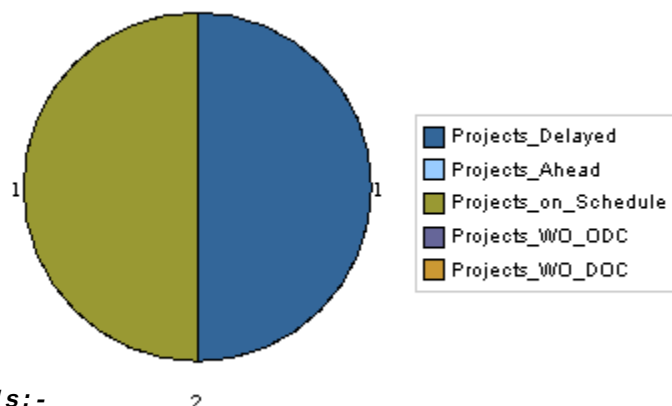


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 24857 crore but this was subsequently anticipated to Rs. 25485 crore implying a cost overrun of 2.5%. The expenditure incurred on these projects till July, 2023 is Rs. 13754.67 crore, which is 54% of the anticipated cost of the projects.

Figures are in Rs. Crore

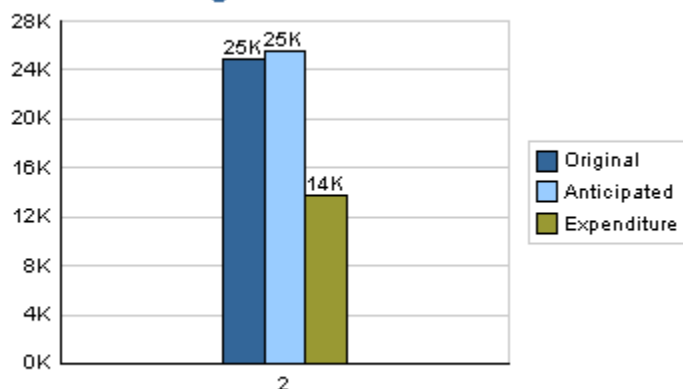

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	5
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are delayed. 1 project does not have fixed dates of commissioning.

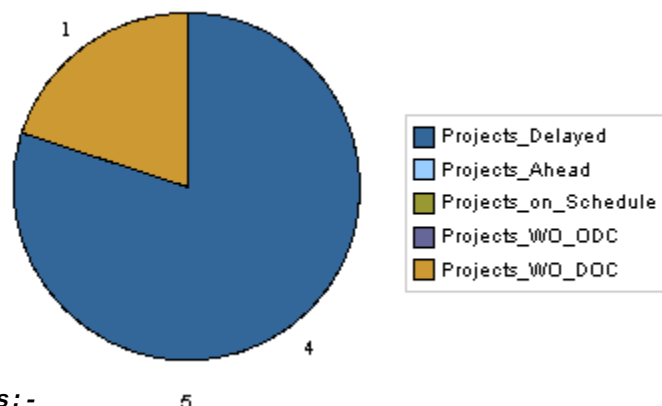


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 2025.73 crore but this was subsequently anticipated to Rs. 2767.45 crore implying a cost overrun of 36.6%. The expenditure incurred on these projects till July, 2023 is Rs. 1980.06 crore, which is 71.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

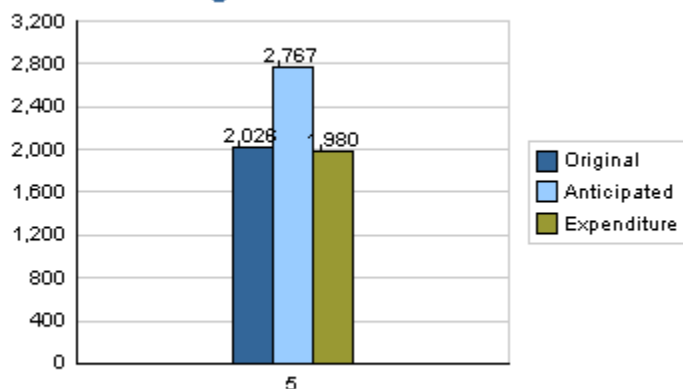

Sector wise current status of projects on the Flash Report


DEPARTMENT OF HIGHER EDUCATION

Current Status:

Number of Projects	21
Number of Projects On Schedule	1
Number of Projects Delayed	13
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 21 projects, 1 project is ahead of schedule, 1 project is on schedule 13 projects are delayed. 6 projects do not have fixed dates of commissioning.

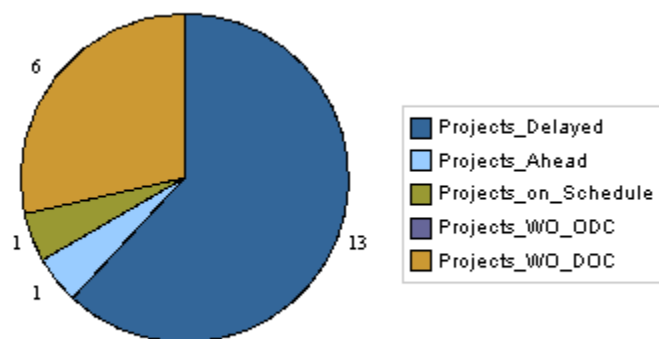


Total No Of Project's:-

21

Investment Scenario

Total original cost of implementation of 21 projects when sanctioned, was of the order of Rs. 9763.78 crore but this was subsequently anticipated to Rs. 10117.16 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till July, 2023 is Rs. 6249.93 crore, which is 61.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

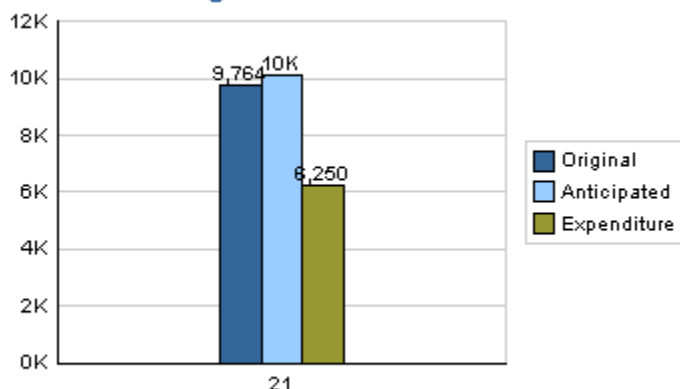

Sector wise current status of projects on the Flash Report

COMMERCE


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

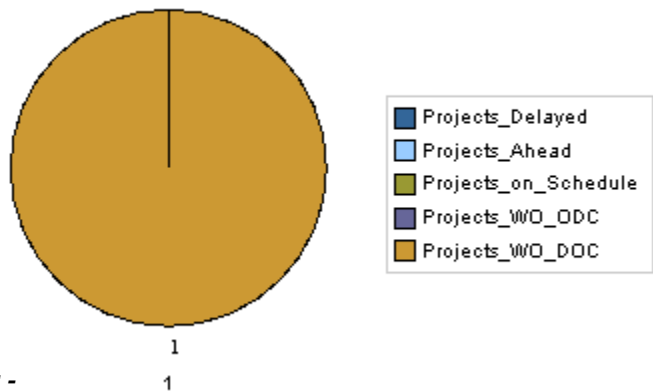


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 302.64 crore but this was subsequently anticipated to Rs. 302.64 crore. The expenditure incurred on these projects till July, 2023 is Rs. 30 crore, which is 9.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

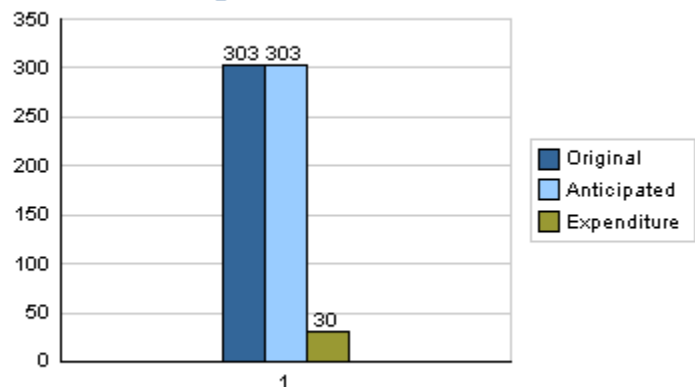

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

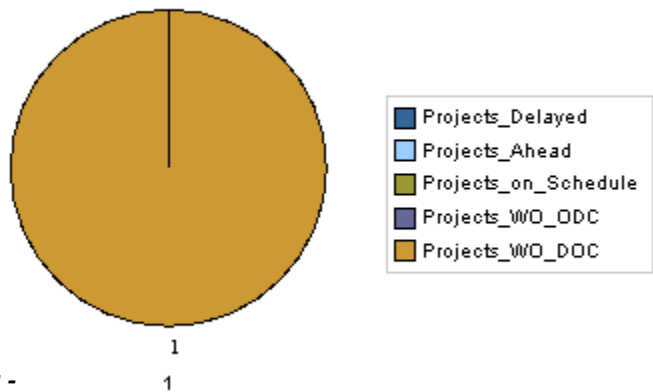

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 246.31 crore but this was subsequently anticipated to Rs. 195 cr. The expenditure incurred on these projects till July, 2023 is Rs. 187.02 crore, which is 95.9% of the anticipated cost of the projects.

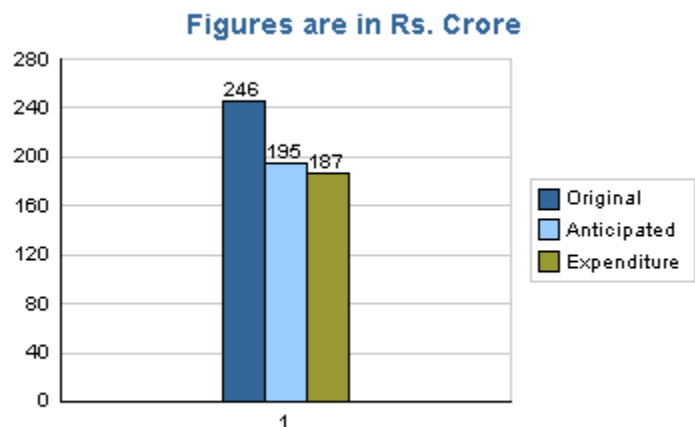

Sector wise current status of projects on the Flash Report

WATER RESOURCES

Current Status:


Number of Projects **41**

Number of Projects Delayed **25**

Number of Projects Without Date Of Commissioning **16**

Brief Analysis

Project Status with respect to Original Schedule: Out of 41 projects, 25 projects are delayed. 16 projects do not have fixed dates of commissioning.

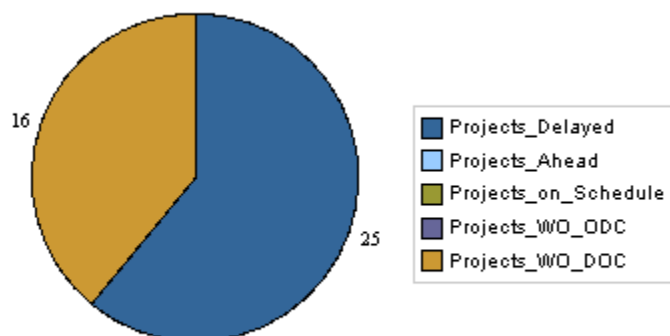


Total No Of Project's:-

41

Investment Scenario

Total original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 23466.28 crore but this was subsequently anticipated to Rs. 69700.98 crore implying a cost overrun of 197%. The expenditure incurred on these projects till July, 2023 is Rs. 28027.73 crore, which is 40.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

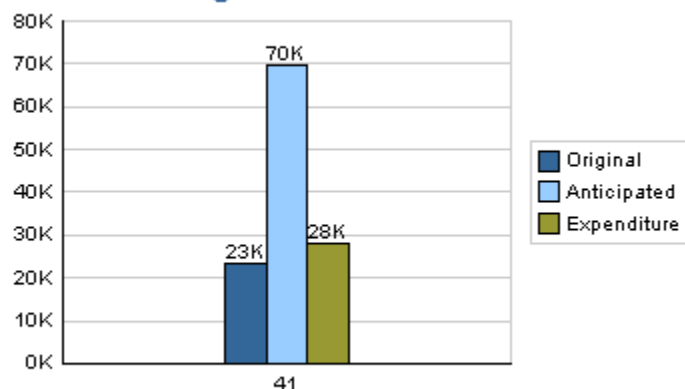

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	26
Number of Projects On Schedule	4
Number of Projects Delayed	16
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 4 projects are on schedule 16 projects are delayed. 5 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

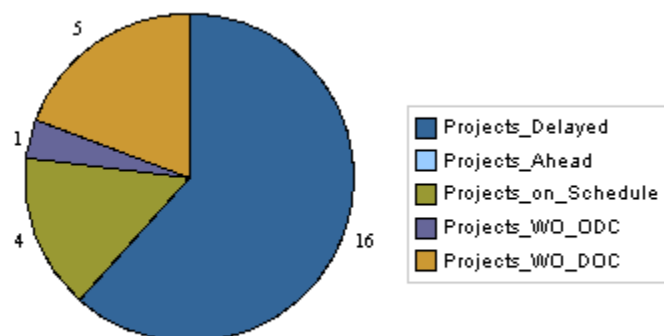


Total No Of Project's:-

26

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 282284.07 crore but this was subsequently anticipated to Rs. 307705.3 crore implying a cost overrun of 9%. The expenditure incurred on these projects till July, 2023 is Rs. 179449.91 crore, which is 58.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

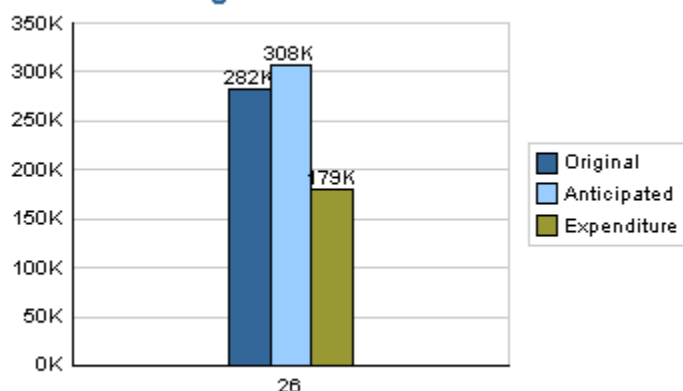

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule 3 projects are delayed.

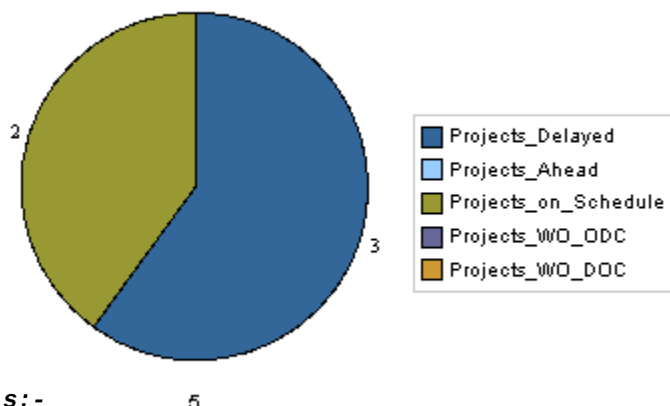


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 14874.02 crore but this was subsequently anticipated to Rs. 14874.02 crore. The expenditure incurred on these projects till July, 2023 is Rs. 22235.8 crore, which is 149.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

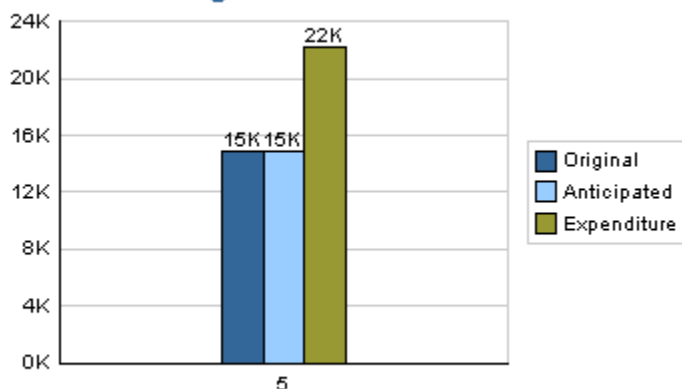

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

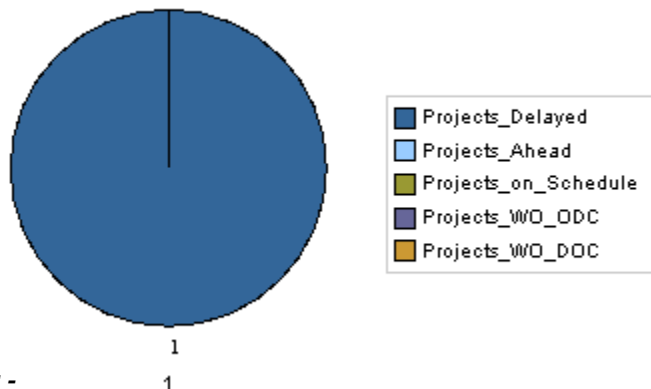

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 5369.18 crore but this was subsequently anticipated to Rs. 5362.27 cr The expenditure incurred on these projects till July, 2023 is Rs. 2498.52 crore, which is 46.6% of the anticipated cost of the projects.

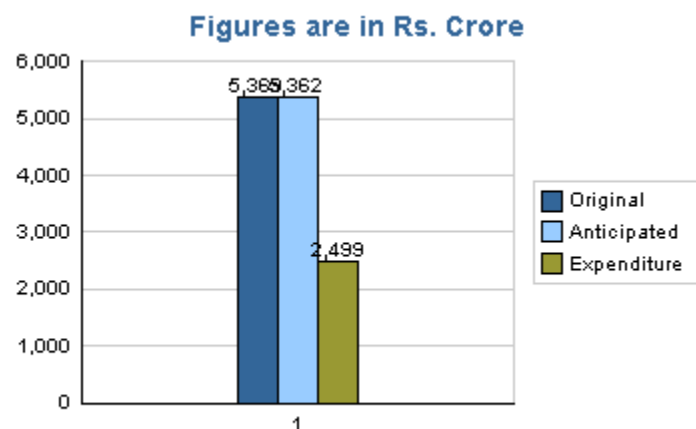

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	972
Number of Projects On Schedule	298
Number of Projects Delayed	419
Number of Projects Ahead	11
Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	238

Brief Analysis

Project Status with respect to Original Schedule: Out of 972 projects, 11 projects are ahead of schedule, 298 projects are on schedule 419 projects are delayed. 238 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

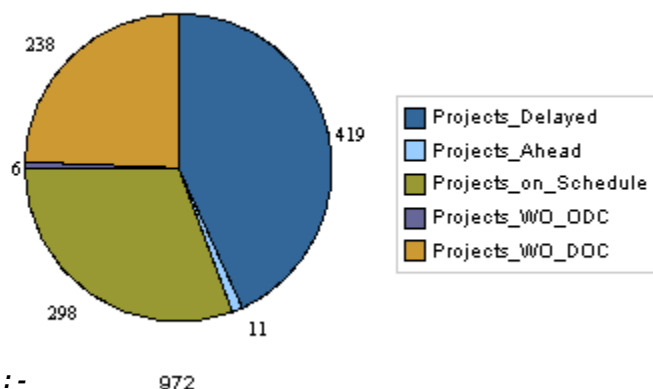


Total No Of Project's:-

972

Investment Scenario

Total original cost of implementation of 972 projects when sanctioned, was of the order of Rs. 720090.4 crore but this was subsequently anticipated to Rs. 756570.16 crore implying a cost overrun of 5.1%. The expenditure incurred on these projects till July, 2023 is Rs. 362069.78 crore, which is 47.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

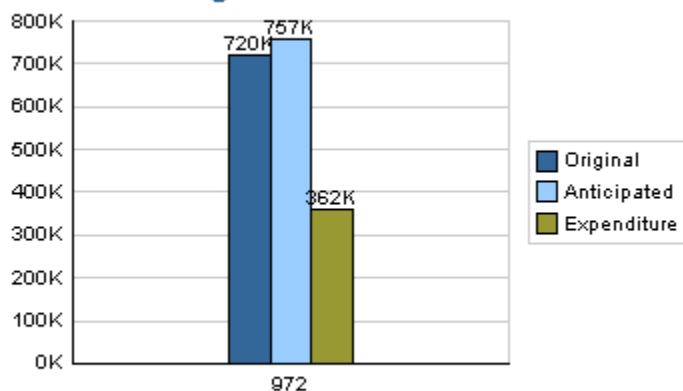

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	148
Number of Projects On Schedule	3
Number of Projects Delayed	98
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	23
Number of Projects Without Date Of Commissioning	23

Brief Analysis

Project Status with respect to Original Schedule: Out of 148 projects, 1 project is ahead of schedule, 3 projects are on schedule 98 projects are delayed. 23 projects do not have fixed dates of commissioning. 23 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

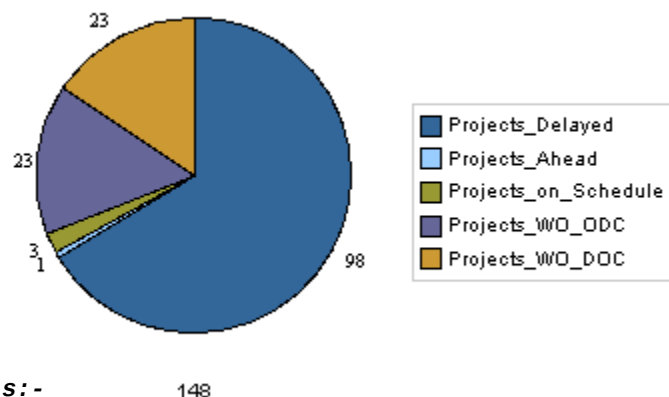


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 350140.21 crore but this was subsequently anticipated to Rs. 593520.1 crore implying a cost overrun of 69.5%. The expenditure incurred on these projects till July, 2023 is Rs. 368880.63 crore, which is 62.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

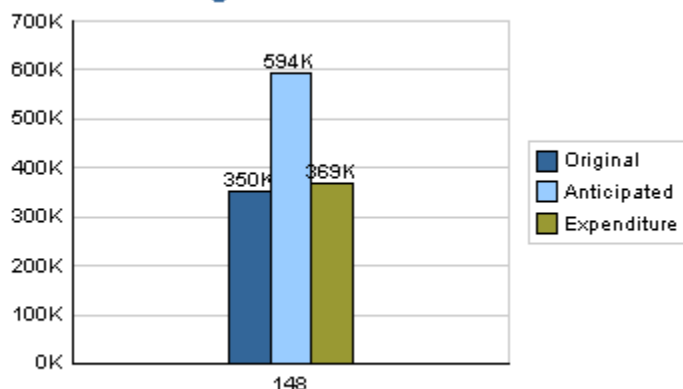

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	8
Number of Projects On Schedule	1
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 1 project is on schedule 4 projects are delayed. 3 projects do not have fixed dates of commissioning.

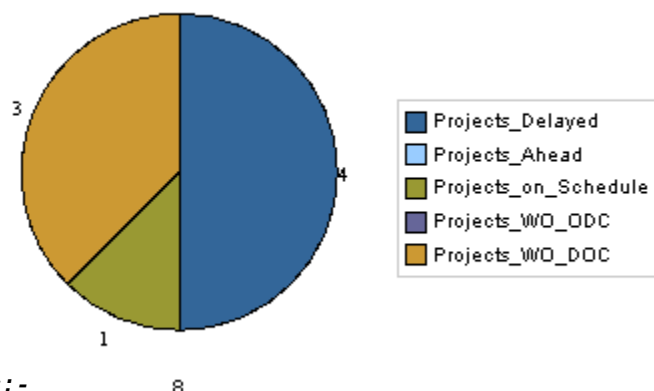


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6032.68 crore but this was subsequently anticipated to Rs. 6080.84 crore implying a cost overrun of .8%. The expenditure incurred on these projects till July, 2023 is Rs. 2153.6 crore, which is 35.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

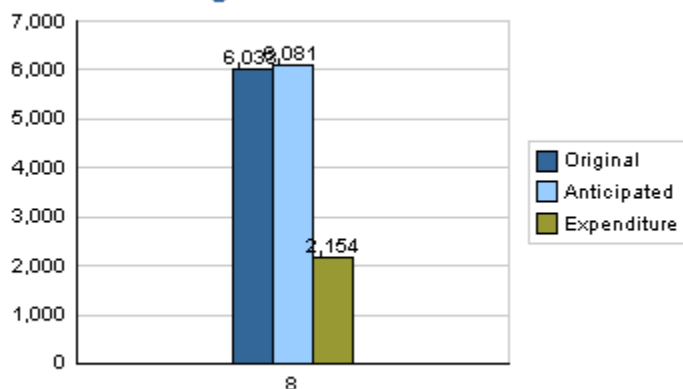

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	89
Number of Projects On Schedule	30
Number of Projects Delayed	55
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 89 projects, 1 project is ahead of schedule, 30 projects are on schedule 55 projects are delayed. 3 projects do not have fixed dates of commissioning.

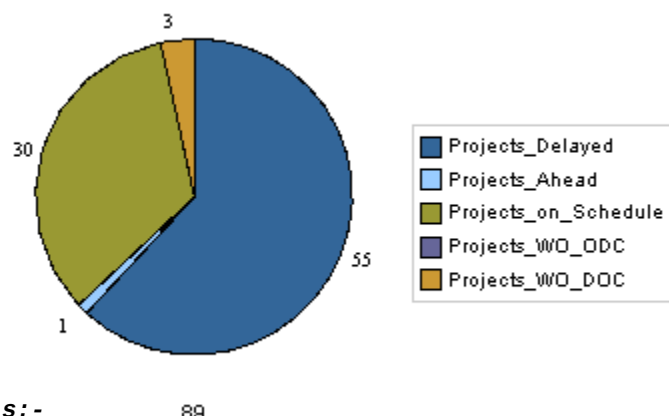


Total No Of Project's:-

89

Investment Scenario

Total original cost of implementation of 89 projects when sanctioned, was of the order of Rs. 250060.99 crore but this was subsequently anticipated to Rs. 305013.33 crore implying a cost overrun of 22%. The expenditure incurred on these projects till July, 2023 is Rs. 163456.26 crore, which is 53.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

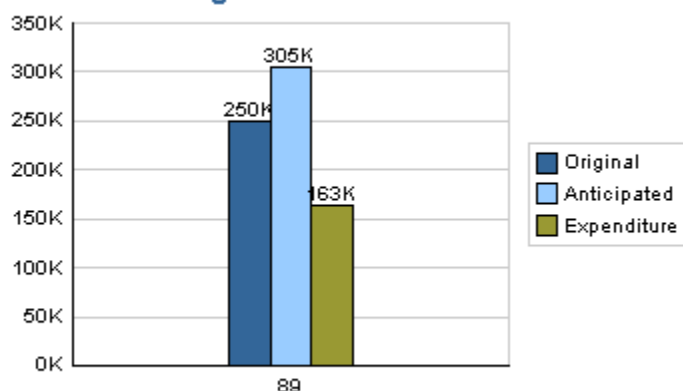

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	148
Number of Projects On Schedule	62
Number of Projects Delayed	81
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 148 projects, 2 projects are ahead of schedule, 62 projects are on schedule 81 projects are delayed. 3 projects do not have fixed dates of commissioning.

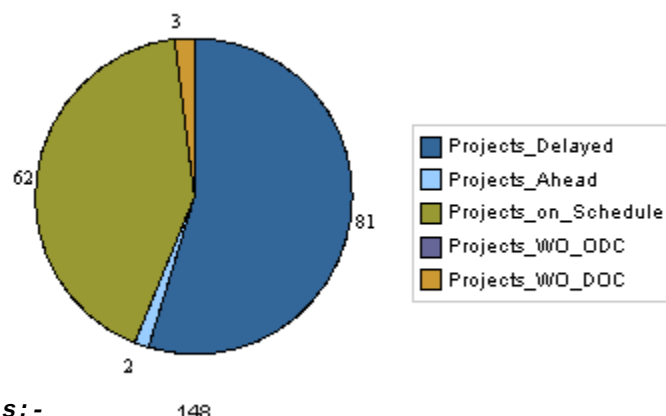


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 364674.15 crore but this was subsequently anticipated to Rs. 386358.19 crore implying a cost overrun of 5.9%. The expenditure incurred on these projects till July, 2023 is Rs. 163771.71 crore, which is 42.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

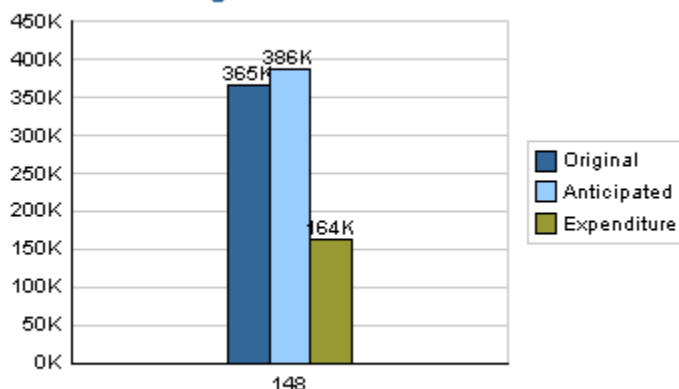

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	8
Number of Projects On Schedule	3
Number of Projects Delayed	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule 5 projects are delayed.

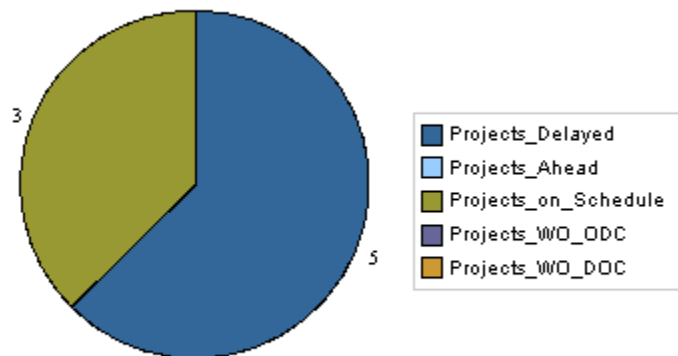


Total No Of Project's:-

8

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 23656.32 crore but this was subsequently anticipated to Rs. 32100.21 crore implying a cost overrun of 35.7%. The expenditure incurred on these projects till July, 2023 is Rs. 26775.25 crore, which is 83.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

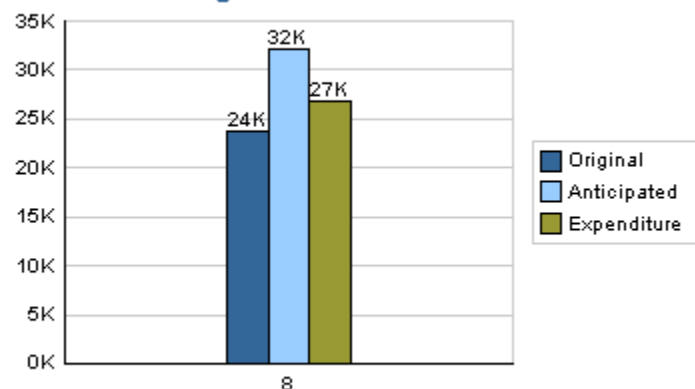

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	7
Number of Projects Delayed	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 7 projects are delayed.

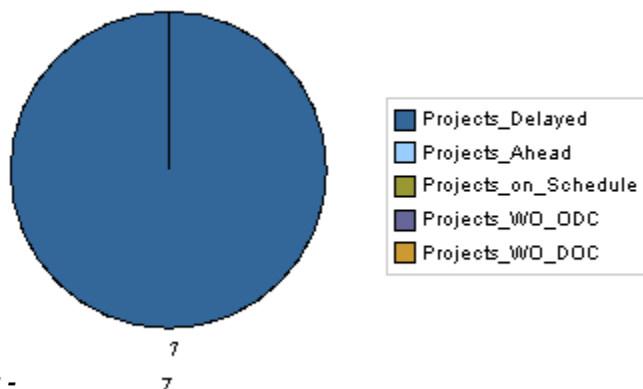


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 7333.99 crore but this was subsequently anticipated to Rs. 8585.77 crore implying a cost overrun of 17.1%. The expenditure incurred on these projects till July, 2023 is Rs. 3918.17 crore, which is 45.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

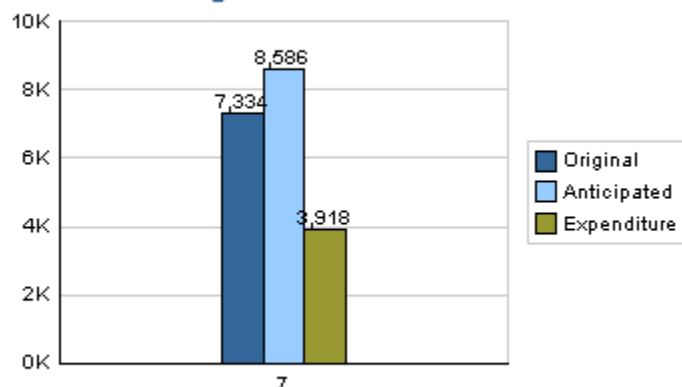

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Ahead	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is ahead of schedule, 1 project is on schedule

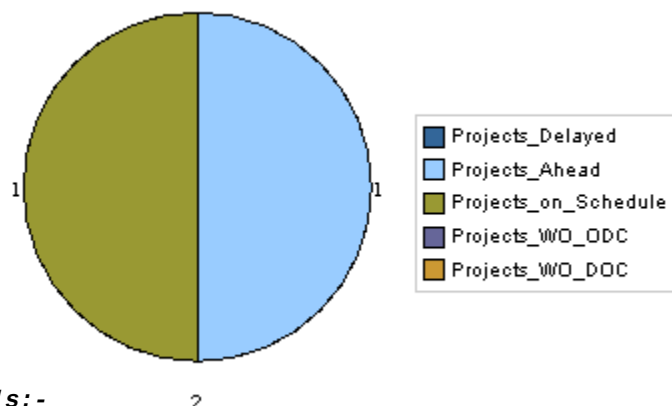


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 425.57 crore but this was subsequently anticipated to Rs. 425.57 crore The expenditure incurred on these projects till July, 2023 is Rs. 18.83 crore, which is 4.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

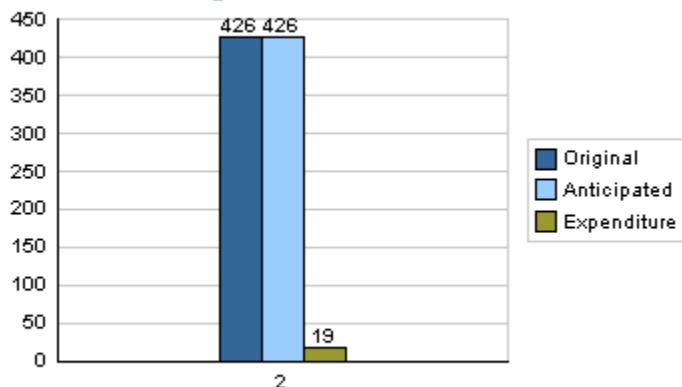

Sector wise current status of projects on the Flash Report

FINANCE


Current Status:

Number of Projects **3**

Number of Projects Without Date Of Commissioning **3**

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects do not have fixed dates of commissioning.

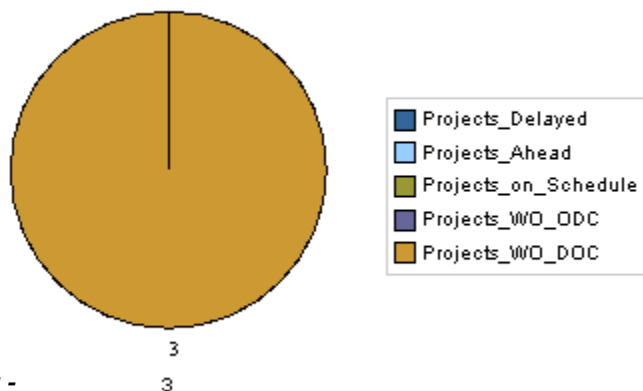


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 786.27 crore but this was subsequently anticipated to Rs. 831.04 crore implying a cost overrun of 5.7%. The expenditure incurred on these projects till July, 2023 is Rs. 721.51 crore, which is 86.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

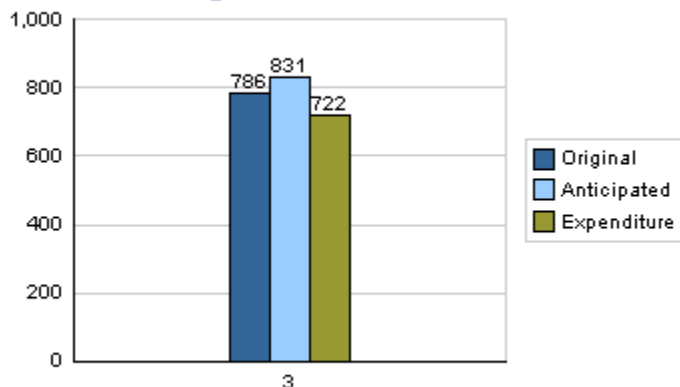

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	123
Number of Projects On Schedule	65
Number of Projects Delayed	51

Number of Projects Without Date Of Commissioning 7

Brief Analysis

Project Status with respect to Original Schedule: Out of 123 projects, 65 projects are on schedule 51 projects are delayed. 7 projects do not have fixed dates of commissioning.

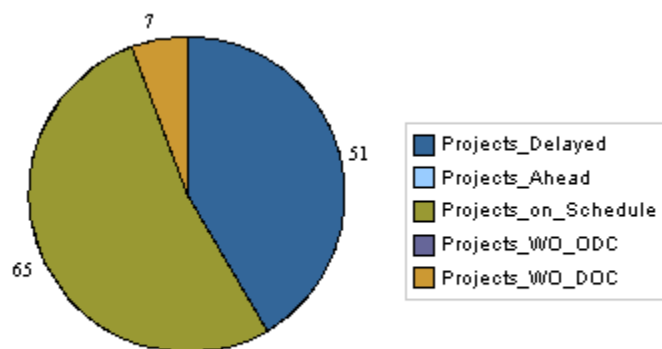


Total No Of Project's:-

123

Investment Scenario

Total original cost of implementation of 123 projects when sanctioned, was of the order of Rs. 171148.45 crore but this was subsequently anticipated to Rs. 178417.46 crore implying a cost overrun of 4.2%. The expenditure incurred on these projects till July, 2023 is Rs. 71469.16 crore, which is 40.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

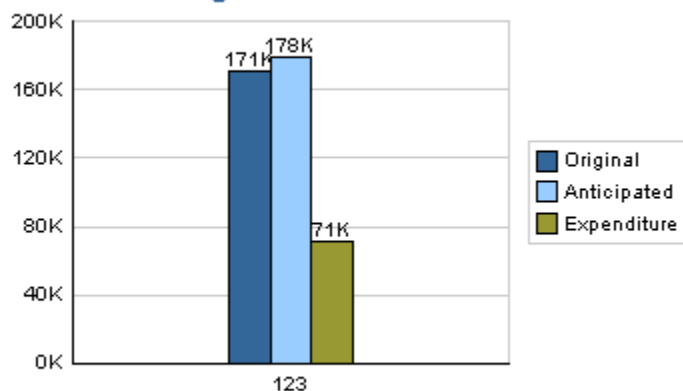

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	27
Number of Projects On Schedule	2
Number of Projects Delayed	22

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 27 projects, 2 projects are on schedule 22 projects are delayed. 3 projects do not have fixed dates of commissioning.

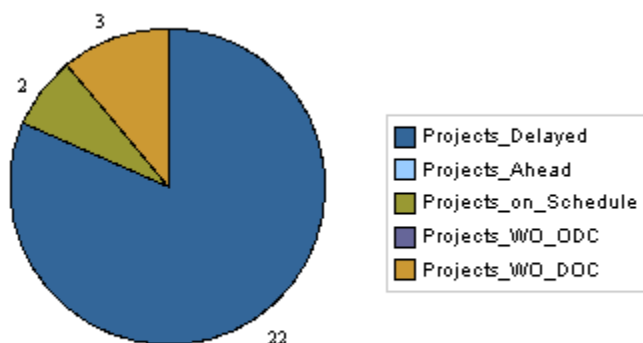


Total No Of Project's:-

27

Investment Scenario

Total original cost of implementation of 27 projects when sanctioned, was of the order of Rs. 17964.63 crore but this was subsequently anticipated to Rs. 19854.46 crore implying a cost overrun of 10.5%. The expenditure incurred on these projects till July, 2023 is Rs. 10412.47 crore, which is 52.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

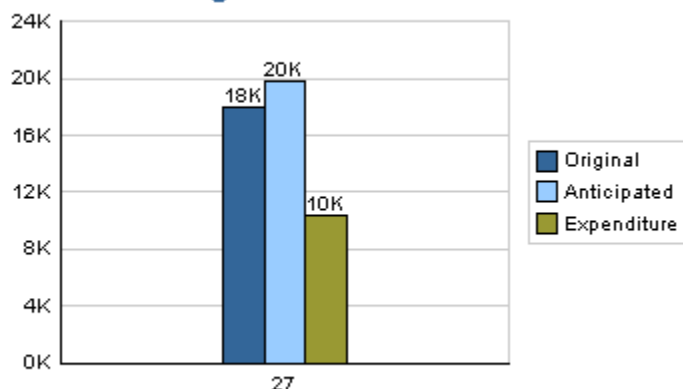

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 1 project is on schedule 4 projects are delayed.

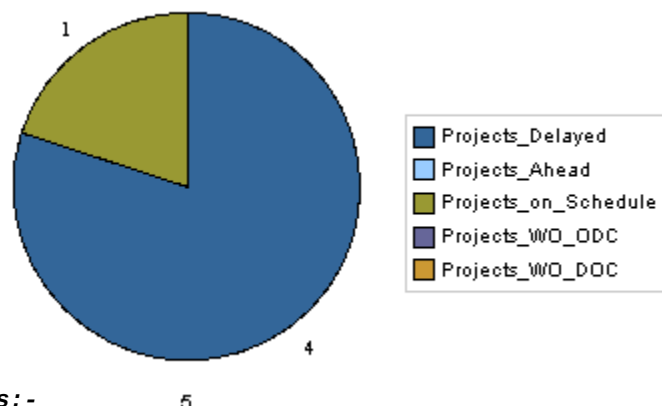


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 116741 crore but this was subsequently anticipated to Rs. 133439 crore implying a cost overrun of 14.3%. The expenditure incurred on these projects till July, 2023 is Rs. 92937.75 crore, which is 69.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

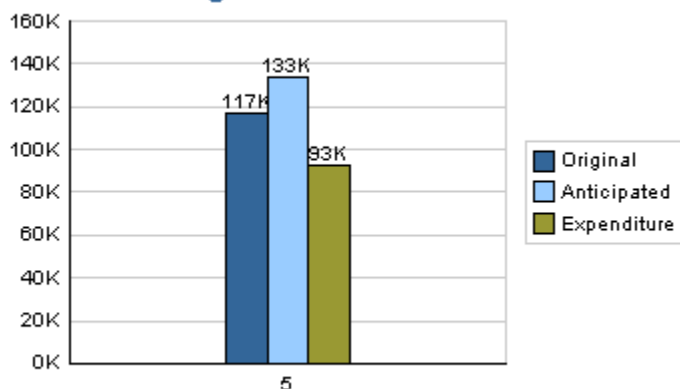

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JULY 2023)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN AND NICOBAR ISLANDS	8	2,611.46	2,882.82	1,854.1
2	ANDHRA PRADESH	74	1,22,477.51	1,79,092	99,544.89
3	ARUNACHAL PRADESH	32	52,608.96	67,629.07	29,188.34
4	ASSAM	56	57,074.33	65,950.38	29,002.97
5	BIHAR	86	1,08,768.6	1,32,337.99	79,782.5
6	CHHATTISGARH	44	77,804.08	87,320.2	51,613.38
7	DELHI	28	91,635.39	95,346.65	65,013
8	GOA	10	6,242.45	6,302.55	4,042.44
9	GUJARAT	73	1,30,509.95	1,43,803.25	65,420.12
10	HARYANA	32	67,853.02	70,747.3	25,791.87
11	HIMACHAL PRADESH	24	24,989.5	36,960.75	23,144.72
12	JAMMU AND KASHMIR	38	63,381.49	98,398.39	53,001.86
13	JHARKHAND	52	76,888.01	83,943.49	42,444.9
14	KARNATAKA	60	94,167.93	1,01,868.75	45,148.98
15	KERALA	29	61,846.14	66,765.25	32,368.44
16	LADAKH	8	2,767.29	2,926.96	1,063.31
17	MADHYA PRADESH	79	67,847.14	75,829.53	38,907.78
18	MAHARASHTRA	220	2,10,341.93	2,32,272.9	1,23,779.21
19	MANIPUR	33	14,725.78	24,594.4	16,906.83
20	MEGHALAYA	14	5,372.73	12,735.93	2,552.69
21	MIZORAM	23	12,027.85	22,182.15	15,691.33
22	MULTI STATE	69	2,93,889.31	3,99,752.12	2,40,637.37
23	NAGALAND	32	11,768.33	16,118.74	7,033.66
24	ODISHA	77	1,19,944.28	1,26,879.62	52,843.47
25	PUDUCHERRY	1	195	195	2.67
26	PUNJAB	32	29,317.7	29,178.81	10,022.3
27	RAJASTHAN	69	79,172.72	84,416.89	44,622.17
28	SIKKIM	20	14,011.54	20,897.41	9,757.02
29	TAMIL NADU	73	2,11,480.1	2,34,102.82	1,15,954.67
30	TELANGANA	46	32,326.07	35,213.7	21,995.44
31	TRIPURA	17	4,962.74	5,272.25	2,153.93
32	UTTAR PRADESH	97	1,38,486.46	1,54,094.86	89,133.14
33	UTTARAKHAND	30	36,188.46	54,008.18	35,025.99
34	WEST BENGAL	60	69,153.64	88,373.28	46,104.89
TOTAL		1,646	23,92,837.89	28,58,394.39	15,21,550.38

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	19,220.00	20,460.00	12/2015 -	03/2024
	Total		11,459.00 -	19,220.00	20,460.00		
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	8,990.00	7,656.86	12/2015 -	02/2021
	Total		5,907.11 -	8,990.00	7,656.86		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
3	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	7,103.00	5,911.37	03/2013 12/2021	12/2024
4	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,998.00	10,831.04	11/2020 07/2022	08/2023
5	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	17,007.00	14,880.63	06/2019 10/2022	06/2024
	<u>Power Grid Corporation Of India Limited</u>						
6	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	5,600.77	12/2018 -	12/2024
7	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	2,635.55	1,952.75	02/2020 -	03/2024
8	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]	3/2019	1,326.00 -	1,326.00	1,367.92	03/2023 -	09/2023
	<u>Satluj Jal Vidyut Nigam Limited</u>						
9	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	1,272.29	1,172.12	12/2021 -	08/2023
	<u>Thdc India Limited</u>						
10	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	4,825.60	5,601.35	02/2016 06/2022	06/2024
	Total		38,261.18 -	54,296.76	47,317.95		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
11	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,805.17	3,491.85	03/2021 03/2025	03/2026

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
12	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	31,304.00	- -	-
	<u>East Central Railways</u>						
13	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,110.00	1,165.40	03/2012 -	06/2023
14	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,510.00	2,102.69	- -	03/2024
15	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	2,445.51	03/2020 -	03/2024
16	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	1,346.62	03/2020 -	03/2023
17	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	4/2004	372.14 -	1,700.00	2,044.95	- -	03/2024
	<u>East Coast Railway</u>						
18	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	4/2005	810.78 -	1,928.07	980.13	06/2021 -	03/2025
	<u>Eastern Railways</u>						
19	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	2,137.81	980.46	03/2022 -	03/2025
	<u>North East Frontier Railway</u>						
20	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	9,362.06	6,591.01	03/2014 -	02/2024
21	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	7,876.92	3,290.96	12/2015 -	12/2023
22	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	2,326.52 -	6,663.00	2,556.74	03/2015 -	03/2026
23	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	4,059.65	2,898.81	03/2022 -	03/2026
24	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	2,647.51	1,999.72	03/2019 -	01/2024
25	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,304.62	1,104.78	03/2019 -	-
26	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	14,322.79	13,763.33	03/2011 03/2025	03/2025
	<u>North Eastern Railway</u>						
27	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	2,560.00	2,121.53	03/2022 -	10/2023
	<u>Northern Railway</u>						
28	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024
	<u>Rail Vikas Nigam Ltd.</u>						
29	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	4,834.54	3,020.54	03/2016 -	07/2025

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
30	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	3,955.01	12/2026 -	03/2025
31	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	8,964.35	5,943.37	03/2016 -	03/2026
32	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,300.00	3,204.74	03/2023 -	03/2024
33	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	943.60 -	1,500.00	1,251.40	03/2022 -	12/2023
34	VIZIANAGARAM-SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	3,327.72	3,674.36	12/2024 -	12/2026
35	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,536.00	1,846.81	03/2020 -	08/2023
36	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	4,306.50	12/2023 -	12/2023
37	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,552.26	1,772.12	03/2019 10/2023	05/2023
38	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,457.79	1,491.77	03/2019 -	03/2024
39	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	5,013.33	12/2023 -	12/2023
	<u>South Central Railway</u>						
40	KOTLALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,500.98	1,129.92	03/2009 -	03/2027
41	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	1,723.00 1.00	3,381.68	2,532.11	03/2000 -	03/2000
	<u>South East Central Railway</u>						
42	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	1,096.00	230.25	12/2021 -	12/2025
	<u>South Western Railway</u>						
43	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,960.00	1,887.40	03/2019 -	12/2024
	<u>Southern Railway</u>						
44	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	3,118.34	1,877.71	02/2019 -	03/2025
45	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	2/2015	1,431.90 -	1,431.90	2,095.35	- -	03/2025
46	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	2,053.39	328.43	03/2019 12/2027	12/2027
47	TIDIVANAM-NAGARI (NL) - [N22000085]	9/2006	582.83 -	3,620.28	758.81	- 12/2025	12/2025
	<u>West Central Railway</u>						
48	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025
49	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,247.64	990.59	03/2022 -	09/2024
	Total		70,018.94 -	1,87,972.20	1,30,771.57		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
50	INDAPUR TO VADPALE - [N24001114	1/2017	1,202.52 1,203.00	1,202.52	1,450.82	12/2019 -	06/2023
	<u>National Highways Authority Of India</u>						
51	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	3,379.45	3,656.21	03/2014 -	06/2024
52	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,855.00	06/2014 12/2023	12/2023
53	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,679.45	08/2019 05/2024	05/2024
54	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826	2/2019	927.77 -	1,603.00	1,104.18	02/2022 -	10/2023
55	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806	3/2018	1,241.38 -	2,122.64	1,577.64	03/2023 -	06/2023
56	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656	6/2021	2,595.00 -	3,994.60	2,696.56	03/2025 -	03/2025
57	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233	3/2019	1,047.00 -	1,047.00	1,169.00	05/2020 03/2023	08/2023
58	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213	12/2017	1,094.97 -	1,094.97	1,188.00	02/2022 11/2022	08/2023
59	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	3/2018	478.74 -	1,136.83	1,016.30	05/2021 11/2022	01/2024
60	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	2,362.99	12/2018 07/2023	07/2023
61	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	2,360.65	4,657.47	09/2016 -	12/2023
	Total		17,235.04 -	22,233.63	24,413.62		
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
62	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	13,334.00	21,913.00	07/2015 12/2022	09/2023
	Total		13,334.00 -	13,334.00	21,913.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
63	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	11,786.54	12/2018 -	12/2023

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Chennai Metro Rail Ltd</u>						
64	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	18,380.00	17,619.68	12/2015 -	12/2015
	<u>Delhi Metro Rail Corporation</u>						
65	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	40,180.91	40,217.45	03/2016 08/2021	08/2021
	<u>Kochi Metro Rail Corporation Ltd</u>						
66	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	6,218.14	6,059.17	07/2017 09/2020	09/2020
	<u>Mumbai Metro Rail Corporation Ltd</u>						
67	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	7/2013	23,136.00 -	37,276.00	24,123.86	03/2020 -	12/2023
	Total		92,275.79 -	1,14,980.27	99,806.70		
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
68	POLAVARAM IRRIGATION PROJECT - [N30000002]	2/2009	10,151.04 -	55,548.87	21,727.98	03/2020 -	03/2024
	Total		10,151.04 -	55,548.87	21,727.98		
	Grand Total		2,58,642.10	4,76,575.73	3,74,067.68		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Sikkim University</u>						
1	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM - [N44000002	8/2020	314.06 -	303.55	15.70	01/2025 -	12/2024
	Total		314.06 -	303.55	15.70		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
2	AN MELT PROJECT AT RCF TROMBAY - [N08000019	5/2022	187.27 187.27	187.27	18.53	09/2024 -	07/2024
	Total		187.27 -	187.27	18.53		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
3	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400	6/2020	1,378.00 -	1,378.00	885.65	12/2022 02/2024	12/2023
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409	9/2020	18,936.00 -	18,936.00	4,182.86	09/2024 -	08/2024
	<u>Oil India Limited</u>						
5	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING - [N16000450	12/2020	430.76 -	430.76	118.55	07/2024 -	03/2024
	Total		20,744.76 -	20,744.76	5,187.06		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
6	SHAJAPUR 325MW SOLAR PV PROJECT - [N18000348	6/2022	1,530.49 -	1,530.49	208.92	03/2024 03/2024	02/2024
	Total		1,530.49 -	1,530.49	208.92		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
7	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	2/2015	1,272.19 -	1,384.72	757.06	03/2022 03/2025	12/2024
8	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	928.90	03/2023 03/2025	03/2024
9	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47 -	6,409.38	2,826.85	03/2024 03/2025	03/2024
10	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361	2/2016	1,035.16 -	1,035.16	830.46	03/2022 03/2025	03/2024

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
11	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	3,955.01	12/2026 -	03/2025
	<u>Western Railway</u>						
12	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 1,873.10	1,873.10	1,136.95	03/2022 03/2026	12/2025
	Total		12,991.76 -	19,905.69	10,435.23		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
13	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP - [N24001462]	4/2020	211.09 -	211.09	31.61	07/2024 -	02/2024
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
14	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	357.03	12/2023 -	09/2023
15	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	191.35	12/2023 -	07/2023
16	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 - [N24001452]	4/2022	170.95 -	170.95	22.38	07/2024 -	01/2024
17	CHURACHANPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	281.57	10/2023 -	08/2023
	<u>National Highways Authority Of India</u>						
18	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]	1/2018	895.39 -	895.39	1,632.71	04/2024 -	03/2024
19	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH - [N24001612]	7/2020	1,788.69 -	1,788.69	411.07	01/2024 09/2024	01/2024
20	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) - [N24001790]	2/2020	752.30 -	766.20	392.85	08/2023 12/2023	08/2023
21	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III) - [N24001758]	1/2020	823.05 -	823.05	120.24	10/2024 -	06/2024
22	4L OF KHEDAKHAJURIYA TO SUHAGADI FROM KM. 41.400 TO KM. 89.200 OF NH-148NG (PKG-II) - [N24001757]	1/2020	876.37 -	876.37	177.45	10/2024 -	06/2024
23	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 - [N24001687]	10/2021	1,331.77 2,508.79	2,508.79	60.90	10/2023 10/2024	10/2023
24	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON - [N24001569]	11/2019	1,425.02 -	1,425.02	1,026.56	03/2023 11/2023	08/2023
25	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-2) - [N24001560]	2/2019	755.16 -	755.16	723.96	10/2023 11/2023	10/2023
26	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) - [N24001564]	10/2019	662.08 -	662.08	32.02	07/2023 11/2023	07/2023
27	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA - [N24001567]	11/2019	1,272.97 -	1,272.97	330.25	10/2022 09/2023	07/2023
28	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N - [N24001568]	11/2019	1,119.35 -	1,119.35	1,108.34	05/2023 10/2023	07/2023

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
29	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) - [N24001563	10/2019	846.59 -	846.59	37.29	08/2023 09/2023	08/2023
30	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340	11/2019	716.00 -	716.00	334.38	07/2021 11/2023	07/2023
	Total		15,291.24 -	16,482.16	7,271.96		
	Grand Total		51,059.58	59,153.92	23,137.40		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	10,592.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	10,592.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. - [N04000099]	6/2022	1,305.00 -	636.45	13.41	12/2025 -	12/2025
3	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT - [N04000101]	5/2022	480.00 -	480.00	0.19	11/2024 -	11/2024
	Total		1,785.00 -	1,116.45	13.60		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
4	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]	8/2020	7,254.37 -	7,254.37	902.16	03/2028 -	03/2028
5	EXPANSION OF KARO OCP - [N06000246]	1/2022	908.47 -	908.47	132.99	03/2026 -	03/2026
6	SIRKA OCP - [N06000239]	5/2020	222.82 -	222.82	139.31	03/2025 -	03/2025
7	JHARKHAND LAIYO OCP - [N06000240]	8/2020	764.57 -	764.57	145.31	03/2031 -	03/2031
8	EXPANSION OF KONAR OCP - [N06000245]	1/2022	799.34 -	799.34	283.00	03/2032 -	03/2032
9	EXPANSION OF ASHOK OCP - [N06000247]	5/2021	2,898.28 -	2,898.28	173.90	03/2026 -	03/2026
10	EPR ROHINI KARKATA OCP - [N06000243]	1/2021	1,020.42 -	1,020.42	79.34	03/2025 -	03/2025
11	EPR PUNDI OCP - [N06000242]	11/2020	713.35 -	713.35	235.72	03/2024 -	03/2024
12	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]	7/2021	778.80 -	778.80	574.94	03/2026 -	03/2026
13	EPR TAPIN SOUTH OCP - [N06000241]	11/2020	230.41 -	230.41	17.20	03/2025 -	03/2025
14	KOTRE BASANTPUR PACHMO OCP - [N06000237]	8/2020	861.06 -	861.06	139.37	03/2032 -	03/2032
15	EXPANSION PROJECT AMRAPALI OCP - [N06000217]	8/2020	5,136.15 -	5,136.15	572.77	03/2028 -	03/2028

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
16	CHANDRAGUPT OCP - [N06000238]	8/2020	973.50 -	973.50	5.95	03/2032 -	03/2032
	<u>Eastern Coal Fields Limited</u>						
17	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]	4/2020	1,210.12 -	1,210.12	259.91	03/2029 -	03/2029
18	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.99	139.51	03/2024 -	03/2024
19	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	389.10	4.47	03/2027 -	03/2027
20	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	42.62	03/2029 -	03/2029
21	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	21.68	03/2025 -	03/2025
22	SONEPUR BAZARI EXPANSION OC - [N06000220]	7/2021	5,365.88 5,366.00	5,365.88	316.12	03/2029 -	03/2029
23	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	749.08	9.72	03/2027 -	03/2027
24	MOHANPUR EXPANSION OC PHASE II - [N06000236]	11/2020	888.99 -	888.99	27.06	03/2025 -	03/2025
25	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	3.33	03/2026 -	03/2026
26	BONJEME HARI EXPANSION OCP - [N06000244]	8/2021	570.12 -	570.11	14.55	03/2025 -	03/2025
	<u>Mahanadi Coal Fields Limited</u>						
27	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	3,339.10	03/2026 -	03/2026
28	BHUBANESWARI EXPANSION OCP - [N06000227]	8/2020	3,145.45 -	3,145.45	941.66	03/2031 -	03/2031
29	RPR OF HINGULA -II EXPANSION PH-III - [N06000261]	12/2022	2,264.68 -	2,264.68	934.65	03/2029 -	03/2029
30	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	1,438.58	03/2027 -	03/2027
31	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,432.59	03/2029 -	03/2029
32	BALARAM EXPANSION OCP - [N06000230]	8/2020	3,504.21 -	3,504.21	656.64	03/2029 -	03/2029
33	GOPALJI-KANIHA OCP - [N06000229]	8/2020	8,416.19 -	8,416.19	1,399.84	03/2028 -	03/2028
	<u>Neyveli Lignite Corporation</u>						
34	PACHWARA SOUTH COAL BLOCK - [N06000193]	7/2013	1,795.01 -	1,795.01	45.19	09/2028 -	09/2028
35	TALABIRA II AND III OCP - [N06000189]	7/2017	2,401.07 -	2,401.07	1,051.59	01/2027 -	01/2027
	<u>Northern Coal Fields Limited</u>						
36	NIGAH I EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	285.78	03/2025 -	03/2025
37	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	8.49	03/2025 -	03/2025
	<u>Singareni Colliers Company Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
38	JAWAHAR KHANI OPENCAST (JK OC) MINE - [N06000259]	12/2021	297.88 -	297.88	25.96	03/2025 -	03/2025
39	GOLETI OPENCAST MINE - [N06000258]	7/2021	345.60 -	345.60	30.72	03/2026 -	03/2026
	<u>South-Eastern Coal Fields Limited</u>						
40	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	88.27	03/2026 -	03/2026
41	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	102.84	03/2026 -	03/2026
42	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	198.08	03/2024 -	03/2024
43	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	721.14	03/2029 -	03/2029
44	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
45	RAMPUR BATURA OC (4.0 MTY) - [N06000233]	7/2019	1,248.93 -	1,248.93	408.00	03/2026 -	03/2026
46	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	15.69	03/2026 -	03/2026
47	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	2,336.23	03/2029 -	03/2029
48	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	39.19	03/2029 -	03/2029
	<u>Western Coal Fields Limited</u>						
49	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	58.79	03/2028 -	03/2028
50	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	505.75	03/2025 -	03/2025
51	GOKUL EXPANSION OC - [N06000264]	4/2021	456.95 -	456.95	147.37	03/2026 -	03/2026
52	RPR PAUNI II EXPANSION OC - [N06000263]	3/2023	464.45 -	464.45	177.30	03/2027 -	03/2027
53	MAKARDHOKDA I EXPANSION OC - [N06000253]	6/2022	497.06 -	497.06	140.99	03/2026 -	03/2026
54	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]	2/2020	1,184.33 -	1,184.33	692.00	03/2027 -	03/2027
55	TAWA III UG MINE - [N06000250]	12/2021	324.25 -	324.25	12.19	03/2027 -	03/2027
56	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	171.31	03/2028 -	03/2028
57	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	24.41	03/2026 -	03/2026
58	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	61.09	03/2026 -	03/2026
59	VISHNUPURI UG TO OC - [N06000260]	11/2022	227.65 -	227.65	7.02	03/2029 -	03/2029
60	BHANEGAON OC (1.15MTY) - [N06000256]	9/2022	494.60 -	494.60	97.51	03/2028 -	03/2028

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
61	BHATADI EXPANSION OC - [N06000254]	2/2020	729.86 -	729.86	158.48	03/2028 -	03/2028
62	NEW MAJARI UG TO OC (3.0 MTY) - [N06000255]	5/2019	496.38 -	496.38	105.47	03/2027 -	03/2027
63	SINGHORI DEEP OC - [N06000252]	5/2022	421.84 -	421.84	110.40	03/2029 -	03/2029
64	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) - [N06000257]	9/2022	497.01 -	497.01	136.72	03/2027 -	03/2027
65	SAONER UG MINE I EXPANSION - [N06000251]	1/2022	253.51 -	253.51	51.26	03/2028 -	03/2028
66	ADASA UG TO OC (1.50 MTY) - [N06000219]	11/2018	333.43 -	333.43	204.07	03/2024 -	03/2024
67	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]	11/2020	826.80 -	826.80	340.53	03/2026 -	03/2026
68	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]	9/2018	313.34 -	313.34	192.55	03/2024 -	03/2024
	Total		91,456.03 -	90,851.17	23,136.37		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Central Public Works Department</u>						
69	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL - [N42000010]	8/2021	316.25 -	316.25	246.36	02/2024 -	02/2024
	Total		316.25 -	316.25	246.36		
	<u>DPIIT</u>						
	<u>Dmic For Dpiit</u>						
70	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001]	9/2011	20,084.00 -	20,084.00	9,682.86	03/2027 03/2027	03/2027
	Total		20,084.00 -	20,084.00	9,682.86		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
71	INSTALLATION OF NEW NANO UREA FERTILIZER PLANT AT RCF TROMBAY - [N08000020]	5/2023	238.30 -	238.30	0.30	03/2024 -	03/2024
	Total		238.30 -	238.30	.30		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
72	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00 -	1,828.00	740.13	09/2025 -	09/2025
	Total		1,828.00 -	1,828.00	740.13		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
73	CITY GAS DISTRIBUTION NETWORK PROJECT AT ANGUL AND DHENKANAL - [N16000463]	4/2019	605.65 -	605.65	158.42	03/2030 -	03/2030
74	CITY GAS DISTRIBUTION NETWORK PROJECT AT JAGATSINGHPUR AND KENDRAPARA - [N16000465]	4/2019	485.91 -	485.91	121.66	03/2030 -	03/2030
75	CITY GAS DISTRIBUTION NETWORK PROJECT AT SANGLI AND SATARA - [N16000460]	4/2019	2,337.98 -	2,337.98	635.90	11/2028 -	11/2028
76	CITY GAS DISTRIBUTION NETWORK PROJECT AT BILASPUR, HAMIRPUR AND UNA - [N16000467]	4/2019	427.94 -	427.94	71.16	09/2030 -	09/2030
77	CITY GAS DISTRIBUTION NETWORK PROJECT AT CHATRA AND PALAMU - [N16000474]	12/2019	230.25 -	230.25	42.85	03/2029 -	03/2029
78	CITY GAS DISTRIBUTION NETWORK PROJECT AT BARGARH, DEBGARH AND SAMBALPUR - [N16000464]	4/2019	599.19 -	599.19	157.48	03/2030 -	03/2030
79	CITY GAS DISTRIBUTION NETWORK PROJECT AT ROHTAK - [N16000473]	4/2018	261.48 -	261.48	137.28	06/2025 -	06/2025
80	CITY GAS DISTRIBUTION NETWORK PROJECT AT BALLARI AND GADAG - [N16000461]	4/2019	897.62 -	897.62	179.90	09/2028 -	09/2028
81	CITY GAS DISTRIBUTION NETWORK PROJECT AT AMETHI, RAEBARELI AND PRATAPGARH - [N16000466]	4/2019	432.06 -	432.06	122.52	09/2028 -	09/2028
82	CITY GAS DISTRIBUTION NETWORK PROJECT AT SIDHI AND SANGRAULI - [N16000468]	12/2019	350.35 -	350.35	66.39	03/2029 -	03/2029
83	CITY GAS DISTRIBUTION NETWORK PROJECT AT SATNA AND SHAHDOL - [N16000472]	4/2019	332.38 -	332.38	86.74	09/2028 -	09/2028
84	CITY GAS DISTRIBUTION NETWORK PROJECT AT AHMEDNAGAR AND AURANGABAD - [N16000459]	4/2019	3,972.18 -	3,972.18	1,233.81	09/2028 -	09/2028
85	CITY GAS DISTRIBUTION NETWORK PROJECT AT JAJPUR AND KENDUJHAR - [N16000462]	4/2019	741.29 -	741.29	209.95	03/2030 -	03/2030
	<u>Gas Authority Of India Limited</u>						
86	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	1,753.85	04/2025 -	04/2025
87	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	1,299.02	430.40	04/2024 -	04/2024
	<u>Hindustan Petroleum Corporation Limited</u>						
88	BHATINDA SANGRUR PIPELINE - [N16000440]	11/2021	367.00 -	367.00	142.19	04/2024 -	04/2024
89	LEASE OF MBPT RECLAIMED LAND AT JAWAHAR DWEEP - [N16000493]	12/2022	410.00 -	410.00	40.71	12/2023 -	12/2023
90	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM - [N16000484]	3/2023	156.36 -	156.36	0.36	03/2026 03/2026	03/2026
91	NEW LPG PLANT AT VARANASI - [N16000447]	8/2017	194.62 -	194.62	154.12	05/2024 -	05/2024
92	HALDIA PANAGARH PIPELINE PROJECT - [N16000478]	11/2022	1,010.00 -	1,010.00	5.55	11/2025 -	11/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
93	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]	9/2021	160.00 -	160.00	0.43	06/2024 -	06/2024
94	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM - [N16000494]	3/2023	384.04 -	384.04	0.35	12/2026 -	12/2026
	<u>Indian Oil Corporation Limited</u>						
95	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	288.06	03/2030 -	03/2030
96	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE - [N16000437]	1/2022	463.00 -	463.00	76.95	07/2025 -	07/2025
97	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAU DISTRICTS - [N16000489]	3/2022	575.00 -	575.00	22.91	03/2030 -	03/2030
98	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA - [N16000457]	6/2022	768.00 -	768.00	1.39	10/2025 -	10/2025
99	POLY BUTADIENE RUBBER PLANT AT PANIPAT - [N16000458]	3/2022	1,459.00 -	1,459.00	69.74	03/2025 -	03/2025
100	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI - [N16000453]	1/2022	389.00 -	389.00	16.42	09/2024 -	09/2024
101	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS - [N16000487]	3/2022	865.00 -	865.00	13.28	03/2030 -	03/2030
102	EXTENSION OF ASANUR-SANKARI SECTION OF CHENNAI-TRICHY-MADURAI PIPELINE UPTO COIMBATORE (IRUGUR) - [N16000479]	1/2023	346.70 -	346.70	0.13	01/2025 -	01/2025
103	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS - [N16000491]	3/2022	609.00 -	609.00	6.56	03/2030 -	03/2030
104	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) - [N16000456]	9/2022	165.00 -	165.00	0.24	08/2025 -	08/2025
105	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT - [N16000454]	1/2022	328.00 -	328.00	12.15	09/2024 -	09/2024
106	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI - [N16000480]	3/2023	202.07 -	202.07	0.23	02/2026 -	02/2026
107	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS - [N16000490]	3/2022	1,328.00 -	1,328.00	41.85	03/2030 -	03/2030
108	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) - [N16000455]	1/2022	829.00 -	829.00	102.68	07/2024 -	07/2024
109	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS - [N16000486]	3/2022	501.00 -	501.00	41.04	03/2030 -	03/2030
110	CGD PROJECT AT PATHANKOT DISTRICT - [N16000488]	3/2022	151.00 -	151.00	6.36	03/2030 -	03/2030
111	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS - [N16000492]	3/2022	1,295.00 -	1,295.00	39.23	03/2030 -	03/2030
112	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS - [N16000485]	3/2022	1,420.00 -	1,420.00	25.37	03/2030 -	03/2030
113	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	4,702.23	09/2024 -	09/2024
114	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT - [N16000495]	6/2022	656.00 -	656.00	98.04	08/2025 -	08/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	236.12	10/2023 -	10/2023
116	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	186.74	02/2028 -	02/2028
117	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE - [N16000451]	3/2022	564.00 -	564.00	96.53	11/2024 -	11/2024
118	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	96.14	03/2030 -	03/2030
	<u>Indradhanush Gas Grid Ltd</u>						
119	NORTH EAST GAS GRID - [N16000439]	11/2020	9,265.00 -	9,265.00	4,481.56	03/2024 -	03/2024
	<u>Numaligarh Refinery Limited</u>						
120	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	18,968.00	6,125.60	10/2024 -	10/2024
121	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	5,608.65	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
122	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	1,018.19	03/2026 -	03/2026
123	PIPELINE REPLACEMENT PROJECT - VII - [N16000436]	1/2022	3,183.58 -	3,183.58	1,276.83	05/2024 -	05/2024
124	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK - [N16000470]	6/2022	4,144.41 -	4,144.41	-	10/2025 -	10/2025
125	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD - [N16000444]	1/2022	621.40 -	621.40	81.21	11/2024 -	11/2024
126	CREATION OF GDU AND DPD FACILITIES AT RAJAHMUNDRY - [N16000471]	3/2022	211.22 -	211.22	6.03	05/2024 -	05/2024
127	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]	8/2021	885.63 -	885.63	275.75	02/2026 -	02/2026
128	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A - [N16000483]	7/2021	173.03 -	173.03	28.68	07/2025 -	07/2025
129	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	214.83	03/2025 -	03/2025
130	CREATION OF GAS DEHYDRATION FACILITIES - [N16000443]	3/2022	209.33 -	209.33	20.50	05/2024 -	05/2024
131	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT - [N16000477]	5/2022	249.43 -	249.43	5.95	02/2025 -	02/2025
132	CONSTRUCTION OF TWO PRODUCED WATER TREATMENT PLANTS (PWT) AT BECHARAJI AND SOBHASAN INSTALLATION OF - [N16000482]	7/2021	320.20 -	320.20	22.53	07/2024 -	07/2024
133	KALOL REDEVELOPMENT PROJECT - [N16000481]	8/2022	1,487.41 -	1,487.41	374.18	03/2027 -	03/2027
	<u>Oil India Limited</u>						
134	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT - [N16000449]	6/2021	860.00 -	860.00	101.03	12/2024 -	12/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,22,619.86 -	1,28,440.32	31,573.93		
	<u>POWER</u>						
	<u>Chenab Valley Power Projects [P] Limited</u>						
135	KWAR HE PROJECT - [N18000363]	5/2022	4,526.12 -	4,526.12	431.06	11/2026 -	11/2026
	<u>National Hydro-Electric Power Corporation</u>						
136	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH - [N18000362]	2/2023	31,876.39 -	31,876.39	2,177.22	02/2032 -	02/2032
	<u>National Thermal Power Corporation</u>						
137	DAYAPAR WIND ENERGY PROJECT 200MW - [N18000345]	7/2022	1,316.02 -	1,316.02	92.02	03/2025 03/2025	03/2025
138	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) - [N18000364]	8/2022	11,844.00 -	11,844.00	635.90	05/2027 -	05/2027
139	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) - [N18000346]	9/2022	7,179.54 -	7,179.54	545.46	09/2024 09/2024	09/2024
140	BHADLA-II 500MW SOLAR PV PROJECT - [N18000347]	6/2022	2,598.92 -	2,598.92	1.75	03/2024 03/2024	03/2024
	<u>Power Grid Corporation Of India Limited</u>						
141	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM - [N18000330]	3/2022	288.71 -	288.71	-	12/2024 -	12/2024
142	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPs - LTA SYSTEM - [N18000328]	2/2022	318.12 -	318.12	102.00	04/2025 -	04/2025
143	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK - [N18000357]	3/2023	922.30 -	922.30	-	12/2024 -	12/2024
144	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII - [N18000354]	3/2023	271.69 -	271.69	-	09/2024 -	09/2024
145	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000361]	3/2023	2,820.99 -	2,820.99	-	03/2025 -	03/2025
146	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK - [N18000359]	3/2023	966.79 -	966.79	-	12/2024 -	12/2024
147	ER WR TRANSMISSION LIMITED - [N18000353]	3/2023	281.16 -	281.16	-	03/2025 -	03/2025
148	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C - [N18000338]	7/2022	186.19 -	186.19	16.84	03/2025 -	03/2025
149	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B - [N18000352]	3/2023	3,546.94 -	3,546.94	51.87	11/2024 -	11/2024
150	EASTERN REGION EXPANSION SCHEME XXIX - [N18000351]	3/2023	524.04 -	524.04	15.25	11/2025 -	11/2025
151	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000360]	3/2023	1,167.55 -	1,167.55	-	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
152	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART - [N18000356]	3/2023	1,433.28 -	1,433.28	-	09/2024 -	09/2024
153	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX - [N18000355]	3/2023	260.30 -	260.30	-	03/2025 -	03/2025
154	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT - [N18000358]	3/2023	815.12 -	815.12	-	03/2025 -	03/2025
155	POWERGRID NEEMUCH TRANSMISSION SYSTEM LIMITED - [N18000341]	8/2022	863.99 -	863.99	118.49	02/2024 -	02/2024
156	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION - [N18000343]	10/2022	307.87 -	307.87	7.34	10/2025 -	10/2025
	<u>Satluj Jal Vidyut Nigam Limited</u>						
157	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	1,172.83	01/2026 -	01/2026
158	SUNNI DAM HYDRO ELECTRIC PROJECT - [N18000344]	1/2023	2,614.51 -	2,614.51	496.15	04/2028 -	04/2028
159	BIKANER SOLAR POWER PROJECT - [N18000335]	4/2022	5,491.89 532.00	6,023.89	2,211.03	05/2024 -	05/2024
160	RAGHANESDA SOLAR POWER PROJECT - [N18000340]	6/2022	642.15 -	642.15	203.25	12/2023 -	12/2023
161	GUJRAI SOLAR POWER PROJECT - [N18000336]	6/2022	279.94 -	279.94	194.48	08/2023 -	08/2023
162	OMKARESHWAR FLOATING SOLAR POWER PROJECT (90 MW) - [N18000342]	11/2022	646.17 -	646.17	255.95	04/2024 -	04/2024
163	GURHAH SOLAR POWER PROJECT - [N18000334]	5/2022	466.82 -	466.82	411.95	08/2023 -	08/2023
164	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	433.34	11/2025 -	11/2025
	Total		86,956.04 -	87,488.04	9,574.18		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
165	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	6,409.38	2,826.85	03/2024 03/2025	03/2024
	<u>Rail Vikas Nigam Ltd.</u>						
166	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	4,306.50	12/2023 -	12/2023
167	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	5,013.33	12/2023 -	12/2023
	Total		10,551.49 -	13,635.82	12,146.68		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296	3/2019	394.27 -	394.27	412.07	03/2027 -	03/2027
169	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 - [N24001850	3/2022	995.04 -	995.04	18.84	09/2025 09/2025	09/2025
170	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M - [N24001529	12/2021	451.66 -	451.66	186.59	08/2024 -	08/2024
171	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF - [N24001587	3/2020	262.37 -	343.77	72.28	09/2024 -	09/2024
172	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291	3/2019	421.48 -	421.48	349.87	03/2027 -	03/2027
173	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW - [N24001480	10/2021	227.06 -	227.06	42.18	04/2024 -	04/2024
174	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF BARMER GHAGARIYA SECTION FROM KM 0 - [N24001531	3/2022	304.87 -	304.87	94.33	08/2024 -	08/2024
175	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294	3/2019	560.39 -	560.39	531.18	03/2027 -	03/2027
176	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297	3/2019	450.65 -	450.65	272.11	03/2027 -	03/2027
177	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 - [N24001463	4/2020	294.84 -	294.84	160.63	07/2024 -	07/2024
178	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO - [N24001469	11/2021	307.11 -	307.11	21.55	05/2024 -	05/2024
179	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375	6/2020	496.47 -	496.47	103.90	03/2027 -	03/2027
180	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413	2/2021	240.99 -	240.99	110.30	01/2024 -	01/2024
181	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I - [N24001465	6/2020	252.19 -	252.19	0.28	09/2024 09/2024	09/2024
182	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373	1/2020	358.26 -	358.26	334.89	02/2024 -	02/2024
183	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376	3/2021	182.55 -	182.55	72.99	03/2027 -	03/2027
184	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K - [N24001447	8/2020	371.93 -	371.93	63.42	12/2024 -	12/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
185	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N - [N24001466	3/2021	297.24 -	297.24	44.41	07/2024 07/2024	07/2024
186	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293	3/2019	486.70 -	486.70	415.54	03/2027 -	03/2027
187	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289	3/2019	403.68 -	403.68	346.74	03/2027 -	03/2027
188	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU - [N24001829	10/2022	172.15 -	172.15	-	11/2024 -	11/2024
189	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE - [N24001528	1/2022	194.88 -	194.88	13.40	12/2024 -	12/2024
190	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM - [N24001456	4/2020	199.39 -	199.39	65.98	02/2024 -	02/2024
191	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP - [N24001461	4/2020	236.47 -	236.47	46.55	03/2024 -	03/2024
192	CONSTRUCTION OF 4 LANE ELEVATED VIADUCT AT KM. 7.500 MUNSHI PULIA OF NH-24A - [N24001460	12/2021	170.60 -	170.60	40.08	09/2024 -	09/2024
193	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH - [N24001530	12/2021	150.11 -	150.11	24.18	09/2024 -	09/2024
194	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292	3/2019	543.05 -	543.05	414.11	03/2027 -	03/2027
195	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 – 29/250 INCLUDING LA AND SHIFTING OF NH-234 - [N24001828	1/2022	221.03 -	243.95	-	11/2024 -	11/2024
196	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR - [N24001527	12/2021	411.40 -	411.40	57.30	05/2024 -	05/2024
197	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408	2/2021	925.47 -	925.47	76.97	07/2025 -	07/2025
198	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) - [N24001479	3/2021	395.62 -	395.62	62.63	05/2024 -	05/2024
199	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP - [N24001471	4/2020	325.24 -	325.24	24.98	11/2024 -	11/2024
200	CONSTRUCTION OF 1 ROB CUM FLYOVER FROM KM 136.200 TO 137.800 AND 2 FLYOVERS - [N24001459	1/2022	297.06 -	297.06	184.94	04/2024 -	04/2024
201	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374	6/2020	437.60 -	437.60	210.88	03/2027 -	03/2027
202	WIDENING AND STRENGTHENING FROM KM.15.000 TO KM, 58.600 (BHADEWARA -DRAMANDGANJ SECTION) OF NATIONAL - [N24001478	12/2021	257.97 -	257.97	68.81	05/2024 -	05/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
203	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO - [N24001467	3/2021	226.44 -	226.44	50.91	02/2024 02/2024	02/2024
204	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) - [N24001442	10/2021	385.15 -	385.15	81.83	05/2024 05/2024	05/2024
205	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F - [N24001457	4/2020	172.50 -	172.50	46.73	07/2024 -	07/2024
206	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372	2/2021	588.09 -	588.09	263.61	03/2024 -	03/2024
207	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA - [N24001840	3/2022	535.03 -	535.03	-	04/2025 -	04/2025
208	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 - [N24001470	8/2020	314.32 -	314.32	24.78	04/2025 -	04/2025
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
209	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683	2/2017	180.57 -	180.57	96.11	11/2023 11/2023	11/2023
210	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196	3/2017	1,049.51 -	1,049.51	293.67	08/2023 -	08/2023
211	2 LANING FROM MANU-SIMLUNG PKG-2 - [N24001542	2/2022	456.88 -	456.88	11.22	01/2025 -	01/2025
212	KARGIL-ZANSKR PACKAGE-7 - [N24001347	1/2021	308.86 -	308.86	185.10	06/2024 -	06/2024
213	DABOKA KATHKATI PACKAGE-7 - [N24001537	11/2021	204.10 -	204.10	54.66	07/2024 -	07/2024
214	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326	11/2020	4,997.04 -	4,997.04	1,340.72	09/2028 -	09/2028
215	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J - [N24001475	3/2022	605.36 -	605.36	82.51	12/2024 -	12/2024
216	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 - [N24001544	3/2022	909.02 -	909.02	72.25	01/2025 -	01/2025
217	JOGIGHOPA BRIDGE - [N24001434	8/2021	746.76 -	746.76	144.33	11/2024 -	11/2024
218	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368	3/2021	286.72 -	286.72	36.36	01/2024 -	01/2024
219	SRIRAMPUR - DHUBRI PKG-1 - [N24001831	3/2022	613.89 -	613.89	-	02/2025 -	02/2025
220	IMPHAL - KHONGSANG PKG-6 - [N24001539	12/2021	504.76 -	504.76	16.43	02/2025 -	02/2025
221	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	284.31	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
222	AKASH BRIDGE - JESSAMI SECTION PKG-2 - [N24001540]	3/2022	152.11 -	152.11	-	02/2025 -	02/2025
223	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 - [N24001451]	3/2022	215.27 -	215.27	50.37	07/2024 -	07/2024
224	FOUR LANING OF JAMMU-AKHNOOR PKG-1 - [N24001543]	7/2022	245.34 -	245.34	3.94	01/2025 -	01/2025
225	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM - [N24001474]	9/2021	359.86 -	359.86	169.42	05/2024 -	05/2024
226	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 - [N24001541]	11/2021	283.50 -	283.50	96.86	06/2024 -	06/2024
227	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 - [N24001832]	1/2023	458.59 -	458.59	-	05/2025 -	05/2025
228	IMPHAL - KHONGSANG PKG-5 - [N24001538]	12/2021	410.68 -	410.68	40.52	05/2024 -	05/2024
229	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]	12/2020	804.00 -	804.00	508.56	08/2023 -	08/2023
230	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B - [N24001833]	7/2022	198.28 -	198.28	1.79	03/2025 -	03/2025
231	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	2,199.36	09/2026 -	09/2026
232	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	379.30	147.62	02/2024 02/2024	02/2024
233	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	171.38	05/2024 -	05/2024
234	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	196.67	12/2023 -	12/2023
235	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	117.90	09/2023 -	09/2023
236	IMPHAL - KHONGSANG PKG-4 - [N24001453]	8/2021	579.63 -	579.63	53.90	12/2023 -	12/2023
237	DABOKA KATHKATI PACKAGE-6 - [N24001450]	9/2021	625.64 -	625.64	265.02	07/2024 -	07/2024
238	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	181.82	12/2023 -	12/2023
239	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM - [N24001473]	9/2021	310.76 -	310.76	66.01	02/2024 -	02/2024
240	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	45.46	12/2023 -	12/2023
241	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	-	12/2023 -	12/2023
<u>National Highways Authority Of India</u>							
242	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 - [N24001432]	12/2021	300.00 -	300.00	223.00	08/2024 -	08/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
243	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD - [N24001666	12/2021	714.00 -	714.00	-	09/2024 -	09/2024
244	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M - [N24001689	12/2020	1,745.00 -	1,279.00	822.13	09/2023 -	09/2023
245	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH -66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 (- [N24001653	11/2021	3,565.82 -	3,064.11	1,570.57	04/2025 -	04/2025
246	BAKHTIYARPUR RAJAUJI PKG-III FROM KM 101.630 TO KM 152.520 NH20 - [N24001708	9/2020	2,156.22 -	2,156.22	1,585.58	06/2024 -	06/2024
247	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) - [N24001819	3/2021	1,102.63 -	1,303.00	212.43	01/2025 -	01/2025
248	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. - [N24001844	12/2022	1,058.90 -	1,058.90	28.23	10/2025 -	10/2025
249	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP - [N24001821	11/2020	1,137.74 -	1,289.00	321.70	10/2024 -	10/2024
250	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE - OD-1) - [N24001669	2/2021	586.00 -	586.00	-	03/2024 -	03/2024
251	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 - [N24001731	12/2021	2,470.64 -	2,335.00	139.84	05/2025 05/2025	05/2025
252	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE - [N24001822	12/2020	1,075.27 -	1,307.00	384.53	10/2024 -	10/2024
253	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 - [N24001687	10/2021	1,331.77 2,083.00	2,508.79	60.90	10/2023 10/2024	10/2023
254	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ - [N24001664	6/2020	1,746.45 -	1,746.45	879.34	04/2024 10/2021	04/2024
255	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ - [N24001663	6/2020	3,041.65 -	3,041.65	1,795.19	04/2024 10/2021	04/2024
256	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO - [N24001728	12/2021	1,138.81 -	1,138.81	122.05	07/2025 -	07/2025
257	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719	2/2021	2,948.31 -	3,392.00	506.57	07/2024 -	07/2024
258	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659	2/2021	3,375.31 -	3,790.17	1,745.63	07/2024 -	07/2024
259	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH - [N24001662	5/2020	1,981.07 -	1,981.07	1,121.13	05/2024 11/2021	05/2024
260	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K - [N24001717	11/2020	1,155.49 -	1,155.49	227.66	08/2024 -	08/2024
261	6L OF BADAUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE - OD-3) - [N24001668	3/2021	1,249.00 -	1,249.00	-	04/2024 -	04/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
262	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655	6/2021	3,606.00 -	3,923.82	2,789.91	02/2025 -	02/2025
263	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA - [N24001847	1/2023	956.14 -	956.14	18.72	11/2025 -	11/2025
264	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH-130A - [N24001611	4/2020	1,855.59 1,870.00	1,869.85	187.36	03/2024 -	03/2024
265	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) - [N24001730	12/2021	1,384.79 -	1,384.79	398.01	01/2025 -	01/2025
266	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 - [N24001654	6/2021	2,641.37 -	2,641.37	138.53	03/2025 03/2025	03/2025
267	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739	10/2019	1,779.83 -	2,200.00	708.00	11/2023 -	11/2023
268	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH - [N24001698	8/2022	1,198.02 -	1,198.02	-	08/2024 -	08/2024
269	6L OF KARKI – KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE – OD-4) - [N24001670	2/2021	593.00 -	593.00	-	03/2024 -	03/2024
270	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH - [N24001660	8/2020	2,714.60 -	2,714.60	1,414.01	02/2024 11/2021	02/2024
271	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 - [N24001845	2/2023	1,253.24 -	1,253.24	68.47	10/2025 -	10/2025
272	CONSTRUCTION OF 4 LANE BANGALORE -CHENNAI EXPRESSWAY FROM KM 53.500 TO KM 71.000 SECTION OF NE-7 (BA - [N24001685	1/2021	1,069.00 -	863.00	508.94	01/2024 -	01/2024
273	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA - [N24001841	12/2022	912.94 -	912.94	59.28	09/2025 -	09/2025
274	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 - [N24001849	5/2022	1,063.72 -	1,063.72	170.67	07/2025 -	07/2025
275	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796	3/2022	1,013.33 -	1,111.33	202.73	10/2024 10/2024	10/2024
276	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) - [N24001697	2/2023	1,358.00 -	1,358.00	0.65	02/2025 -	02/2025
277	4L OF DHROL-BHADRA-PATIYA SECTION FROM 0.000 TO KM 13.600 AND BHADRA PATIYA - PIPALIYA SECTION FROM - [N24001787	5/2020	971.03 -	971.03	411.77	10/2023 10/2023	10/2023
278	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE-7(ALONG WITH 0.700 - [N24001688	10/2020	3,184.00 -	3,184.00	799.94	09/2023 -	09/2023
279	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 - [N24001718	12/2020	843.48 -	966.00	203.01	07/2024 -	07/2024
280	INDORE - HARDI (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] - [N24001762	10/2021	1,146.22 -	1,146.22	444.64	01/2024 -	01/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
281	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI - [N24001704	3/2021	1,020.84 -	1,020.84	84.78	03/2024 -	03/2024
282	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT - [N24001785	3/2022	1,373.06 -	1,373.06	202.38	06/2025 -	06/2025
283	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC - [N24001657	6/2021	2,842.14 -	2,842.14	117.96	10/2024 10/2024	10/2024
284	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU - [N24001701	4/2022	1,769.50 -	1,769.50	-	04/2024 -	04/2024
285	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG - II) - [N24001834	5/2023	839.00 -	839.00	4.51	05/2025 -	05/2025
286	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 - [N24001842	12/2022	750.81 -	750.81	22.03	11/2025 -	11/2025
287	6L OF HATIBENA - BADA KUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE - OD-2) - [N24001671	2/2021	925.00 -	925.00	-	03/2024 -	03/2024
288	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 - [N24001665	12/2021	1,592.00 -	1,592.00	-	10/2024 -	10/2024
289	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656	6/2021	2,595.00 -	3,994.60	2,696.56	03/2025 -	03/2025
290	6L GREENFIELD KALIAGURA - BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG - [N24001667	9/2021	1,734.00 -	1,734.00	6.94	05/2024 -	05/2024
291	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) - [N24001811	4/2021	583.93 -	583.93	33.42	06/2024 -	06/2024
292	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) - [N24001820	2/2021	1,484.83 -	1,768.00	383.07	12/2024 -	12/2024
293	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU - [N24001774	12/2020	1,524.03 -	1,524.03	890.82	11/2023 -	11/2023
294	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. - [N24001846	2/2023	1,200.42 -	1,200.42	56.79	10/2025 -	10/2025
295	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG-III) - [N24001835	5/2023	986.00 -	986.00	-	05/2025 -	05/2025
296	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812	3/2021	1,002.11 -	1,358.00	28.69	05/2024 -	05/2024
297	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE - - [N24001678	8/2021	1,460.00 -	1,460.00	-	06/2024 -	06/2024
298	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM - [N24001716	7/2022	186.50 -	201.00	-	08/2023 -	08/2023
299	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE - [N24001639	5/2020	864.23 -	864.23	342.25	12/2024 12/2024	12/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
300	PATAS-VASUNDE PHATA - BARAMATI BYPASS - [N24001501	9/2021	531.86 -	532.41	489.85	09/2023 09/2023	09/2023
301	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR – DEHRADUN SECTION FROM KM. - [N24001525	3/2021	169.08 -	169.08	60.65	03/2024 03/2024	03/2024
302	4L OF HARIDWAR NAGINA SECTION DESIGN CH. LME FROM KM 13.829 TO KM 17.110 AND KM 26.077 TO KM 27.508 - [N24001554	6/2020	183.92 -	183.92	20.62	02/2024 -	02/2024
303	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 - [N24001519	9/2020	1,198.55 -	1,198.55	431.31	11/2023 -	11/2023
304	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 - [N24001623	1/2020	336.01 -	336.01	91.52	01/2024 01/2024	01/2024
305	FOUR LANING OF AURANGABAD-PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . - [N24001795	10/2022	490.40 -	289.00	13.29	07/2024 -	07/2024
306	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI - [N24001548	3/2022	457.72 -	457.72	33.65	06/2024 -	06/2024
307	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR - [N24001771	6/2020	1,479.22 -	1,479.22	667.80	12/2024 -	12/2024
308	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S - [N24001610	1/2022	1,833.73 -	1,833.73	126.16	05/2024 05/2024	05/2024
309	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR - [N24001772	8/2021	1,147.26 -	1,147.26	49.00	03/2024 -	03/2024
310	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K - [N24001736	1/2022	1,159.96 -	1,159.96	268.31	08/2024 -	08/2024
311	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 - [N24001677	11/2022	226.76 -	226.76	39.80	05/2024 05/2024	05/2024
312	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 - [N24001770	2/2022	417.51 -	417.51	52.14	03/2024 -	03/2024
313	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA - [N24001682	3/2022	294.62 -	294.62	5.40	03/2024 03/2024	03/2024
314	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 - [N24001443	5/2020	690.30 -	690.30	422.62	03/2024 -	03/2024
315	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA - [N24001532	11/2021	694.00 -	694.00	1,212.57	11/2023 11/2023	11/2023
316	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D - [N24001759	1/2020	909.84 -	909.84	130.08	06/2024 -	06/2024
317	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A - [N24001823	1/2022	1,852.12 -	1,787.00	255.61	01/2025 01/2023	01/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
318	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP - [N24001824	3/2020	1,863.09 -	2,238.00	894.15	01/2024 01/2022	01/2024
319	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) - [N24001818	2/2021	818.73 -	1,105.00	73.20	01/2025 -	01/2025
320	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK - [N24001848	2/2023	909.02 -	909.02	27.25	10/2025 -	10/2025
321	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM - [N24001626	2/2022	972.06 -	972.06	8.38	01/2025 -	01/2025
322	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 - [N24001720	10/2020	1,023.91 -	1,285.00	318.78	05/2024 -	05/2024
323	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 - [N24001625	1/2022	1,227.57 -	1,227.57	4.98	01/2025 -	01/2025
324	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658	1/2021	4,265.42 -	4,708.42	2,751.50	07/2024 -	07/2024
325	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH - [N24001843	12/2022	992.89 -	992.89	28.26	11/2025 -	11/2025
326	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N - [N24001745	12/2021	1,972.10 -	1,936.00	158.30	07/2025 07/2025	07/2025
327	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C - [N24001705	3/2022	1,485.66 -	1,485.66	-	03/2024 -	03/2024
328	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 - [N24001616	1/2021	428.04 -	328.77	291.27	10/2023 -	10/2023
329	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE - [N24001648	8/2022	2,429.52 -	2,429.52	-	01/2026 -	01/2026
330	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO (NEAR MOHAND) OF GANESHPUR – DEHRADUN SECTION FROM K - [N24001523	3/2021	836.24 -	836.24	489.16	10/2023 10/2023	10/2023
331	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR - [N24001641	3/2021	1,641.75 -	1,641.75	69.48	10/2024 -	10/2024
332	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
333	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND - [N24001767	1/2021	1,001.69 -	1,001.69	29.75	04/2024 -	04/2024
334	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] - [N24001766	1/2022	1,011.29 -	1,011.29	-	10/2024 -	10/2024
335	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP - [N24001810	2/2022	190.60 -	163.00	51.65	06/2024 -	06/2024
336	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] - [N24001761	2/2023	520.28 -	520.28	75.46	02/2025 -	02/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
337	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL - KHYAWARI TO VILL-LATIFPUR AT SAHARANPUR BYPASS FROM KM - [N24001735	3/2022	1,428.19 -	1,428.19	211.90	08/2024 -	08/2024
338	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV - [N24001644	12/2020	524.88 -	524.88	122.22	09/2023 -	09/2023
339	DEVELOPMENT OF 6L UER II [PACKAGE - III] (NANGLOI - NAJAFGARH ROAD TILL SECTOR 24 DWARKA) FROM KM. 2 - [N24001776	7/2020	1,069.27 -	1,069.27	748.48	10/2023 -	10/2023
340	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 - [N24001516	9/2020	1,185.69 -	1,185.69	432.47	02/2024 -	02/2024
341	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) - [N24001546	1/2023	1,025.20 -	1,025.20	80.27	01/2025 -	01/2025
342	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS - [N24001692	1/2022	467.99 -	468.00	18.83	09/2024 -	09/2024
343	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 - [N24001777	7/2020	2,171.80 -	2,171.80	958.13	10/2023 -	10/2023
344	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A - [N24001813	7/2021	1,692.05 -	1,692.05	598.25	09/2024 -	09/2024
345	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT - SHAMLI - MUZAFFARNAGAR) AND NH-709A (KARN - [N24001729	8/2022	326.79 -	329.79	18.75	04/2024 -	04/2024
346	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU - [N24001809	5/2022	469.95 -	280.00	188.16	03/2024 -	03/2024
347	SPUR OF MEERUT-GARH-MUKTESHVAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN - [N24001754	1/2022	953.79 -	953.79	384.66	10/2024 -	10/2024
348	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) - [N24001790	2/2020	752.30 -	766.20	392.85	08/2023 12/2023	08/2023
349	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG - [N24001446	5/2020	894.00 -	894.00	437.91	12/2023 -	12/2023
350	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 - [N24001518	11/2019	1,669.56 -	1,669.56	575.33	09/2023 -	09/2023
351	4LBERKHEDI TO GODPEHRA NH-44 - [N24001614	2/2022	524.84 -	524.84	1,600.30	11/2024 -	11/2024
352	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) - [N24001563	10/2019	846.59 -	846.59	37.29	08/2023 09/2023	08/2023
353	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 - [N24001753	2/2022	570.98 -	570.98	186.06	06/2024 -	06/2024
354	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX - [N24001622	7/2021	1,401.87 -	1,401.87	138.72	06/2024 06/2024	06/2024
355	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO - [N24001700	12/2021	552.55 553.00	553.00	292.70	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
356	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O - [N24001651	9/2021	2,878.97 -	2,878.97	154.45	09/2024 09/2024	09/2024
357	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 - [N24001556	12/2021	521.53 -	521.53	126.88	07/2024 -	07/2024
358	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI-PRA - [N24001815	12/2022	1,699.00 -	1,699.00	13.76	11/2024 -	11/2024
359	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, - [N24001555	3/2022	955.49 -	955.49	84.06	01/2025 -	01/2025
360	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) - [N24001615	3/2021	790.78 -	790.78	133.42	04/2024 -	04/2024
361	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B - [N24001727	3/2022	762.62 -	762.62	170.66	02/2025 -	02/2025
362	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV - [N24001738	9/2021	300.79 -	300.79	122.56	10/2023 -	10/2023
363	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH - [N24001612	7/2020	1,788.69 -	1,788.69	411.07	01/2024 09/2024	01/2024
364	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 - [N24001520	11/2019	1,604.06 -	1,604.06	1,057.90	05/2024 -	05/2024
365	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- - [N24001619	8/2022	200.05 200.00	200.05	5.75	06/2024 -	06/2024
366	TUMKUR - NELAMANGALA(6L) - [N24001681	8/2022	2,032.15 1,351.00	2,032.15	29.46	08/2025 -	08/2025
367	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O - [N24001629	4/2022	796.65 -	796.65	26.55	11/2024 -	11/2024
368	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N - [N24001765	8/2022	207.77 -	207.77	-	07/2024 -	07/2024
369	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 - [N24001515	9/2020	1,542.02 -	1,542.02	363.32	02/2024 -	02/2024
370	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR - [N24001746	3/2021	364.47 -	364.47	28.87	04/2024 -	04/2024
371	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) - [N24001598	1/2022	1,388.70 -	1,388.70	73.09	04/2025 -	04/2025
372	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM - [N24001594	2/2022	534.73 -	534.73	-	01/2025 -	01/2025
373	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) - [N24001608	9/2021	2,208.68 -	2,208.68	56.93	07/2025 -	07/2025
374	BANGALORE/TN BORDER TO HOSKOTE - [N24001674	2/2023	1,240.60 -	1,240.60	403.45	02/2025 -	02/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
375	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S - [N24001571]	11/2019	1,341.36 -	1,341.36	806.97	12/2023 -	12/2023
376	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZZAFARNAGAR) AND NH-58 (MEERUT - [N24001726]	1/2023	391.26 -	391.26	14.12	08/2024 -	08/2024
377	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 - [N24001798]	2/2021	540.21 -	540.21	164.19	11/2023 -	11/2023
378	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 - [N24001778]	7/2020	801.46 -	801.46	382.03	10/2023 -	10/2023
379	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-2) - [N24001560]	2/2019	755.16 -	755.16	723.96	10/2023 11/2023	10/2023
380	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) - [N24001561]	10/2019	839.63 -	839.63	38.16	10/2023 -	10/2023
381	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 - [N24001679]	10/2022	1,479.30 -	1,479.30	86.76	04/2025 04/2025	04/2025
382	BALANCE WORKS OF 4L PANVEL-INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 (- [N24001607]	10/2022	332.00 -	332.00	-	05/2024 -	05/2024
383	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI - [N24001642]	2/2021	1,474.77 -	1,474.77	146.71	08/2024 -	08/2024
384	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO - [N24001712]	8/2020	690.00 -	690.00	594.41	07/2023 -	07/2023
385	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 - [N24001830]	6/2020	2,002.79 -	2,002.79	753.29	11/2023 -	11/2023
386	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT-GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 - [N24001699]	3/2022	312.58 -	312.58	37.38	12/2024 -	12/2024
387	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O - [N24001635]	3/2022	1,269.50 -	1,269.50	35.00	02/2025 -	02/2025
388	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-1) - [N24001562]	2/2019	738.90 -	738.90	778.02	10/2023 -	10/2023
389	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION - [N24001488]	9/2021	618.45 -	618.45	353.77	09/2023 -	09/2023
390	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 - [N24001638]	11/2021	646.42 -	646.42	158.90	07/2024 07/2024	07/2024
391	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: - [N24001702]	12/2021	184.90 185.00	185.00	79.79	09/2024 -	09/2024
392	6 L OF AURANGABAD TO BIHAR-JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N - [N24001703]	2/2022	786.81 787.00	787.00	-	05/2025 -	05/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
393	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SKIP ZONES AT KM 130.550 TO KM.130.750; KM. - [N24001620]	9/2021	442.14 -	442.14	107.84	10/2023 10/2023	10/2023
394	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595]	8/2020	1,034.00 -	1,589.00	41.50	03/2024 -	03/2024
395	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR – DEHRADUN SECTION FROM - [N24001524]	3/2021	990.28 -	990.28	671.82	10/2023 10/2023	10/2023
396	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K - [N24001733]	3/2022	1,602.48 -	1,602.48	162.20	08/2024 -	08/2024
397	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO - [N24001609]	1/2023	151.26 -	151.26	15.85	12/2023 -	12/2023
398	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD - [N24001631]	3/2021	1,525.31 -	1,525.31	132.46	10/2024 -	10/2024
399	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 - [N24001650]	12/2021	3,635.64 -	3,635.64	75.12	01/2025 01/2025	01/2025
400	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. - [N24001621]	7/2021	614.48 -	614.48	58.21	08/2024 08/2024	08/2024
401	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK - [N24001559]	9/2021	672.35 -	672.35	224.87	06/2024 -	06/2024
402	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III - [N24001737]	11/2021	923.15 -	923.15	455.61	04/2024 -	04/2024
403	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM - [N24001825]	7/2020	1,894.96 -	1,894.96	741.88	10/2023 -	10/2023
404	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 - [N24001649]	12/2021	3,273.61 -	3,273.61	75.26	02/2025 02/2025	02/2025
405	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 - [N24001797]	10/2021	815.77 -	815.77	227.75	01/2024 -	01/2024
406	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) - [N24001558]	11/2021	736.75 -	736.75	61.63	08/2024 -	08/2024
407	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K - [N24001627]	7/2021	1,912.17 -	1,912.17	0.26	02/2025 02/2025	02/2025
408	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. - [N24001734]	3/2022	1,335.45 -	1,335.45	173.11	08/2024 -	08/2024
409	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S - [N24001489]	5/2022	519.93 -	519.93	126.16	05/2024 -	05/2024
410	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) - [N24001564]	10/2019	662.08 -	662.08	32.02	07/2023 11/2023	07/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
411	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA – RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR - [N24001636]	5/2021	1,368.91 -	1,368.91	63.88	12/2024 12/2024	12/2024
412	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V - [N24001483]	2/2022	637.11 -	637.11	162.16	09/2024 -	09/2024
413	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO - [N24001634]	1/2021	1,306.95 -	1,306.95	761.02	12/2023 -	12/2023
414	4 LANING OF CHAMPA-KORBA-CHHURI-KATGHORA SECTION OF NH 149B FROM KM.0.000 TO KM.38.200 - [N24001591]	2/2021	999.97 -	999.97	831.22	01/2024 -	01/2024
415	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721]	2/2019	1,008.99 -	1,361.00	12.42	05/2024 -	05/2024
416	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] - [N24001590]	9/2020	748.99 -	903.00	675.22	10/2023 -	10/2023
417	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR - [N24001557]	3/2022	1,636.15 -	1,636.15	281.01	11/2024 -	11/2024
418	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA - [N24001593]	11/2021	1,368.19 -	1,368.19	595.79	09/2024 -	09/2024
419	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA) - [N24001630]	7/2021	1,501.02 -	1,501.02	33.00	02/2025 -	02/2025
420	4L OF AHMEDNAGAR - MIRAJGAON - KARMALA - TEMBHURNI (PKG-I) [AHMEDNAGAR TO GHOGARGAON] FROM KM. 0.00 - [N24001498]	12/2021	605.00 -	605.00	415.21	12/2023 -	12/2023
421	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N - [N24001640]	3/2021	1,229.38 -	1,229.38	499.62	11/2024 -	11/2024
422	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 (- [N24001495]	11/2022	930.00 -	930.00	104.34	11/2024 -	11/2024
423	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) - [N24001506]	2/2022	2,747.00 -	2,747.00	544.65	02/2024 -	02/2024
424	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM - [N24001482]	8/2022	772.11 -	772.11	234.08	10/2024 -	10/2024
425	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 - [N24001675]	11/2022	1,732.73 -	1,732.73	214.41	05/2025 -	05/2025
426	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR (NEAR RANITAL) TO KANGRA BYPASS SECTION OF - [N24001808]	3/2021	1,322.95 -	1,442.47	498.17	12/2024 12/2024	12/2024
427	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 - [N24001522]	1/2021	1,307.95 -	1,307.95	420.17	01/2024 -	01/2024
428	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) - [N24001507]	11/2022	1,124.00 -	1,124.00	116.71	05/2024 -	05/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
429	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E - [N24001707	3/2021	1,143.46 1,143.00	1,143.00	268.70	01/2024 -	01/2024
430	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE - [N24001680	3/2021	1,409.68 -	1,409.68	512.39	10/2024 -	10/2024
431	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 - [N24001696	2/2019	1,291.37 -	1,291.37	215.02	08/2023 -	08/2023
432	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) - [N24001508	11/2022	1,450.00 -	1,450.00	153.30	10/2024 -	10/2024
433	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA - [N24001484	9/2022	804.69 -	804.69	257.86	02/2024 -	02/2024
434	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA - [N24001588	12/2021	1,470.73 -	1,470.73	179.31	01/2025 -	01/2025
435	SIX LANNING OF MANDI DABWALI (PUNJAB/HARYANA BORDER)- CHAUTALA ROAD SECTION FROM PROPOSED MANDI DABW - [N24001672	1/2021	864.27 864.00	864.27	327.36	01/2024 01/2024	01/2024
436	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 - [N24001547	3/2022	1,909.98 -	1,909.98	22.90	01/2026 -	01/2026
437	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 - [N24001628	11/2021	2,155.95 -	2,155.95	793.18	02/2025 -	02/2025
438	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 - [N24001676	12/2022	2,718.46 -	2,718.46	-	06/2025 -	06/2025
439	4L OF HARDA - BETUL (PKG-I) FROM KM.0 TO KM.30 [HARDA - TEMAGAON] - [N24001763	9/2021	774.16 -	774.16	336.63	09/2023 -	09/2023
440	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K - [N24001637	3/2021	1,754.84 -	1,754.84	758.50	01/2025 -	01/2025
441	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I - [N24001643	12/2020	857.91 -	857.91	73.50	06/2024 -	06/2024
442	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B - [N24001552	10/2021	2,714.95 -	2,714.95	276.91	09/2024 -	09/2024
443	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. - [N24001706	3/2021	1,097.18 1,097.00	1,097.00	329.35	01/2024 -	01/2024
444	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F - [N24001633	12/2020	1,430.88 -	1,430.88	872.76	12/2023 -	12/2023
445	4L OF AHMEDNAGAR - MIRAJGAON - KARMALA - TEMBHURNI (PKG-II) [GHOGARGAON TO AHMEDNAGAR- SOLPAUR DISTR - [N24001499	1/2022	629.00 -	629.00	426.44	01/2024 -	01/2024
446	6L KANTAKAPALLE - SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) - [N24001836	2/2021	824.29 -	924.00	306.38	10/2024 -	10/2024
447	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 - [N24001693	9/2021	1,751.18 -	1,751.18	308.26	10/2024 -	10/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
448	AHMEDNAGAR BYPASS - [N24001497]	7/2021	715.00 -	715.00	398.42	07/2023 -	07/2023
449	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) - [N24001553]	3/2022	1,092.90 -	1,092.90	0.03	02/2025 -	02/2025
450	4L OF HARDA - BETUL (PKG-III) FROM KM. 81.00 TO KM.121.248 [CHICHOLI - BETUL] - [N24001764]	9/2021	814.04 -	814.04	391.67	09/2023 -	09/2023
451	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) - [N24001505]	3/2022	1,549.02 -	1,549.02	290.04	03/2024 -	03/2024
452	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D - [N24001756]	10/2020	1,352.56 -	1,352.56	178.51	10/2024 -	10/2024
453	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - [N24001589]	9/2020	755.26 -	1,039.00	385.01	03/2024 -	03/2024
454	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) - [N24001504]	5/2022	1,260.00 -	1,260.00	295.36	05/2024 -	05/2024
455	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 - [N24001550]	9/2021	1,821.72 -	1,917.32	248.20	09/2024 -	09/2024
456	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM - [N24001694]	2/2019	1,243.57 -	1,243.57	171.63	12/2023 -	12/2023
457	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM - [N24001632]	1/2021	1,741.86 -	1,741.86	849.17	05/2024 -	05/2024
458	6L KORLAM-KANTAKAPALLE SECTION OF NH-130CD ROAD FROM KM 421.100 TO KM 445.100 (PKG-3) - [N24001839]	2/2021	772.70 -	980.51	321.87	02/2024 -	02/2024
459	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 - [N24001551]	10/2021	3,044.02 -	3,044.02	214.97	09/2024 -	09/2024
460	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF - [N24001526]	8/2021	1,377.79 -	1,377.79	678.86	10/2024 10/2024	10/2024
461	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) - [N24001493]	12/2022	1,749.86 -	1,749.86	228.15	12/2024 -	12/2024
462	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 - [N24001747]	3/2020	2,193.23 -	2,314.00	1,191.60	09/2024 -	09/2024
463	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA - [N24001748]	3/2021	2,200.93 -	2,200.93	1,255.60	09/2024 -	09/2024
464	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS - [N24001732]	12/2021	540.97 -	540.97	50.31	10/2024 -	10/2024
465	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]	12/2017	2,598.00 -	1,962.50	1,012.87	10/2024 10/2024	10/2024
	Total		3,23,358.10 -	3,29,882.69	87,396.88		
	<u>SOCIAL JUSTICE</u>						
	<u>Central Public Works Department</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
466	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	73.80	03/2024 -	03/2024
	Total		170.99 -	170.99	73.80		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmdc)</u>						
467	SCREENING PLANT-III AT KIRANDUL - [N12000127	3/2021	2,092.97 -	2,221.86	704.51	08/2024 -	08/2024
	<u>Steel Authority Of India Limited (Sail)</u>						
468	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT - [N12000126	2/2022	207.74 -	207.74	104.27	06/2024 -	06/2024
469	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125	1/2022	970.18 -	970.18	168.95	05/2025 -	05/2025
	Total		3,270.89 -	3,399.78	977.73		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
470	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and - [N26000115	3/2023	185.27 -	185.27	-	03/2024 -	03/2024
471	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT - [N26000116	5/2023	645.13 -	645.13	-	08/2024 -	08/2024
	Total		830.40 -	830.40	.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Bangalore Metro Rail Corporation Limited</u>						
472	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151	6/2021	14,788.10 -	14,788.10	2,424.04	06/2026 -	06/2026
	<u>Central Public Works Department</u>						
473	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D) - [N28000154	4/2022	512.34 -	512.34	-	11/2024 -	11/2024
	<u>Nagpur Metro Rail Corporation Ltd</u>						
474	NAGPUR METRO RAIL PROJECT PHASE II - [N28000155	12/2022	6,708.00 -	6,708.00	-	12/2027 -	12/2027
	<u>National Capital Region Transport Corp</u>						
475	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134	3/2019	30,274.00 -	30,274.00	16,368.35	06/2025 -	06/2025
	Total		52,282.44 -	52,282.44	18,792.39		
	Grand Total		7,65,368.79	7,80,185.65	2,04,947.21		

Details of On Schedule Projects w.r.t. Original Schedule

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	7,670.00	6,569.75	09/2010 -	12/2024	119.64
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	19,220.00	20,460.00	12/2015 -	03/2024	67.73
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	16,576.00	12/2016 -	12/2023	38.63
	Total		27,271.00 -	43,969.00	43,605.75			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	3,291.81	769.80	09/2021 -	12/2024	138.02
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	365.49	03/2021 -	03/2025	7.88
	Total		2,525.00 -	4,523.81	1,135.29			
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	713.53	08/2019 -	08/2024	93.35
	<u>Neyveli Lignite Corporation</u>							
7	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	8,990.00	7,656.86	12/2015 -	02/2021	52.19
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	19,406.12	15,652.81	11/2021 -	12/2023	12.58
	Total		25,805.84 -	33,542.60	24,023.20			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
9	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	01/2018	676.00 -	1,085.04	24.75	04/2023 -	12/2023	60.51
	Total		676.00 -	1,085.04	24.75			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>DPIIT</u>							
	<u>licc For Dpiit</u>							
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002	11/2017	4,773.00 -	5,401.00	4,071.81	12/2019 -	09/2023	13.16
	Total		4,773.00 -	5,401.00	4,071.81			
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
11	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,900.00	1,583.95	10/2019 -	12/2023	55.84
	Total		1,219.21 -	1,900.00	1,583.95			
	<u>MINES</u>							
	<u>National Aluminum Company Limited (Nalco)</u>							
12	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	4,103.00 5,055.00	5,055.00	2,259.22	04/2021 -	03/2025	23.20
	Total		4,103.00 -	5,055.00	2,259.22			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
13	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,732.00	30.71	02/2017 -	01/2026	155.46
14	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	1,094.66	06/2019 -	02/2025	35.54
	<u>Gas Authority Of India Limited</u>							
15	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275	03/2017	1,740.00 -	2,433.15	1,547.50	12/2020 -	06/2024	39.84
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,510.30	12/2012 -	11/2024	102.71
17	BARAUNI-GUWAHATI PIPELINE - [N16000334	06/2018	3,308.00 -	3,992.00	3,537.30	12/2021 -	10/2023	20.68
18	60 KTA POLYPROPYLENE PROJECT - [N16000429	03/2019	910.56 -	1,299.02	430.40	04/2024 -	04/2024	42.66
	<u>Hindustan Petroleum Corporation Limited</u>							
19	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	23,860.04	07/2020 -	04/2024	25.50
	<u>Indian Oil Corporation Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
20	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	05/2016	1,945.00 -	2,251.00	2,005.03	02/2022 -	12/2023	15.73
21	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	5,303.14	12/2018 -	03/2024	33.98
22	R and D CAMPUS II AT FARIDABAD - [N16000375]	06/2019	2,281.94 -	3,219.94	1,122.50	12/2022 -	07/2025	41.11
23	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,587.00	726.79	12/2023 -	02/2024	13.52
	<u>Numaligarh Refinery Limited</u>							
24	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	01/2019	12,366.00 -	18,968.00	6,125.60	10/2024 -	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>							
25	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,897.83	04/2018 -	05/2026	5.80
26	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	954.95	03/2023 -	03/2024	38.20
27	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	3,793.93	03/2022 -	12/2023	23.16
	Total		61,322.26 -	83,677.71	56,940.68			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
28	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	11,134.54	10,807.99	09/2009 -	03/2024	184.07
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	21,247.54	18,903.19	09/2010 -	05/2025	238.05
	<u>National Thermal Power Corporation</u>							
30	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	7,103.00	5,911.37	03/2013 -	12/2024	138.48
31	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	14,880.63	06/2019 -	06/2024	18.38
32	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	909.90	09/2019 -	09/2026	30.48
33	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	21,304.21	10/2011 -	07/2024	145.16
34	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	10,831.04	11/2020 -	08/2023	3.76
	<u>Power Grid Corporation Of India Limited</u>							
35	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	5,600.77	12/2018 -	12/2024	92.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
36	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	4,578.01	12/2018 -	01/2024	31.08
37	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	1,952.75	02/2020 -	03/2024	36.46
	<u>Satluj Jal Vidyut Nigam Limited</u>							
38	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	1,272.29	1,172.12	12/2021 -	08/2023	96.24
39	BIKANER SOLAR POWER PROJECT - [N18000335]	04/2022	5,491.89 532.00	6,023.89	2,211.03	05/2024 -	05/2024	9.69
	<u>Thdc India Limited</u>							
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	3,163.57	06/2013 -	06/2026	54.94
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	5,601.35	02/2016 -	06/2024	191.23
	Total		70,309.71 -	1,25,052.19	107,827.93			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
42	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,666.35	03/2023 -	03/2024	8.75
43	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,805.17	3,491.85	03/2021 -	03/2026	111.54
44	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,384.72	757.06	03/2022 -	12/2024	8.85
45	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	6,409.38	2,826.85	03/2024 -	03/2024	76.69
46	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	1,335.69	03/2023 -	03/2026	10.94
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
47	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	31,304.00	- -	-	341.96
48	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	47,476.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>							
49	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,822.92	- -	12/2024	290.95
50	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,110.00	1,165.40	03/2012 -	06/2023	241.82
51	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	1,323.75	- -	03/2024	253.52

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
52	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,700.00	2,044.95	- -	03/2024	356.82
53	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	950.34	03/2021 -	12/2024	63.37
54	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	965.84	03/2021 -	03/2024	62.06
55	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,510.00	2,102.69	- -	03/2024	358.42
	<u>East Coast Railway</u>							
56	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	980.13	06/2021 -	03/2025	137.80
57	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	2,904.31	03/2009 -	12/2026	29.71
58	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,152.38	02/2019 -	02/2023	38.43
59	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,440.00	1,058.66	03/2020 -	03/2024	24.14
	<u>Eastern Railways</u>							
60	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	1,141.34	03/2019 12/2009	03/2024	36.22
61	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	980.46	03/2022 -	03/2025	133.39
	<u>Indian Railway Construction Company Limited</u>							
62	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,438.39	2,976.72	09/2018 -	12/2023	12.55
	<u>Metropolitan Rapid Transport Projects</u>							
63	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	10,442.41	8,008.94	03/2016 -	12/2023	114.22
	<u>North Central Railway</u>							
64	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	1,024.32	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>							
65	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	9,362.06	6,591.01	03/2014 -	02/2024	291.15
66	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.79	13,763.33	03/2011 -	03/2025	221.56
67	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,304.62	1,104.78	03/2019 -	-	238.69
68	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,650.00	1,761.52	03/2019 -	03/2024	397.31

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
69	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	6,663.00	2,556.74	03/2015 -	03/2026	186.39
70	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	7,876.92	3,290.96	12/2015 -	12/2023	488.06
71	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,647.51	1,999.72	03/2019 -	01/2024	47.25
72	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	8,324.28	269.80	03/2021 -	-	818.33
73	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	1,187.49	349.63	03/2020 -	10/2024	186.25
74	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	4,059.65	2,898.81	03/2022 -	03/2026	81.86
	<u>North Eastern Railway</u>							
75	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	2,560.00	2,121.53	03/2022 -	10/2023	97.62
76	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]	04/2016	1,177.96 -	1,500.95	1,119.47	12/2019 -	03/2024	27.42
	<u>Northern Railway</u>							
77	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024	348.44
78	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	37,012.26	36,017.83	11/2002 -	01/2024	1,380.49
79	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.14	482.67	03/2023 -	06/2025	369.35
	<u>Rail Vikas Nigam Ltd.</u>							
80	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,834.54	3,020.54	03/2016 -	07/2025	65.94
81	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	3,955.01	12/2026 -	03/2025	127.62
82	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,300.00	3,204.74	03/2023 -	03/2024	55.15
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	8,964.35	5,943.37	03/2016 -	03/2026	126.83
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	355.80	03/2014 -	12/2025	18.95
85	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	5,013.33	12/2023 -	12/2023	9.32
86	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,500.00	1,251.40	03/2022 -	12/2023	58.97
87	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,457.79	1,491.77	03/2019 -	03/2024	57.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
88	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	24,659.00	14,020.06	12/2024 -	03/2025	52.07
89	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	3,674.36	12/2024 -	12/2026	42.47
90	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,552.26	1,772.12	03/2019 -	05/2023	64.62
91	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,846.81	03/2020 -	08/2023	102.11
	<u>South Central Railway</u>							
92	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,500.98	1,129.92	03/2009 -	03/2027	139.28
93	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	3,014.00	1,071.53	03/2010 -	03/2025	159.72
94	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	1,533.64	03/2023 -	03/2025	5.16
95	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	3,122.35	1,267.65	03/2021 -	03/2021	36.42
96	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,381.68	2,532.11	03/2000 -	03/2000	96.27
97	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	2,728.66	03/2022 -	12/2025	7.06
98	KAZIPET-BALHRSHA - [N22000367]	04/2015	2,063.03 -	2,909.00	2,355.36	03/2021 -	01/2025	41.01
	<u>South East Central Railway</u>							
99	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,544.25	2,238.21	03/2023 -	12/2024	85.71
100	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	230.25	12/2021 -	12/2025	378.60
101	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	1,488.70	03/2021 -	10/2024	8.23
102	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,680.00	1,171.79	12/2021 -	12/2024	22.63
	<u>South Eastern Railway</u>							
103	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	3,029.04	1,693.74	03/2021 -	03/2024	75.68
	<u>South Western Railway</u>							
104	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,649.31	363.80	03/2016 -	03/2026	67.22
105	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,404.03	1,161.58	- -	12/2025	16.57
106	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	159.49	- -	03/2030	123.51
107	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,960.00	1,887.40	03/2019 -	12/2024	21.39
	<u>Southern Railway</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
108	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	3,118.34	1,877.71	02/2019 -	03/2025	330.30
109	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,620.28	758.81	- -	12/2025	521.16
110	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,053.39	328.43	03/2019 -	12/2027	1,601.23
111	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	0.93	- -	03/2025	33.90
	<u>West Central Railway</u>							
112	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	3,032.46	2,080.00	03/2021 -	12/2025	614.19
113	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	3,230.57
114	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,445.30	2,020.86	03/2020 -	10/2024	38.63
115	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,938.00	1,279.35	03/2022 -	06/2024	18.55
116	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	990.59	03/2022 -	09/2024	114.32
	<u>Western Railway</u>							
117	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,021.00	2,919.74	03/2022 -	03/2026	71.85
118	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	1,095.12	201.24	03/2012 -	03/2024	244.12
119	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,793.63	1,222.16	03/2022 -	12/2026	33.13
120	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	04/2007	1,640.04 -	1,873.10	1,136.95	03/2022 -	12/2025	14.21
	Total		1,67,689.78 -	4,10,506.09	280,441.22			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
121	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]	01/2014	1,408.85 -	2,138.16	1,560.46	10/2016 -	11/2023	51.77
122	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	1,253.04	- -	05/2023	2.93
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
123	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]	04/2017	642.96 -	1,139.85	528.71	06/2023 -	01/2024	77.28
	<u>National Highways Authority Of India</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
124	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]	09/2010	946.00 -	1,046.56	827.99	06/2018 -	08/2023	10.63
125	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,656.21	03/2014 -	06/2024	18.66
126	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	05/2014	1,655.01 -	2,639.00	1,771.52	08/2016 -	07/2023	59.46
127	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) [N24000463]	12/2015	1,083.00 -	1,414.01	1,059.61	06/2018 -	08/2023	30.56
128	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	01/2016	1,027.53 -	2,628.31	2,615.85	06/2018 -	06/2023	155.79
129	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	3,006.53	3,022.15	06/2018 -	06/2023	350.75
130	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	589.65	12/2019 -	12/2023	1.33
131	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,657.47	09/2016 -	12/2023	41.78
132	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] [N24000551]	03/2016	1,587.49 -	3,063.99	2,938.25	04/2019 -	07/2023	93.01
133	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	03/2016	899.00 -	1,381.45	939.15	04/2019 -	02/2024	53.67
134	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 [N24000564]	03/2016	1,408.00 -	1,659.12	1,115.46	07/2020 -	02/2024	17.84
135	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,679.45	08/2019 -	05/2024	16.55
136	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]	01/2017	1,251.11 -	1,361.00	563.93	12/2020 -	10/2023	8.78
137	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	1,007.00	257.01	03/2020 -	07/2024	35.23
138	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	837.73	03/2017 -	06/2023	1.06
139	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 [N24000696]	08/2017	950.64 -	1,168.33	729.78	02/2022 -	10/2024	22.90
140	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,503.86	1,405.49	05/2020 -	11/2023	33.78
141	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]	01/2018	953.09 -	1,014.08	731.39	05/2020 -	05/2023	6.40
142	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]	01/2018	686.65 -	1,015.16	355.84	09/2020 -	12/2023	47.84

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
143	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738	01/2018	999.00 -	1,152.70	339.23	09/2021 -	06/2023	15.39
144	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,862.77	465.92	02/2023 -	09/2024	30.74
145	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU - [N24000788	03/2018	841.57 -	1,619.48	1,368.06	09/2022 -	03/2024	92.44
146	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834	03/2018	1,161.39 -	1,404.00	396.76	10/2021 -	03/2024	20.89
147	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835	03/2018	1,484.30 -	2,182.41	1,219.02	12/2020 -	05/2023	47.03
148	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851	03/2018	1,162.92 -	1,182.87	160.20	07/2021 -	09/2024	1.72
149	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 -	1,136.83	1,016.30	05/2021 -	01/2024	137.46
150	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854	03/2018	1,005.08 -	1,073.10	699.05	03/2021 -	06/2023	6.77
151	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185	11/2017	2,159.00 -	2,262.00	2,212.19	07/2021 -	05/2023	4.77
152	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,569.68	1,054.39	02/2021 -	08/2023	27.94
153	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428	03/2018	998.70 -	1,358.32	785.96	11/2021 -	11/2023	36.01
154	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429	03/2018	1,294.47 -	1,588.40	605.20	11/2021 -	11/2023	22.71
155	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430	03/2018	2,120.40 -	2,565.63	1,147.79	01/2022 -	01/2024	21.00
156	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431	03/2018	1,872.68 -	2,756.09	848.82	10/2020 -	09/2024	47.17
157	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533	11/2020	1,690.23 -	2,010.17	1,067.66	12/2023 -	03/2024	18.93
158	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 - [N24001550	09/2021	1,821.72 -	1,917.32	248.20	09/2024 -	09/2024	5.25

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
159	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 [N24001589]	09/2020	755.26 -	1,039.00	385.01	03/2024 -	03/2024	37.57
160	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595]	08/2020	1,034.00 -	1,589.00	41.50	03/2024 -	03/2024	53.68
161	4 LANE OF BILASPUR TO URGGA PROJECT (KM 0.00 TO KM 70.2) OF NH-130A - [N24001611]	04/2020	1,855.59 1,870.00	1,869.85	187.36	03/2024 -	03/2024	.77
162	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655]	06/2021	3,606.00 -	3,923.82	2,789.91	02/2025 -	02/2025	8.81
163	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656]	06/2021	2,595.00 -	3,994.60	2,696.56	03/2025 -	03/2025	53.93
164	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658]	01/2021	4,265.42 -	4,708.42	2,751.50	07/2024 -	07/2024	10.39
165	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659]	02/2021	3,375.31 -	3,790.17	1,745.63	07/2024 -	07/2024	12.29
166	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 - [N24001661]	10/2020	3,219.47 3,713.00	3,713.14	1,911.28	04/2024 -	05/2025	15.33
167	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 - [N24001686]	03/2021	1,065.06 1,445.00	1,577.92	26.31	03/2023 -	12/2023	48.15
168	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 - [N24001687]	10/2021	1,331.77 2,083.00	2,508.79	60.90	10/2023 -	10/2023	88.38
169	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN - [N24001691]	10/2019	1,225.24 1,506.00	1,676.11	14.76	10/2021 -	01/2024	36.80
170	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - [N24001710]	09/2020	2,334.68 2,335.00	2,335.00	714.12	03/2023 -	11/2023	.01
171	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719]	02/2021	2,948.31 -	3,392.00	506.57	07/2024 -	07/2024	15.05
172	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1 - [N24001720]	10/2020	1,023.91 -	1,285.00	318.78	05/2024 -	05/2024	25.50
173	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721]	02/2019	1,008.99 -	1,361.00	12.42	05/2024 -	05/2024	34.89
174	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739]	10/2019	1,779.83 -	2,200.00	708.00	11/2023 -	11/2023	23.61
175	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743]	01/2018	1,916.38 -	2,078.00	1,158.54	02/2023 -	08/2023	8.43

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
176	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 - [N24001747]	03/2020	2,193.23 -	2,314.00	1,191.60	09/2024 -	09/2024	5.51
177	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 - [N24001752]	12/2018	2,375.87 -	2,566.80	2,299.14	02/2023 -	08/2023	8.04
178	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545. IN TH - [N24001755]	10/2019	1,936.68 -	2,458.03	1,380.90	03/2023 -	08/2023	26.92
179	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779]	03/2018	2,507.00 -	3,030.73	1,155.70	09/2022 -	12/2023	20.89
180	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781]	01/2018	2,067.67 -	2,160.00	1,496.49	10/2021 -	11/2023	4.47
181	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786]	03/2021	1,259.00 -	1,910.00	60.25	03/2024 -	12/2024	51.71
182	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788]	07/2020	2,271.86 -	3,916.00	426.80	12/2023 -	06/2024	72.37
183	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789]	07/2020	1,710.30 -	1,927.00	265.19	08/2023 -	06/2024	12.67
184	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796]	03/2022	1,013.33 -	1,111.33	202.73	10/2024 -	10/2024	9.67
185	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799]	02/2021	1,166.96 -	1,251.00	755.96	10/2023 -	04/2024	7.20
186	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805]	03/2018	1,169.04 -	1,693.95	1,010.33	03/2021 -	06/2023	44.90
187	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806]	03/2018	1,241.38 -	2,122.64	1,577.64	03/2023 -	06/2023	70.99
188	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF - [N24001808]	03/2021	1,322.95 -	1,442.47	498.17	12/2024 -	12/2024	9.03
189	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812]	03/2021	1,002.11 -	1,358.00	28.69	05/2024 -	05/2024	35.51
190	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) - [N24001818]	02/2021	818.73 -	1,105.00	73.20	01/2025 -	01/2025	34.97
191	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) - [N24001819]	03/2021	1,102.63 -	1,303.00	212.43	01/2025 -	01/2025	18.17
192	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) - [N24001820]	02/2021	1,484.83 -	1,768.00	383.07	12/2024 -	12/2024	19.07

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
193	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP - [N24001821	11/2020	1,137.74 -	1,289.00	321.70	10/2024 -	10/2024	13.29
194	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE - [N24001822	12/2020	1,075.27 -	1,307.00	384.53	10/2024 -	10/2024	21.55
195	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP - [N24001824	03/2020	1,863.09 -	2,238.00	894.15	01/2024 -	01/2024	20.12
196	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826	02/2019	927.77 -	1,603.00	1,104.18	02/2022 -	10/2023	72.78
197	6L ALURU - JAKKURU SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838	02/2021	922.50 -	1,128.68	435.46	03/2024 -	06/2024	22.35
	Total		1,16,356.96 -	1,50,012.57	78,918.35			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
198	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,840.00	23,131.35	05/2015 -	08/2023	53.56
199	SCREENING PLANT-III AT KIRANDUL - [N12000127	03/2021	2,092.97 -	2,221.86	704.51	08/2024 -	08/2024	6.16
	Total		17,617.97 -	26,061.86	23,835.86			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
200	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	11,786.54	12/2018 -	12/2023	19.98
	<u>Chennai Metro Rail Ltd</u>							
201	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	18,380.00	17,619.68	12/2015 -	12/2015	25.89
	<u>Delhi Metro Rail Corporation</u>							
202	DELHI MRTS PHASE-III - [N28000056	09/2011	38,585.00 -	40,180.91	40,217.45	03/2016 -	08/2021	4.14
	<u>Kochi Metro Rail Corporation Ltd</u>							
203	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	09/2020	20.00
	<u>Maharashtra Metro Rail Corporation Ltd.</u>							
204	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	13,656.22	10,829.00	11/2021 -	12/2023	19.58
	<u>Mumbai Metro Rail Corporation Ltd</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2023)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
205	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	37,276.00	24,123.86	03/2020 -	12/2023	61.12
	<u>Patna Metro Rail Corporation</u>							
206	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 -	13,925.50	1,353.32	06/2024 -	09/2024	4.19
	Total		1,17,061.56 -	1,42,561.99	111,989.02			
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
207	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	21,727.98	03/2020 -	03/2024	447.22
	Total		10,151.04 -	55,548.87	21,727.98			
	Grand Total		6,26,882.33	10,88,897.73	758,385.01			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N02100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 6,840.00	7,670.00	6,569.75	09/2010 10/2022	12/2024	171	119.64	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	38,740.00	11/2020 -	11/2023	36	0	
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	16,576.00	12/2016 -	12/2023	84	38.63	
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 19,220.00	19,220.00	20,460.00	12/2015 -	03/2024	99	67.73	
	Total		67,120.00 -	83,818.00	82,345.75					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	351.21	304.71	04/2020 -	08/2023	40	15.61	Nil
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	458.00 -	458.00	218.86	03/2020 06/2022	08/2023	41	0	Nil
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	475.39	391.54	04/2021 -	09/2023	29	0	Nil
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	446.26	09/2020 -	09/2023	36	0	Nil
9	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	412.24	354.98	06/2021 -	09/2023	27	0	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
10	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. - [N04000093]AAI, GUJARAT	08/2018	353.25 -	353.25	254.94	02/2021 -	09/2023	31	0	Nil
11	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 - [N04000094]AAI, UTTAR PRADESH	03/2021	242.14 328.00	328.00	215.08	12/2022 09/2023	09/2023	9	35.46	As above.
12	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM - [N04000096]AAI, MAHARASHTRA	06/2017	255.68 -	255.68	225.87	12/2020 -	09/2023	33	0	Process of acquisition of land is in progress by State Government.
13	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 - [N04000098]AAI, MADHYA PRADESH	10/2021	446.12 -	446.12	271.14	08/2023 09/2023	09/2023	1	0	1. Construction of Six Lane approach road from Bhind Road to Airport Land (Length: 400 m.) 2. Diversion of existing Shanichara road through D.D. Nagar in Gwalior district.
14	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI, ANDHRA PRADESH	08/2017	177.10 -	177.10	142.52	02/2020 12/2021	10/2023	44	0	1. A portion of the site measuring 3.40 acres is not available due to write petition between land owner & State Govt., which is fouling in the Runway extension and Basic Strip due to which the work will be delayed further. 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men, materials & Machinery for the work.
15	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI, TAMIL NADU	08/2018	951.28 -	951.28	867.64	10/2021 -	12/2023	26	0	Nil
16	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	1,405.00	1,008.10	08/2022 12/2023	12/2023	16	0	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	357.00	168.32	03/2022 12/2023	12/2023	21	-6.27	Nil
18	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63 -	645.63	636.43	08/2022 12/2023	12/2023	16	0	Nil
19	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH	07/2018	480.33 -	640.00	245.19	09/2021 12/2023	03/2024	30	33.24	Nil
20	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH	04/2020	611.80 -	611.80	217.58	03/2023 -	06/2024	15	0	Nil
21	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. - [N04000095]AAI,GOA	11/2017	255.69 -	255.69	45.34	09/2021 -	06/2024	33	0	Nil
22	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	3,291.81	769.80	09/2021 -	12/2024	39	138.02	
23	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	466.96	10/2022 -	12/2024	26	0	AUGUMENTATION OF STORM WATER DRAINAGE SYSTEM FOR CONNECTIONING NEW STORM WATER SYSTEM OF AIRPORT WITH ENLARGED CAPACITY.
24	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX - [N04000100]AAI,MANIPUR	11/2021	499.00 -	499.00	83.88	07/2024 12/2024	12/2024	5	0	Acquisition of AAI Land for proposed 6 lane road is pending.
25	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	365.49	03/2021 -	03/2025	48	7.88	
26	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	1,335.88	02/2022 -	12/2025	46	0	Nil
	Total		15,019.08 -	17,286.96	9,036.51					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
27	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	302.00	297.18	05/2014 -	11/2023	114	4.34	
28	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	341.22	207.24	03/2017 -	12/2023	81	12.2	
29	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	379.46	03/2021 -	03/2024	36	0	
30	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 -	334.27	80.44	04/2018 -	03/2024	71	37.56	
31	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	582.15	03/2019 -	04/2025	73	0	
32	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	151.04	04/2014 -	10/2025	138	0	
	<u>Central Coal Fields Limited</u>									
33	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	133.28	03/2011 -	03/2024	156	0	
34	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	94.69	03/2014 -	03/2024	120	0	
35	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	487.68	03/2016 -	03/2025	108	0	
36	TETARIAKHAR EXPANSION OCP - [N06000186]CCL,JHARKHAND	11/2019	243.52 -	243.52	41.66	03/2023 -	03/2025	24	0	
	<u>Eastern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
37	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73	5,146.48	713.53	08/2019	08/2024	60	93.35	1. Publication of final figure of Demographic survey report for Non-ECL houses and valuation of immovable properties for Legal Title Holder (LTH) households by ADDA. 2. Identification and finalization of balance land by ADDA for construction of remaining houses. In this connection, approval of Deptt. of Industry Commerce & Enterprises (IC & E), Govt. of WB regarding utilization of further 100.32 acres vested land which was identified and finalized by ADDA for this rehabilitation project was pending since 22.09.2020. 3. Construction of balance quarters for shifting of NLTH houses/ encroachers. 4. Shifting of affected families at the resettlement sites by ADDA where construction of flats have been completed and after shifting demolition of vacated houses by ADDA/State implementing agency, which was under the threat of subsidence at the old rehabilitation site. 5. As per resolution of review meeting taken by Sec(Coal) priority should be given for shifting of 10,144 NLTH houses from vulnerable locations/sites to those resettlement sites, where construction work is ongoing and likely to be completed shortly. 6. Approval of revised rehabilitation package by Cabinet of Government of West Bengal.
38	HURA - C OC (3 MTY) - [N06000143]ECL, JHARKHAND	10/2015	359.69	859.41	283.39	03/2022	03/2029	84	138.93	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Mahanadi Coal Fields Limited</u>									
39	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	259.49	03/2019 -	03/2026	84	0	
40	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	779.83	03/2021 -	03/2026	60	0	
41	KULDA EXPANSION OCP- 15 MTY - [N06000248]MCL,ODISHA	06/2014	348.16 -	348.16	186.02	03/2018 -	03/2026	96	0	
42	SUBHADRA OCP - [N06000249]MCL,ODISHA	05/2021	1,693.81 -	1,693.81	904.20	03/2027 03/2029	03/2029	24	0	
	<u>Neyveli Lignite Corporation</u>									
43	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	19,406.12	15,652.81	11/2021 -	12/2023	25	12.58	
44	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	709.06	541.79	06/2015 -	09/2027	147	-51.37	Acquisition of required lands for capacity expansion is currently under progress.
	<u>Northern Coal Fields Limited</u>									
45	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	1,011.43	03/2022 -	08/2023	17	0	
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	1,447.90	03/2021 -	10/2023	31	0	
47	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH	07/2019	998.71 -	998.71	106.29	03/2023 -	03/2025	24	0	Delayed by 24 months as FC proposal was rejected by FAC of MoEF and CC and is under process now for getting FC with modified proposal of forest land causing delay in project implementation.
48	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE	08/2020	836.42 -	836.42	361.69	03/2024 -	03/2025	12	0	Stage-II Forestry Clearance of MP Forest land and Stage-I Forestry Clearance of UP Forest land
	<u>Singareni Colliers Company Limited</u>									
49	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	409.48	03/2022 -	03/2024	24	0	
50	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	153.75	03/2018 -	03/2024	72	0	
51	GODAVARIKHANI COAL MINE - [N06000202]SCCL,TELANGANA	07/2019	438.98 -	438.98	123.25	03/2023 -	03/2024	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
52	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]SCCL, TELANGANA	11/2015	489.62 -	489.62	392.20	03/2023 -	03/2024	12	0	
53	RCE OF INDARAM OPENCAST PROJECT - [N06000211]SCCL, TELANGANA	08/2017	349.28 -	424.81	335.24	03/2021 -	03/2024	36	21.62	
54	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213]SCCL, TELANGANA	03/2016	384.32 -	384.32	180.58	03/2020 -	03/2024	48	0	
55	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214]SCCL, TELANGANA	08/2017	442.42 -	442.42	222.33	03/2020 -	03/2024	48	0	
56	RCE OF KISTARAM OPENCAST PROJECT - [N06000215]SCCL, TELANGANA	03/2017	164.04 -	164.04	143.08	03/2021 -	03/2024	36	0	
57	NAINI COAL MINE - [N06000203]SCCL, ODISHA	03/2020	494.30 -	494.30	397.67	03/2024 -	03/2025	12	0	
58	VENKATESH KHANI COAL MINE - [N06000204]SCCL, TELANGANA	10/2020	484.51 -	484.51	64.04	03/2023 -	03/2025	24	0	
	<u>South-Eastern Coal Fields Limited</u>									
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL, MADHYA PRADESH	12/2014	357.80 -	357.80	86.99	03/2021 -	03/2024	36	0	
60	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	100.88	03/2021 -	03/2024	36	0	
61	BATURA HIGHWALL PROJECT - [N06000134]SECL, MADHYA PRADESH	07/2015	231.92 -	231.92	2.26	03/2022 -	03/2024	24	0	
62	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL, CHHATTISGARH	07/2016	459.49 -	459.49	223.15	03/2020 -	03/2024	48	0	
63	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATTISGARH	06/2010	11,816.40 -	11,816.40	5,887.31	03/2023 -	03/2025	24	0	
64	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATTISGARH	08/2013	7,612.33 -	7,612.33	4,109.56	03/2023 -	03/2025	24	0	
65	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATTISGARH	12/2013	610.63 -	610.63	482.80	03/2022 03/2025	03/2025	36	0	
66	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATTISGARH	07/2015	316.10 -	316.10	156.33	03/2020 -	03/2025	60	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
67	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	201.12	03/2021 03/2025	03/2025	48	0	
68	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATTISGARH	07/2008	178.44 -	178.44	9.22	03/2014 -	03/2026	144	0	
69	AMERA OC RCE - [N06000123]SECL,CHHATTISGARH	02/2015	335.97 -	335.97	49.00	03/2018 -	03/2026	96	0	
70	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	1.08	03/2023 -	03/2027	48	0	
71	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATTISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	0	
72	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATTISGARH	02/2015	916.24 -	916.24	13.73	03/2023 -	03/2030	84	0	
73	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATTISGARH	11/2014	1,624.59 -	1,624.59	49.60	03/2023 -	03/2031	96	0	
	<u>Western Coal Fields Limited</u>									
74	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	121.58	03/2021 03/2024	03/2024	36	0	
75	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE	08/2016	319.76 319.76	319.76	275.11	03/2022 03/2025	03/2025	36	0	
76	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	310.44	03/2021 03/2025	03/2025	48	0	Reason of delay: Project could not achieve its PR capacity due to delay in diversion of 121.58 Ha forest land. Stage II issued on 22.12.2021.
77	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	249.15	03/2021 03/2025	03/2025	48	0	
	Total		67,739.03 -	72,359.95	39,454.12					
	<u>MINES</u>									
	<u>Central Public Works Department</u>									
78	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]CPWD, WEST BENGAL	04/2019	255.37 -	255.37	37.77	04/2022 -	10/2025	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>National Aluminum Company Limited (Nalco)</u>									
79	UTKAL D AND E COAL BLOCK - [N10000011]NALCO, ODISHA	05/2016	534.00 667.23	667.23	605.95	01/2020 11/2023	11/2023	46	24.95	
80	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO, TAMIL NADU	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2023	12/2023	54	-2.07	Extension of NFR (Noted For Record) is pending with TANGEDCO.
81	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO, ODISHA	11/2017	483.00 483.00	483.00	197.42	04/2021 05/2024	05/2024	37	0	
82	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO, ODISHA	12/2014	4,103.00 5,055.00	5,055.00	2,259.22	04/2021 12/2022	03/2025	47	23.2	
83	POTTANGI BAUXITE MINES - [N10000016]NALCO, ODISHA	05/2018	1,437.00 1,381.00	1,381.00	603.12	12/2024 03/2025	05/2025	5	-3.9	1) Delay in issuance of Terms and Conditions for grant of Mining Lease by Govt of Odisha over an area of 697.979 Ha. 2) Delay in Issuance of Forest Right Act (FRA) certificate. 3) Delay in approval of Compensatory Afforestation (CA) Scheme.
84	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO, ODISHA	12/2015	355.00 581.00	581.00	79.69	11/2020 09/2025	09/2025	58	63.66	
	Total		7,333.99 -	8,585.77	3,918.17					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
85	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATTISGARH	01/2010	15,525.00 23,840.00	23,840.00	23,131.35	05/2015 06/2023	08/2023	99	53.56	
86	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC, CHHATTISGARH	11/2015	2,907.00 -	2,907.00	1,362.32	06/2023 07/2024	05/2025	23	0	
	<u>Steel Authority Of India Limited (SAIL)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
87	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA	11/2020	377.18 -	377.18	299.73	05/2023 -	02/2024	9	0	
88	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATTISGARH	11/2020	542.24 -	542.24	160.15	12/2023 -	04/2025	16	0	
89	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	843.97	10/2017 12/2021	09/2025	95	0	
	Total		20,385.43 -	28,700.43	25,797.52					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
90	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI - [N16000452]BPCL,MAHARASHTRA	05/2022	423.39 -	423.39	63.90	03/2024 -	09/2024	6	0	Nil
91	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	867.50	08/2022 06/2023	10/2024	26	0	Delay by State Govt. Authorities for development of infrastructure for sourcing power and water for the project. Delay in getting CTE for 1G Plant.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
92	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	1,094.66	06/2019 02/2024	02/2025	68	35.54	With the help of District administration, 3(1) notices distributed to all concerned patadhars on October, November and December 2021. Out of 528 Patadhars, 6 Patadhars attended enquiry, further enquiry could not be completed for rest of patadhars due to resistance. The new nodal officer took over the office of the CA on 26th Feb 22' and the notification of him as the Competent Authority was published in the official gazette of India on 14.06.2022. District collector Coimbatore intervened and convened a coordination meeting between all stake holders on 15th March 22' and a common consensus was arrived in selection of the most probable pipeline route. The farmer's association suggested various routes and the same has been inspected by CA and KSPPL team Private land usage reduced up to 1.5 KM in Phase I. KSPPL was advised to carry out detail survey. Detailed and cadastral has been completed from Palakkad RT to Kattampatti Proposed BPCL Plant. Draft for fresh 3(1) notification has been sent for publication. The applications for laying the pipeline along State Highways and other roads till Coimbatore are submitted for approval. Site investigation for River crossings and panchayat roads in progress. All the applications for crossings except one Railway and one NH is submitted and inspection in progress. A Progress

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
93	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442]BPCL, MAHARASHTRA	04/2021	1,164.69 -	1,164.69	169.72	06/2024 -	07/2025	13	0	CIDCO Approval for ROU for 20" pipeline from JNPT to Uran Terminal
94	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,732.00	1,732.00	30.71	02/2017 01/2026	01/2026	107	155.46	Nil
	<u>Gas Authority Of India Limited</u>									
95	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL, BIHAR	10/2017	359.25 -	359.25	272.02	10/2022 -	10/2023	12	0	NIL
96	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]GAIL, JHARKHAND	10/2017	226.45 -	226.45	217.29	10/2022 -	10/2023	12	0	NIL
97	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL, MULTI STATE	06/2018	3,308.00 3,992.00	3,992.00	3,537.30	12/2021 10/2023	10/2023	22	20.68	1) [West Bengal] Laying works at 8 Km stretch of RoU is held up in Mainaguri Block, Jalapaiguri district due to resistance of the land owners demanding re-route of the pipeline alignment. 2) [Assam] 250 mtrs RoU affected in Radhakuchi Village, Kamrup (R) since June 2020 due to writ petition filed in Gauhati High Court against construction activities. 3) Slow RoU acquisition, Panchnama, compensation disbursement in West Bengal. 4) [West Bengal] 500 mtrs RoU hindrance by the villagers in Phasidewa block of Darjeeling district. 5) [Bihar] Construction works in HURL premises at Barauni is held up due to pending permission from HURL
98	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL, ODISHA	07/2017	243.53 -	243.53	223.48	07/2022 -	12/2023	17	0	
99	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL, ODISHA	07/2017	182.20 -	182.20	137.31	07/2022 -	12/2023	17	0	NIL

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
100	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	247.90	219.43	02/2021 12/2023	12/2023	34	9.91	Nil
101	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]GAIL,JHARKHAND	10/2017	221.45 -	221.45	152.54	10/2022 -	12/2023	14	0	NIL
102	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 2,433.15	2,433.15	1,547.50	12/2020 06/2024	06/2024	42	39.84	Slow progress in RoU acquisition, Panchnama, Compensation disbursement & RoU Release (~ affected length ~ 134 Km for Durgapur Haldia section in West Bengal).
103	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE	03/2020	1,030.65 -	1,030.65	625.20	11/2022 06/2024	06/2024	19	0	Delay in RoU acquisition & release in West Bengal.
104	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE	09/2019	2,658.34 -	2,658.34	1,553.40	07/2022 09/2024	09/2024	26	0	- Delay in RoU acquisition in Andhra Pradesh & Odisha due to non-availability of dedicated Competent Authority for GAIL's project. - Lengthy Process of Forest Permissions in Odisha.
105	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE	06/2020	7,844.25 -	7,844.25	4,595.80	05/2023 10/2024	10/2024	17	0	- Hindrances in MSRDC RoW in Mumbai Nagpur section. - Lengthy process for Forest permission & Wildlife clearance. - Delay in acquisition of Permanent Plots for SV/IP stations
106	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,510.30	12/2012 11/2024	11/2024	143	102.71	- Non - availability of hindrance free RoU in Tamil Nadu. - Delay in pipeline laying permission from SH-86 & NH-544. - Hindrances in execution of laying works along NH-844 in stretches due to non-payment of compensation to the landowners by NHAI
	<u>Hindustan Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
107	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL, ANDHRA PRADESH	09/2019	196.26 196.26	196.26	141.51	07/2020 07/2023	10/2023	39	0	
108	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL, KARNATAKA	12/2018	854.00 854.00	854.00	384.42	12/2022 12/2023	12/2023	12	0	
109	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]HPCL, PUNJAB	05/2020	1,421.46 -	1,421.46	735.28	02/2023 12/2023	12/2023	10	0	
110	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	23,860.04	07/2020 07/2022	04/2024	45	25.5	
111	RUF PITCH LOADING GANTRY - [N16000406]HPCL, ANDHRA PRADESH	10/2020	332.61 332.61	332.61	214.55	11/2022 -	04/2024	17	0	
112	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]HPCL, CHHATTISGARH	03/2021	456.00 -	456.00	181.92	03/2024 03/2025	03/2025	12	0	
113	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL, HARYANA	09/2018	520.00 -	520.00	353.70	09/2026 02/2027	02/2027	5	0	
114	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL, UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	1,340.47	03/2029 08/2029	08/2029	5	0	
115	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL	03/2019	5,830.20 -	5,830.20	414.68	03/2031 08/2031	08/2031	5	0	
	<u>Indian Oil Corporation Limited</u>									
116	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL, ODISHA	10/2018	1,297.50 -	1,297.50	1,119.42	10/2021 04/2023	07/2023	21	0	
117	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL, UTTAR PRADESH	08/2017	255.40 -	255.40	216.40	08/2020 11/2022	08/2023	36	0	
118	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL, ODISHA	01/2020	202.16 -	202.16	135.57	07/2022 -	08/2023	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
119	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 161.59	161.59	135.83	12/2019 01/2023	09/2023	45	0	
120	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	810.76	01/2021 08/2022	09/2023	32	0	
121	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	186.05	06/2021 07/2023	09/2023	27	0	
122	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	403.00	250.14	08/2022 06/2023	09/2023	13	0	
123	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 340.76	340.76	274.27	02/2020 06/2023	10/2023	44	64.91	
124	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	349.08	04/2022 -	10/2023	18	0	
125	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	1,329.13	08/2020 07/2023	11/2023	39	0	
126	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT	11/2019	5,251.00 5,894.00	5,251.00	3,116.31	05/2023 11/2023	11/2023	6	0	
127	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	1,019.00	658.96	01/2023 11/2023	11/2023	10	0	
128	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 2,251.00	2,251.00	2,005.03	02/2022 04/2023	12/2023	22	15.73	1. Stiff resistance in opening of RoU in Maharashtra due to demand of exorbitant compensation and diversion of route. As on date, work is hampered in 2.0 Km of RoU in different stretches in Beed (0.2 Km) and Solapur (1.8 Km) districts.
129	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	163.45	10/2020 06/2023	12/2023	38	0	
130	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL	03/2018	3,712.00 3,696.00	3,696.00	2,852.90	09/2022 06/2023	12/2023	15	-43	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
131	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	1,255.00	776.69	12/2021 12/2023	12/2023	24	0	
132	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	124.00	07/2021 03/2022	12/2023	29	0	
133	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	1,378.00	885.65	12/2022 02/2024	12/2023	12	0	
134	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	77.46	07/2022 06/2023	02/2024	19	0	
135	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 1,587.00	1,587.00	726.79	12/2023 -	02/2024	2	13.52	
136	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	5,303.14	12/2018 11/2023	03/2024	63	33.98	1. Delay in finalization of Market value of land for payment of enhanced compensation. Till date, Market value for 629 villages out of total 665 villages received.
137	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA	05/2019	3,361.00 -	3,361.00	2,497.03	08/2021 03/2024	03/2024	31	0	
138	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 427.10	427.10	204.58	09/2022 03/2024	03/2024	18	15.12	
139	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	1,614.00	513.56	08/2023 -	03/2024	7	0	Delay in purchase of land at Vadinar and Surendranagar. Delay in obtaining Statutory clearance such as PESO, CTE
140	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 543.00	543.00	393.54	09/2021 07/2023	04/2024	31	17.46	
141	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY - [N16000446]IOCL,MAHARASHTRA	09/2021	378.00 -	378.00	66.49	10/2023 05/2024	05/2024	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
142	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]IOCL,BIHAR	01/2020	14,810.00 -	14,810.00	6,350.87	04/2023 12/2024	12/2024	20	0	"State Govt/Local Govt related issues: a) Issues related to closure of Roads (viz. Merger of Refinery & Biological Treatment Plant (BTP) Premises, and Boundary Wall Construction near Mahna Village for Polypropylene Unit construction) is pending with local administration and b) There are restrictions imposed on plying of heavy vehicle carrying sand, stone & construction materials over Rajendra Setu Bridge (Simariya Bridge on river Ganga)."
143	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	315.45	09/2023 -	12/2024	15	0	
144	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]IOCL,RAJASTHAN	12/2021	9,028.00 -	9,028.00	4,088.75	10/2024 12/2024	12/2024	2	0	
145	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI - [N16000438]IOCL,TAMIL NADU	01/2022	827.00 -	827.00	222.66	07/2024 -	12/2024	5	0	
146	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	198.26	04/2022 -	03/2025	35	0	
147	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,219.94	3,219.94	1,122.50	12/2022 07/2023	07/2025	31	41.11	
148	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	13,805.00	3,776.82	01/2024 -	07/2025	18	0	
149	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM - [N16000441]IOCL,ASSAM	03/2022	277.00 -	277.00	35.19	07/2026 -	09/2026	2	0	
150	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	177.00	107.21	02/2027 09/2028	09/2028	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	176.00	135.37	08/2027 02/2029	02/2029	18	0	
152	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	439.00	195.43	02/2028 08/2029	08/2029	18	0	
153	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	347.00	147.32	02/2028 08/2029	08/2029	18	0	
154	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	2,996.00	517.47	02/2028 08/2029	08/2029	18	0	
155	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	613.00	224.64	12/2029 03/2030	03/2030	3	0	
156	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	2,880.00	206.83	08/2027 03/2030	03/2030	31	0	
157	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	988.00	84.87	12/2029 03/2030	03/2030	3	0	
158	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	163.00	62.69	12/2029 03/2030	03/2030	3	0	
159	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE	06/2019	169.00 -	169.00	64.99	12/2029 03/2030	03/2030	3	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
160	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 304.00	304.00	162.85	06/2023 01/2024	01/2024	7	52	
	<u>Oil & Natural Gas Corporation Limited</u>									
161	DEVELOPMENT OF NELP BLOCK KG-ONN-2003/1 NAGAYALANKA FIELD-PH II - [N16000469]ONGC,ANDHRA PRADESH	03/2022	284.79 -	284.79	201.63	06/2023 -	11/2023	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
162	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	3,793.93	03/2022 12/2023	12/2023	21	23.16	
163	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	06/2019	2,494.68 -	2,494.68	2,354.10	03/2022 12/2023	12/2023	21	0	
164	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND	12/2015	823.27 1,137.79	1,137.79	954.95	03/2023 03/2024	03/2024	12	38.2	LAQ issues for remaining well locations.
165	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	25,464.83	06/2020 05/2024	05/2024	47	0	
166	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433]ONGC,ASSAM	08/2021	218.38 -	218.38	66.27	02/2023 -	07/2024	17	0	LAQ could not be completed due to protest by local dwellers.
167	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	469.54	03/2019 09/2021	12/2024	69	0	* Facilities: Grant of Consent to Establish (CTE) by TNPCB (Tamil Nadu Pollution Control Board) for construction of Central Processing Facility (CPF). * Drilling: Getting EC for drilling 6 new development wells in delta districts hampered due to enactment of New act as "Tamil Nadu Protected Agricultural Zone Development Act'2020" by Govt of TN.
168	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) - [N16000445]ONGC,JHARKHAND	11/2019	431.00 -	431.00	76.44	01/2024 -	12/2024	11	0	
169	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,897.83	04/2018 12/2023	05/2026	97	5.8	
	<u>Oil India Limited</u>									
170	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	661.21	439.99	02/2020 03/2023	09/2023	43	21.57	
	Total		1,90,392.98 -	2,06,256.56	1,26,356.54					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
171	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59	4,287.59	1,168.94	08/2024	03/2026	19	0	Release of balance equity pending for Kiru HEP with JKPDC. • The total equity share for the project is Rs 1286.28 crore and NHPC has released its 100% equity share of Rs 656.00 crore to CVPPPL whereas equity share of JKSPDC released by MHA, Gol is Rs 500.50 crore only against sanctioned equity of Rs 630.28 crore. Thus balance equity of Rs 129.78 crore is required towards matching equity contribution of JKSPDC. • The matter is being regularly pursued with GoJK to release the equity.
172	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12	8,112.12	3,194.18	04/2020	09/2026	77	0	Signing of PPA for 1000MW Pakal Dul HE Projects – Pending with J&K Govt.
	<u>National Hydro-Electric Power Corporation</u>									
173	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 11,134.54	11,134.54	10,807.99	09/2009 03/2024	03/2024	174	184.07	
174	KALPI SOLAR POWER PROJECT - [N18000323]NHPC,UTTAR PRADESH	07/2020	314.64 350.46	350.46	242.14	03/2022 03/2024	03/2024	24	11.38	
175	RANGIT IV HE PROJECT - [N18000326]NHPC,SIKKIM	03/2021	938.29 938.29	938.29	658.71	05/2024 08/2024	08/2024	3	0	
176	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 21,247.54	21,247.54	18,903.19	09/2010 05/2025	05/2025	176	238.05	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
177	RATLE HE PROJECT - [N18000324]NHPC,JAMMU AND KASHMIR	02/2021	5,281.94 5,281.94	5,281.94	333.41	02/2026 05/2026	05/2026	3	0	
178	TEESTA VI HE PROJECT - [N18000325]NHPC,SIKKIM	03/2019	5,748.04 -	5,748.04	2,643.25	03/2024 08/2026	08/2026	29	0	
	<u>National Thermal Power Corporation</u>									
179	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,998.00	10,831.04	11/2020 07/2022	08/2023	33	3.76	
180	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	679.00	560.81	11/2018 03/2023	11/2023	60	28.19	None
181	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	382.22	65.29	03/2022 03/2024	03/2024	24	0	
182	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	1,221.73	153.13	07/2022 03/2024	03/2024	20	0	
183	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	599.99	262.95	07/2022 03/2024	03/2024	20	0	
184	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	842.27	93.82	07/2022 03/2024	03/2024	20	0	
185	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT	05/2021	674.92 -	674.92	89.67	09/2022 03/2024	03/2024	18	0	
186	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	17,007.00	14,880.63	06/2019 10/2022	06/2024	60	18.38	1.Maintaining Law & order and resolution of following issue: 2.Handover of Land to NTPC by CCL after land acquisition for external CHP. 3.Readiness of ATS Line(NK-GAYA) by NKTL.
187	DAYAPAR WIND ENERGY PROJECT 150MW - [N18000319]NTPC,GUJARAT	11/2021	937.80 -	937.80	314.00	05/2023 06/2024	06/2024	13	0	
188	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) - [N18000349]NTPC,GUJARAT	11/2022	1,442.60 -	1,442.60	80.60	03/2024 06/2024	06/2024	3	0	
189	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	21,304.21	10/2011 07/2023	07/2024	153	145.16	
190	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	1,267.99	09/2021 09/2024	09/2024	36	0	
191	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320]NTPC,RAJASTHAN	03/2022	1,352.71 -	1,352.71	91.14	08/2023 09/2024	09/2024	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
192	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321]NTPC,RAJASTHAN	03/2022	1,409.52 -	1,409.52	160.80	08/2023 09/2024	09/2024	13	0	
193	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322]NTPC,RAJASTHAN	03/2022	1,426.94 -	1,426.94	164.82	08/2023 09/2024	09/2024	13	0	
194	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	7,103.00	5,911.37	03/2013 12/2021	12/2024	141	138.48	Main construction Work stopped at site since 05-Jan-2023, as per Order by ADM(chamoli).
195	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	18,668.00	11,484.39	03/2023 -	03/2025	24	0	Readiness ATS matching with units commissioning schedule of the project. Readiness of Patratu-KODERMA & Patratu - Chandil Line. Physical possession of encumbrance free land for Ash Mound-I.
196	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,803.00	909.90	09/2019 12/2024	09/2026	84	30.48	
	<u>Power Grid Corporation Of India Limited</u>									
197	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]PGCIL,RAJASTHAN	03/2021	1,340.81 -	1,340.81	1,087.22	12/2022 -	07/2023	7	0	
198	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	243.74	168.69	06/2019 -	08/2023	50	3.49	
199	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	219.66	178.40	07/2019 -	08/2023	49	17.99	
200	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]PGCIL,BIHAR	05/2021	179.29 -	179.29	108.51	04/2023 -	08/2023	4	0	
201	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	159.47	03/2018 -	09/2023	66	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
202	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]PGCIL,HARYANA	01/2019	267.33 -	267.33	109.36	03/2022 -	09/2023	18	0	
203	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]PGCIL,RAJASTHAN	03/2021	353.85 -	353.85	239.56	12/2022 -	09/2023	9	0	
204	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE	09/2015	167.31 -	167.31	129.77	12/2017 -	09/2023	69	0	
205	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE	11/2018	241.38 -	241.38	236.89	11/2021 -	09/2023	22	0	
206	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]PGCIL,ASSAM	03/2019	1,326.00 -	1,326.00	1,367.92	03/2023 -	09/2023	6	0	
207	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - [N18000329]PGCIL,MULTI STATE	03/2022	176.22 -	176.22	39.82	03/2023 -	10/2023	7	0	
208	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN	05/2021	1,184.88 -	1,184.88	712.85	09/2022 -	12/2023	15	0	
209	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	4,578.01	12/2018 -	01/2024	61	31.08	
210	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]PGCIL,MULTI STATE	05/2021	576.42 -	576.42	366.29	03/2023 -	02/2024	11	0	
211	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	2,635.55	1,952.75	02/2020 -	03/2024	49	36.46	
212	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]PGCIL,RAJASTHAN	06/2021	713.82 -	713.82	433.26	12/2022 -	03/2024	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
213	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	1,562.00	805.08	12/2022 -	03/2024	15	0	
214	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	1,006.00	791.18	12/2022 -	03/2024	15	0	
215	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000331]PGCIL,MULTI STATE	02/2022	359.47 -	359.47	54.26	09/2023 -	03/2024	6	0	
216	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332]PGCIL,MULTI STATE	05/2022	1,666.00 -	1,666.00	511.39	11/2023 -	03/2024	4	0	
217	WESTERN REGION EXPANSION SCHEME XXV - [N18000350]PGCIL,CHHATTISGARH	02/2023	385.84 -	385.84	-	11/2023 -	03/2024	4	0	
218	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337]PGCIL,MULTI STATE	07/2022	4,546.26 -	4,546.26	633.23	06/2023 -	06/2024	12	0	
219	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	5,600.77	12/2018 -	12/2024	72	92.02	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
220	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	1,272.29	1,172.12	12/2021 -	08/2023	20	96.24	
221	Bagodara Solar Power Project - [N18000297]SJVN,GUJARAT	05/2021	339.35 -	339.35	253.94	10/2022 -	12/2023	14	0	
222	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR	03/2019	10,439.09 -	10,439.09	8,067.59	01/2024 -	03/2024	2	0	
	<u>Thdc India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
223	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	4,825.60	5,601.35	02/2016 06/2022	06/2024	100	191.23	
224	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	7,902.37	09/2023 -	08/2024	11	0	
225	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	3,163.57	06/2013 -	06/2026	156	54.94	Due to Joshimath issue the works in TBM & PH area which were held up have resumed from 07.05.2023 with controlled blasting with the support of MoP and GoUK/ District Administration, Chamoli. Presently, the works at Project are in progress. However, in TBM & PH area works are going on with controlled blasting due to which the pace of work has been impeded in these areas. Hence, intervention / support of GoUK is requested in above matter.
	Total		1,59,310.66 -	2,13,747.98	1,53,003.99					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Cpwd For Health</u>									
226	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	1,404.00	95.63	09/2023 -	10/2023	1	0	
227	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	260.00	-	06/2021 -	08/2025	50	0	
	<u>HII Infra Tech Services Limited</u>									
228	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	860.00	684.50	05/2021 12/2022	10/2023	29	-1.71	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
229	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR - [N21000031]HITES,TELANGANA	12/2018	1,110.55 -	1,110.55	269.09	07/2024 -	10/2024	3	0	
	Total		3,649.55 -	3,634.55	1,049.22					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
230	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	3,445.48	1,666.35	03/2023 -	03/2024	12	8.75	
231	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	928.90	03/2023 03/2025	03/2024	12	0	
232	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	830.46	03/2022 03/2025	03/2024	24	0	
233	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	410.94	03/2022 -	12/2024	33	0	
234	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,384.72	757.06	03/2022 03/2025	12/2024	33	8.85	
235	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	513.52	03/2023 -	12/2024	21	0	
236	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,805.17	3,491.85	03/2021 03/2025	03/2026	60	111.54	
237	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	792.89	578.90	03/2021 -	03/2026	60	0	
238	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	2,081.27	1,335.69	03/2023 03/2025	03/2026	36	10.94	
	<u>East Central Railways</u>									
239	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	1,160.75	03/2020 -	12/2023	45	0	
240	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	2,445.51	03/2020 -	03/2024	48	0	
241	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	965.84	03/2021 -	03/2024	36	62.06	
242	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	950.34	03/2021 -	12/2024	45	63.37	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
243	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 548.00	783.83	543.54	03/2020 -	03/2025	60	43.03	
	<u>East Coast Railway</u>									
244	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 1,284.39	843.04	723.04	10/2020 -	03/2024	41	0	
245	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATTISGARH	12/2012	1,160.00 -	1,440.00	1,058.66	03/2020 -	03/2024	48	24.14	
246	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	790.93	03/2022 -	03/2024	24	0	
247	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	1,052.09	12/2018 -	02/2025	74	0	
248	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	980.13	06/2021 -	03/2025	45	137.8	
249	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	179.43	11/2018 -	03/2025	76	15.45	
250	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	967.78	03/2022 03/2026	03/2026	48	0	
251	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	2,904.31	03/2009 -	12/2026	213	29.71	
	<u>Eastern Railways</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
252	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91	1,619.48	1,141.34	03/2019 12/2009	03/2024	60	36.22	Land Acquisition – 1. Kamarapur – Jairambati (5.19 KM) falling in Hooghly District : Land acquisition in progress. Hooghly District (3.30 KM) – Land in 0.755 KM length has been handed over by State Govt. In balance 2.545 KM length, though award has been declared long back, but compensation has not been accepted by the land losers. State Govt. vide their letter dated 25.06.2021 had asked for enhanced value of land with excess payment of 1.4 Crore, which has also been handed over to State Govt on 08.11.2021. Further district admin insisted about obtaining the consent of affected landowners. In the last meeting on 8.7.22 & 29.09.22, DM/Hooghly has intimated that demand for special compensation to land losers will be placed to Railways shortly. But formal communication in this regard is awaited. Last meeting with Addl CS /Govt of WB on 21/02/2023 has yielded no such fruitful result Early acquisition of land in balance portion & handing over possession of land by State Govt is requested 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarapur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala –

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
253	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	980.46	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
	<u>Indian Railway Construction Company Limited</u>									
254	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATTISGARH	04/2013	3,055.00 -	3,438.39	2,976.72	09/2018 -	12/2023	63	12.55	1-Agitation by Land losers.
255	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	5,200.00	-	03/2020 -	12/2025	69	0	
	<u>Metropolitan Rapid Transport Projects</u>									
256	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	576.39	06/2013 -	12/2023	126	48.06	
257	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 8,574.98	10,442.41	8,008.94	03/2016 12/2023	12/2023	93	114.22	
	<u>North Central Railway</u>									
258	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 2,001.00	2,001.00	1,118.80	03/2021 -	12/2023	33	0	
259	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	1,024.32	03/2022 -	12/2024	33	32.02	
260	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	60.37	03/2023 -	03/2026	36	0	
	<u>North East Frontier Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
261	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	7,876.92	3,290.96	12/2015 -	12/2023	96	488.06	
262	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	2,647.51	1,999.72	03/2019 -	01/2024	58	47.25	
263	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	9,362.06	6,591.01	03/2014 -	02/2024	119	291.15	
264	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,650.00	1,761.52	03/2019 -	03/2024	60	397.31	
265	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	1,187.49	349.63	03/2020 -	10/2024	55	186.25	
266	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	632.63	172.50	03/2020 -	12/2024	57	161.18	
267	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 12,264.15	14,322.79	13,763.33	03/2011 03/2025	03/2025	168	221.56	
268	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,663.00	2,556.74	03/2015 -	03/2026	132	186.39	
269	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	4,059.65	2,898.81	03/2022 -	03/2026	48	81.86	
	<u>North Eastern Railway</u>									
270	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	2,560.00	2,121.53	03/2022 -	10/2023	19	97.62	
271	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	830.00	853.32	01/2019 -	02/2024	61	181.36	
272	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,500.95	1,119.47	12/2019 -	03/2024	51	27.42	
273	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	1.20	04/2017 -	12/2024	92	127.77	
	<u>North Western Railway</u>									
274	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	970.00	935.00	02/2019 -	09/2023	55	136.54	
275	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	585.21	03/2020 -	02/2024	47	16.97	
	<u>Northern Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
276	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 37,012.26	37,012.26	36,017.83	11/2002 12/2023	01/2024	254	1380.49	1. Law & Order issues (close liaison is maintained with State Govt) 2. Due to ban on mining of minor aggregates in UT of J&K wef Nov' 2019, the works of tunnel and bridges were adversely affected till July 2021 resulting in accumulation of arrears of around 35 Kms.Private E-Auctions for open mining blocks have been finalised by the J&K UT government in July 21.
277	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024	148	348.44	
278	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.14	1,540.14	482.67	03/2023 06/2025	06/2025	27	369.35	
279	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	0	
	<u>National High Speed Rail Corporation Limited</u>									
280	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	1,08,000.00	46,912.58	12/2023 -	08/2027	44	0	
	<u>Rail Vikas Nigam Ltd.</u>									
281	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	433.00	518.32	03/2009 03/2009	07/2023	172	224.56	
282	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,846.81	03/2020 -	08/2023	41	102.11	
283	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,556.55	03/2022 -	10/2023	19	-23.24	
284	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,500.00	1,251.40	03/2022 -	12/2023	21	58.97	
285	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	3,300.00	3,204.74	03/2023 -	03/2024	12	55.15	
286	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,457.79	1,491.77	03/2019 -	03/2024	60	57.26	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
287	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,587.43	03/2023 -	12/2024	21	0	
288	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	24,659.00	14,020.06	12/2024 -	03/2025	3	52.07	
289	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,834.54	3,020.54	03/2016 -	07/2025	112	65.94	
290	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	355.80	03/2014 -	12/2025	141	18.95	
291	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	8,964.35	5,943.37	03/2016 -	03/2026	120	126.83	
292	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	3,674.36	12/2024 -	12/2026	24	42.47	
	<u>South Central Railway</u>									
293	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,909.00	2,909.00	2,355.36	03/2021 -	01/2025	46	41.01	
294	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	3,014.00	1,071.53	03/2010 -	03/2025	180	159.72	
295	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	1,533.64	03/2023 -	03/2025	24	5.16	
296	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	2,728.66	03/2022 -	12/2025	45	7.06	
297	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,500.98	1,129.92	03/2009 -	03/2027	216	139.28	
	<u>South East Central Railway</u>									
298	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATTISGARH	04/2015	1,973.00 2,135.34	2,135.34	1,488.70	03/2021 12/2023	10/2024	43	8.23	
299	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 2,753.05	3,544.25	2,238.21	03/2023 12/2023	12/2024	21	85.71	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
300	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,680.00	1,171.79	12/2021 12/2023	12/2024	36	22.63	
301	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	230.25	12/2021 -	12/2025	48	378.6	
	<u>South Eastern Railway</u>									
302	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	513.92	429.26	12/2021 -	08/2023	20	31.64	
303	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	393.83	67.88	06/2022 -	02/2024	20	16.52	
304	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 3,029.04	3,029.04	1,693.74	03/2021 -	03/2024	36	75.68	
305	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	472.50	254.61	06/2022 -	03/2024	21	10.23	
306	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	1,148.32	05/2023 -	02/2025	21	0	
	<u>South Western Railway</u>									
307	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,960.00	1,887.40	03/2019 -	12/2024	69	21.39	1. In Bagalkot yard, land acquisition to the tune of 4A-39G is in progress under general land acquisition and the same is under progress. 2. Local people is obstructing railway works for doubling project at Navanagar yard and work can be started only after issue is sorted in Hon'ble court.
308	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	38.69	03/2016 -	05/2025	110	0	Out of 101.36 Ha of land in Andhra Pradesh, GoAP has handed over 42.72 Ha of land only. Balance 58.64 Ha of land to be handed over by GoAP to Railways.
309	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 1,378.00	1,649.31	363.80	03/2016 -	03/2026	120	67.22	Out of 2473.41 acres of land, 2266.20 acres of land has been handed over by GOK. For balance 207.21 acres of land acquisition by GOK is in progress as land to be given free by GOK.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
310	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	722.55	12/2018 -	03/2026	87	0	Out of 1621.19 Ha of land, 1150.78 Ha of land has been handed over by GoK. For balance 470.38 Ha, land acquisition by GoK is in progress as land to be given free by GoK.
311	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	826.18	500.25	03/2017 -	03/2026	108	28.13	Out of 143.29 Ha of land, 102.11 Ha of land only handed over by GoK. Balance 41.18 Ha of land yet to be acquired & handed over to Railways by GoK.
312	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	12/2028	153	0	GoK have not initiated land acquisition process, although requisition to acquire land for 1205.87 acres has been submitted by the Railways in the year 2013 & GoK have not released any funds to concerned DCs for this purpose. Hence work could not be commenced till date.
	<u>Southern Railway</u>									
313	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,118.34	1,877.71	02/2019 -	03/2025	73	330.3	
314	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,053.39	328.43	03/2019 12/2027	12/2027	105	1601.23	
	<u>West Central Railway</u>									
315	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 2,938.00	2,938.00	1,279.35	03/2022 -	06/2024	27	18.55	
316	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	990.59	03/2022 -	09/2024	30	114.32	
317	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	2,020.86	03/2020 -	10/2024	55	38.63	
318	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	202	3230.57	
319	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 2,909.99	3,032.46	2,080.00	03/2021 12/2025	12/2025	57	614.19	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Western Railway</u>									
320	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	639.96	06/2020 -	10/2023	40	-13.76	
321	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.03	1,095.12	201.24	03/2012 -	03/2024	144	244.12	
322	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 692.26	692.26	116.70	03/2020 12/2024	12/2024	57	0	
323	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31 537.31	537.31	191.29	03/2024 12/2024	12/2024	9	0	
324	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	1,873.10	1,136.95	03/2022 03/2026	12/2025	45	14.21	
325	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,677.80	6,021.00	2,919.74	03/2022 03/2026	03/2026	48	71.85	
326	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 495.18	495.18	.83	03/2022 03/2026	03/2026	48	0	
327	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,793.63	1,793.63	1,222.16	03/2022 12/2026	12/2026	57	33.13	
	Total		2,66,666.73 -	4,06,606.01	2,41,531.41					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
328	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 225.06	225.06	227.48	05/2016 07/2023	07/2023	86	25.84	
329	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	192.67	171.11	07/2019 06/2022	07/2023	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
330	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STATE OF KARNATAKA - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	314.90	234.09	03/2017 07/2023	07/2023	76	0	
331	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	159.12	128.18	01/2016 07/2023	07/2023	90	0	
332	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 270.00	270.00	215.52	06/2021 07/2023	07/2023	25	-23.08	Delayed due to Land Acquisition, Utility Shifting, Forest Clearance & COVID-19
333	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	140.29	03/2017 12/2021	08/2023	77	0	
334	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	221.19	07/2018 08/2021	08/2023	61	0	
335	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	283.15	250.50	05/2020 12/2022	08/2023	39	0	
336	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	313.95	270.26	06/2019 -	08/2023	50	0	
337	AMDIA TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	396.91	289.79	06/2019 -	08/2023	50	0	
338	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	363.82	154.65	09/2019 -	08/2023	47	0	
339	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	211.34	136.33	07/2019 -	08/2023	49	0	
340	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	210.81	210.81	07/2019 -	08/2023	49	0	
341	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	232.77	151.60	07/2019 -	08/2023	49	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
342	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	217.14	157.89	02/2020 -	08/2023	42	0	
343	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	238.19	194.54	12/2019 -	08/2023	44	0	
344	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	336.47	203.39	12/2019 -	08/2023	44	0	
345	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	228.31	100.97	12/2019 -	08/2023	44	0	
346	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	256.15	126.62	12/2019 -	08/2023	44	0	
347	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	216.90	164.00	12/2019 -	08/2023	44	0	
348	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	205.72	85.71	06/2019 -	08/2023	50	0	
349	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	313.58	230.41	04/2020 -	08/2023	40	0	
350	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 470.72	470.72	431.91	03/2018 03/2022	08/2023	65	19.98	
351	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATTISGARH	03/2017	423.79 -	423.79	324.86	01/2018 -	08/2023	67	0	
352	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATTISGARH	11/2017	188.80 -	188.80	131.38	05/2019 -	08/2023	51	0	
353	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 296.53	296.53	274.50	08/2017 03/2022	08/2023	72	.76	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
354	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 306.14	306.14	293.37	02/2021 -	08/2023	30	1.16	
355	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT - [N24001427]MoRTH,GUJARAT	06/2020	166.21 -	166.21	89.45	04/2023 08/2023	08/2023	4	0	
356	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	165.67	126.47	11/2015 06/2023	09/2023	94	0	
357	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	295.67	203.61	02/2017 09/2023	09/2023	79	0	
358	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	206.88	123.50	04/2018 09/2023	09/2023	65	0	
359	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	214.23	179.48	08/2018 09/2023	09/2023	61	0	
360	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	199.16	101.34	08/2018 09/2023	09/2023	61	0	
361	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 394.44	394.44	276.30	11/2020 09/2023	09/2023	34	-1.58	Delayed due to Land Acquisition, Forest clearance & COVID-19
362	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	228.89	154.82	06/2019 -	09/2023	51	0	
363	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	227.19	141.92	12/2019 -	09/2023	45	0	
364	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	194.23	136.55	02/2020 -	09/2023	43	0	
365	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	301.38	240.32	08/2020 -	09/2023	37	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
366	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	294.87	183.17	12/2019 -	09/2023	45	0	
367	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	177.84	110.20	12/2019 -	09/2023	45	0	
368	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	307.63	232.57	07/2019 -	09/2023	50	0	
369	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	218.38	182.63	07/2019 -	09/2023	50	0	
370	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	242.09	06/2019 -	09/2023	51	0	
371	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	232.56	09/2018 -	09/2023	60	0	
372	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	362.96	273.57	06/2019 -	09/2023	51	0	
373	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	306.59	251.95	06/2021 -	09/2023	27	0	
374	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 320.00	320.00	296.73	11/2019 -	09/2023	46	7.54	
375	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	144.86	11/2022 -	09/2023	10	-12	
376	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	216.72	151.46	12/2022 -	09/2023	9	0	
377	CONSTRUCTION OF FOUR LANE PINJORE BYPASS FROM KM 0.00 TO 7.70 ON EPC MODE. - [N24001513]MoRTH,HARYANA	12/2016	170.27 -	170.27	98.77	12/2017 -	09/2023	69	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
378	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	295.47	221.36	02/2017 12/2022	10/2023	80	0	
379	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	287.70	196.92	02/2017 10/2023	10/2023	80	0	
380	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	223.50	139.44	08/2018 10/2023	10/2023	62	0	
381	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 978.93	978.93	818.30	09/2020 10/2023	10/2023	37	1.71	Delay in Approval of GAD & Construction drawing, Delay in Approvals of Mix Design, Proof Consultant, Construction Material and steel etc from Authority
382	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	376.19	113.66	05/2019 -	10/2023	53	0	
383	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	344.85	281.41	12/2019 -	10/2023	46	0	
384	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	337.46	335.30	06/2019 -	10/2023	52	0	
385	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	171.60	138.16	05/2018 10/2023	10/2023	65	0	
386	MOPA AIRPORT - [N24001458]MoRTH,GOA	12/2021	1,183.16 -	1,183.16	485.75	04/2022 -	10/2023	18	0	
387	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	2,138.16	1,560.46	10/2016 -	11/2023	85	51.77	
388	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	192.48	94.84	11/2020 -	11/2023	36	12.85	Work on ROB in Km 12, Truck Lay bye, Toll Plaza & RE wall is held up due to non possession of Land.
389	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	276.95	160.17	12/2019 -	11/2023	47	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
390	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 - [N24001464]MoRTH,UTTAR PRADESH	03/2021	264.86 -	264.86	52.66	08/2023 -	11/2023	3	0	
391	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	455.78	08/2017 12/2023	12/2023	76	0	
392	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	248.00	111.85	05/2020 12/2023	12/2023	43	0	
393	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	151.50	11/2018 12/2023	12/2023	61	7.39	
394	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	103.61	03/2018 12/2022	12/2023	69	0	
395	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	339.05	09/2020 12/2023	12/2023	39	0	
396	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	101.84	03/2018 12/2023	12/2023	69	0	
397	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	739.08	10/2019 -	12/2023	50	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
398	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 913.49	913.49	778.14	11/2020 12/2023	12/2023	37	5.24	Delay in obtaining utility shifting estimate from the concern department,obtaining forest clearance and tree cutting operation,obtaining approval for GAD and finalization of COS
399	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	263.11	06/2019 -	12/2023	54	0	
400	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	247.86	06/2019 -	12/2023	54	0	
401	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	237.40	73.12	05/2020 -	12/2023	43	0	
402	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	304.58	150.26	12/2019 -	12/2023	48	0	
403	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	274.50	143.39	12/2019 -	12/2023	48	0	
404	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	336.21	236.11	12/2019 -	12/2023	48	0	
405	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	299.92	188.96	08/2020 -	12/2023	40	0	
406	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	344.25	188.48	08/2020 -	12/2023	40	0	
407	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	488.60	279.42	07/2019 -	12/2023	53	0	
408	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	381.08	45.66	05/2020 -	12/2023	43	0	
409	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	77.83	04/2019 -	12/2023	56	0	
410	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	406.54	274.30	09/2019 -	12/2023	51	0	
411	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	406.51	340.26	06/2019 -	12/2023	54	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
412	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	1,230.02	791.80	11/2019 -	12/2023	49	0	
413	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	241.60	178.73	02/2017 07/2023	12/2023	82	37.66	
414	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	242.61	135.31	06/2019 12/2023	12/2023	54	51.66	
415	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATTISGARH	11/2015	335.32 -	335.32	321.06	06/2017 -	12/2023	78	0	
416	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATTISGARH	01/2016	476.20 543.73	543.73	476.08	09/2016 -	12/2023	87	14.18	
417	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATTISGARH	01/2016	624.98 731.50	731.50	539.88	10/2016 -	12/2023	86	17.04	
418	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATTISGARH	03/2016	452.94 -	435.61	205.99	07/2016 -	12/2023	89	-3.83	
419	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. - [N24001227]MoRTH,CHHATTISGARH	03/2018	349.03 -	349.03	277.34	01/2019 -	12/2023	59	0	
420	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FROM - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	179.27	10/2022 -	12/2023	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
421	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH - [N24001448]MoRTH,MAHARASHTRA	11/2021	223.35 -	223.35	114.32	02/2022 -	12/2023	22	0	
422	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	170.12	03/2018 -	01/2024	70	0	
423	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 - [N24001441]MoRTH,MEGHALAYA	08/2020	302.88 -	302.88	91.62	02/2022 01/2024	01/2024	23	0	
424	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE - I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	12/2019	282.41 -	319.96	248.23	04/2022 -	02/2024	22	13.3	
425	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	163.40	09/2021 02/2024	02/2024	29	11.18	
426	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO) - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	254.30	171.67	10/2020 03/2024	03/2024	41	0	
427	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	189.46	111.73	12/2019 -	03/2024	51	0	
428	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	404.33	140.65	05/2020 -	03/2024	46	0	
429	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	341.80	203.09	06/2019 -	03/2024	57	0	
430	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	381.77	199.48	06/2019 -	03/2024	57	0	
431	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATTISGARH	01/2016	497.14 -	572.66	309.49	08/2016 -	03/2024	91	15.19	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
432	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	75.90	03/2021 03/2024	03/2024	36	0	
433	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W - [N24001424]MoRTH,UTTAR PRADESH	03/2021	185.09 -	185.09	92.62	09/2023 -	03/2024	6	0	
434	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 385.97	385.97	187.74	11/2014 05/2024	05/2024	114	97.48	
435	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	70.95	09/2023 03/2024	06/2024	9	33.51	
436	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	626.76	255.13	07/2020 06/2024	06/2024	47	0	
437	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	379.23	143.30	10/2023 -	06/2024	8	0	
438	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	339.65	170.39	10/2023 -	06/2024	8	0	
439	REPANPALLI TO SIRONCHA - [N24001468]MoRTH,MAHARASHTRA	03/2022	282.07 -	282.07	34.65	06/2022 -	06/2024	24	0	
440	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	319.09	77.04	03/2024 -	07/2024	4	0	
441	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR - [N24001454]MoRTH,TAMIL NADU	02/2022	184.15 -	184.15	82.06	08/2022 -	08/2024	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
442	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH	07/2018	1,948.25 -	1,948.25	640.55	02/2024 -	09/2024	7	0	
443	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 - [N24001455]MoRTH,TAMIL NADU	02/2022	191.33 -	191.33	28.48	08/2022 -	10/2024	26	0	
444	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	187.61	43.16	05/2019 -	11/2024	66	19.25	
445	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	423.15	308.74	12/2019 11/2024	11/2024	59	0	
446	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT - [N24001423]MoRTH,UTTAR PRADESH	04/2021	309.48 -	309.48	63.83	09/2023 -	12/2024	15	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
447	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 229.70	167.28	138.66	04/2022 07/2023	07/2023	15	0	
448	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 610.09	553.51	290.35	09/2021 09/2021	07/2023	22	0	
449	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA	06/2020	347.36 -	347.36	224.48	01/2022 04/2023	07/2023	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
450	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND	09/2020	257.15 -	257.15	124.52	04/2022 02/2023	07/2023	15	0	
451	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA	03/2020	154.51 -	154.51	73.74	07/2022 03/2023	07/2023	12	0	
452	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]NHIDCL,ARUNACHAL PRADESH	08/2020	228.71 -	228.71	90.14	04/2022 07/2023	07/2023	15	0	
453	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]NHIDCL,ARUNACHAL PRADESH	08/2020	294.04 -	294.04	129.38	04/2022 07/2023	07/2023	15	0	
454	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]NHIDCL,ARUNACHAL PRADESH	08/2020	199.03 -	199.03	101.66	04/2022 07/2023	07/2023	15	0	
455	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 330.30	330.30	146.28	12/2021 12/2019	08/2023	20	31.07	
456	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	155.93	09/2022 01/2023	08/2023	11	0	
457	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	218.36	10/2020 08/2023	08/2023	34	0	
458	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	253.44	167.30	07/2021 03/2023	08/2023	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
459	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL, ARUNACHAL PRADESH	12/2016	200.44 200.44	200.44	146.43	01/2020 01/2022	08/2023	43	0	
460	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL, ASSAM	03/2020	220.20 -	220.20	168.60	12/2022 -	08/2023	8	0	
461	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL, TRIPURA	03/2020	247.76 251.89	251.89	137.58	01/2022 10/2022	08/2023	19	1.67	
462	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL, NAGALAND	09/2020	315.63 -	315.63	42.64	04/2022 -	08/2023	16	0	
463	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL, TRIPURA	03/2020	178.43 -	208.74	77.89	07/2022 08/2023	08/2023	13	16.99	
464	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL, MANIPUR	08/2020	379.39 -	379.39	186.51	04/2022 -	08/2023	16	0	
465	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL, NAGALAND	03/2020	320.97 -	320.97	168.47	06/2022 03/2023	08/2023	14	0	
466	DOGINALA - GAU - [N24001320]NHIDCL, ARUNACHAL PRADESH	12/2020	242.30 -	242.30	21.47	09/2022 -	08/2023	11	0	
467	KHELLANI-KHANABAL PKG-6 - [N24001324]NHIDCL, JAMMU AND KASHMIR	02/2021	285.28 -	285.28	218.89	09/2022 -	08/2023	11	0	
468	KARGIL-ZANSKR PACKAGE-8 - [N24001348]NHIDCL, LADAKH	03/2021	398.37 -	398.37	93.05	01/2023 08/2023	08/2023	7	0	
469	MARIAM - PEREN PKG-2B - [N24001351]NHIDCL, MANIPUR	02/2021	232.26 -	232.26	147.43	12/2022 -	08/2023	8	0	
470	IMPHAL - MOREH PACKAGE- 3 - [N24001352]NHIDCL, MANIPUR	03/2021	259.31 -	259.31	136.05	12/2022 -	08/2023	8	0	
471	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 489.01	387.00	377.90	09/2019 09/2019	09/2023	48	3.73	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
472	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 519.72	396.52	330.51	08/2019 08/2019	09/2023	49	0	
473	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	387.00	384.58	09/2020 08/2022	09/2023	36	0	
474	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 568.92	568.92	493.58	12/2019 03/2023	09/2023	45	0	
475	AJANTHA TO BULDHANA - [N24001008]NHIDCL,ANDAMAN AND NICOBAR ISLANDS	02/2017	401.00 401.00	401.00	260.08	07/2019 -	09/2023	50	0	
476	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]NHIDCL,SIKKIM	08/2020	230.45 244.91	244.91	190.66	04/2023 09/2023	09/2023	5	6.27	
477	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR	07/2021	467.00 -	467.00	139.15	03/2023 -	09/2023	6	0	
478	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	145.48	10/2022 10/2022	10/2023	12	0	
479	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	196.84	03/2022 -	10/2023	19	0	
480	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]NHIDCL,SIKKIM	07/2020	345.38 395.59	395.59	300.58	04/2023 -	10/2023	6	14.54	
481	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM	09/2020	275.02 -	275.02	166.23	10/2022 07/2023	10/2023	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
482	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM	03/2020	281.78 253.41	253.41	228.20	07/2022 07/2023	10/2023	15	-10.07	
483	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]NHIDCL,TRIPURA	11/2020	159.13 171.50	171.50	67.62	06/2022 06/2023	10/2023	16	7.77	
484	KHELLANI-KHANABAL PKG-1 - [N24001323]NHIDCL,JAMMU AND KASHMIR	03/2021	486.45 -	486.45	92.05	09/2022 06/2023	10/2023	13	0	
485	KARGIL-ZANSKR PACKAGE-3 - [N24001345]NHIDCL,LADAKH	08/2020	381.01 -	381.01	83.24	01/2023 10/2023	10/2023	9	0	
486	MARIAM - PEREN PKG-1A - [N24001349]NHIDCL,MANIPUR	02/2021	226.32 -	226.32	47.15	12/2022 -	10/2023	10	0	
487	MARIAM - PEREN (PKG 1B) - [N24001350]NHIDCL,MANIPUR	02/2021	188.36 -	188.36	81.38	12/2022 -	10/2023	10	0	
488	DABOKA KATHKATI PACKAGE-5 - [N24001366]NHIDCL,ASSAM	03/2021	288.85 -	288.85	110.33	01/2023 -	10/2023	9	0	
489	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM	03/2021	636.42 -	418.49	544.79	12/2022 -	10/2023	10	-34.24	
490	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR	02/2021	431.28 -	431.28	173.60	03/2023 05/2023	10/2023	7	0	
491	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	224.61	08/2023 -	11/2023	3	0	
492	DEMBUEN - BRUNI - [N24001321]NHIDCL,ARUNACHAL PRADESH	12/2020	606.63 606.63	606.63	270.03	03/2023 -	11/2023	8	0	
493	KHELLANI-KHANABAL PKG-3 - [N24001341]NHIDCL,JAMMU AND KASHMIR	03/2021	398.51 -	398.51	53.04	12/2022 -	11/2023	11	0	
494	KARGIL-ZANSKR PACKAGE-1 - [N24001343]NHIDCL,LADAKH	03/2021	384.23 -	384.23	48.09	01/2023 11/2023	11/2023	10	0	
495	KARGIL-ZANSKR PACKAGE-2 - [N24001344]NHIDCL,LADAKH	03/2021	404.89 -	404.89	40.59	01/2023 11/2023	11/2023	10	0	
496	IMPHAL - KHONGSANG PKG-2 - [N24001353]NHIDCL,MANIPUR	03/2021	195.14 -	195.14	34.94	12/2022 -	11/2023	11	0	
497	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]NHIDCL,MIZORAM	03/2021	374.39 374.39	374.39	267.81	12/2022 11/2023	11/2023	11	0	
498	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-3 - [N24001360]NHIDCL,MEGHALAYA	03/2021	260.21 -	260.21	149.15	12/2022 -	11/2023	11	0	
499	MANU-SIMLUNG (PKG 4) - [N24001363]NHIDCL,TRIPURA	03/2021	354.79 -	354.79	33.27	12/2022 06/2023	11/2023	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
500	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]NHIDCL, ARUNACHAL PRADESH	08/2020	184.88 -	184.88	71.91	04/2022 11/2023	11/2023	19	0	
501	MARAM - PEREN PKG-3 - [N24001439]NHIDCL, MANIPUR	08/2021	467.41 -	467.41	126.80	05/2023 -	11/2023	6	0	
502	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31 -	274.31	240.98	11/2020 12/2022	12/2023	37	0	
503	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL, NAGALAND	03/2018	500.09 583.31	500.09	299.49	11/2022 06/2023	12/2023	13	0	
504	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	97.45	12/2021 08/2022	12/2023	24	0	
505	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL, SIKKIM	03/2017	375.80 -	375.80	270.63	04/2022 05/2022	12/2023	20	0	
506	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM	10/2017	818.00 887.68	818.00	659.65	06/2020 06/2020	12/2023	42	0	
507	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL, SIKKIM	08/2020	295.97 -	295.97	190.56	04/2023 08/2023	12/2023	8	0	
508	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL, SIKKIM	03/2020	242.97 -	242.97	204.16	06/2022 -	12/2023	18	0	
509	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL, MIZORAM	03/2020	206.88 219.33	278.98	227.33	07/2022 08/2023	12/2023	17	34.85	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
510	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM	03/2020	292.24 331.17	331.17	235.26	07/2022 08/2023	12/2023	17	13.32	
511	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND	03/2020	355.79 -	355.79	109.24	06/2022 02/2023	12/2023	18	0	
512	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND	03/2020	361.53 -	361.53	112.55	06/2022 06/2023	12/2023	18	0	
513	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA	06/2020	201.99 -	201.99	117.12	01/2022 06/2023	12/2023	23	0	
514	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,ANDAMAN AND NICOBAR ISLANDS	03/2017	409.85 -	409.85	207.65	12/2019 03/2023	01/2024	49	0	
515	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,ANDAMAN AND NICOBAR ISLANDS	03/2018	234.27 -	234.27	124.29	09/2020 11/2022	01/2024	40	0	
516	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 775.47	775.47	532.37	04/2023 01/2024	01/2024	9	49.39	
517	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 1,139.85	1,139.85	528.71	06/2023 12/2023	01/2024	7	77.28	
518	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 667.06	667.06	465.49	04/2023 11/2023	01/2024	9	40.97	
519	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 820.42	820.42	619.87	04/2023 10/2023	01/2024	9	52.55	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
520	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM	03/2019	402.94 -	402.94	188.53	04/2022 -	01/2024	21	0	
521	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]NHIDCL,SIKKIM	08/2020	311.00 273.78	273.78	200.01	04/2023 -	01/2024	9	-11.97	
522	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA	06/2020	277.50 302.02	302.02	201.23	01/2022 06/2023	01/2024	24	8.84	
523	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR	07/2020	210.79 -	210.79	46.44	04/2022 05/2023	01/2024	21	0	
524	RANIKOR-MAHESKHOLA-BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL,MEGHALAYA	10/2020	157.86 -	157.86	102.41	04/2022 -	01/2024	21	0	
525	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]NHIDCL,MIZORAM	03/2021	233.25 233.25	233.25	153.10	12/2022 07/2023	01/2024	13	0	
526	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]NHIDCL,MIZORAM	03/2021	674.71 674.71	674.71	521.28	06/2023 01/2024	01/2024	7	0	
527	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR	07/2021	497.09 -	497.09	74.15	02/2023 -	01/2024	11	0	
528	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 1,134.72	640.07	965.74	07/2023 02/2024	02/2024	7	0	
529	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 902.20	902.20	623.42	06/2023 02/2024	02/2024	8	73.99	
530	LADDA - BASAI - [N24001316]NHIDCL,ARUNACHAL PRADESH	02/2021	445.96 -	445.96	75.67	04/2023 -	02/2024	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
531	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	70.01	09/2018 06/2023	03/2024	66	0	
532	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 1,718.59	1,718.59	656.26	03/2022 12/2023	03/2024	24	0	
533	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH	09/2020	353.90 -	353.90	41.82	05/2022 10/2022	03/2024	22	0	
534	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND	08/2020	202.36 -	202.36	62.66	04/2022 -	03/2024	23	0	
535	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR	07/2020	228.39 -	228.39	36.59	04/2022 06/2023	03/2024	23	0	
536	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND	04/2020	330.80 -	330.80	83.11	12/2021 12/2022	03/2024	27	0	
537	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL,ASSAM	03/2020	261.13 -	261.13	51.90	06/2022 -	03/2024	21	0	
538	MERANGKONG-TAMLU-MON (MTM) PKG-5 - [N24001438]NHIDCL,NAGALAND	07/2021	161.73 -	161.73	32.41	12/2023 -	03/2024	3	0	
539	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	403.36	328.94	11/2020 12/2022	04/2024	41	0	
540	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	417.24	337.20	11/2020 12/2022	04/2024	41	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
541	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM	09/2020	183.31 439.56	439.56	322.34	05/2022 -	04/2024	23	139.79	
542	KEIFANG - TUVAI PKG-1 - [N24001440]NHIDCL,MIZORAM	09/2021	492.94 492.94	492.94	230.26	05/2023 02/2024	04/2024	11	0	
543	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	542.67	07/2022 07/2022	05/2024	22	0	
544	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 777.50	777.50	437.46	09/2023 05/2024	05/2024	8	81.61	
545	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH	08/2020	301.06 -	301.06	96.33	04/2022 05/2024	05/2024	25	0	
546	CONSTRUCTION AND UPGRADEATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL,SIKKIM	10/2020	493.42 478.79	478.79	230.22	11/2023 -	05/2024	6	-2.97	
547	SENAPATI- IMPHAL PKG-5B - [N24001400]NHIDCL,MANIPUR	03/2021	211.70 -	211.70	1.64	01/2023 -	05/2024	16	0	
548	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,ANDAMAN AND NICOBAR ISLANDS	02/2018	391.00 -	391.00	170.37	09/2020 01/2023	06/2024	45	0	
549	TADADEGE - HENKAR - [N24001315]NHIDCL,ARUNACHAL PRADESH	02/2021	550.45 -	550.45	61.12	03/2023 -	06/2024	15	0	
550	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	248.08	01/2016 -	07/2024	102	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
551	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 723.80	723.80	452.54	04/2024 07/2024	07/2024	3	79.03	
552	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM	08/2020	208.84 -	208.84	90.92	04/2022 -	07/2024	27	0	
553	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND	09/2020	277.44 -	277.44	134.18	10/2022 -	07/2024	21	0	
554	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL,SIKKIM	09/2020	262.84 414.20	414.20	185.56	05/2023 -	08/2024	15	57.59	
555	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]NHIDCL,SIKKIM	10/2020	816.79 786.60	786.60	204.88	12/2023 09/2024	09/2024	9	-3.7	
556	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR	07/2021	859.67 -	859.67	66.85	08/2023 -	09/2024	13	0	
557	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR	07/2021	512.43 -	512.43	38.94	02/2023 -	10/2024	20	0	
558	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM	08/2020	292.80 -	292.80	94.56	05/2022 10/2023	11/2024	30	0	
559	TLABUNG - LUNGLEI PKG-A - [N24001358]NHIDCL,MIZORAM	03/2021	698.44 698.45	698.45	227.20	12/2022 10/2023	12/2024	24	0	
560	TLABUNG - LUNGLEI PKG-B - [N24001359]NHIDCL,MIZORAM	03/2021	740.58 740.58	740.58	104.66	01/2023 11/2023	12/2024	23	0	
561	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,ANDAMAN AND NICOBAR ISLANDS	03/2015	262.97 -	262.97	92.73	01/2022 -	03/2024	26	0	
	<u>National Highways Authority Of India</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
562	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 2,639.00	2,639.00	1,771.52	08/2016 06/2023	07/2023	83	59.46	a. Slow progress due to non deployment of adequate men, machineries, resources and poor management by Concessionaire. b. Non posting of Dedicated SLAO at Honnavar for a period 2 years. c. Missing survey numbers in 1st and 2nd 3D. d. Reduction in ROW from 45 m to 30 m at 6 locations based on GoK directions. e. Delay in Disposal of excess boulders by State Govt. f. Due to Covid 19 Pandemic ,work has been hampered g. Auction of 2.1 Lacs MT of boulders. h. Balance length Stretches could not be connected /taken up due to various VIPs, Public representatives reference and Local public demand for structures like flyover, elevated highway, VUP, VOP, service road, FOB etc. and other LA issues.
563	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,288.97	2,136.97	2,362.99	12/2018 07/2023	07/2023	55	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
564	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 4,041.80	1,396.74	3,738.01	10/2019 05/2023	07/2023	45	0	
565	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 3,150.00	3,063.99	2,938.25	04/2019 12/2022	07/2023	51	93.01	
566	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 571.45	571.45	648.26	06/2018 07/2023	07/2023	61	-29.01	Nil
567	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	304.07	299.26	03/2019 07/2023	07/2023	52	-24.03	Nil
568	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	354.35	10/2022 07/2023	07/2023	9	0	
569	FOUR LANING OF MADURAI-CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	583.02	11/2020 07/2023	07/2023	32	0	
570	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	716.00	334.38	07/2021 11/2023	07/2023	24	0	
571	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29 - [N24001517]NHAI,GUJARAT	09/2020	1,523.77 -	1,523.77	963.02	04/2023 -	07/2023	3	0	
572	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA - [N24001567]NHAI,RAJASTHAN	11/2019	1,272.97 -	1,272.97	330.25	10/2022 09/2023	07/2023	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
573	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N - [N24001568]NHAI,RAJASTHAN	11/2019	1,119.35 -	1,119.35	1,108.34	05/2023 10/2023	07/2023	2	0	
574	4L OF SHAMLI TO MUZAFFARNAGAR SECTION OF NH-709AD, PKG-II - [N24001742]NHAI,UTTAR PRADESH	06/2020	1,621.07 -	1,621.07	977.49	10/2022 -	07/2023	9	0	
575	FOUR LANNING OF JAGDISHPUR-FAIZABAD SECTION FROM KM 47.930 TO KM 107.680 OF NH-330A - [N24001816]NHAI,UTTAR PRADESH	03/2021	1,980.00 -	1,980.00	1,043.39	03/2023 -	07/2023	4	0	
576	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 1,046.56	1,046.56	827.99	06/2018 08/2023	08/2023	62	10.63	
577	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 1,414.01	1,414.01	1,059.61	06/2018 08/2023	08/2023	62	30.56	binnaguri 5.1 km land acquisition issue
578	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	282.54	04/2018 08/2023	08/2023	64	0	No issue.
579	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	802.04	08/2019 -	08/2023	48	0	
580	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 668.74	668.74	677.74	03/2020 08/2023	08/2023	41	-11.37	
581	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 375.78	290.69	319.53	04/2021 06/2023	08/2023	28	25.03	
582	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,471.75	1,471.75	1,439.30	07/2021 07/2023	08/2023	25	0	
583	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 416.07	416.07	333.18	06/2019 05/2023	08/2023	50	26.59	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
584	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	649.00	634.53	04/2021 08/2023	08/2023	28	-12.52	
585	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	828.29	448.81	02/2023 06/2023	08/2023	6	0	
586	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	832.00	12/2021 11/2022	08/2023	20	0	
587	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	1,103.00	11/2022 -	08/2023	9	27.86	
588	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	1,188.00	02/2022 11/2022	08/2023	18	0	
589	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODMI - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	884.00	2,298.00	12/2022 -	08/2023	8	305.58	
590	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	1,092.00	12/2021 09/2022	08/2023	20	0	
591	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	920.50	03/2022 11/2022	08/2023	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
592	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	1,169.00	05/2020 03/2023	08/2023	39	0	
593	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	996.27	1,079.00	03/2022 11/2022	08/2023	17	0	
594	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,569.68	1,569.68	1,054.39	02/2021 08/2023	08/2023	30	27.94	
595	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.99	731.99	626.45	01/2022 05/2023	08/2023	19	.01	
596	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	613.75	532.55	01/2022 05/2023	08/2023	19	3.19	
597	INTEGRATED STRUCTURE WITH DEVELOPMENT OF OTHER ALLIED STRUCTURES ON BOTH SIDES OF CHANDNI CHOWK JUNC - [N24001485]NHAI,MAHARASHTRA	02/2019	397.60 -	397.60	335.38	02/2022 -	08/2023	18	0	
598	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON - [N24001569]NHAI,RAJASTHAN	11/2019	1,425.02 -	1,425.02	1,026.56	03/2023 11/2023	08/2023	5	0	
599	4 LANING OF PATHRAPALI TO KATGHORA FROM KM.53.300 TO KM.92.600 - [N24001592]NHAI,CHHATTISGARH	11/2019	865.10 -	865.10	655.41	12/2022 03/2023	08/2023	8	0	-

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
600	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI - [N24001624]NHAI,JAMMU AND KASHMIR	07/2019	157.05 -	157.05	109.95	10/2020 04/2023	08/2023	34	0	Nil
601	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0 - [N24001645]NHAI,PUNJAB	12/2020	366.85 366.85	366.85	252.03	06/2023 08/2023	08/2023	2	0	
602	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 - [N24001647]NHAI,ODISHA	08/2020	200.00 154.73	154.73	137.04	03/2022 -	08/2023	17	-22.64	
603	8L OF GUDUVANCHERY (KM 38.00) - MARAIMALAI NAGAR (KM 42.00) - SINGAPERUMAL KOIL (47.00) - CHETTIPU - [N24001695]NHAI,TAMIL NADU	12/2020	230.69 -	230.69	174.08	02/2022 -	08/2023	18	0	
604	2ND FLYOVER (LCW) PARALLEL TO EXISTING FLYOVER IN KISHANGANJ TOWN. - [N24001713]NHAI,BIHAR	03/2018	150.21 150.00	150.00	148.40	06/2020 08/2023	08/2023	38	-14	
605	BALANCE WORK OF 2L PS OF TINDIVANAM KRISHNAGIRI FROM KM 37.600 TO 219.782 - [N24001724]NHAI,TAMIL NADU	05/2019	602.57 621.38	548.89	313.44	07/2021 05/2023	08/2023	25	-8.91	
606	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743]NHAI,UTTAR PRADESH	01/2018	1,916.38 -	2,078.00	1,158.54	02/2023 08/2023	08/2023	6	8.43	
607	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 - [N24001752]NHAI,WEST BENGAL	12/2018	2,375.87 2,566.80	2,566.80	2,299.14	02/2023 08/2023	08/2023	6	8.04	
608	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755]NHAI,UTTAR PRADESH	10/2019	1,936.68 -	2,458.03	1,380.90	03/2023 -	08/2023	5	26.92	
609	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A - [N24001782]NHAI,HARYANA	11/2018	2,312.26 -	2,312.26	1,361.51	09/2021 -	08/2023	23	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
610	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN - [N24001783]NHAI,HARYANA	11/2018	2,252.75 -	2,252.75	1,223.07	09/2021 -	08/2023	23	0	
611	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA - [N24001784]NHAI,HARYANA	11/2018	1,935.61 -	1,935.61	856.41	09/2021 -	08/2023	23	0	
612	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) - [N24001791]NHAI,GUJARAT	02/2020	606.51 -	657.00	446.88	06/2023 -	08/2023	2	8.32	
613	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) - [N24001794]NHAI,GUJARAT	02/2020	778.15 -	785.67	429.03	03/2023 -	08/2023	5	.97	
614	BALANCE WORKS OF 4L AMRAVATI CHIKHLI (PKG IV) [NANDURA TO CHIKHLI FROM KM. 315.00 TO KM. 360.00] - [N24001802]NHAI,MAHARASHTRA	11/2019	583.61 -	583.61	237.57	05/2023 -	08/2023	3	0	
615	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	880.00	04/2020 09/2023	09/2023	41	3.95	
616	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 767.45	767.45	737.93	04/2021 09/2023	09/2023	29	-4.8	
617	4L OF ADDAHOLE TO BANTWAL CROSS SECTION - [N24001426]NHAI,KARNATAKA	03/2021	317.90 317.90	317.90	214.13	10/2021 09/2023	09/2023	23	0	NA
618	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB - [N24001445]NHAI,GUJARAT	05/2020	691.52 -	691.52	342.22	07/2023 -	09/2023	2	0	
619	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS - [N24001604]NHAI,TAMIL NADU	02/2019	166.90 -	166.90	118.82	03/2021 -	09/2023	30	0	
620	AURAD - BIDAR KM 0.00 TO KM 45.878 - [N24001683]NHAI,KARNATAKA	09/2021	912.37 -	912.37	222.63	04/2023 -	09/2023	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
621	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI-MOTIHARI- RAXAUL SECTION OF NH-28A FRO - [N24001715]NHAI,BIHAR	12/2018	333.60 459.89	461.41	399.69	10/2020 -	09/2023	35	38.31	
622	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG II) [KURANKHED TO SHELAD FROM KM. 220.00 TO KM. 270.00] - [N24001801]NHAI,MAHARASHTRA	11/2019	633.70 -	633.70	244.30	02/2023 -	09/2023	7	0	
623	4L OF AKOLA - MEDSHI FROM KM. 0.00 TO KM. 47.70 OF NH-161 INCLUDING BYPASSES AT PATUR AND MEDSHI - [N24001803]NHAI,MAHARASHTRA	12/2019	1,393.95 1,393.95	576.00	527.13	11/2022 09/2023	09/2023	10	-58.68	
624	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	551.69	09/2019 -	10/2023	49	0	
625	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	408.37	08/2019 -	10/2023	50	0	
626	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,361.00	563.93	12/2020 10/2023	10/2023	34	8.78	
627	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	521.56	02/2020 -	10/2023	44	0	
628	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 503.30	757.12	641.00	08/2021 -	10/2023	26	23.21	
629	SIX / FOUR LANING OF NH 5 (NEW NH 16) FROM PUINTOLA TO TANGI (KM. 284.000 TO KM. 355.000) - [N24000845]NHAI,ODISHA	03/2018	538.41 478.32	478.32	415.11	12/2020 -	10/2023	34	-11.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
630	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) - [N24001600]NHAI,TAMIL NADU	10/2020	434.12 -	434.12	161.17	05/2023 10/2023	10/2023	5	0	
631	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K - [N24001673]NHAI,HARYANA	03/2020	510.97 -	510.97	506.37	03/2023 -	10/2023	7	0	
632	ALIGARH-KANPUR SECTION PACKAGEV FROM MITRASEN-KANPUR - [N24001740]NHAI,UTTAR PRADESH	10/2019	2,325.28 -	2,325.28	1,836.49	09/2023 -	10/2023	1	0	
633	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG I) [AMRAVATI TO KURANKHED FROM KM. 166.00 TO KM. 220.00] - [N24001800]NHAI,MAHARASHTRA	11/2019	713.07 -	713.07	281.00	07/2023 -	10/2023	3	0	
634	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826]NHAI,UTTAR PRADESH	02/2019	927.77 -	1,603.00	1,104.18	02/2022 -	10/2023	20	72.78	
635	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE - [N24001827]NHAI,GUJARAT	03/2022	162.73 -	162.73	54.00	03/2023 -	10/2023	7	0	
636	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	303.15	03/2019 11/2023	11/2023	56	0	
637	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 1,503.86	1,503.86	1,405.49	05/2020 11/2023	11/2023	42	33.78	
638	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	950.49	564.62	11/2021 -	11/2023	24	-17.72	
639	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]NHAI,TAMIL NADU	03/2018	998.70 1,358.32	1,358.32	785.96	11/2021 -	11/2023	24	36.01	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
640	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429]NHAI,TAMIL NADU	03/2018	1,294.47 1,588.40	1,588.40	605.20	11/2021 -	11/2023	24	22.71	
641	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 - [N24001535]NHAI,HARYANA	07/2020	899.00 -	947.00	920.51	07/2022 11/2023	11/2023	16	5.34	
642	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI - [N24001536]NHAI,HARYANA	07/2020	817.00 -	817.00	851.73	07/2022 -	11/2023	16	0	
643	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - [N24001710]NHAI,BIHAR	09/2020	2,334.68 2,335.00	2,335.00	714.12	03/2023 11/2023	11/2023	8	.01	
644	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF - [N24001768]NHAI,MADHYA PRADESH	08/2019	323.51 -	323.51	2.46	04/2023 -	11/2023	7	0	
645	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781]NHAI,DELHI	01/2018	2,067.67 -	2,160.00	1,496.49	10/2021 -	11/2023	25	4.47	
646	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) - [N24001804]NHAI,MAHARASHTRA	12/2019	1,654.07 -	980.00	724.63	09/2022 -	11/2023	14	-40.75	
647	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	2,170.28	08/2013 -	12/2023	124	0	
648	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,855.00	06/2014 12/2023	12/2023	114	0	
649	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,182.94	589.65	12/2019 -	12/2023	48	1.33	
650	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	2,360.65	4,657.47	09/2016 -	12/2023	87	41.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
651	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	450.68	07/2019 07/2023	12/2023	53	0	Nil
652	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	329.71	07/2020 -	12/2023	41	0	
653	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	783.15	08/2019 -	12/2023	52	0	
654	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	800.70	07/2021 12/2023	12/2023	29	-4.12	Nil
655	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	356.62	318.13	03/2019 -	12/2023	57	-20.07	Nil
656	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 565.00	686.65	461.14	07/2020 -	12/2023	41	0	
657	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 504.09	1,015.16	355.84	09/2020 -	12/2023	39	47.84	
658	REHABILITATION AND UPGRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) - [N24000739]NHAI,ODISHA	01/2018	503.88 609.03	609.03	221.76	06/2021 06/2022	12/2023	30	20.87	
659	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	699.89	12/2021 12/2023	12/2023	24	0	
660	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	649.90	456.06	12/2020 -	12/2023	36	0	Project Not Delayed.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
661	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI, BIHAR	10/2013	446.97 -	446.97	384.28	11/2020 -	12/2023	37	0	Project Not Delayed.
662	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI, BIHAR	10/2013	464.09 -	464.09	461.45	11/2020 -	12/2023	37	0	
663	TUNNEL AT KHAMBATKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 - [N24001486]NHAI, MAHARASHTRA	02/2019	493.00 -	493.00	374.15	02/2022 03/2023	12/2023	22	0	
664	4L OF KM 0.00 TO KM 42.00 OF OFDOBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALORE - [N24001509]NHAI, KARNATAKA	01/2020	1,307.00 -	1,307.00	701.00	04/2021 12/2023	12/2023	32	0	
665	BALANCE WORK OF RANCHI-MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG - [N24001597]NHAI, JHARKHAND	01/2019	466.55 518.00	466.55	-	12/2020 -	12/2023	36	0	
666	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) - [N24001603]NHAI, TAMIL NADU	01/2019	1,518.53 -	1,518.53	844.56	10/2022 -	12/2023	14	0	
667	4L MISSING LINK (OF REWA BYPASS) FROM JN. WITH NH 30 NEAR BELA TO JN. WITH MPRDC RING ROAD (NEAR SIL - [N24001617]NHAI, MADHYA PRADESH	02/2021	197.87 -	197.87	35.62	01/2023 -	12/2023	11	0	
668	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WORK - [N24001652]NHAI, KERALA	03/2020	210.37 213.06	213.06	171.75	06/2022 01/2023	12/2023	18	1.28	
669	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 - [N24001686]NHAI, KARNATAKA	03/2021	1,065.06 1,577.92	1,577.92	26.31	03/2023 12/2023	12/2023	9	48.15	
670	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G - [N24001711]NHAI, BIHAR	09/2020	939.43 -	939.43	40.02	03/2023 -	12/2023	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
671	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 - [N24001723]NHAI,TAMIL NADU	10/2018	707.90 -	717.00	343.05	02/2021 -	12/2023	34	1.29	
672	4L OF SHAMLI BYAPSS-SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II - [N24001744]NHAI,UTTAR PRADESH	05/2019	779.17 -	779.17	-	11/2022 -	12/2023	13	0	
673	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE - [N24001749]NHAI,WEST BENGAL	08/2021	557.55 -	557.55	393.31	08/2023 -	12/2023	4	0	
674	BALANCE 4 LANING WORK OF RAIGANJ DALKHOLA SECTION OF NH34 FROM KM 398.000 TO KM 452.750 (PACKAGE V) - [N24001751]NHAI,WEST BENGAL	12/2018	1,548.07 -	1,548.07	1,086.32	09/2021 -	12/2023	27	0	
675	DHANGAON - BORGAON SECTION (KM 81.000 TO KM 139.000) [INDORE - EDLABAD PKG IV] - [N24001769]NHAI,MADHYA PRADESH	11/2018	831.00 -	831.00	608.00	08/2023 -	12/2023	4	0	
676	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779]NHAI,DELHI	03/2018	2,507.00 -	3,030.73	1,155.70	09/2022 -	12/2023	15	20.89	
677	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) - [N24001792]NHAI,GUJARAT	03/2021	536.03 -	536.03	350.00	09/2022 -	12/2023	15	0	
678	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) - [N24001793]NHAI,GUJARAT	03/2021	485.75 -	485.75	207.82	09/2022 -	12/2023	15	0	
679	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	1,136.83	1,016.30	05/2021 11/2022	01/2024	32	137.46	
680	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 -	724.60	464.18	03/2023 -	01/2024	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
681	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430]NHAI,TAMIL NADU	03/2018	2,120.40 2,565.63	2,565.63	1,147.79	01/2022 -	01/2024	24	21	
682	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA - [N24001472]NHAI,JAMMU AND KASHMIR	09/2021	811.19 -	811.19	593.45	12/2023 01/2024	01/2024	1	0	
683	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN - [N24001691]NHAI,KARNATAKA	10/2019	1,225.24 1,676.11	1,676.11	14.76	10/2021 01/2024	01/2024	27	36.8	
684	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 1,381.45	1,381.45	939.15	04/2019 02/2024	02/2024	58	53.67	
685	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 1,659.12	1,659.12	1,115.46	07/2020 02/2024	02/2024	43	17.84	Nil
686	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGOUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	309.04	12/2020 -	02/2024	38	0	
687	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. - [N24001599]NHAI,KARNATAKA	03/2018	440.16 -	440.16	126.80	12/2022 12/2023	02/2024	14	0	NIL
688	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 - [N24001601]NHAI,TAMIL NADU	01/2019	1,051.69 -	1,051.69	349.20	01/2023 02/2024	02/2024	13	0	
689	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) - [N24001602]NHAI,TAMIL NADU	01/2019	1,409.38 -	1,409.38	520.63	12/2022 -	02/2024	14	0	
690	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 - [N24001725]NHAI,TAMIL NADU	01/2019	654.26 -	821.00	295.75	05/2021 -	02/2024	33	25.49	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
691	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 567.00	639.58	530.28	04/2019 07/2022	03/2024	59	-38.57	Nil
692	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 810.60	810.60	348.45	10/2019 03/2024	03/2024	53	12.58	
693	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	591.66	429.66	07/2019 03/2024	03/2024	56	0	Nil
694	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 736.01	830.31	347.17	03/2020 03/2024	03/2024	48	23.39	Procedural delay in Land Acquisition. Now, disbursement to land owner is under progress and possession of land received.
695	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P. - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	1,433.11	06/2020 -	03/2024	45	0	
696	REHABILITATION AND UPGRADEMENT OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 644.50	726.99	371.11	12/2021 12/2019	03/2024	27	26.72	Procedural delay in Land Acquisition. Now, disbursement is in progress and possession received.
697	REHABILITATION AND UPGRADEMENT OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 492.83	633.68	560.38	08/2022 -	03/2024	19	0	
698	REHABILITATION AND UPGRADEMENT OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU - [N24000788]NHAI, WEST BENGAL	03/2018	841.57 1,619.48	1,619.48	1,368.06	09/2022 12/2022	03/2024	18	92.44	
699	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINAGE - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	2,140.93	1,912.14	11/2021 -	03/2024	28	0	Nil
700	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 1,404.00	1,404.00	396.76	10/2021 03/2024	03/2024	29	20.89	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
701	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION - [N24001444]NHAI, GUJARAT	05/2020	882.00 -	882.00	319.15	01/2024 -	03/2024	2	0	
702	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) - [N24001502]NHAI, MAHARASHTRA	09/2021	624.45 627.79	627.79	309.89	09/2023 09/2023	03/2024	6	.53	
703	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) - [N24001503]NHAI, MAHARASHTRA	09/2021	667.66 666.21	666.21	329.65	09/2023 09/2023	03/2024	6	-22	
704	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533]NHAI, HARYANA	11/2020	1,690.23 -	2,010.17	1,067.66	12/2023 -	03/2024	3	18.93	
705	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP - [N24001534]NHAI, HARYANA	12/2020	1,334.04 -	1,334.00	717.42	01/2024 03/2024	03/2024	2	0	
706	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF - [N24001596]NHAI, JHARKHAND	11/2021	1,302.72 -	1,302.72	521.32	07/2023 -	03/2024	8	0	
707	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 - [N24001817]NHAI, ANDHRA PRADESH	02/2019	757.45 -	757.45	261.31	03/2023 -	03/2024	12	0	
708	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN - [N24001425]NHAI, KARNATAKA	03/2021	1,100.88 1,100.88	1,100.88	561.13	11/2021 04/2024	04/2024	29	0	Delay in Utility Shifting permission, Tree cutting permission, stoppage of crushing operations, shifting of school and religious structures
709	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH-383 - [N24001605]NHAI, TAMIL NADU	06/2018	1,103.86 -	1,103.86	295.97	03/2022 -	04/2024	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
710	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799]NHAI,MAHARASHTRA	02/2021	1,166.96 -	1,251.00	755.96	10/2023 -	04/2024	6	7.2	
711	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	1,108.00	1,679.45	08/2019 05/2024	05/2024	57	16.55	
712	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	296.66	03/2020 05/2024	05/2024	50	0	
713	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRA ROAD (SH-1 - [N24001414]NHAI,PUNJAB	12/2020	733.00 -	733.00	522.95	01/2024 05/2024	05/2024	4	0	
714	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,656.21	03/2014 -	06/2024	123	18.66	
715	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	1,264.66	07/2020 -	06/2024	47	0	
716	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	970.43	09/2020 06/2024	06/2024	45	0	
717	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	1,097.03	08/2020 06/2024	06/2024	46	0	
718	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH - [N24001545]NHAI,ASSAM	08/2022	175.00 -	175.00	66.50	12/2022 -	06/2024	18	0	
719	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788]NHAI,GUJARAT	07/2020	2,271.86 -	3,916.00	426.80	12/2023 -	06/2024	6	72.37	
720	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789]NHAI,GUJARAT	07/2020	1,710.30 -	1,927.00	265.19	08/2023 -	06/2024	10	12.67	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
721	6L JAKKUVA – KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) - [N24001837]NHAI,ANDHRA PRADESH	02/2021	663.60 -	768.00	241.99	03/2024 -	06/2024	3	15.73	
722	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838]NHAI,ANDHRA PRADESH	02/2021	922.50 -	1,128.68	435.46	03/2024 -	06/2024	3	22.35	
723	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	1,007.00	257.01	03/2020 07/2022	07/2024	52	35.23	Nil
724	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 641.90	641.90	610.69	01/2020 07/2024	07/2024	54	7.4	
725	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	1,601.10	738.85	01/2024 -	07/2024	6	0	
726	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB	12/2020	881.00 -	881.00	546.76	04/2024 07/2024	07/2024	3	0	
727	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB	12/2020	1,234.40 -	1,234.40	344.12	04/2024 07/2024	07/2024	3	0	
728	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB	12/2020	1,094.46 -	1,094.46	357.25	04/2024 07/2024	07/2024	3	0	
729	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) - [N24001606]NHAI,TAMIL NADU	12/2018	854.94 -	854.94	169.70	03/2022 07/2024	07/2024	28	0	
730	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY - [N24001511]NHAI,JAMMU AND KASHMIR	03/2021	2,919.96 -	2,919.96	1,659.64	02/2024 08/2024	08/2024	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
731	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 1,862.77	1,862.77	465.92	02/2023 -	09/2024	19	30.74	
732	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	1,182.87	160.20	07/2021 -	09/2024	38	1.72	
733	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431]NHAI,TAMIL NADU	03/2018	1,872.68 2,661.51	2,756.09	848.82	10/2020 -	09/2024	47	47.17	
734	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI - [N24001476]NHAI,ANDHRA PRADESH	09/2021	517.05 -	655.06	174.28	09/2022 09/2024	09/2024	24	26.69	
735	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP - [N24001477]NHAI,ANDHRA PRADESH	09/2021	622.00 -	817.91	116.11	09/2022 09/2024	09/2024	24	31.5	
736	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	1,168.33	729.78	02/2022 08/2023	10/2024	32	22.9	Delay in providing the vacant access and Right of way to the site and adverse law and order situation in an around the project area.
737	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB	02/2021	1,269.96 -	1,269.96	241.67	04/2024 11/2024	11/2024	7	0	
738	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	282.96	03/2019 12/2023	12/2024	69	0	NA
739	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	348.72	85.61	12/2020 12/2022	12/2024	48	10.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
740	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	1,101.99	563.96	08/2023 12/2024	12/2024	16	0	
741	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA - [N24001750]NHAI,WEST BENGAL	08/2018	622.04 -	622.04	295.81	12/2021 -	12/2024	36	0	
742	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786]NHAI,GUJARAT	03/2021	1,259.00 -	1,910.00	60.25	03/2024 -	12/2024	9	51.71	
743	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	989.66	46.35	01/2024 03/2025	03/2025	14	0	
744	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION - [N24001684]NHAI,KARNATAKA	09/2020	688.00 -	688.00	399.88	01/2023 -	03/2025	26	0	NA
745	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	408.72	03/2019 05/2025	05/2025	74	-25.48	
746	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 - [N24001661]NHAI,KERALA	10/2020	3,219.47 3,713.14	3,713.14	1,911.28	04/2024 05/2025	05/2025	13	15.33	
	Total		2,72,843.85 -	2,94,086.86	1,81,441.65					
	<u>SHIPPING AND PORTS</u>									
	<u>Inland Waterways Authority Of India</u>									
747	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	5,369.18 4,633.10	5,362.27	2,498.52	03/2023 -	12/2026	45	-13	Land acquisition issues are pending with the State Government.
	Total		5,369.18 -	5,362.27	2,498.52					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
748	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	461.42 461.42	461.42	134.92	06/2021 11/2021	12/2023	30	0	
	<u>Cpwd For Telecom</u>									
749	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	187.88	03/2018 -	12/2023	69	0	
	<u>Department Of Telecommunication</u>									
750	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	21,913.00	07/2015 12/2022	09/2023	98	0	
	Total		14,043.62 -	14,043.62	22,235.80					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
751	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,925.22	11,786.54	12/2018 -	12/2023	60	19.98	NIL
752	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17 -	5,384.17	1,428.76	03/2024 -	12/2024	9	0	NIL
753	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	12,020.32	2,396.13	03/2024 -	03/2025	12	0	NIL
	<u>Bangalore Metro Rail Corporation Limited</u>									
754	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	20,936.29	02/2021 -	03/2025	49	0	
	<u>Central Public Works Department</u>									
755	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATTISGARH	05/2019	299.97 299.97	299.97	150.93	09/2020 02/2024	02/2024	41	0	
756	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	36.69	07/2021 -	06/2024	35	-6.71	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
757	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	1,128.00	166.06	03/2022 06/2024	06/2024	27	0	
758	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI - [N28000153]CPWD,DELHI	01/2022	646.52 -	646.52	38.46	11/2024 05/2025	05/2025	6	0	
	<u>Delhi Metro Rail Corporation</u>									
759	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	24,948.65	7,812.66	03/2025 -	03/2026	12	0	Nil
	<u>Lucknow Metro Rail Corporation Limited</u>									
760	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	2,611.47	03/2024 -	12/2025	21	0	NO
761	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	5,323.53	03/2024 -	06/2026	27	0	NO
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
762	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 13,656.22	13,656.22	10,829.00	11/2021 12/2023	12/2023	25	19.58	Contribution of Pune Municipal Corporation amounting to Rs. 197.5 Cr is still pending. Contribution of Pimpri Chinchwad Municipal Corporation amounting to Rs. 55.1 Cr is still pending.
	<u>Mumbai Metro Rail Corporation Ltd.</u>									
763	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	37,276.00	24,123.86	03/2020 -	12/2023	45	61.12	
	<u>Madhya Pradesh Metro Rail Co Limited</u>									
764	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	6,941.40	1,271.31	02/2023 12/2026	12/2026	46	0	
765	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	7,500.80	1,615.18	02/2023 12/2026	12/2026	46	0	
	<u>Patna Metro Rail Corporation</u>									
766	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL,BIHAR	02/2019	13,365.77 -	13,925.50	1,353.32	06/2024 -	09/2024	3	4.19	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2023)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		1,64,605.84 -	1,83,614.81	91,880.19					
	<u>WATER RESOURCES</u>									
	<u>Brahmaputra Board</u>									
767	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	233.57	209.79	12/2019 09/2023	12/2023	48	0	
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
768	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	236.15	110.63	12/2020 -	08/2023	32	0	
769	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	282.74	08/2021 -	08/2023	24	0	
770	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 350.79	294.02	212.03	10/2021 03/2018	12/2023	26	0	
771	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 413.29	413.29	59.00	09/2020 11/2020	03/2024	42	62.63	
772	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 453.83	578.89	45.41	06/2022 -	03/2024	21	0	
773	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 734.09	824.00	198.83	06/2022 -	03/2024	21	0	
	<u>Delhi Jal Board</u>									
774	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD - 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	665.78	522.28	12/2022 -	09/2023	9	0	
775	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 314.71	239.11	252.01	02/2022 09/2023	09/2023	19	0	
	<u>Kolkata Metropolitan Development Authority</u>									
776	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL	08/2017	185.22 -	185.22	49.99	12/2021 02/2021	08/2023	20	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
777	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	172.10	47.20	12/2021 02/2021	09/2023	21	0	
778	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	32.86	02/2022 -	03/2024	25	13.23	
779	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	165.16	-	06/2022 -	03/2024	21	0	
780	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	164.93	45.45	12/2021 02/2021	03/2024	27	0	
781	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	56.61	02/2022 09/2020	06/2024	28	-3.29	
782	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	384.96	-	04/2022 -	12/2024	32	0	
783	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	287.53	-	04/2022 -	12/2024	32	0	
784	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	234.31	-	04/2022 -	12/2024	32	0	
785	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	653.67	-	09/2022 -	12/2026	51	112.84	
	<u>Polavaram Project Authority</u>									
786	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	21,727.98	03/2020 -	03/2024	48	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
787	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 708.70	967.23	220.73	09/2021 -	09/2023	24	0	
788	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	271.39	59.32	08/2021 -	03/2024	31	0	
789	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62 261.12	261.12	69.96	03/2022 02/2021	04/2024	25	22.24	
790	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam, UTTAR PRADESH	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	22	1.31	
791	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 -	213.91	36.94	07/2021 05/2020	04/2024	33	-28.25	
	Total		18,473.78 -	64,370.53	24,239.76					
	DEPARTMENT OF HIGHER EDUCATION									
	Cpwd Of Higher Education									
792	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION, WEST BENGAL	03/2020	193.83 -	193.83	150.97	06/2020 -	07/2023	37	0	
793	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION, BIHAR	09/2018	375.00 -	375.00	278.08	09/2020 -	08/2023	35	0	
794	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION, MAHARASHTRA	01/2018	223.37 275.00	230.00	168.67	07/2020 09/2023	09/2023	38	2.97	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
795	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	424.93	363.19	07/2022 09/2023	09/2023	14	0	IIM Jammu has taken up the matter with J & K administration to waive off the conversion fee of land use change. The revised drawing approval is required for obtaining of completion certificate. Change of land use is to be accorded by Jammu Development Authority.
796	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	460.00	396.27	06/2017 10/2023	10/2023	76	-7.29	
797	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90 334.45	364.00	295.00	08/2021 -	11/2023	27	19.78	
798	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD EDUCATION,JAMMU AND KASHMIR	01/2018	676.00 1,085.04	1,085.04	24.75	04/2023 12/2023	12/2023	8	60.51	
799	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	457.26	09/2022 -	12/2023	15	0	3. Provisional approval from local bodies conveyed on 24th October 2020.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2023)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
800	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH	09/2018	392.51	446.43	213.56	06/2022 01/2024	01/2024	19	13.74	The land provided by the Government of Himachal Pradesh is not free from encumbrances: 1.Approx., 60 Bighas of land is still to be demarcated: On May 23, 2023 the representatives of the District Administration have demarcated approx. 29 Bighas less land. Nearby villagers are not allowing construction agency for boundary wall work in this area. Handing over of land at area of illegal hose (as per revenue department) is also still pending. Updated revenue record to be issued by the revenue department on priority to the Institute so that the Institute can get it checked independently. 2. Existing PWD road passing through the middle of allocated land still to be handed over: The District Administration & HPPWD is yet to hand over the existing PWD road to the Institute. Work of various services, road & development is held up due to not handing over of this road/ non completion of subsidiary road by HPPWD. 3. 33KV electrical connection from the HPSEBL: Institute has paid Rs. 9.78 Cr as advance to the HPSEBL for 33KV power supply. Tender for the Substation has called for. Work is still to start. II KV interim power supply has been assured by the SE, HPSEBL by August 2023. 4. Piped water supply from the Jal Shakti Vibhag: Institute has paid Rs. 50 lakhs as advance to the Jal Shakti Vibhag for piped water supply. Revised DPR is waiting for TS from the Chief Engineer. Work is still to start.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
801	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA	01/2019	790.79 -	790.79	502.79	03/2022 -	03/2024	24	0	
802	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	346.00	03/2021 03/2023	03/2024	36	0	
803	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	175.07	05/2022 -	03/2024	22	0	
	<u>Rites Of Higher Education</u>									
804	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 429.70	429.70	262.25	09/2014 12/2023	12/2023	111	-11.28	Due to Law and Order and subsequent delay
	Total		6,051.42 -	6,490.31	3,633.86					
	<u>HOME AFFAIRS</u>									
	<u>Cpwd For Mha</u>									
805	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 1,735.25	1,900.00	1,583.95	10/2019 -	12/2023	50	55.84	Mandatory Approvals/NOC from Local Bodies, Fire Deptt., SDMC, Delhi Monument Authority & CEC.
806	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" - [N28000147]CPWD FOR MHA,HARYANA	01/2020	166.98 167.00	166.98	41.73	10/2023 03/2024	03/2024	5	0	
807	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35 -	290.33	90.12	07/2022 -	05/2024	22	4.68	
808	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL	10/2014	162.88 210.83	210.83	177.77	04/2018 -	12/2024	80	29.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2023)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		1,826.42 -	2,568.14	1,893.57					
	<u>DPIIT</u>									
	<u>IICC For Dpiit</u>									
809	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,401.00	4,071.81	12/2019 -	09/2023	45	13.16	
	Total		4,773.00 -	5,401.00	4,071.81					
	Grand Total		12,85,604.56	16,16,933.75	10,14,388.39					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(July 2023)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	7,670.00	6,569.75	09/2010 -	12/2024	119.64	171
	<u>Nuclear Power Corporation Of India Limited</u>								
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	16,576.00	12/2016 -	12/2023	38.63	84
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	19,220.00	20,460.00	12/2015 -	03/2024	67.73	99
	Total		27,271.00 -	43,969.00	43,605.75				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	365.49	03/2021 -	03/2025	7.88	48
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	3,291.81	769.80	09/2021 -	12/2024	138.02	39
	Total		2,525.00 -	4,523.81	1,135.29				
	<u>COAL</u>								
	<u>Eastern Coal Fields Limited</u>								
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	713.53	08/2019 -	08/2024	93.35	60
	<u>Neyveli Lignite Corporation</u>								
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	19,406.12	15,652.81	11/2021 -	12/2023	12.58	25
	Total		19,898.73 -	24,552.60	16,366.34				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
8	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	01/2018	676.00 -	1,085.04	24.75	04/2023 -	12/2023	60.51	8
	Total		676.00 -	1,085.04	24.75				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

Date of Commissioning (Month/Year)									
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>DPIIT</u>								
	<u>licc For Dpiit</u>								
9	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00	5,401.00	4,071.81	12/2019	09/2023	13.16	45
	Total		4,773.00	5,401.00	4,071.81				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								
10	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21	1,900.00	1,583.95	10/2019	12/2023	55.84	50
	Total		1,219.21	1,900.00	1,583.95				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
11	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	4,103.00	5,055.00	2,259.22	04/2021	03/2025	23.20	47
	Total		4,103.00	5,055.00	2,259.22				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
12	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00	1,507.24	1,094.66	06/2019	02/2025	35.54	68
13	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00	1,732.00	30.71	02/2017	01/2026	155.46	107
	<u>Gas Authority Of India Limited</u>								
14	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	03/2017	1,740.00	2,433.15	1,547.50	12/2020	06/2024	39.84	42
15	BARAUNI-GUWAHATI PIPELINE - [N16000334]	06/2018	3,308.00	3,992.00	3,537.30	12/2021	10/2023	20.68	22
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00	5,909.00	3,510.30	12/2012	11/2024	102.71	143
	<u>Hindustan Petroleum Corporation Limited</u>								
17	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00	26,264.00	23,860.04	07/2020	04/2024	25.50	45
	<u>Indian Oil Corporation Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
18	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,587.00	726.79	12/2023 -	02/2024	13.52	2
19	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	05/2016	1,945.00 -	2,251.00	2,005.03	02/2022 -	12/2023	15.73	22
20	R and D CAMPUS II AT FARIDABAD - [N16000375]	06/2019	2,281.94 -	3,219.94	1,122.50	12/2022 -	07/2025	41.11	31
21	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	5,303.14	12/2018 -	03/2024	33.98	63
	<u>Oil & Natural Gas Corporation Limited</u>								
22	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	954.95	03/2023 -	03/2024	38.20	12
23	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,897.83	04/2018 -	05/2026	5.80	97
24	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	3,793.93	03/2022 -	12/2023	23.16	21
	Total		48,045.70 -	63,410.69	50,384.68				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
25	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	11,134.54	10,807.99	09/2009 -	03/2024	184.07	174
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	21,247.54	18,903.19	09/2010 -	05/2025	238.05	176
	<u>National Thermal Power Corporation</u>								
27	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	909.90	09/2019 -	09/2026	30.48	84
28	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	7,103.00	5,911.37	03/2013 -	12/2024	138.48	141
29	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	10,831.04	11/2020 -	08/2023	3.76	33
30	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	14,880.63	06/2019 -	06/2024	18.38	60
31	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	21,304.21	10/2011 -	07/2024	145.16	153
	<u>Power Grid Corporation Of India Limited</u>								
32	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	1,952.75	02/2020 -	03/2024	36.46	49
33	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	4,578.01	12/2018 -	01/2024	31.08	61

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
34	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42	9,129.32	5,600.77	12/2018	12/2024	92.02	72
	<u>Satluj Jal Vidyut Nigam Limited</u>								
35	NAITWAR MORI HEP - [N18000265]	10/2017	648.33	1,272.29	1,172.12	12/2021	08/2023	96.24	20
	<u>Thdc India Limited</u>								
36	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	3,860.35	3,163.57	06/2013	06/2026	54.94	156
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	4,825.60	5,601.35	02/2016	06/2024	191.23	100
	Total		64,817.82	1,19,028.30	105,616.90				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
38	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19	1,384.72	757.06	03/2022	12/2024	8.85	33
39	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00	2,081.27	1,335.69	03/2023	03/2026	10.94	36
40	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29	3,445.48	1,666.35	03/2023	03/2024	8.75	12
41	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50	4,805.17	3,491.85	03/2021	03/2026	111.54	60
	<u>East Central Railways</u>								
42	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64	1,185.73	965.84	03/2021	03/2024	62.06	36
43	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04	1,215.54	950.34	03/2021	12/2024	63.37	45
	<u>East Coast Railway</u>								
44	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00	1,440.00	1,058.66	03/2020	03/2024	24.14	48
45	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78	1,928.07	980.13	06/2021	03/2025	137.80	45
46	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13	3,791.66	2,904.31	03/2009	12/2026	29.71	213
	<u>Eastern Railways</u>								
47	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91	1,619.48	1,141.34	03/2019 12/2009	03/2024	36.22	60
48	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98	2,137.81	980.46	03/2022	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
49	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00	3,438.39	2,976.72	09/2018	12/2023	12.55	63

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Metropolitan Rapid Transport Projects</u>								
50	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58	10,442.41	8,008.94	03/2016	12/2023	114.22	93
	<u>North Central Railway</u>								
51	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96	3,845.60	1,024.32	03/2022	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
52	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84	1,187.49	349.63	03/2020	10/2024	186.25	55
53	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00	2,647.51	1,999.72	03/2019	01/2024	47.25	58
54	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87	2,650.00	1,761.52	03/2019	03/2024	397.31	60
55	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32	4,059.65	2,898.81	03/2022	03/2026	81.86	48
56	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52	6,663.00	2,556.74	03/2015	03/2026	186.39	132
57	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48	7,876.92	3,290.96	12/2015	12/2023	488.06	96
58	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47	9,362.06	6,591.01	03/2014	02/2024	291.15	119
59	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17	14,322.79	13,763.33	03/2011	03/2025	221.56	168
	<u>North Eastern Railway</u>								
60	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]	04/2016	1,177.96	1,500.95	1,119.47	12/2019	03/2024	27.42	51
61	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42	2,560.00	2,121.53	03/2022	10/2023	97.62	19
	<u>Northern Railway</u>								
62	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14	1,540.14	482.67	03/2023	06/2025	369.35	27
63	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00	2,017.96	845.23	07/2012	11/2024	348.44	148
64	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	37,012.26	36,017.83	11/2002	01/2024	1,380.49	254
	<u>Rail Vikas Nigam Ltd.</u>								
65	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01	1,457.79	1,491.77	03/2019	03/2024	57.26	60
66	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60	1,500.00	1,251.40	03/2022	12/2023	58.97	21

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
67	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,536.00	1,846.81	03/2020 -	08/2023	102.11	41
68	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	355.80	03/2014 -	12/2025	18.95	141
69	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,300.00	3,204.74	03/2023 -	03/2024	55.15	12
70	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	3,674.36	12/2024 -	12/2026	42.47	24
71	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,834.54	3,020.54	03/2016 -	07/2025	65.94	112
72	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	8,964.35	5,943.37	03/2016 -	03/2026	126.83	120
73	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	24,659.00	14,020.06	12/2024 -	03/2025	52.07	3
	<u>South Central Railway</u>								
74	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	1,533.64	03/2023 -	03/2025	5.16	24
75	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,500.98	1,129.92	03/2009 -	03/2027	139.28	216
76	KAZIPET-BALHRSHA - [N22000367]	04/2015	2,063.03 -	2,909.00	2,355.36	03/2021 -	01/2025	41.01	46
77	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	3,014.00	1,071.53	03/2010 -	03/2025	159.72	180
78	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	2,728.66	03/2022 -	12/2025	7.06	45
	<u>South East Central Railway</u>								
79	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	230.25	12/2021 -	12/2025	378.60	48
80	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,680.00	1,171.79	12/2021 -	12/2024	22.63	36
81	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	1,488.70	03/2021 -	10/2024	8.23	43
82	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,544.25	2,238.21	03/2023 -	12/2024	85.71	21
	<u>South Eastern Railway</u>								
83	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	3,029.04	1,693.74	03/2021 -	03/2024	75.68	36
	<u>South Western Railway</u>								
84	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,649.31	363.80	03/2016 -	03/2026	67.22	120
85	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,960.00	1,887.40	03/2019 -	12/2024	21.39	69

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Southern Railway</u>								
86	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,053.39	328.43	03/2019 -	12/2027	1,601.23	105
87	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	3,118.34	1,877.71	02/2019 -	03/2025	330.30	73
	<u>West Central Railway</u>								
88	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	990.59	03/2022 -	09/2024	114.32	30
89	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,445.30	2,020.86	03/2020 -	10/2024	38.63	55
90	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,938.00	1,279.35	03/2022 -	06/2024	18.55	27
91	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	3,032.46	2,080.00	03/2021 -	12/2025	614.19	57
92	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
93	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	1,095.12	201.24	03/2012 -	03/2024	244.12	144
94	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,793.63	1,222.16	03/2022 -	12/2026	33.13	57
95	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	04/2007	1,640.04 -	1,873.10	1,136.95	03/2022 -	12/2025	14.21	45
96	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,021.00	2,919.74	03/2022 -	03/2026	71.85	48
	Total		1,14,334.81 -	2,51,699.88	171,226.67				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
97	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]	01/2014	1,408.85 -	2,138.16	1,560.46	10/2016 -	11/2023	51.77	85
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
98	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]	04/2017	642.96 -	1,139.85	528.71	06/2023 -	01/2024	77.28	7
	<u>National Highways Authority Of India</u>								
99	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	1,007.00	257.01	03/2020 -	07/2024	35.23	52

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
100	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]	01/2018	686.65	1,015.16	355.84	09/2020	12/2023	47.84	39
101	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]	09/2010	946.00	1,046.56	827.99	06/2018	08/2023	10.63	62
102	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69	1,108.00	1,679.45	08/2019	05/2024	16.55	57
103	6L ALURU - JAKKUBA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838]	02/2021	922.50	1,128.68	435.46	03/2024	06/2024	22.35	3
104	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]	03/2018	478.74	1,136.83	1,016.30	05/2021	01/2024	137.46	32
105	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]	08/2017	950.64	1,168.33	729.78	02/2022	10/2024	22.90	32
106	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]	03/2018	1,162.92	1,182.87	160.20	07/2021	09/2024	1.72	38
107	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45	1,182.94	589.65	12/2019	12/2023	1.33	48
108	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799]	02/2021	1,166.96	1,251.00	755.96	10/2023	04/2024	7.20	6
109	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]	03/2018	998.70	1,358.32	785.96	11/2021	11/2023	36.01	24
110	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]	01/2017	1,251.11	1,361.00	563.93	12/2020	10/2023	8.78	34
111	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	03/2016	899.00	1,381.45	939.15	04/2019	02/2024	53.67	58
112	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]	03/2018	1,161.39	1,404.00	396.76	10/2021	03/2024	20.89	29
113	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00	1,414.01	1,059.61	06/2018	08/2023	30.56	62
114	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11	1,503.86	1,405.49	05/2020	11/2023	33.78	42
115	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]	11/2019	1,226.88	1,569.68	1,054.39	02/2021	08/2023	27.94	30
116	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 - [N24001686]	03/2021	1,065.06	1,577.92	26.31	03/2023	12/2023	48.15	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
117	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429	03/2018	1,294.47	1,588.40	605.20	11/2021	11/2023	22.71	24
118	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826	02/2019	927.77	1,603.00	1,104.18	02/2022	10/2023	72.78	20
119	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU - [N24000788	03/2018	841.57	1,619.48	1,368.06	09/2022	03/2024	92.44	18
120	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 - [N24000564	03/2016	1,408.00	1,659.12	1,115.46	07/2020	02/2024	17.84	43
121	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN - [N24001691	10/2019	1,225.24	1,676.11	14.76	10/2021	01/2024	36.80	27
122	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77	1,862.77	465.92	02/2023	09/2024	30.74	19
123	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786	03/2021	1,259.00	1,910.00	60.25	03/2024	12/2024	51.71	9
124	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789	07/2020	1,710.30	1,927.00	265.19	08/2023	06/2024	12.67	10
125	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533	11/2020	1,690.23	2,010.17	1,067.66	12/2023	03/2024	18.93	3
126	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743	01/2018	1,916.38	2,078.00	1,158.54	02/2023	08/2023	8.43	6
127	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781	01/2018	2,067.67	2,160.00	1,496.49	10/2021	11/2023	4.47	25
128	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - [N24001710	09/2020	2,334.68	2,335.00	714.12	03/2023	11/2023	.01	8
129	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00	2,360.65	4,657.47	09/2016	12/2023	41.78	87
130	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755	10/2019	1,936.68	2,458.03	1,380.90	03/2023	08/2023	26.92	5
131	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430	03/2018	2,120.40	2,565.63	1,147.79	01/2022	01/2024	21.00	24
132	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 - [N24001752	12/2018	2,375.87	2,566.80	2,299.14	02/2023	08/2023	8.04	6
133	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	05/2014	1,655.01	2,639.00	1,771.52	08/2016	07/2023	59.46	83

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
134	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431	03/2018	1,872.68 -	2,756.09	848.82	10/2020 -	09/2024	47.17	47
135	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779	03/2018	2,507.00 -	3,030.73	1,155.70	09/2022 -	12/2023	20.89	15
136	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	3,063.99	2,938.25	04/2019 -	07/2023	93.01	51
137	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	3,656.21	03/2014 -	06/2024	18.66	123
138	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 - [N24001661	10/2020	3,219.47 3,713.00	3,713.14	1,911.28	04/2024 -	05/2025	15.33	13
139	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788	07/2020	2,271.86 -	3,916.00	426.80	12/2023 -	06/2024	72.37	6
	Total		62,197.79 -	80,954.18	46,758.12				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
140	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,840.00	23,131.35	05/2015 -	08/2023	53.56	99
	Total		15,525.00 -	23,840.00	23,131.35				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
141	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	11,786.54	12/2018 -	12/2023	19.98	60
	<u>Maharashtra Metro Rail Corporation Ltd.</u>								
142	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	13,656.22	10,829.00	11/2021 -	12/2023	19.58	25
	<u>Mumbai Metro Rail Corporation Ltd</u>								
143	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	37,276.00	24,123.86	03/2020 -	12/2023	61.12	45
	<u>Patna Metro Rail Corporation</u>								
144	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 -	13,925.50	1,353.32	06/2024 -	09/2024	4.19	3
	Total		58,694.77 -	77,782.94	48,092.72				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2023)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
145	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	21,727.98	03/2020 -	03/2024	447.22	48
	Total		10,151.04 -	55,548.87	21,727.98				
	Grand Total		4,34,232.87	7,58,751.31	535,985.53				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 1000 Crore and above				(July 2023)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Neyveli Lignite Corporation</u>				
1	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	09/2020
2	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	09/2020
3	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	12/2015 -	02/2021
	Total		10,216.01 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
4	CBR 9 MMTPA PROJECT - [N16000434]CPCL,TAMIL NADU	01/2021	31,580.00 31,580.00	06/2025 -	-
	Total		31,580.00 -		
	<u>POWER</u>				
	<u>National Thermal Power Corporation</u>				
5	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	08/2017
	Total		1,527.00 -		
	<u>RAILWAYS</u>				
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
6	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020
7	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
8	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	03/2020 -	03/2023
9	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	03/2012 -	06/2023
	<u>East Coast Railway</u>				
10	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	09/2022
11	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 02/2023	02/2023
	<u>Kolkata Metro Rail Corporation Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 1000 Crore and above				(July 2023)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
12	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	03/2016
	<u>North East Frontier Railway</u>				
13	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	-
14	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
15	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 10/2023	05/2023
	<u>South Central Railway</u>				
16	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2000
17	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	03/2021 -	03/2021
	Total		41,961.66 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
18	KALMATH TO ZARAP - [N24001137]MoRTH, MAHARASHTRA	09/2016	1,338.13 2,617.44	03/2020 -	01/2023
19	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH, MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	02/2023
20	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH, MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	02/2023
21	WAKED TO TALEGAON - [N24001135]MoRTH, MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	02/2023
22	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH, ARUNACHAL PRADESH	09/2011	1,979.00 -	- 12/2021	05/2023
23	INDAPUR TO VADPALE - [N24001114]MoRTH, MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	06/2023
	<u>National Highways Authority Of India</u>				
24	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA	01/2018	953.09 1,014.08	05/2020 -	05/2023
25	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	12/2020 08/2023	05/2023
26	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 2,262.00	07/2021 04/2023	05/2023
27	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL - [N24001566]NHAI, RAJASTHAN	11/2019	1,640.10 -	05/2023 08/2023	05/2023
28	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) - [N24001780]NHAI, HARYANA	01/2018	2,228.00 -	11/2020 08/2023	05/2023

Details of Projects Without Date of Commissioning

Costing Rs. 1000 Crore and above				(July 2023)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
29	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,950.04	06/2018 07/2023	06/2023
30	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,192.10	06/2018 07/2023	06/2023
31	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	03/2017 05/2021	06/2023
32	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 1,152.70	09/2021 -	06/2023
33	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	03/2021 06/2023	06/2023
34	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M - [N24001573]NHAI,RAJASTHAN	11/2019	1,658.06 -	12/2022 08/2023	06/2023
35	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A - [N24001690]NHAI,KARNATAKA	01/2021	1,167.52 1,157.00	01/2023 12/2023	06/2023
36	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805]NHAI,MAHARASHTRA	03/2018	1,169.04 -	03/2021 -	06/2023
37	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806]NHAI,MAHARASHTRA	03/2018	1,241.38 -	03/2023 -	06/2023
	Total		26,964.32 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
38	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	12/2015
39	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	02/2021
	<u>Delhi Metro Rail Corporation</u>				
40	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	08/2021
	<u>Kochi Metro Rail Corporation Ltd</u>				
41	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	09/2020
	Total		62,136.79 -		
	Grand Total		1,74,385.78		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 1000 Crore and above (July 2023)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
1	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	1,323.75	- -	03/2024	-	0/0
2	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,700.00	2,044.95	- -	03/2024	-	0/0
3	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	1,510.00	2,102.69	- -	03/2024	-	0/0
4	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,822.92	- -	12/2024	-	0/0
5	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	834.76	- -	12/2025	-	0/0
	<u>South Western Railway</u>								
6	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 2,404.03	2,404.03	1,161.58	- -	12/2025	-	2/2
7	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,801.01	126.80	- -	12/2026	-	0/0
8	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	5,174.30	159.49	- -	03/2030	-	0/0
	<u>Southern Railway</u>								
9	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	1,431.90	2,095.35	- -	03/2025	-	0/0
10	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	1,339.00	.93	- -	03/2025	-	0/0
11	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	3,620.28	758.81	- 12/2025	12/2025	0(R3)	0/0
	Total		12,488.30 -	24,278.34	12,432.03				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
12	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	1,101.58	608.53	- -	12/2023	-	0/0
13	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	1,478.40	621.30	- -	06/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 1000 Crore and above (July 2023)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	2,926.42	787.79	- 09/2024	-	-	0/0
	Total		5,506.40 -	5,506.40	2,017.62				0/0
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
15	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	1,832.74	- -	09/2023	-	2/9
	Total		2,694.00 -	2,694.00	1,832.74				2/9
	Grand Total		20,688.70	32,478.74	16,282.39				4/11

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 1000 Crore and Above (July 2023)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>COAL</u>					
	<u>Central Coal Fields Limited</u>					
1	EPR ROHINI KARKATA OCP - [N06000243]CCL,JHARKHAND	01/2021	1,020.42 -	03/2025 -	03/2025	0/0
2	EXPANSION OF ASHOK OCP - [N06000247]CCL,JHARKHAND	05/2021	2,898.28 -	03/2026 -	03/2026	0/0
3	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]CCL,JHARKHAND	08/2020	7,254.37 -	03/2028 -	03/2028	0/0
4	EXPANSION PROJECT AMRAPALI OCP - [N06000217]CCL,JHARKHAND	08/2020	5,136.15 -	03/2028 -	03/2028	0/0
	<u>Eastern Coal Fields Limited</u>					
5	SONEPUR BAZARI EXPANSION OC - [N06000220]ECL, WEST BENGAL	07/2021	5,365.88 5,366.00	03/2029 -	03/2029	0/0
6	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]ECL, WEST BENGAL	04/2020	1,210.12 -	03/2029 -	03/2029	0/0
	<u>Mahanadi Coal Fields Limited</u>					
7	GOPALJI-KANIHA OCP - [N06000229]MCL, ODISHA	08/2020	8,416.19 -	03/2028 -	03/2028	0/0
8	BALARAM EXPANSION OCP - [N06000230]MCL, ODISHA	08/2020	3,504.21 -	03/2029 -	03/2029	0/0
9	SUBHADRA OCP - [N06000249]MCL, ODISHA	05/2021	1,693.81 -	03/2027 03/2029	03/2029	0/0
10	RPR OF HINGULA -II EXPANSION PH-III - [N06000261]MCL, ODISHA	12/2022	2,264.68 -	03/2029 -	03/2029	0/0
11	BHUBANESWARI EXPANSION OCP - [N06000227]MCL, ODISHA	08/2020	3,145.45 -	03/2031 -	03/2031	0/0
	<u>Neyveli Lignite Corporation</u>					
12	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	09/2020	0/0
13	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	09/2020	0/0
	<u>MINES</u>					
	<u>National Aluminum Company Limited (Nalco)</u>					
14	POTTANGI BAUXITE MINES - [N10000016]NALCO, ODISHA	05/2018	1,437.00 1,381.00	12/2024 03/2025	05/2025	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
15	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442]BPCL, MAHARASHTRA	04/2021	1,164.69 -	06/2024 -	07/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
16	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,732.00	02/2017 01/2026	01/2026	0/0
17	CITY GAS DISTRIBUTION NETWORK PROJECT AT SANGLI AND SATARA - [N16000460]BPCL,MAHARASHTRA	04/2019	2,337.98 -	11/2028 -	11/2028	0/0
	<u>Indian Oil Corporation Limited</u>					
18	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 02/2024	12/2023	0/0
19	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 1,587.00	12/2023 -	02/2024	0/0
20	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	03/2024	0/0
21	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]IOCL,RAJASTHAN	12/2021	9,028.00 -	10/2024 12/2024	12/2024	0/0
22	POLY BUTADIENE RUBBER PLANT AT PANIPAT - [N16000458]IOCL,HARYANA	03/2022	1,459.00 2,102.79	03/2025 -	03/2025	0/0
23	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	02/2028 08/2029	08/2029	0/0
24	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU	10/2018	2,998.00 -	03/2030 -	03/2030	0/0
25	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU	10/2018	1,304.00 -	03/2030 -	03/2030	0/0
26	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	08/2027 03/2030	03/2030	0/0
27	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS - [N16000485]IOCL,ANDHRA PRADESH	03/2022	1,420.00 -	03/2030 -	03/2030	0/0
28	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS - [N16000490]IOCL,TAMIL NADU	03/2022	1,328.00 -	03/2030 -	03/2030	0/0
29	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS - [N16000492]IOCL,TAMIL NADU	03/2022	1,295.00 -	03/2030 -	03/2030	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
30	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	08/2024 -	03/2026	0/0
31	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 07/2025	09/2026	0/0
32	KWAR HE PROJECT - [N18000363]CVPPPL,JAMMU AND KASHMIR	05/2022	4,526.12 -	11/2026 -	11/2026	0/0
	<u>National Hydro-Electric Power Corporation</u>					
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 21,247.54	09/2010 05/2025	05/2025	0/0
34	RATLE HE PROJECT - [N18000324]NHPC,JAMMU AND KASHMIR	02/2021	5,281.94 5,281.94	02/2026 05/2026	05/2026	0/0
35	TEESTA VI HE PROJECT - [N18000325]NHPC,SIKKIM	03/2019	5,748.04 -	03/2024 08/2026	08/2026	0/0
36	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH - [N18000362]NHPC,ARUNACHAL PRADESH	02/2023	31,876.39 -	02/2032 -	02/2032	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>National Thermal Power Corporation</u>					
37	SHAJAPUR 325MW SOLAR PV PROJECT - [N18000348]NTPC,MADHYA PRADESH	06/2022	1,530.49 -	03/2024 03/2024	02/2024	0/0
38	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	07/2022 03/2024	03/2024	0/0
39	BHADLA-II 500MW SOLAR PV PROJECT - [N18000347]NTPC,RAJASTHAN	06/2022	2,598.92 -	03/2024 03/2024	03/2024	0/0
40	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) - [N18000349]NTPC,GUJARAT	11/2022	1,442.60 -	03/2024 06/2024	06/2024	0/0
41	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 09/2024	09/2024	0/0
42	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320]NTPC,RAJASTHAN	03/2022	1,352.71 -	08/2023 09/2024	09/2024	0/0
43	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321]NTPC,RAJASTHAN	03/2022	1,409.52 -	08/2023 09/2024	09/2024	0/0
44	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322]NTPC,RAJASTHAN	03/2022	1,426.94 -	08/2023 09/2024	09/2024	0/0
45	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) - [N18000346]NTPC,GUJARAT	09/2022	7,179.54 -	09/2024 09/2024	09/2024	0/0
46	DAYAPAR WIND ENERGY PROJECT 200MW - [N18000345]NTPC,GUJARAT	07/2022	1,316.02 -	03/2025 03/2025	03/2025	0/0
47	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) - [N18000364]NTPC,ODISHA	08/2022	11,844.00 -	05/2027 -	05/2027	0/0
	<u>Power Grid Corporation Of India Limited</u>					
48	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]PGCIL,RAJASTHAN	03/2021	1,340.81 -	12/2022 -	07/2023	0/0
49	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]PGCIL,ASSAM	03/2019	1,326.00 -	03/2023 -	09/2023	0/0
50	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN	05/2021	1,184.88 -	09/2022 -	12/2023	0/0
51	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	01/2024	0/0
52	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	03/2024	0/0
53	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	12/2022 -	03/2024	0/0
54	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	12/2022 -	03/2024	0/0
55	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332]PGCIL,MULTI STATE	05/2022	1,666.00 -	11/2023 -	03/2024	0/0
56	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337]PGCIL,MULTI STATE	07/2022	4,546.26 -	06/2023 -	06/2024	0/0
57	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART - [N18000356]PGCIL,RAJASTHAN	03/2023	1,433.28 -	09/2024 -	09/2024	0/0
58	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B - [N18000352]PGCIL,MULTI STATE	03/2023	3,546.94 -	11/2024 -	11/2024	0/0
59	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
60	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000360]PGCIL,GUJARAT	03/2023	1,167.55 -	03/2025 -	03/2025	0/0
61	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000361]PGCIL,GUJARAT	03/2023	2,820.99 -	03/2025 -	03/2025	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
62	BIKANER SOLAR POWER PROJECT - [N18000335]SJVN,MAHARASHTRA	04/2022	5,491.89 532.00	05/2024 -	05/2024	0/0
63	SUNNI DAM HYDRO ELECTRIC PROJECT - [N18000344]SJVN,HIMACHAL PRADESH	01/2023	2,614.51 -	04/2028 -	04/2028	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Cpwd For Health</u>					
64	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	10/2023	0/0
65	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					
66	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR - [N21000031]HITES,TELANGANA	12/2018	1,110.55 -	07/2024 -	10/2024	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
67	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2024	0/0
68	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 03/2025	03/2024	0/0
69	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 03/2025	03/2024	0/0
70	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 03/2025	03/2024	0/0
71	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 03/2025	12/2024	0/0
72	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 03/2025	03/2026	0/0
73	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 03/2025	03/2026	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
74	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
75	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	03/2012 -	06/2023	0/0
77	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	- -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
78	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2024	0/0
79	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
80	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2024	0/0
81	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	- -	03/2024	0/0
82	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- -	12/2024	0/0
83	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 -	12/2024	0/0
84	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	- -	12/2025	0/0
	<u>East Coast Railway</u>					
85	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	09/2022	0/0
86	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 02/2023	02/2023	0/0
87	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2022 -	03/2024	0/0
88	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	02/2025	0/0
89	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2025	0/0
90	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
91	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 -	12/2026	0/0
	<u>Eastern Railways</u>					
92	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2024	0/0
93	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
	<u>Indian Railway Construction Company Limited</u>					
94	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	12/2025	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	03/2016	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
96	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 8,574.98	03/2016 12/2023	12/2023	0/0
	<u>North Central Railway</u>					
97	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2026	0/0
	<u>North East Frontier Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
98	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	12/2023	0/0
99	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	01/2024	0/0
100	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	02/2024	0/0
101	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0
102	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	10/2024	0/0
103	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 12,264.15	03/2011 03/2025	03/2025	0/0
104	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	03/2026	0/0
105	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2026	0/0
106	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	03/2019 -	-	0/0
107	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-	0/0
	<u>North Eastern Railway</u>					
108	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	10/2023	0/0
109	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	03/2024	0/0
	<u>Northern Railway</u>					
110	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 37,012.26	11/2002 12/2023	01/2024	0/0
111	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	11/2024	0/0
112	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.14	03/2023 06/2025	06/2025	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
113	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 10/2023	05/2023	0/0
114	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	03/2020 -	08/2023	0/0
115	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	10/2023	0/0
116	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
117	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2023	0/0
118	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0
119	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
120	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
121	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	03/2025	0/0
122	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	07/2025	0/0
124	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
125	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2026	0/0
126	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
<u>South Central Railway</u>						
127	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2000	0/0
128	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,909.00	03/2021 -	01/2025	0/0
129	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2025	0/0
130	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	12/2025	0/0
131	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2027	0/0
<u>South East Central Railway</u>						
132	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 12/2023	12/2024	0/0
<u>South Eastern Railway</u>						
133	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 3,029.04	03/2021 -	03/2024	0/0
134	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	05/2023 -	02/2025	0/0
<u>South Western Railway</u>						
135	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	12/2024	0/0
136	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	03/2026	0/0
137	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2026	0/0
138	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	03/2030	0/0
<u>Southern Railway</u>						
139	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
140	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
141	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	03/2025	0/0
142	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- 12/2025	12/2025	0/0
143	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 12/2027	12/2027	0/0
	<u>Western Railway</u>					
144	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.03	03/2012 -	03/2024	0/0
145	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	03/2022 03/2026	12/2025	0/0
146	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,677.80	03/2022 03/2026	03/2026	0/0
147	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,793.63	03/2022 12/2026	12/2026	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
148	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	02/2023	0/0
149	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	02/2023	0/0
150	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 12/2021	05/2023	0/0
151	MOPA AIRPORT - [N24001458]MoRTH,GOA	12/2021	1,183.16 -	04/2022 -	10/2023	0/0
152	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	11/2023	0/0
153	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	12/2023	0/0
154	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	06/2024	0/0
155	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH	07/2018	1,948.25 -	02/2024 -	09/2024	0/0
156	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- 09/2024	-	0/0
	<u>National Highways Authority Of India</u>					
157	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 1,014.08	05/2020 -	05/2023	0/0
158	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	12/2020 08/2023	05/2023	0/0
159	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 2,262.00	07/2021 04/2023	05/2023	0/0
160	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL - [N24001566]NHAI,RAJASTHAN	11/2019	1,640.10 -	05/2023 08/2023	05/2023	0/0
161	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	03/2017 05/2021	06/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
162	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 1,152.70	09/2021 -	06/2023	0/0
163	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	03/2021 06/2023	06/2023	0/0
164	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M - [N24001573]NHAI,RAJASTHAN	11/2019	1,658.06 -	12/2022 08/2023	06/2023	0/0
165	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A - [N24001690]NHAI,KARNATAKA	01/2021	1,167.52 1,157.00	01/2023 12/2023	06/2023	0/0
166	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805]NHAI,MAHARASHTRA	03/2018	1,169.04 -	03/2021 -	06/2023	0/0
167	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806]NHAI,MAHARASHTRA	03/2018	1,241.38 -	03/2023 -	06/2023	0/0
168	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29 - [N24001517]NHAI,GUJARAT	09/2020	1,523.77 -	04/2023 -	07/2023	0/0
169	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA - [N24001567]NHAI,RAJASTHAN	11/2019	1,272.97 -	10/2022 09/2023	07/2023	0/0
170	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N - [N24001568]NHAI,RAJASTHAN	11/2019	1,119.35 -	05/2023 10/2023	07/2023	0/0
171	4L OF SHAMLI TO MUZAFFARNAGAR SECTION OF NH-709AD, PKG-II - [N24001742]NHAI,UTTAR PRADESH	06/2020	1,621.07 -	10/2022 -	07/2023	0/0
172	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 1,414.01	06/2018 08/2023	08/2023	0/0
173	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,569.68	02/2021 08/2023	08/2023	0/0
174	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON - [N24001569]NHAI,RAJASTHAN	11/2019	1,425.02 -	03/2023 11/2023	08/2023	0/0
175	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 - [N24001696]NHAI,TAMIL NADU	02/2019	1,291.37 -	08/2023 -	08/2023	0/0
176	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743]NHAI,UTTAR PRADESH	01/2018	1,916.38 -	02/2023 08/2023	08/2023	0/0
177	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 - [N24001752]NHAI, WEST BENGAL	12/2018	2,375.87 2,566.80	02/2023 08/2023	08/2023	0/0
178	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755]NHAI,UTTAR PRADESH	10/2019	1,936.68 -	03/2023 -	08/2023	0/0
179	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A - [N24001782]NHAI,HARYANA	11/2018	2,312.26 -	09/2021 -	08/2023	0/0
180	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN - [N24001783]NHAI,HARYANA	11/2018	2,252.75 -	09/2021 -	08/2023	0/0
181	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA - [N24001784]NHAI,HARYANA	11/2018	1,935.61 -	09/2021 -	08/2023	0/0
182	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 - [N24001518]NHAI,GUJARAT	11/2019	1,669.56 -	09/2023 -	09/2023	0/0
183	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE-7(ALONG WITH 0.700 - [N24001688]NHAI,KARNATAKA	10/2020	3,184.00 -	09/2023 -	09/2023	0/0
184	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M - [N24001689]NHAI,KARNATAKA	12/2020	1,745.00 -	09/2023 -	09/2023	0/0
185	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 - [N24001687]NHAI,KARNATAKA	10/2021	1,331.77 2,508.79	10/2023 10/2024	10/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
186	ALIGARH-KANPUR SECTION PACKAGE-V FROM MITRASEN-KANPUR - [N24001740]NHAI,UTTAR PRADESH	10/2019	2,325.28 -	09/2023 -	10/2023	0/0
187	DEVELOPMENT OF 6L UER-II [PACKAGE - III] (NANGLOI - NAJAFGARH ROAD TILL SECTOR 24 DWARKA) FROM KM. 2 - [N24001776]NHAI,DELHI	07/2020	1,069.27 -	10/2023 -	10/2023	0/0
188	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 - [N24001777]NHAI,DELHI	07/2020	2,171.80 -	10/2023 -	10/2023	0/0
189	DEVELOPMENT OF 6L UER-II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM - [N24001825]NHAI,DELHI	07/2020	1,894.96 -	10/2023 -	10/2023	0/0
190	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 1,503.86	05/2020 11/2023	11/2023	0/0
191	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]NHAI,TAMIL NADU	03/2018	998.70 1,358.32	11/2021 -	11/2023	0/0
192	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429]NHAI,TAMIL NADU	03/2018	1,294.47 1,588.40	11/2021 -	11/2023	0/0
193	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 - [N24001519]NHAI,GUJARAT	09/2020	1,198.55 -	11/2023 -	11/2023	0/0
194	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - [N24001710]NHAI,BIHAR	09/2020	2,334.68 2,335.00	03/2023 11/2023	11/2023	0/0
195	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739]NHAI,UTTAR PRADESH	10/2019	1,779.83 -	11/2023 -	11/2023	0/0
196	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU - [N24001774]NHAI,HARYANA	12/2020	1,524.03 -	11/2023 -	11/2023	0/0
197	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781]NHAI,DELHI	01/2018	2,067.67 -	10/2021 -	11/2023	0/0
198	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 - [N24001830]NHAI,UTTAR PRADESH	06/2020	2,002.79 -	11/2023 -	11/2023	0/0
199	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 12/2023	12/2023	0/0
200	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	12/2019 -	12/2023	0/0
201	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	09/2016 -	12/2023	0/0
202	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	12/2023	0/0
203	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 504.09	09/2020 -	12/2023	0/0
204	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	12/2021 12/2023	12/2023	0/0
205	4L OF KM 0.00 TO KM 42.00 OF OFDOBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALO - [N24001509]NHAI,KARNATAKA	01/2020	1,307.00 -	04/2021 12/2023	12/2023	0/0
206	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V - [N24001514]NHAI,PUNJAB	01/2021	1,060.29 -	01/2024 12/2023	12/2023	0/0
207	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S - [N24001571]NHAI,RAJASTHAN	11/2019	1,341.36 -	12/2023 -	12/2023	0/0
208	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) - [N24001603]NHAI,TAMIL NADU	01/2019	1,518.53 -	10/2022 -	12/2023	0/0
209	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F - [N24001633]NHAI,HARYANA	12/2020	1,430.88 -	12/2023 -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
210	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO - [N24001634]NHAI,HARYANA	01/2021	1,306.95 -	12/2023 -	12/2023	0/0
211	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 - [N24001686]NHAI,KARNATAKA	03/2021	1,065.06 1,577.92	03/2023 12/2023	12/2023	0/0
212	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM - [N24001694]NHAI,TAMIL NADU	02/2019	1,243.57 -	12/2023 -	12/2023	0/0
213	BALANCE 4 LANING WORK OF RAIGANJ DALKHOLA SECTION OF NH34 FROM KM 398.000 TO KM 452.750 (PACKAGE V) - [N24001751]NHAI, WEST BENGAL	12/2018	1,548.07 -	09/2021 -	12/2023	0/0
214	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779]NHAI,DELHI	03/2018	2,507.00 -	09/2022 -	12/2023	0/0
215	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	05/2021 11/2022	01/2024	0/0
216	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430]NHAI,TAMIL NADU	03/2018	2,120.40 2,565.63	01/2022 -	01/2024	0/0
217	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 - [N24001522]NHAI,TELANGANA	01/2021	1,307.95 -	01/2024 -	01/2024	0/0
218	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH - [N24001612]NHAI,RAJASTHAN	07/2020	1,788.69 -	01/2024 09/2024	01/2024	0/0
219	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN - [N24001691]NHAI,KARNATAKA	10/2019	1,225.24 1,676.11	10/2021 01/2024	01/2024	0/0
220	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. - [N24001706]NHAI,BIHAR	03/2021	1,097.18 1,097.00	01/2024 -	01/2024	0/0
221	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E - [N24001707]NHAI,BIHAR	03/2021	1,143.46 1,143.00	01/2024 -	01/2024	0/0
222	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] - [N24001762]NHAI,MADHYA PRADESH	10/2021	1,146.22 -	01/2024 -	01/2024	0/0
223	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	12/2020 -	02/2024	0/0
224	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) - [N24001506]NHAI,MAHARASHTRA	02/2022	2,747.00 -	02/2024 -	02/2024	0/0
225	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 - [N24001515]NHAI, GUJARAT	09/2020	1,542.02 -	02/2024 -	02/2024	0/0
226	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 - [N24001516]NHAI, GUJARAT	09/2020	1,185.69 -	02/2024 -	02/2024	0/0
227	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 - [N24001601]NHAI,TAMIL NADU	01/2019	1,051.69 -	01/2023 02/2024	02/2024	0/0
228	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) - [N24001602]NHAI,TAMIL NADU	01/2019	1,409.38 -	12/2022 -	02/2024	0/0
229	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH - [N24001660]NHAI,KERALA	08/2020	2,714.60 3,319.41	02/2024 11/2021	02/2024	0/0
230	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	03/2024	0/0
231	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU - [N24000788]NHAI, WEST BENGAL	03/2018	841.57 1,619.48	09/2022 12/2022	03/2024	0/0
232	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	11/2021 -	03/2024	0/0
233	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 1,404.00	10/2021 03/2024	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
234	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) - [N24001505]NHAI, MAHARASHTRA	03/2022	1,549.02 -	03/2024 -	03/2024	0/0
235	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533]NHAI, HARYANA	11/2020	1,690.23 -	12/2023 -	03/2024	0/0
236	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP - [N24001534]NHAI, HARYANA	12/2020	1,334.04 -	01/2024 03/2024	03/2024	0/0
237	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - [N24001589]NHAI, JHARKHAND	09/2020	755.26 -	03/2024 -	03/2024	0/0
238	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595]NHAI, JHARKHAND	08/2020	1,034.00 -	03/2024 -	03/2024	0/0
239	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF - [N24001596]NHAI, JHARKHAND	11/2021	1,302.72 -	07/2023 -	03/2024	0/0
240	4 LANE OF BILASPUR TO URGU PROJECT (KM 0.00 TO KM 70.2) OF NH-130A - [N24001611]NHAI, CHHATTISGARH	04/2020	1,855.59 1,869.85	03/2024 -	03/2024	0/0
241	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI - [N24001704]NHAI, BIHAR	03/2021	1,020.84 -	03/2024 -	03/2024	0/0
242	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C - [N24001705]NHAI, BIHAR	03/2022	1,485.66 -	03/2024 -	03/2024	0/0
243	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR - [N24001772]NHAI, UTTAR PRADESH	08/2021	1,147.26 -	03/2024 -	03/2024	0/0
244	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH-383 - [N24001605]NHAI, TAMIL NADU	06/2018	1,103.86 -	03/2022 -	04/2024	0/0
245	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ - [N24001663]NHAI, KERALA	06/2020	3,041.65 3,799.76	04/2024 10/2021	04/2024	0/0
246	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ - [N24001664]NHAI, KERALA	06/2020	1,746.45 2,377.88	04/2024 10/2021	04/2024	0/0
247	6L OF BADAUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE - OD-3) - [N24001668]NHAI, ODISHA	03/2021	1,249.00 -	04/2024 -	04/2024	0/0
248	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU - [N24001701]NHAI, BIHAR	04/2022	1,769.50 -	04/2024 -	04/2024	0/0
249	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND - [N24001767]NHAI, MADHYA PRADESH	01/2021	1,001.69 -	04/2024 -	04/2024	0/0
250	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799]NHAI, MAHARASHTRA	02/2021	1,166.96 -	10/2023 -	04/2024	0/0
251	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209 (EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	08/2019 05/2024	05/2024	0/0
252	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) - [N24001504]NHAI, MAHARASHTRA	05/2022	1,260.00 -	05/2024 -	05/2024	0/0
253	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) - [N24001507]NHAI, MAHARASHTRA	11/2022	1,124.00 -	05/2024 -	05/2024	0/0
254	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 - [N24001520]NHAI, GUJARAT	11/2019	1,604.06 -	05/2024 -	05/2024	0/0
255	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL - ALANDI S - [N24001610]NHAI, MAHARASHTRA	01/2022	1,833.73 -	05/2024 05/2024	05/2024	0/0
256	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM - [N24001632]NHAI, PUNJAB	01/2021	1,741.86 -	05/2024 -	05/2024	0/0
257	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH - [N24001662]NHAI, KERALA	05/2020	1,981.07 2,430.53	05/2024 11/2021	05/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
258	6L GREENFIELD KALIAGURA – BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG - [N24001667]NHAI,ODISHA	09/2021	1,734.00 1,734.00	05/2024 -	05/2024	0/0
259	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAJHPET) FROM KM 156.000 TO KM 1 - [N24001720]NHAI,TAMIL NADU	10/2020	1,023.91 -	05/2024 -	05/2024	0/0
260	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721]NHAI,TAMIL NADU	02/2019	1,008.99 -	05/2024 -	05/2024	0/0
261	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812]NHAI,HIMACHAL PRADESH	03/2021	1,002.11 1,247.93	05/2024 -	05/2024	0/0
262	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	06/2024	0/0
263	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	07/2020 -	06/2024	0/0
264	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	09/2020 06/2024	06/2024	0/0
265	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	08/2020 06/2024	06/2024	0/0
266	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX - [N24001622]NHAI,JAMMU AND KASHMIR	07/2021	1,401.87 -	06/2024 06/2024	06/2024	0/0
267	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE -- [N24001678]NHAI,ODISHA	08/2021	1,460.00 1,460.00	06/2024 -	06/2024	0/0
268	BAKHTIYARPUR RAJLAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 - [N24001708]NHAI,BIHAR	09/2020	2,156.22 -	06/2024 -	06/2024	0/0
269	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADDARA MU - [N24001788]NHAI,GUJARAT	07/2020	2,271.86 -	12/2023 -	06/2024	0/0
270	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789]NHAI,GUJARAT	07/2020	1,710.30 -	08/2023 -	06/2024	0/0
271	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 07/2022	07/2024	0/0
272	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658]NHAI,KERALA	01/2021	4,265.42 -	07/2024 -	07/2024	0/0
273	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659]NHAI,KERALA	02/2021	3,375.31 -	07/2024 -	07/2024	0/0
274	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719]NHAI,TAMIL NADU	02/2021	2,948.31 -	07/2024 -	07/2024	0/0
275	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI - [N24001642]NHAI,PUNJAB	02/2021	1,474.77 -	08/2024 -	08/2024	0/0
276	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH - [N24001698]NHAI,BIHAR	08/2022	1,198.02 -	08/2024 -	08/2024	0/0
277	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K - [N24001717]NHAI,TAMIL NADU	11/2020	1,155.49 -	08/2024 -	08/2024	0/0
278	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.- MAVIKALAN) TO VILL.-LOHADDA FROM K - [N24001733]NHAI,UTTAR PRADESH	03/2022	1,602.48 -	08/2024 -	08/2024	0/0
279	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. - [N24001734]NHAI,UTTAR PRADESH	03/2022	1,335.45 -	08/2024 -	08/2024	0/0
280	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KHYAWARI TO VILL.-LATIPUR AT SAHARANPUR BYPASS FROM KM - [N24001735]NHAI,UTTAR PRADESH	03/2022	1,428.19 -	08/2024 -	08/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
281	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K - [N24001736]NHAI,UTTAR PRADESH	01/2022	1,159.96 -	08/2024 -	08/2024	0/0
282	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 1,862.77	02/2023 -	09/2024	0/0
283	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	07/2021 -	09/2024	0/0
284	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431]NHAI,TAMIL NADU	03/2018	1,872.68 2,661.51	10/2020 -	09/2024	0/0
285	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 - [N24001550]NHAI,JAMMU AND KASHMIR	09/2021	1,821.72 1,917.32	09/2024 -	09/2024	0/0
286	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 - [N24001551]NHAI,JAMMU AND KASHMIR	10/2021	3,044.02 3,044.02	09/2024 -	09/2024	0/0
287	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B - [N24001552]NHAI,JAMMU AND KASHMIR	10/2021	2,714.95 2,714.95	09/2024 -	09/2024	0/0
288	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA - [N24001593]NHAI,CHHATTISGARH	11/2021	1,368.19 -	09/2024 -	09/2024	0/0
289	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O - [N24001651]NHAI,KERALA	09/2021	2,878.97 -	09/2024 09/2024	09/2024	0/0
290	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 - [N24001747]NHAI,WEST BENGAL	03/2020	2,193.23 2,314.00	09/2024 -	09/2024	0/0
291	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA - [N24001748]NHAI,WEST BENGAL	03/2021	2,200.93 -	09/2024 -	09/2024	0/0
292	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A - [N24001813]NHAI,HIMACHAL PRADESH	07/2021	1,692.05 -	09/2024 -	09/2024	0/0
293	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	02/2022 08/2023	10/2024	0/0
294	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	10/2024 10/2024	10/2024	0/0
295	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) - [N24001508]NHAI,MAHARASHTRA	11/2022	1,450.00 -	10/2024 -	10/2024	0/0
296	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF - [N24001526]NHAI,UTTARAKHAND	08/2021	1,377.79 1,384.11	10/2024 10/2024	10/2024	0/0
297	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD - [N24001631]NHAI,PUNJAB	03/2021	1,525.31 -	10/2024 -	10/2024	0/0
298	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR - [N24001641]NHAI,PUNJAB	03/2021	1,641.75 -	10/2024 -	10/2024	0/0
299	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC - [N24001657]NHAI,KERALA	06/2021	2,842.14 -	10/2024 10/2024	10/2024	0/0
300	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 - [N24001665]NHAI,ODISHA	12/2021	1,592.00 1,592.00	10/2024 -	10/2024	0/0
301	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 - [N24001693]NHAI,TAMIL NADU	09/2021	1,751.18 -	10/2024 -	10/2024	0/0
302	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D - [N24001756]NHAI,MADHYA PRADESH	10/2020	1,352.56 -	10/2024 -	10/2024	0/0
303	INDORE - HARDI (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] - [N24001766]NHAI,MADHYA PRADESH	01/2022	1,011.29 -	10/2024 -	10/2024	0/0
304	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796]NHAI,MAHARASHTRA	03/2022	1,013.33 -	10/2024 10/2024	10/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
305	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR - [N24001557]NHAI,RAJASTHAN	03/2022	1,636.15 -	11/2024 -	11/2024	0/0
306	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N - [N24001640]NHAI,PUNJAB	03/2021	1,229.38 -	11/2024 -	11/2024	0/0
307	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR - [N24001771]NHAI,DELHI	06/2020	1,479.22 -	12/2024 -	12/2024	0/0
308	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786]NHAI,GUJARAT	03/2021	1,259.00 -	03/2024 -	12/2024	0/0
309	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF - [N24001808]NHAI,HIMACHAL PRADESH	03/2021	1,322.95 1,442.47	12/2024 12/2024	12/2024	0/0
310	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA - [N24001588]NHAI,CHHATTISGARH	12/2021	1,470.73 -	01/2025 -	01/2025	0/0
311	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 - [N24001625]NHAI,TELANGANA	01/2022	1,227.57 -	01/2025 -	01/2025	0/0
312	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K - [N24001637]NHAI,PUNJAB	03/2021	1,754.84 -	01/2025 -	01/2025	0/0
313	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 - [N24001650]NHAI,KERALA	12/2021	3,635.64 -	01/2025 01/2025	01/2025	0/0
314	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) - [N24001730]NHAI,UTTAR PRADESH	12/2021	1,384.79 -	01/2025 -	01/2025	0/0
315	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) - [N24001553]NHAI,UTTARAKHAND	03/2022	1,092.90 1,092.90	02/2025 -	02/2025	0/0
316	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K - [N24001627]NHAI,JAMMU AND KASHMIR	07/2021	1,912.17 -	02/2025 02/2025	02/2025	0/0
317	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 - [N24001628]NHAI,MULTI STATE	11/2021	2,155.95 -	02/2025 -	02/2025	0/0
318	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA - [N24001630]NHAI,PUNJAB	07/2021	1,501.02 -	02/2025 -	02/2025	0/0
319	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O - [N24001635]NHAI,HARYANA	03/2022	1,269.50 -	02/2025 -	02/2025	0/0
320	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 - [N24001649]NHAI,KERALA	12/2021	3,273.61 -	02/2025 02/2025	02/2025	0/0
321	SIX LANING FROM KAPPRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655]NHAI,KERALA	06/2021	3,606.00 -	02/2025 -	02/2025	0/0
322	BANGALORE/TN BORDER TO HOSKOTE - [N24001674]NHAI,KARNATAKA	02/2023	1,240.60 -	02/2025 -	02/2025	0/0
323	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) - [N24001697]NHAI,BIHAR	02/2023	1,358.00 -	02/2025 -	02/2025	0/0
324	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 - [N24001654]NHAI,KERALA	06/2021	2,641.37 -	03/2025 03/2025	03/2025	0/0
325	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656]NHAI,KERALA	06/2021	2,595.00 -	03/2025 -	03/2025	0/0
326	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 (- [N24001653]NHAI,KERALA	11/2021	3,565.82 -	04/2025 -	04/2025	0/0
327	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 - [N24001661]NHAI,KERALA	10/2020	3,219.47 3,713.14	04/2024 05/2025	05/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
328	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 - [N24001675]NHAI,KARNATAKA	11/2022	1,732.73 -	05/2025 -	05/2025	0/0
329	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 - [N24001731]NHAI,UTTAR PRADESH	12/2021	2,470.64 -	05/2025 05/2025	05/2025	0/0
330	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT - [N24001785]NHAI,GUJARAT	03/2022	1,373.06 1,085.00	06/2025 -	06/2025	0/0
331	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) - [N24001608]NHAI,MAHARASHTRA	09/2021	2,208.68 -	07/2025 -	07/2025	0/0
332	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO - [N24001728]NHAI,UTTAR PRADESH	12/2021	1,138.81 -	07/2025 -	07/2025	0/0
333	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N - [N24001745]NHAI,UTTAR PRADESH	12/2021	1,972.10 -	07/2025 07/2025	07/2025	0/0
334	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 - [N24001849]NHAI,ANDHRA PRADESH	05/2022	1,063.72 -	07/2025 -	07/2025	0/0
335	TUMKUR - NELAMANGALA(6L) - [N24001681]NHAI,KARNATAKA	08/2022	2,032.15 1,351.00	08/2025 -	08/2025	0/0
336	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. - [N24001844]NHAI,ANDHRA PRADESH	12/2022	1,058.90 -	10/2025 -	10/2025	0/0
337	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 - [N24001845]NHAI,ANDHRA PRADESH	02/2023	1,253.24 -	10/2025 -	10/2025	0/0
338	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. - [N24001846]NHAI,ANDHRA PRADESH	02/2023	1,200.42 -	10/2025 -	10/2025	0/0
339	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 - [N24001547]NHAI,ASSAM	03/2022	1,909.98 -	01/2026 -	01/2026	0/0
340	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE - [N24001648]NHAI,KERALA	08/2022	2,429.52 -	01/2026 -	01/2026	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Department Of Telecommunication</u>					
341	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 12/2022	09/2023	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
342	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 06/2024	06/2024	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
343	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
344	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	12/2025	0/0
345	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	06/2026	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 1000 Crore and Above (July 2023)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
346	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 13,656.22	11/2021 12/2023	12/2023	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
347	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	03/2020 -	12/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
348	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 12/2026	12/2026	0/0
349	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 12/2026	12/2026	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
350	NAGPUR METRO RAIL PROJECT PHASE II - [N28000155]NMRCL,MAHARASHTRA	12/2022	6,708.00 -	12/2027 -	12/2027	0/0
	<u>Patna Metro Rail Corporation</u>					
351	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR	02/2019	13,365.77 -	06/2024 -	09/2024	0/0
	<u>DPIIT</u>					
	<u>Dmic For Dpiit</u>					
352	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	20,084.00 20,084.00	03/2027 03/2027	03/2027	0/0
	<u>Iicc For Dpiit</u>					
353	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	12/2019 -	09/2023	0/0
	Total		8,61,748.68 -			0/0
	Grand Total		8,61,748.68			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
1	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400	6/2020	1,378.00 -	1,378.00	885.65	12/2022 02/2024	12/2023
2	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409	9/2020	18,936.00 -	18,936.00	4,182.86	09/2024 -	08/2024
	Total		20,314.00 -	20,314.00	5,068.51		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
3	SHAJAPUR 325MW SOLAR PV PROJECT - [N18000348	6/2022	1,530.49 -	1,530.49	208.92	03/2024 03/2024	02/2024
	Total		1,530.49 -	1,530.49	208.92		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
4	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	2/2015	1,272.19 -	1,384.72	757.06	03/2022 03/2025	12/2024
5	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	928.90	03/2023 03/2025	03/2024
6	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47 -	6,409.38	2,826.85	03/2024 03/2025	03/2024
7	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361	2/2016	1,035.16 -	1,035.16	830.46	03/2022 03/2025	03/2024
	<u>Rail Vikas Nigam Ltd.</u>						
8	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	6,753.42	3,955.01	12/2026 -	03/2025
	<u>Western Railway</u>						
9	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04 1,873.10	1,873.10	1,136.95	03/2022 03/2026	12/2025
	Total		12,991.76 -	19,905.69	10,435.23		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
10	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA - [N24001567	11/2019	1,272.97 -	1,272.97	330.25	10/2022 09/2023	07/2023

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N - [N24001568	11/2019	1,119.35 -	1,119.35	1,108.34	05/2023 10/2023	07/2023
12	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 - [N24001687	10/2021	1,331.77 2,508.79	2,508.79	60.90	10/2023 10/2024	10/2023
13	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON - [N24001569	11/2019	1,425.02 -	1,425.02	1,026.56	03/2023 11/2023	08/2023
14	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH - [N24001612	7/2020	1,788.69 -	1,788.69	411.07	01/2024 09/2024	01/2024
	Total		6,937.80 -	8,114.82	2,937.12		
	Grand Total		41,774.05	49,865.00	18,649.78		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	10,592.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	10,592.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	1,008.10	08/2022 12/2023	12/2023
	Total		1,405.00 -	1,405.00	1,008.10		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
3	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]	8/2020	7,254.37 -	7,254.37	902.16	03/2028 -	03/2028
4	EXPANSION PROJECT AMRAPALI OCP - [N06000217]	8/2020	5,136.15 -	5,136.15	572.77	03/2028 -	03/2028
5	EXPANSION OF ASHOK OCP - [N06000247]	5/2021	2,898.28 -	2,898.28	173.90	03/2026 -	03/2026
6	EPR ROHINI KARKATA OCP - [N06000243]	1/2021	1,020.42 -	1,020.42	79.34	03/2025 -	03/2025
	<u>Eastern Coal Fields Limited</u>						
7	SONEPUR BAZARI EXPANSION OC - [N06000220]	7/2021	5,365.88 5,366.00	5,365.88	316.12	03/2029 -	03/2029
8	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]	4/2020	1,210.12 -	1,210.12	259.91	03/2029 -	03/2029
	<u>Mahanadi Coal Fields Limited</u>						
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	3,339.10	03/2026 -	03/2026
10	RPR OF HINGULA -II EXPANSION PH-III - [N06000261]	12/2022	2,264.68 -	2,264.68	934.65	03/2029 -	03/2029
11	SUBHADRA OCP - [N06000249]	5/2021	1,693.81 -	1,693.81	904.20	03/2027 03/2029	03/2029
12	BALARAM EXPANSION OCP - [N06000230]	8/2020	3,504.21 -	3,504.21	656.64	03/2029 -	03/2029
13	GOPALJI-KANIHA OCP - [N06000229]	8/2020	8,416.19 -	8,416.19	1,399.84	03/2028 -	03/2028
14	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	1,438.58	03/2027 -	03/2027

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,432.59	03/2029 -	03/2029
16	BHUBANESWARI EXPANSION OCP - [N06000227]	8/2020	3,145.45 -	3,145.45	941.66	03/2031 -	03/2031
	<u>Neyveli Lignite Corporation</u>						
17	TALABIRA II AND III OCP - [N06000189]	7/2017	2,401.07 -	2,401.07	1,051.59	01/2027 -	01/2027
18	PACHWARA SOUTH COAL BLOCK - [N06000193]	7/2013	1,795.01 -	1,795.01	45.19	09/2028 -	09/2028
	<u>Northern Coal Fields Limited</u>						
19	NIGAHI EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	285.78	03/2025 -	03/2025
	<u>South-Eastern Coal Fields Limited</u>						
20	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	721.14	03/2029 -	03/2029
21	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	39.19	03/2029 -	03/2029
22	RAMPUR BATURA OC (4.0 MTY) - [N06000233]	7/2019	1,248.93 -	1,248.93	408.00	03/2026 -	03/2026
23	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	2,336.23	03/2029 -	03/2029
	<u>Western Coal Fields Limited</u>						
24	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]	2/2020	1,184.33 -	1,184.33	692.00	03/2027 -	03/2027
	Total		69,159.88 -	69,159.88	18,930.58		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
25	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	1,085.04	24.75	04/2023 12/2023	12/2023
	Total		676.00 -	1,085.04	24.75		
	<u>DPIIT</u>						
	<u>Dmic For Dpiit</u>						
26	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001]	9/2011	20,084.00 -	20,084.00	9,682.86	03/2027 03/2027	03/2027
	Total		20,084.00 -	20,084.00	9,682.86		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
27	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00 -	1,828.00	740.13	09/2025 -	09/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,828.00 -	1,828.00	740.13		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
28	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,732.00	30.71	02/2017 01/2026	01/2026
29	CITY GAS DISTRIBUTION NETWORK PROJECT AT AHMEDNAGAR AND AURANGABAD - [N16000459]	4/2019	3,972.18 -	3,972.18	1,233.81	09/2028 -	09/2028
30	CITY GAS DISTRIBUTION NETWORK PROJECT AT SANGLI AND SATARA - [N16000460]	4/2019	2,337.98 -	2,337.98	635.90	11/2028 -	11/2028
	<u>Gas Authority Of India Limited</u>						
31	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	2,433.15	1,547.50	12/2020 06/2024	06/2024
32	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	1,753.85	04/2025 -	04/2025
33	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	1,299.02	430.40	04/2024 -	04/2024
34	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,992.00	3,537.30	12/2021 10/2023	10/2023
35	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	1,553.40	07/2022 09/2024	09/2024
36	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	625.20	11/2022 06/2024	06/2024
37	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	4,595.80	05/2023 10/2024	10/2024
38	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,510.30	12/2012 11/2024	11/2024
	<u>Hindustan Petroleum Corporation Limited</u>						
39	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	1,340.47	03/2029 08/2029	08/2029
40	HALDIA PANAGARH PIPELINE PROJECT - [N16000478]	11/2022	1,010.00 -	1,010.00	5.55	11/2025 -	11/2025
41	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	735.28	02/2023 12/2023	12/2023
42	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	414.68	03/2031 08/2031	08/2031
	<u>Indian Oil Corporation Limited</u>						
43	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	2,497.03	08/2021 03/2024	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
44	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS - [N16000492]	3/2022	1,295.00 -	1,295.00	39.23	03/2030 -	03/2030
45	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS [N16000490]	3/2022	1,328.00 -	1,328.00	41.85	03/2030 -	03/2030
46	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS [N16000485]	3/2022	1,420.00 -	1,420.00	25.37	03/2030 -	03/2030
47	POLY BUTADIENE RUBBER PLANT AT PANIPAT - [N16000458]	3/2022	1,459.00 -	1,459.00	69.74	03/2025 -	03/2025
48	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]	12/2021	9,028.00 -	9,028.00	4,088.75	10/2024 12/2024	12/2024
49	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS [N16000425]	6/2019	2,996.00 -	2,996.00	517.47	02/2028 08/2029	08/2029
50	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS [N16000420]	6/2019	2,880.00 -	2,880.00	206.83	08/2027 03/2030	03/2030
51	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	96.14	03/2030 -	03/2030
52	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	288.06	03/2030 -	03/2030
53	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	4,702.23	09/2024 -	09/2024
54	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY [N16000393]	6/2020	1,019.00 -	1,019.00	658.96	01/2023 11/2023	11/2023
55	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	6,350.87	04/2023 12/2024	12/2024
56	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	3,116.31	05/2023 11/2023	11/2023
57	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	776.69	12/2021 12/2023	12/2023
	<u>Indradhanush Gas Grid Ltd</u>						
58	NORTH EAST GAS GRID - [N16000439]	11/2020	9,265.00 -	9,265.00	4,481.56	03/2024 -	03/2024
	<u>Numaligarh Refinery Limited</u>						
59	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY [N16000379]	1/2019	12,366.00 -	18,968.00	6,125.60	10/2024 -	10/2024
60	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	5,608.65	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
61	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	954.95	03/2023 03/2024	03/2024
62	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	1,018.19	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
63	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	3,793.93	03/2022 12/2023	12/2023
64	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK [N16000470]	6/2022	4,144.41 -	4,144.41	-	10/2025 -	10/2025
65	KALOL REDEVELOPMENT PROJECT - [N16000481]	8/2022	1,487.41 -	1,487.41	374.18	03/2027 -	03/2027
66	PIPELINE REPLACEMENT PROJECT - VII - [N16000436]	1/2022	3,183.58 -	3,183.58	1,276.83	05/2024 -	05/2024
67	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,494.68	2,354.10	03/2022 12/2023	12/2023
68	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	25,464.83	06/2020 05/2024	05/2024
	Total		2,15,330.53 -	2,27,638.53	96,878.50		
	<u>POWER</u>						
	<u>Chenab Valley Power Projects [P] Limited</u>						
69	KWAR HE PROJECT - [N18000363]	5/2022	4,526.12 -	4,526.12	431.06	11/2026 -	11/2026
	<u>National Hydro-Electric Power Corporation</u>						
70	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	11,134.54	10,807.99	09/2009 03/2024	03/2024
71	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	21,247.54	18,903.19	09/2010 05/2025	05/2025
72	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH [N18000362]	2/2023	31,876.39 -	31,876.39	2,177.22	02/2032 -	02/2032
73	TEESTA VI HE PROJECT - [N18000325]	3/2019	5,748.04 -	5,748.04	2,643.25	03/2024 08/2026	08/2026
74	RATLE HE PROJECT - [N18000324]	2/2021	5,281.94 -	5,281.94	333.41	02/2026 05/2026	05/2026
	<u>National Thermal Power Corporation</u>						
75	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	1,267.99	09/2021 09/2024	09/2024
76	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320]	3/2022	1,352.71 -	1,352.71	91.14	08/2023 09/2024	09/2024
77	BHENSARA 320 MW - [N18000293]	1/2021	1,221.73 -	1,221.73	153.13	07/2022 03/2024	03/2024
78	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322]	3/2022	1,426.94 -	1,426.94	164.82	08/2023 09/2024	09/2024
79	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) - [N18000346]	9/2022	7,179.54 -	7,179.54	545.46	09/2024 09/2024	09/2024
80	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) - [N18000349]	11/2022	1,442.60 -	1,442.60	80.60	03/2024 06/2024	06/2024
81	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) - [N18000364]	8/2022	11,844.00 -	11,844.00	635.90	05/2027 -	05/2027

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
82	BHADLA-II 500MW SOLAR PV PROJECT - [N18000347	6/2022	2,598.92 -	2,598.92	1.75	03/2024 03/2024	03/2024
83	DAYAPAR WIND ENERGY PROJECT 200MW - [N18000345	7/2022	1,316.02 -	1,316.02	92.02	03/2025 03/2025	03/2025
84	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321	3/2022	1,409.52 -	1,409.52	160.80	08/2023 09/2024	09/2024
	<u>Power Grid Corporation Of India Limited</u>						
85	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B - [N18000352	3/2023	3,546.94 -	3,546.94	51.87	11/2024 -	11/2024
86	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART - [N18000356	3/2023	1,433.28 -	1,433.28	-	09/2024 -	09/2024
87	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000361	3/2023	2,820.99 -	2,820.99	-	03/2025 -	03/2025
88	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA - [N18000360	3/2023	1,167.55 -	1,167.55	-	03/2025 -	03/2025
	<u>Satluj Jal Vidyut Nigam Limited</u>						
89	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279	11/2020	1,810.56 -	1,810.56	1,172.83	01/2026 -	01/2026
90	SUNNI DAM HYDRO ELECTRIC PROJECT - [N18000344	1/2023	2,614.51 -	2,614.51	496.15	04/2028 -	04/2028
91	BIKANER SOLAR POWER PROJECT - [N18000335	4/2022	5,491.89 532.00	6,023.89	2,211.03	05/2024 -	05/2024
	Total		1,08,097.11 -	1,30,806.27	42,421.61		
	<u>RAILWAYS</u>						
	<u>East Coast Railway</u>						
92	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,361.74 -	2,361.74	967.78	03/2022 03/2026	03/2026
	<u>Metropolitan Rapid Transport Projects</u>						
93	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135	3/2013	4,874.58 -	10,442.41	8,008.94	03/2016 12/2023	12/2023
	<u>North East Frontier Railway</u>						
94	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	4/2003	4,454.17 -	14,322.79	13,763.33	03/2011 03/2025	03/2025
	<u>Northern Railway</u>						
95	CHANDIGARH-BADDI - [N22000467	4/2007	328.14 -	1,540.14	482.67	03/2023 06/2025	06/2025
	<u>Rail Vikas Nigam Ltd.</u>						
96	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.68	5,013.33	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
97	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501 <u>Southern Railway</u>	6/2016	3,677.76 -	3,677.76	4,306.50	12/2023 -	12/2023
98	TIDIVANAM-NAGARI (NL) - [N22000085	9/2006	582.83 -	3,620.28	758.81	- 12/2025	12/2025
99	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215 <u>West Central Railway</u>	4/2011	120.70 -	2,053.39	328.43	03/2019 12/2027	12/2027
100	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314 <u>Western Railway</u>	4/2001	424.60 -	3,032.46	2,080.00	03/2021 12/2025	12/2025
101	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	4/2008	3,503.69 -	6,021.00	2,919.74	03/2022 03/2026	03/2026
102	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,793.63	1,222.16	03/2022 12/2026	12/2026
	Total		24,921.73 -	52,414.28	39,851.69		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
103	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196	3/2017	1,049.51 -	1,049.51	293.67	08/2023 -	08/2023
104	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326	11/2020	4,997.04 -	4,997.04	1,340.72	09/2028 -	09/2028
105	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	2,199.36	09/2026 -	09/2026
106	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	-	12/2023 -	12/2023
	<u>National Highways Authority Of India</u>						
107	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER [N24000138	9/2010	946.00 -	1,046.56	827.99	06/2018 08/2023	08/2023
108	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR [N24000205	12/2011	1,047.00 -	1,047.00	1,855.00	06/2014 12/2023	12/2023
109	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,414.01	1,059.61	06/2018 08/2023	08/2023
110	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628	11/2016	1,064.88 -	1,021.00	800.70	07/2021 12/2023	12/2023
111	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697	8/2017	1,176.37 -	1,176.37	970.43	09/2020 06/2024	06/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
112	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708	9/2017	1,227.87 -	1,227.87	1,097.03	08/2020 06/2024	06/2024
113	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796	3/2018	1,117.84 -	1,117.84	699.89	12/2021 12/2023	12/2023
114	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY - [N24001511	3/2021	2,919.96 -	2,919.96	1,659.64	02/2024 08/2024	08/2024
115	4L OF KM 0.00 TO KM 42.00 OF OFDOBBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALO - [N24001509	1/2020	1,307.00 -	1,307.00	701.00	04/2021 12/2023	12/2023
116	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) - [N24001508	11/2022	1,450.00 -	1,450.00	153.30	10/2024 -	10/2024
117	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) - [N24001507	11/2022	1,124.00 -	1,124.00	116.71	05/2024 -	05/2024
118	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) - [N24001506	2/2022	2,747.00 -	2,747.00	544.65	02/2024 -	02/2024
119	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) - [N24001505	3/2022	1,549.02 -	1,549.02	290.04	03/2024 -	03/2024
120	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) - [N24001504	5/2022	1,260.00 -	1,260.00	295.36	05/2024 -	05/2024
121	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) - [N24001493	12/2022	1,749.86 -	1,749.86	228.15	12/2024 -	12/2024
122	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN - [N24001425	3/2021	1,100.88 -	1,100.88	561.13	11/2021 04/2024	04/2024
123	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP - [N24001534	12/2020	1,334.04 -	1,334.00	717.42	01/2024 03/2024	03/2024
124	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF - [N24001526	8/2021	1,377.79 -	1,377.79	678.86	10/2024 10/2024	10/2024
125	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 - [N24001522	1/2021	1,307.95 -	1,307.95	420.17	01/2024 -	01/2024
126	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 - [N24001519	9/2020	1,198.55 -	1,198.55	431.31	11/2023 -	11/2023
127	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 - [N24001520	11/2019	1,604.06 -	1,604.06	1,057.90	05/2024 -	05/2024
128	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 - [N24001518	11/2019	1,669.56 -	1,669.56	575.33	09/2023 -	09/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 - [N24001516]	9/2020	1,185.69 -	1,185.69	432.47	02/2024 -	02/2024
130	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V - [N24001514]	1/2021	1,060.29 -	1,060.29	745.17	01/2024 12/2023	12/2023
131	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 - [N24001515]	9/2020	1,542.02 -	1,542.02	363.32	02/2024 -	02/2024
132	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S - [N24001571]	11/2019	1,341.36 -	1,341.36	806.97	12/2023 -	12/2023
133	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 - [N24001649]	12/2021	3,273.61 -	3,273.61	75.26	02/2025 02/2025	02/2025
134	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR - [N24001557]	3/2022	1,636.15 -	1,636.15	281.01	11/2024 -	11/2024
135	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) - [N24001553]	3/2022	1,092.90 -	1,092.90	.03	02/2025 -	02/2025
136	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B - [N24001552]	10/2021	2,714.95 -	2,714.95	276.91	09/2024 -	09/2024
137	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 - [N24001551]	10/2021	3,044.02 -	3,044.02	214.97	09/2024 -	09/2024
138	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 - [N24001550]	9/2021	1,821.72 -	1,917.32	248.20	09/2024 -	09/2024
139	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 - [N24001547]	3/2022	1,909.98 -	1,909.98	22.90	01/2026 -	01/2026
140	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) - [N24001546]	1/2023	1,025.20 -	1,025.20	80.27	01/2025 -	01/2025
141	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F - [N24001633]	12/2020	1,430.88 -	1,430.88	872.76	12/2023 -	12/2023
142	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM - [N24001632]	1/2021	1,741.86 -	1,741.86	849.17	05/2024 -	05/2024
143	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD - [N24001631]	3/2021	1,525.31 -	1,525.31	132.46	10/2024 -	10/2024
144	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA - [N24001630]	7/2021	1,501.02 -	1,501.02	33.00	02/2025 -	02/2025
145	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 - [N24001628]	11/2021	2,155.95 -	2,155.95	793.18	02/2025 -	02/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
146	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K - [N24001627	7/2021	1,912.17 -	1,912.17	.26	02/2025 02/2025	02/2025
147	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 - [N24001625	1/2022	1,227.57 -	1,227.57	4.98	01/2025 -	01/2025
148	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX - [N24001622	7/2021	1,401.87 -	1,401.87	138.72	06/2024 06/2024	06/2024
149	4 LANE OF BILASPUR TO URGU PROJECT (KM 0.00 TO KM 70.2) OF NH-130A - [N24001611	4/2020	1,855.59 1,870.00	1,869.85	187.36	03/2024 -	03/2024
150	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659	2/2021	3,375.31 -	3,790.17	1,745.63	07/2024 -	07/2024
151	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658	1/2021	4,265.42 -	4,708.42	2,751.50	07/2024 -	07/2024
152	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC - [N24001657	6/2021	2,842.14 -	2,842.14	117.96	10/2024 10/2024	10/2024
153	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656	6/2021	2,595.00 -	3,994.60	2,696.56	03/2025 -	03/2025
154	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655	6/2021	3,606.00 -	3,923.82	2,789.91	02/2025 -	02/2025
155	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 - [N24001654	6/2021	2,641.37 -	2,641.37	138.53	03/2025 03/2025	03/2025
156	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH -66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 (- [N24001653	11/2021	3,565.82 -	3,064.11	1,570.57	04/2025 -	04/2025
157	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O - [N24001651	9/2021	2,878.97 -	2,878.97	154.45	09/2024 09/2024	09/2024
158	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE - [N24001648	8/2022	2,429.52 -	2,429.52	-	01/2026 -	01/2026
159	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM - [N24001694	2/2019	1,243.57 -	1,243.57	171.63	12/2023 -	12/2023
160	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 - [N24001693	9/2021	1,751.18 -	1,751.18	308.26	10/2024 -	10/2024
161	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN - [N24001691	10/2019	1,225.24 1,506.00	1,676.11	14.76	10/2021 01/2024	01/2024
162	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M - [N24001689	12/2020	1,745.00 -	1,279.00	822.13	09/2023 -	09/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
163	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE-7(ALONG WITH 0.700 - [N24001688	10/2020	3,184.00 -	3,184.00	799.94	09/2023 -	09/2023
164	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 - [N24001686	3/2021	1,065.06 1,445.00	1,577.92	26.31	03/2023 12/2023	12/2023
165	TUMKUR - NELAMANGALA(6L) - [N24001681	8/2022	2,032.15 1,351.00	2,032.15	29.46	08/2025 -	08/2025
166	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE [N24001680	3/2021	1,409.68 -	1,409.68	512.39	10/2024 -	10/2024
167	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 [N24001679	10/2022	1,479.30 -	1,479.30	86.76	04/2025 04/2025	04/2025
168	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 [N24001731	12/2021	2,470.64 -	2,335.00	139.84	05/2025 05/2025	05/2025
169	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) - [N24001730	12/2021	1,384.79 -	1,384.79	398.01	01/2025 -	01/2025
170	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO - [N24001728	12/2021	1,138.81 -	1,138.81	122.05	07/2025 -	07/2025
171	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721	2/2019	1,008.99 -	1,361.00	12.42	05/2024 -	05/2024
172	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 - [N24001720	10/2020	1,023.91 -	1,285.00	318.78	05/2024 -	05/2024
173	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719	2/2021	2,948.31 -	3,392.00	506.57	07/2024 -	07/2024
174	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K - [N24001717	11/2020	1,155.49 -	1,155.49	227.66	08/2024 -	08/2024
175	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - [N24001710	9/2020	2,334.68 2,335.00	2,335.00	714.12	03/2023 11/2023	11/2023
176	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 - [N24001708	9/2020	2,156.22 -	2,156.22	1,585.58	06/2024 -	06/2024
177	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 [N24001849	5/2022	1,063.72 -	1,063.72	170.67	07/2025 -	07/2025
178	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. - [N24001846	2/2023	1,200.42 -	1,200.42	56.79	10/2025 -	10/2025
179	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 - [N24001845	2/2023	1,253.24 -	1,253.24	68.47	10/2025 -	10/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
180	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. - [N24001844	12/2022	1,058.90 -	1,058.90	28.23	10/2025 -	10/2025
181	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 - [N24001830	6/2020	2,002.79 -	2,002.79	753.29	11/2023 -	11/2023
182	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM - [N24001825	7/2020	1,894.96 -	1,894.96	741.88	10/2023 -	10/2023
183	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE - [N24001822	12/2020	1,075.27 -	1,307.00	384.53	10/2024 -	10/2024
184	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP - [N24001821	11/2020	1,137.74 -	1,289.00	321.70	10/2024 -	10/2024
185	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) - [N24001820	2/2021	1,484.83 -	1,768.00	383.07	12/2024 -	12/2024
186	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) - [N24001819	3/2021	1,102.63 -	1,303.00	212.43	01/2025 -	01/2025
187	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) - [N24001818	2/2021	818.73 -	1,105.00	73.20	01/2025 -	01/2025
188	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA - [N24001815	12/2022	1,699.00 -	1,699.00	13.76	11/2024 -	11/2024
189	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A - [N24001813	7/2021	1,692.05 -	1,692.05	598.25	09/2024 -	09/2024
190	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812	3/2021	1,002.11 -	1,358.00	28.69	05/2024 -	05/2024
191	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR (NEAR RANITAL) TO KANGRA BYPASS SECTION OF - [N24001808	3/2021	1,322.95 -	1,442.47	498.17	12/2024 12/2024	12/2024
192	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796	3/2022	1,013.33 -	1,111.33	202.73	10/2024 10/2024	10/2024
193	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT - [N24001785	3/2022	1,373.06 -	1,373.06	202.38	06/2025 -	06/2025
194	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 - [N24001777	7/2020	2,171.80 -	2,171.80	958.13	10/2023 -	10/2023
195	DEVELOPMENT OF 6L UER II [PACKAGE - III] (NANGLOI - NAJAFGARH ROAD TILL SECTOR 24 DWARKA) FROM KM. 2 - [N24001776	7/2020	1,069.27 -	1,069.27	748.48	10/2023 -	10/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
196	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU - [N24001774	12/2020	1,524.03 -	1,524.03	890.82	11/2023 -	11/2023
197	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR - [N24001772	8/2021	1,147.26 -	1,147.26	49.00	03/2024 -	03/2024
198	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR - [N24001771	6/2020	1,479.22 -	1,479.22	667.80	12/2024 -	12/2024
199	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND - [N24001767	1/2021	1,001.69 -	1,001.69	29.75	04/2024 -	04/2024
200	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] - [N24001766	1/2022	1,011.29 -	1,011.29	-	10/2024 -	10/2024
201	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] - [N24001762	10/2021	1,146.22 -	1,146.22	444.64	01/2024 -	01/2024
202	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D - [N24001756	10/2020	1,352.56 -	1,352.56	178.51	10/2024 -	10/2024
203	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 - [N24001752	12/2018	2,375.87 -	2,566.80	2,299.14	02/2023 08/2023	08/2023
204	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA - [N24001748	3/2021	2,200.93 -	2,200.93	1,255.60	09/2024 -	09/2024
205	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 - [N24001747	3/2020	2,193.23 -	2,314.00	1,191.60	09/2024 -	09/2024
206	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N - [N24001745	12/2021	1,972.10 -	1,936.00	158.30	07/2025 07/2025	07/2025
207	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743	1/2018	1,916.38 -	2,078.00	1,158.54	02/2023 08/2023	08/2023
208	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739	10/2019	1,779.83 -	2,200.00	708.00	11/2023 -	11/2023
209	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K - [N24001736	1/2022	1,159.96 -	1,159.96	268.31	08/2024 -	08/2024
210	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL-LATIFPUR AT SAHARANPUR BYPASS FROM KM - [N24001735	3/2022	1,428.19 -	1,428.19	211.90	08/2024 -	08/2024
211	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. - [N24001734	3/2022	1,335.45 -	1,335.45	173.11	08/2024 -	08/2024
212	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K - [N24001733	3/2022	1,602.48 -	1,602.48	162.20	08/2024 -	08/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
213	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E - [N24001707	3/2021	1,143.46 1,143.00	1,143.00	268.70	01/2024 -	01/2024
214	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. - [N24001706	3/2021	1,097.18 1,097.00	1,097.00	329.35	01/2024 -	01/2024
215	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C - [N24001705	3/2022	1,485.66 -	1,485.66	-	03/2024 -	03/2024
216	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI - [N24001704	3/2021	1,020.84 -	1,020.84	84.78	03/2024 -	03/2024
217	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU - [N24001701	4/2022	1,769.50 -	1,769.50	-	04/2024 -	04/2024
218	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH - [N24001698	8/2022	1,198.02 -	1,198.02	-	08/2024 -	08/2024
219	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) - [N24001697	2/2023	1,358.00 -	1,358.00	.65	02/2025 -	02/2025
220	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 - [N24001696	2/2019	1,291.37 -	1,291.37	215.02	08/2023 -	08/2023
221	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE -- - [N24001678	8/2021	1,460.00 -	1,460.00	-	06/2024 -	06/2024
222	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 - [N24001676	12/2022	2,718.46 -	2,718.46	-	06/2025 -	06/2025
223	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 - [N24001675	11/2022	1,732.73 -	1,732.73	214.41	05/2025 -	05/2025
224	BANGALORE/TN BORDER TO HOSKOTE - [N24001674	2/2023	1,240.60 -	1,240.60	403.45	02/2025 -	02/2025
225	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE -- OD-3) - [N24001668	3/2021	1,249.00 -	1,249.00	-	04/2024 -	04/2024
226	6L GREENFIELD KALIAGURA -- BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG - [N24001667	9/2021	1,734.00 -	1,734.00	6.94	05/2024 -	05/2024
227	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 - [N24001665	12/2021	1,592.00 -	1,592.00	-	10/2024 -	10/2024
228	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 - [N24001661	10/2020	3,219.47 3,713.00	3,713.14	1,911.28	04/2024 05/2025	05/2025
229	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 - [N24001650	12/2021	3,635.64 -	3,635.64	75.12	01/2025 01/2025	01/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
230	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI - [N24001642	2/2021	1,474.77 -	1,474.77	146.71	08/2024 -	08/2024
231	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR - [N24001641	3/2021	1,641.75 -	1,641.75	69.48	10/2024 -	10/2024
232	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N - [N24001640	3/2021	1,229.38 -	1,229.38	499.62	11/2024 -	11/2024
233	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K - [N24001637	3/2021	1,754.84 -	1,754.84	758.50	01/2025 -	01/2025
234	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA – RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR - [N24001636	5/2021	1,368.91 -	1,368.91	63.88	12/2024 12/2024	12/2024
235	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O - [N24001635	3/2022	1,269.50 -	1,269.50	35.00	02/2025 -	02/2025
236	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO - [N24001634	1/2021	1,306.95 -	1,306.95	761.02	12/2023 -	12/2023
237	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S - [N24001610	1/2022	1,833.73 -	1,833.73	126.16	05/2024 05/2024	05/2024
238	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) - [N24001608	9/2021	2,208.68 -	2,208.68	56.93	07/2025 -	07/2025
239	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 - [N24001601	1/2019	1,051.69 -	1,051.69	349.20	01/2023 02/2024	02/2024
240	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) - [N24001598	1/2022	1,388.70 -	1,388.70	73.09	04/2025 -	04/2025
241	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595	8/2020	1,034.00 -	1,589.00	41.50	03/2024 -	03/2024
242	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA - [N24001593	11/2021	1,368.19 -	1,368.19	595.79	09/2024 -	09/2024
243	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - [N24001589	9/2020	755.26 -	1,039.00	385.01	03/2024 -	03/2024
244	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA - [N24001588	12/2021	1,470.73 -	1,470.73	179.31	01/2025 -	01/2025
245	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419	2/2021	1,269.96 -	1,269.96	241.67	04/2024 11/2024	11/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
246	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	357.25	04/2024 07/2024	07/2024
247	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	344.12	04/2024 07/2024	07/2024
248	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371	10/2019	1,101.99 -	1,101.99	563.96	08/2023 12/2024	12/2024
249	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,569.68	1,054.39	02/2021 08/2023	08/2023
250	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834	3/2018	1,161.39 -	1,404.00	396.76	10/2021 03/2024	03/2024
251	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714	12/2017	2,598.00 -	1,962.50	1,012.87	10/2024 10/2024	10/2024
252	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	9/2017	1,124.11 -	1,503.86	1,405.49	05/2020 11/2023	11/2023
253	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	1/2017	1,251.11 -	1,361.00	563.93	12/2020 10/2023	10/2023
254	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,679.45	08/2019 05/2024	05/2024
255	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	2,362.99	12/2018 07/2023	07/2023
256	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	1,381.45	939.15	04/2019 02/2024	02/2024
257	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 - [N24000564	3/2016	1,408.00 -	1,659.12	1,115.46	07/2020 02/2024	02/2024
	Total		2,61,878.43 -	2,71,114.51	80,876.98		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
258	SCREENING PLANT-III AT KIRANDUL - [N12000127	3/2021	2,092.97 -	2,221.86	704.51	08/2024 -	08/2024
	Total		2,092.97 -	2,221.86	704.51		
	<u>URBAN DEVELOPMENT</u>						
	<u>Bangalore Metro Rail Corporation Limited</u>						
259	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151	6/2021	14,788.10 -	14,788.10	2,424.04	06/2026 -	06/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Central Public Works Department</u>						
260	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	166.06	03/2022 06/2024	06/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
261	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	13,656.22	10,829.00	11/2021 12/2023	12/2023
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
262	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	1,271.31	02/2023 12/2026	12/2026
263	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	1,615.18	02/2023 12/2026	12/2026
	<u>Nagpur Metro Rail Corporation Ltd</u>						
264	NAGPUR METRO RAIL PROJECT PHASE II - [N28000155]	12/2022	6,708.00 -	6,708.00	-	12/2027 -	12/2027
	<u>National Capital Region Transport Corp</u>						
265	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	16,368.35	06/2025 -	06/2025
	Total		78,760.30 -	80,996.52	32,673.94		
	Grand Total		8,33,854.95	9,08,374.89	3,34,385.65		

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 6,840.00	7,670.00	09/2010 -	12/2024	119.64
	Total		3,492.00 .00 6,840.00	7,670.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 - 1,383.00	3,291.81	09/2021 -	12/2024	138.02
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2025	7.88
	Total		2,525.00 .00 2,525.00	4,523.81			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
4	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Neyveli Lignite Corporation</u>						
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 - 5,907.11	8,990.00	12/2015 -	02/2021	52.19
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	19,406.12	11/2021 -	12/2023	12.58
	Total		25,805.84 .00 25,805.84	33,542.60			
	<u>DPIIT</u>						
	<u>Iicc For Dpiit</u>						
7	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,401.00	12/2019 -	09/2023	13.16

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		4,773.00 .00 4,773.00	5,401.00			
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
8	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,735.25	1,900.00	10/2019 -	12/2023	55.84
	Total		1,219.21 .00 1,735.25	1,900.00			
	<u>PETROLEUM</u>						
	<u>Numaligarh Refinery Limited</u>						
9	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379	01/2019	12,366.00 - 12,366.00	18,968.00	10/2024 -	10/2024	53.39
	Total		12,366.00 .00 12,366.00	18,968.00			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
10	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 - 5,867.38	7,103.00	03/2013 -	12/2024	138.48
11	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 - 14,366.58	17,007.00	06/2019 -	06/2024	18.38
12	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 - 1,381.84	1,803.00	09/2019 -	09/2026	30.48
13	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	01/2016	10,598.98 - 10,598.98	10,998.00	11/2020 -	08/2023	3.76
	<u>Power Grid Corporation Of India Limited</u>						
14	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 - 4,754.42	9,129.32	12/2018 -	12/2024	92.02
15	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 - 5,111.33	6,700.00	12/2018 -	01/2024	31.08
16	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	08/2017	1,931.39 - 1,931.39	2,635.55	02/2020 -	03/2024	36.46

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Satluj Jal Vidyut Nigam Limited</u>						
17	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 - 648.33	1,272.29	12/2021 -	08/2023	96.24
18	BIKANER SOLAR POWER PROJECT - [N18000335]	04/2022	5,491.89 532.00 532.00	6,023.89	05/2024 -	05/2024	1,032.31
	<u>Thdc India Limited</u>						
19	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 - 1,657.00	4,825.60	02/2016 -	06/2024	191.23
	Total		48,920.24 532.00 46,849.25	67,497.65			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
20	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 - 3,168.29	3,445.48	03/2023 -	03/2024	8.75
21	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,805.17	03/2021 -	03/2026	111.54
22	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,384.72	03/2022 -	12/2024	8.85
23	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	6,409.38	03/2024 -	03/2024	76.71
24	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2026	10.94
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
25	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00 30,357.00	51,219.00	- - -	-	68.72
	<u>East Central Railways</u>						
26	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 967.29	1,110.00	03/2012 -	06/2023	241.82
27	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 - 1,470.50	1,700.00	- - -	03/2024	356.82
28	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 - 1,483.14	1,510.00	- - -	03/2024	358.42
	<u>East Coast Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
29	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 - 810.78	1,928.07	06/2021 -	03/2025	137.80
30	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 - 1,160.00	1,440.00	03/2020 -	03/2024	24.14
	<u>Eastern Railways</u>						
31	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2024	36.22
32	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
	<u>Indian Railway Construction Company Limited</u>						
33	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 - 3,055.00	3,438.39	09/2018 -	12/2023	12.55
	<u>Metropolitan Rapid Transport Projects</u>						
34	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 8,574.98	10,442.41	03/2016 -	12/2023	114.22
	<u>North Central Railway</u>						
35	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>						
36	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	9,362.06	03/2014 -	02/2024	291.15
37	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 12,264.15	14,322.79	03/2011 -	03/2025	221.56
38	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,304.62	03/2019 -	-	238.69
39	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 - 2,132.03	2,650.00	03/2019 -	03/2024	397.31
40	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 - 2,326.52	6,663.00	03/2015 -	03/2026	186.39
41	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 1,339.48	7,876.92	12/2015 -	12/2023	488.06
42	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 - 1,798.00	2,647.51	03/2019 -	01/2024	47.25

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
43	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	8,324.28	03/2021 -	-	818.33
44	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	1,187.49	03/2020 -	10/2024	186.25
45	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	4,059.65	03/2022 -	03/2026	81.86
<u>North Eastern Railway</u>							
46	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 - 1,295.42	2,560.00	03/2022 -	10/2023	97.62
47	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]	04/2016	1,177.96 - 1,177.96	1,500.95	12/2019 -	03/2024	27.42
<u>Northern Railway</u>							
48	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,017.96	07/2012 -	11/2024	348.44
<u>Rail Vikas Nigam Ltd.</u>							
49	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,834.54	03/2016 -	07/2025	65.94
50	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	03/2025	127.62
51	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,300.00	03/2023 -	03/2024	55.15
52	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	8,964.35	03/2016 -	03/2026	126.83
53	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
54	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
55	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,500.00	03/2022 -	12/2023	58.97
56	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,457.79	03/2019 -	03/2024	57.26
57	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	24,659.00	12/2024 -	03/2025	52.07

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
58	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
59	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,552.26	03/2019 -	05/2023	64.62
60	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	08/2023	102.11
	<u>South Central Railway</u>						
61	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,500.98	03/2009 -	03/2027	139.28
62	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 - 1,160.48	3,014.00	03/2010 -	03/2025	159.72
63	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2025	5.16
64	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 - 2,288.70	3,122.35	03/2021 -	03/2021	36.42
65	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,381.68	03/2000 -	03/2000	3,38,068.00
66	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	12/2025	7.06
	<u>South East Central Railway</u>						
67	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 - 2,753.05	3,544.25	03/2023 -	12/2024	85.71
68	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 229.00	1,096.00	12/2021 -	12/2025	378.60
69	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 - 1,370.00	1,680.00	12/2021 -	12/2024	22.63
	<u>South Western Railway</u>						
70	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 - 1,378.00	1,649.31	03/2016 -	03/2026	67.22
71	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	5,174.30	- -	03/2030	123.51
72	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,960.00	03/2019 -	12/2024	21.39

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Southern Railway</u>						
73	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 - 724.69	3,118.34	02/2019 -	03/2025	330.30
74	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	3,620.28	- -	12/2025	521.16
75	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,053.39	03/2019 -	12/2027	1,601.23
76	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,000.00	1,339.00	- -	03/2025	33.90
	<u>West Central Railway</u>						
77	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 2,909.99	3,032.46	03/2021 -	12/2025	614.19
78	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
79	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 - 582.13	1,247.64	03/2022 -	09/2024	114.32
	<u>Western Railway</u>						
80	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 - 5,677.80	6,021.00	03/2022 -	03/2026	71.85
81	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 - 321.03	1,095.12	03/2012 -	03/2024	244.12
	Total		1,26,718.29 33,985.00 1,68,590.41	2,89,900.39			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
82	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	02/2023	2.47
83	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	12/2023	.00
84	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 - 1,979.00	2,036.90	- -	05/2023	2.93
	<u>National Highways Authority Of India</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
85	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	06/2024	18.66
86	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507	12/2015	1,167.45 - 1,167.45	1,182.94	12/2019 -	12/2023	1.33
87	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 - 1,665.00	2,360.65	09/2016 -	12/2023	41.78
88	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 - 950.69	1,108.00	08/2019 -	05/2024	16.55
89	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 - 1,251.11	1,361.00	12/2020 -	10/2023	8.78
90	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	1,007.00	03/2020 -	07/2024	35.23
91	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 - 1,161.00	1,168.33	02/2022 -	10/2024	22.90
92	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736	01/2018	686.65 - 504.09	1,015.16	09/2020 -	12/2023	47.84
93	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835	03/2018	1,484.30 - 1,484.30	2,182.41	12/2020 -	05/2023	47.03
94	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 - 478.74	1,136.83	05/2021 -	01/2024	137.46
95	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431	03/2018	1,872.68 - 2,661.51	2,756.09	10/2020 -	09/2024	47.17
96	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533	11/2020	1,690.23 - 1,690.23	2,010.17	12/2023 -	03/2024	18.93
97	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - [N24001589	09/2020	755.26 - 755.26	1,039.00	03/2024 -	03/2024	37.57
98	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595	08/2020	1,034.00 - 1,034.00	1,589.00	03/2024 -	03/2024	53.68
99	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655	06/2021	3,606.00 - 3,606.00	3,923.82	02/2025 -	02/2025	8.81
100	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656	06/2021	2,595.00 - 2,595.00	3,994.60	03/2025 -	03/2025	53.93

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658	01/2021	4,265.42 - 4,265.42	4,708.42	07/2024 -	07/2024	10.39
102	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659	02/2021	3,375.31 - 3,375.31	3,790.17	07/2024 -	07/2024	12.29
103	TUMKUR - NELAMANGALA(6L) - [N24001681	08/2022	2,032.15 1,351.00 1,351.00	2,032.15	08/2025 -	08/2025	50.42
104	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A - [N24001690	01/2021	1,167.52 1,658.00 1,157.00	1,167.52	01/2023 -	06/2023	-29.58
105	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719	02/2021	2,948.31 - 2,948.31	3,392.00	07/2024 -	07/2024	15.05
106	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 - [N24001720	10/2020	1,023.91 - 1,023.91	1,285.00	05/2024 -	05/2024	25.50
107	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721	02/2019	1,008.99 - 1,008.99	1,361.00	05/2024 -	05/2024	34.89
108	REHABILITATION and UPGADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739	10/2019	1,779.83 - 1,779.83	2,200.00	11/2023 -	11/2023	23.61
109	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743	01/2018	1,916.38 - 1,916.38	2,078.00	02/2023 -	08/2023	8.43
110	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755	10/2019	1,936.68 - 1,936.68	2,458.03	03/2023 -	08/2023	26.92
111	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779	03/2018	2,507.00 - 2,507.00	3,030.73	09/2022 -	12/2023	20.89
112	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781	01/2018	2,067.67 - 2,067.67	2,160.00	10/2021 -	11/2023	4.47
113	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT - [N24001785	03/2022	1,373.06 - 1,085.00	1,373.06	06/2025 -	06/2025	.00
114	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786	03/2021	1,259.00 - 1,259.00	1,910.00	03/2024 -	12/2024	51.71
115	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788	07/2020	2,271.86 - 2,271.86	3,916.00	12/2023 -	06/2024	72.37
116	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789	07/2020	1,710.30 - 1,710.30	1,927.00	08/2023 -	06/2024	12.67

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
117	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796]	03/2022	1,013.33 - 1,013.33	1,111.33	10/2024 -	10/2024	9.67
118	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799]	02/2021	1,166.96 - 1,166.96	1,251.00	10/2023 -	04/2024	7.20
119	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805]	03/2018	1,169.04 - 1,169.04	1,693.95	03/2021 -	06/2023	44.90
120	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806]	03/2018	1,241.38 - 1,241.38	2,122.64	03/2023 -	06/2023	70.99
121	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812]	03/2021	1,002.11 - 1,247.93	1,358.00	05/2024 -	05/2024	35.51
122	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) - [N24001818]	02/2021	818.73 - 818.73	1,105.00	01/2025 -	01/2025	34.97
123	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) - [N24001819]	03/2021	1,102.63 - 1,102.63	1,303.00	01/2025 -	01/2025	18.17
124	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) - [N24001820]	02/2021	1,484.83 - 1,484.83	1,768.00	12/2024 -	12/2024	19.07
125	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP - [N24001821]	11/2020	1,137.74 - 1,137.74	1,289.00	10/2024 -	10/2024	13.29
126	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE - [N24001822]	12/2020	1,075.27 - 1,075.27	1,307.00	10/2024 -	10/2024	21.55
127	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP - [N24001824]	03/2020	1,863.09 - 1,863.09	2,238.00	01/2024 -	01/2024	20.12
128	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826]	02/2019	927.77 - 927.77	1,603.00	02/2022 -	10/2023	72.78
129	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838]	02/2021	922.50 - 922.50	1,128.68	03/2024 -	06/2024	22.35
	Total		76,156.65 5,799.00 76,200.88	94,147.52			
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
130	JAL MARG VIKAS PROJECT - [N25000072]	01/2018	5,369.18 - 4,633.10	5,362.27	03/2023 -	12/2026	-13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 1000 Crore and above					(July 2023)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,369.18 .00 4,633.10	5,362.27			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
131	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 - 10,773.00	12,925.22	12/2018 -	12/2023	19.98
	<u>Chennai Metro Rail Ltd</u>						
132	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 - 14,600.00	18,380.00	12/2015 -	12/2015	25.89
	<u>Delhi Metro Rail Corporation</u>						
133	DELHI MRTS PHASE-III - [N28000056]	09/2011	38,585.00 - 38,585.00	40,180.91	03/2016 -	08/2021	4.14
	<u>Kochi Metro Rail Corporation Ltd</u>						
134	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 - 5,181.79	6,218.14	07/2017 -	09/2020	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>						
135	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 - 23,136.00	37,276.00	03/2020 -	12/2023	61.12
	<u>Patna Metro Rail Corporation</u>						
136	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 - 13,365.77	13,925.50	06/2024 -	09/2024	4.19
	Total		1,05,641.56 .00 1,05,641.56	1,28,905.77			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
137	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 - 10,151.04	55,548.87	03/2020 -	03/2024	447.22
	Total		10,151.04 .00 10,151.04	55,548.87			
	Grand Total		4,23,138.01 40,316.00 4,66,111.33	7,13,367.88			

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	12320	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	03/2024	11459	99
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	12/2024	3492	171
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM	AAI	06/2017	12/2020	09/2023	255.68	33
6	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	AAI	02/2019	08/2022	12/2023	645.63	16
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	AAI	04/2020	03/2023	06/2024	611.8	15
8	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	12/2023	1405	16
9	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	09/2023	412.24	27
10	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	10/2023	177.1	44
11	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	12/2023	380.87	21
12	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	09/2023	456.86	36
13	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	AAI	05/2018	10/2022	12/2024	1216.9	26
14	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01	AAI	03/2021	12/2022	09/2023	242.14	9
15	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT.	AAI	11/2017	09/2021	06/2024	255.69	33
16	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	12/2025	2467	46
17	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	AAI	08/2018	10/2021	12/2023	951.28	26
18	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	08/2023	303.8	40
19	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2024	1383	39
20	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	03/2024	480.33	30
21	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF	AAI	03/2017	04/2021	09/2023	475.39	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	OLD TERMINAL BUILDING, MODIFICAT						
22	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	08/2023	458	41
23	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT.	AAI	08/2018	02/2021	09/2023	353.25	31
24	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2025	1142	48

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
25	SUBHADRA OCP	MCL	05/2021	03/2027	03/2029	1693.81	24
26	JAGANNATHPUR OC RCE (3.0 MTY)	SECL	07/2016	03/2020	03/2024	459.49	48
27	KULDA EXPANSION OCP- 15 MTY	MCL	06/2014	03/2018	03/2026	348.16	96
28	RCE OF KISTARAM OPENCAST PROJECT	SCCL	03/2017	03/2021	03/2024	164.04	36
29	RCE OF KALYANIKHANI OPENCAST PROJECT	SCCL	03/2016	03/2020	03/2024	384.32	48
30	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT	SCCL	11/2015	03/2023	03/2024	489.62	12
31	RCE OF INDARAM OPENCAST PROJECT	SCCL	08/2017	03/2021	03/2024	349.28	36
32	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	WCL	08/2016	03/2022	03/2025	319.76	36
33	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	03/2025	328	48
34	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2022	03/2024	413.84	24
35	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	08/2023	1255.17	17
36	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
37	SRP OC-II EXPANSION PROJECT	SCCL	11/2016	03/2018	03/2024	272.73	72
38	UKNI DEEP OC	WCL	11/2018	03/2021	03/2025	318.14	48
39	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	03/2024	252.71	36
40	BLOCK-B EXPANSION OPENCAST PROJECT	NCL	07/2019	03/2023	03/2025	998.71	24
41	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	10/2023	1783.09	31
42	TETARIAKHAR EXPANSION OCP	CCL	11/2019	03/2023	03/2025	243.52	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2025	316.1	60
44	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2030	916.24	84
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	SECL	08/2013	03/2023	03/2025	7612.33	24
46	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2025	510.85	108
47	GEVRA EXPANSION OCP (SECL) (35-70) MTY	SECL	06/2010	03/2023	03/2025	11816.4	24
48	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2025	339.88	138
49	MOONIDIH XV SEAM UG	BCCL	08/2011	03/2019	04/2025	1230.27	73
50	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2025	869.44	48
51	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	12/2023	17237	25
52	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2024	163.51	156
53	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2024	162.46	120
54	PELMA OCP(15.00MTY)	SECL	11/2014	03/2023	03/2031	1624.59	96
55	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2026	178.44	144
56	CHHAL OC SEAM -III (6.00 MTY)	SECL	12/2013	03/2022	03/2025	610.63	36
57	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2027	1458.17	147
58	MADANNAGAR OPENCAST PROJECT	SECL	10/2015	03/2024	03/2027	1875.32	36
59	HURA - C OC (3 MTY)	ECL	10/2015	03/2022	03/2029	359.69	84
60	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2024	555.52	36
61	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2026	479.15	84
62	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2026	1375.38	60
63	AMRITDHARA OC PROJECT	SECL	02/2015	03/2023	03/2027	481.6	48
64	AMERA OC RCE	SECL	02/2015	03/2018	03/2026	335.97	96
65	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	03/2024	357.8	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
66	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
67	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	11/2023	289.45	114
68	BATURA HIGHWALL PROJECT	SECL	07/2015	03/2022	03/2024	231.92	24
69	BINA KAKRI AMALGAMATION OCP 14 MTPA	NCL	08/2020	03/2024	03/2025	836.42	12
70	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	03/2024	243	71
71	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	12/2023	304.13	81
72	GODAVARIKHANI COAL MINE	SCCL	07/2019	03/2023	03/2024	438.98	12
73	NAINI COAL MINE	SCCL	03/2020	03/2024	03/2025	494.3	12
74	VENKATESH KHANI COAL MINE	SCCL	10/2020	03/2023	03/2025	484.51	24
75	RCE OF KAKATHIYAKHANI OC - 2 PROJECT	SCCL	08/2017	03/2020	03/2024	442.42	48

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
76	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD EDUCATION	09/2018	09/2020	08/2023	375	35
77	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD EDUCATION	07/2019	03/2021	03/2024	753.63	36
78	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH 6 PLUS 8 STOREYED	CPWD EDUCATION	03/2020	06/2020	07/2023	193.83	37
79	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD EDUCATION	02/2016	06/2017	10/2023	496.18	76
80	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD EDUCATION	01/2018	07/2020	09/2023	223.37	38
81	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	CPWD EDUCATION	01/2019	03/2022	03/2024	790.79	24
82	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	CPWD EDUCATION	03/2019	07/2022	09/2023	424.93	14
83	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	CPWD EDUCATION	01/2018	04/2023	12/2023	676	8
84	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	MITES OF HIGHER	09/2013	09/2014	12/2023	484.32	111
85	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	CPWD EDUCATION	09/2018	06/2022	01/2024	392.51	19
86	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	CPWD EDUCATION	09/2019	09/2022	12/2023	588.72	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
87	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	CPWD EDUCATION	10/2019	05/2022	03/2024	348.24	22
88	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	CPWD EDUCATION	05/2019	08/2021	11/2023	303.9	27

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
89	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	09/2023	4773	45

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD FOR HEALTH	12/2018	06/2021	08/2025	260	50
91	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	HITES	05/2017	05/2021	10/2023	875	29

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
92	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	12/2023	1219.21	50
93	NSG AT KOLKATA	CPWD FOR MHA	10/2014	04/2018	12/2024	162.88	80
94	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	CPWD FOR MHA	06/2019	07/2022	05/2024	277.35	22

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
95	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	NALCO	09/2017	06/2019	12/2023	166.62	54
96	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	09/2025	355	58
97	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	11/2023	534	46
98	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	03/2025	4103	47
99	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	CPWD	04/2019	04/2022	10/2025	255.37	42
100	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	05/2024	483	37

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
101	EXPANSION OF CRYOGENICS GROUP BY	IOCL	09/2021	10/2023	05/2024	378	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SETTING UP NEW MANUFACTURING FACILITY						
102	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	IOCL	06/2019	02/2028	08/2029	2996	18
103	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	IOCL	06/2019	02/2028	08/2029	439	18
104	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	01/2026	678	107
105	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	04/2024	20928	45
106	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	03/2024	823.27	12
107	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	12/2024	650.82	69
108	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	05/2024	34012	47
109	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	02/2022	12/2023	1945	22
110	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	03/2024	4497	63
111	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	10/2023	611	18
112	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	09/2023	909	32
113	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	12/2023	3228.8	21
114	HEERA REDEVELOPMENT - PHASE III	ONGC	06/2019	03/2022	12/2023	2494.68	21
115	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	04/2024	462.3	31
116	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	03/2024	3361	31
117	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	09/2023	278.6	27
118	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2024	371	18
119	CITY GAS DISTRIBUTION, JAMSHEDPUR	GAIL	10/2017	10/2022	12/2023	221.45	14
120	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2024	1740	42
121	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2025	1112	68
122	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	10/2023	206.63	44
123	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	08/2023	255.4	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
124	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	12/2023	199.36	38
125	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	GAIL	10/2017	10/2022	10/2023	359.25	12
126	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	GAIL	07/2017	07/2022	12/2023	182.2	17
127	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	GAIL	10/2017	10/2022	10/2023	226.45	12
128	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	09/2023	543.91	43
129	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	IOCL	03/2018	09/2022	12/2023	3712	15
130	BARAUNI-GUWAHATI PIPELINE	GAIL	06/2018	12/2021	10/2023	3308	22
131	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	11/2023	1636	39
132	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	03/2025	355	35
133	PARADIP SOMNATHPUR HALDIA PIPELINE	IOCL	10/2018	10/2021	07/2023	1297.5	21
134	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	12/2023	225.54	34
135	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	09/2023	161.59	45
136	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	11/2024	2915	143
137	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	GAIL	07/2017	07/2022	12/2023	243.53	17
138	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	IOCL	01/2020	07/2022	08/2023	202.16	13
139	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	IOCL	07/2020	01/2024	07/2025	13805	18
140	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI	BPCL	05/2022	03/2024	09/2024	423.39	6
141	RUF PITCH LOADING GANTRY	HPCL	10/2020	11/2022	04/2024	332.61	17
142	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	HPCL	03/2021	03/2024	03/2025	456	12
143	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	ONGC	08/2021	02/2023	07/2024	218.38	17
144	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2026	3190.69	97
145	DHAMRA HALDIA PIPELINE PROJECT	GAIL	03/2020	11/2022	06/2024	1030.65	19
146	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	IOCL	06/2020	01/2023	11/2023	1019	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
147	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	GAIL	06/2020	05/2023	10/2024	7844.25	17
148	MUZAFFARPUR-MOTIHARI LPG PIPELINE	IOCL	06/2020	08/2022	09/2023	403	13
149	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	IOCL	06/2020	12/2022	12/2023	1378	12
150	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFI	06/2020	06/2023	01/2024	200	7
151	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	HPCL	05/2020	02/2023	12/2023	1421.46	10
152	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	IOCL	10/2020	09/2023	12/2024	921	15
153	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1)	ONGC	11/2019	01/2024	12/2024	431	11
154	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	HPCL	12/2018	12/2022	12/2023	854	12
155	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha	BPCL	08/2019	08/2022	10/2024	1607	26
156	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2025	2281.94	31
157	PX-PTA REVAMP AT PANIPAT REFINERY	IOCL	08/2019	12/2021	12/2023	1255	24
158	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	10/2023	196.26	39
159	LPG BP PROJECT CHITTOOR	IOCL	07/2019	07/2022	02/2024	167	19
160	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	IOCL	11/2019	05/2023	11/2023	5251	6
161	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	12/2023	164.69	29
162	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	IOCL	01/2020	04/2023	12/2024	14810	20
163	SRIKAKULAM ANGUL PIPELINE PROJECT	GAIL	09/2019	07/2022	09/2024	2658.34	26
164	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	IOCL	10/2020	08/2023	03/2024	1614	7
165	CGD PROJECT AT REWA DISTRICT	IOCL	10/2018	02/2027	09/2028	177	19
166	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	IOCL	10/2018	08/2027	02/2029	176	18
167	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	IOCL	06/2019	08/2027	03/2030	2880	31
168	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	IOCL	06/2019	02/2028	08/2029	347	18
169	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG	BPCL	04/2021	06/2024	07/2025	1164.69	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	IMPORT TERMINAL						

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
170	TEESTA VI HE PROJECT	NHPC	03/2019	03/2024	08/2026	5748.04	29
171	NOKH PLOT-2 SOLAR PV PROJECT 245MW	NTPC	03/2022	08/2023	09/2024	1409.52	13
172	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA	PGCIL	01/2019	03/2022	09/2023	267.33	18
173	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	03/2021	12/2022	09/2023	353.85	9
174	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	03/2021	12/2022	07/2023	1340.81	7
175	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	06/2021	12/2022	03/2024	713.82	15
176	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	06/2021	12/2022	03/2024	1562	15
177	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	06/2021	12/2022	03/2024	1006	15
178	NORTH EASTERN REGION STRENGTHENING SCHEME - III	PGCIL	09/2015	12/2017	09/2023	167.31	69
179	NORTH EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2021	03/2023	02/2024	576.42	11
180	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	PGCIL	11/2018	11/2021	09/2023	241.38	22
181	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	08/2023	186.17	49
182	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	03/2024	1931.39	49
183	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B	PGCIL	07/2022	06/2023	06/2024	4546.26	12
184	SAMBHU KI BHURJ-II SOLAR 300MW	NTPC	03/2020	09/2021	09/2024	1782	36
185	ANTA SOLAR 90 MW	NTPC	01/2021	03/2022	03/2024	382.22	24
186	BHENSARA 320 MW	NTPC	01/2021	07/2022	03/2024	1221.73	20
187	CHHATTARGARH 150 MW	NTPC	02/2021	07/2022	03/2024	599.99	20
188	GUJARAT 200 MW (GUVNL TENDER)	NTPC	01/2021	07/2022	03/2024	842.27	20
189	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	NTPC	05/2021	09/2022	03/2024	674.92	18
190	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C	PGCIL	03/2019	03/2023	09/2023	1326	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
191	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION.	PGCIL	03/2022	03/2023	10/2023	176.22	7
192	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	02/2022	09/2023	03/2024	359.47	6
193	KALPI SOLAR POWER PROJECT	NHPC	07/2020	03/2022	03/2024	314.64	24
194	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2024	3919.59	174
195	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	05/2025	6285.33	176
196	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2024	2978.48	141
197	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	09/2026	8112.12	77
198	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	06/2024	14366.58	60
199	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	09/2026	1381.84	84
200	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	09/2023	197.4	66
201	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	06/2026	2491.58	156
202	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2024	1657	100
203	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2024	8692.97	153
204	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	08/2023	10598.98	33
205	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	08/2023	235.53	50
206	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2024	4754.42	72
207	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	01/2024	5111.33	61
208	NAITWAR MORI HEP	SJVN	10/2017	12/2021	08/2023	648.33	20
209	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
210	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	03/2025	18668	24
211	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	11/2023	529.68	60
212	KIRU HYDRO ELECTRIC PROJECT	CVPPPL	03/2019	08/2024	03/2026	4287.59	19
213	Bagodara Solar Power Project	SJVN	05/2021	10/2022	12/2023	339.35	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
214	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	05/2021	09/2022	12/2023	1184.88	15
215	NOKH PLOT-3 SOLAR PV PROJECT 245MW	NTPC	03/2022	08/2023	09/2024	1426.94	13
216	NOKH PLOT-1 SOLAR PV PROJECT 245MW	NTPC	03/2022	08/2023	09/2024	1352.71	13
217	DAYAPAR WIND ENERGY PROJECT 150MW	NTPC	11/2021	05/2023	06/2024	937.8	13

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
218	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	SER	04/2018	06/2022	02/2024	338	20
219	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	SER	04/2018	06/2022	03/2024	428.65	21
220	ANAND GODHRA DOUBLING PROJECT 79 KMS	WR	04/2017	03/2020	12/2024	692.25	57
221	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	36
222	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2025	229	48
223	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	10/2024	1973	43
224	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2024	1370	36
225	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2026	644.78	108
226	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2023	3055	63
227	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	10/2023	700	40
228	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	NCR	03/2018	03/2023	03/2026	4329.53	36
229	JHANSI BINA DOUBLING	NCR	09/2016	03/2021	12/2023	2001	33
230	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	12/2025	5200	69
231	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2024	1908.51	21
232	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	RVNL	02/2015	03/2022	10/2023	1700	19
233	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	08/2023	760	41
234	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	12/2024	150	92

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
235	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	NHSRCL	12/2015	12/2023	08/2027	108000	44
236	CHANDIGARH-BADDI	NR	04/2007	03/2023	06/2025	328.14	27
237	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	03/2024	1177.96	51
238	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	12/2024	744.04	45
239	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
240	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
241	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	10/2023	1295.42	19
242	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2023	1491.47	45
243	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2024	1763.93	55
244	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	12/2024	1272.19	33
245	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
246	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	03/2026	1876	36
247	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
248	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	12/2024	637.95	21
249	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	12/2025	3631	45
250	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	1547.38	24
251	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
252	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2025	701.61	76
253	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	02/2025	1172.92	74
254	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2026	2232.32	48
255	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	01/2025	2063.03	46
256	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	03/2024	1724.2	36
257	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2023	943.6	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
258	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2024	927.01	60
259	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
260	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
261	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2024	2478.23	27
262	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2024	582.13	30
263	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
264	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2027	1045.2	216
265	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2024	1188.91	60
266	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	12/2025	424.6	57
267	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	07/2023	133.41	172
268	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
269	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI- THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
270	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	02/2024	2393.47	119
271	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	180
272	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	07/2025	2913.51	112
273	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2026	3503.69	48
274	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	03/2024	3168.29	12
275	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2026	792.89	60
276	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	12/2024	540.02	33
277	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	03/2026	986.3	120
278	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2025	1856.95	24
279	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	12/2028	832.47	153
280	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
281	GADAG-WADI NL	SWR	04/2013	12/2018	03/2026	2841.84	87
282	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	05/2025	279.54	110
283	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2026	2271.5	60
284	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
285	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2026	2923.13	213
286	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2025	4454.17	168
287	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2023	495.74	126
288	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
289	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	132
290	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96
291	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	09/2023	410.08	55
292	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	11/2024	450	148
293	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	01/2024	2500	254
294	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2026	3951.98	120
295	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
296	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2024	318.24	144
297	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2024	295	61
298	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	12/2023	4874.58	93
299	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	12/2026	1347.26	57
300	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	12/2025	1640.04	45
301	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
302	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2025	548	60
303	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	01/2024	1798	58

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
304	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	12/2024	242.22	57
305	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	10/2024	414.84	55
306	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
307	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2024	1160	48
308	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	02/2024	600	47
309	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	12/2024	1614.59	69
310	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108
311	NIMACH BADI SADRI NEW LINE PROJECT	WR	04/2017	03/2022	03/2026	495.18	48
312	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	WR	04/2018	03/2024	12/2024	537.31	9
313	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	SER	03/2019	05/2023	02/2025	1866.31	21
314	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	08/2023	390.39	20

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
315	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	NHAI	03/2018	10/2020	09/2024	1872.68	47
316	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	MORTH	08/2020	11/2022	09/2023	196.23	10
317	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	MORTH	03/2019	11/2019	09/2023	297.55	46
318	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	MORTH	03/2018	06/2019	12/2023	159.97	54
319	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	MORTH	11/2016	03/2017	07/2023	314.9	76
320	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	MORTH	03/2015	01/2016	07/2023	159.12	90
321	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	MORTH	05/2018	05/2018	10/2023	171.6	65
322	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	MORTH	02/2017	05/2019	11/2024	157.32	66
323	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	MORTH	03/2018	06/2021	07/2023	351	25
324	CONSTRUCTION OF EIGHT LANE ACCESS	NHAI	10/2019	12/2021	08/2023	743.88	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA						
325	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	MORTH	03/2018	06/2021	09/2023	306.59	27
326	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	12/2023	624.98	86
327	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MORTH	03/2016	07/2016	12/2023	452.94	89
328	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MORTH	03/2017	01/2018	08/2023	423.79	67
329	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299.	MORTH	03/2018	01/2019	12/2023	349.03	59
330	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MORTH	11/2017	05/2019	08/2023	188.8	51
331	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2021	08/2023	990.97	20
332	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2022	08/2023	847	17
333	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	NHAI	03/2019	05/2020	08/2023	1047	39
334	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	NHAI	02/2019	03/2022	08/2023	996.27	17
335	WARDHA TO ARVI	MORTH	02/2018	04/2020	08/2023	313.58	40
336	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MORTH	11/2017	03/2018	08/2023	392.33	65
337	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	MORTH	08/2016	02/2017	12/2023	175.5	82
338	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	11/2022	08/2023	656.98	9
339	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	NHAI	12/2017	02/2022	08/2023	1094.97	18
340	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	12/2022	08/2023	217.96	8
341	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MORTH	01/2016	08/2016	03/2024	497.14	91
342	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MORTH	11/2015	06/2017	12/2023	335.32	78
343	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MORTH	01/2016	09/2016	12/2023	476.2	87
344	WARDHA TO HINGAGHAT	MORTH	01/2018	12/2019	08/2023	216.9	44
345	MHASWAD TO TEMBHURNI	MORTH	01/2017	07/2019	12/2023	488.6	53
346	KURUDWADI TO PANDHARPUR	MORTH	01/2017	07/2019	09/2023	307.63	50

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
347	PANDHARPUR TO SANGOLA	MoRTH	07/2017	07/2019	09/2023	218.38	50
348	MALEWADA TO CHIMUR	MoRTH	10/2016	06/2019	09/2023	322.55	51
349	PEN TO KHOPOLI	MoRTH	03/2018	03/2018	01/2024	301.39	70
350	PANCHARAL TO MANDANGHAR	MoRTH	07/2018	05/2020	12/2023	381.08	43
351	KOLHA TO NASRATPUR	MoRTH	04/2016	04/2019	12/2023	281.78	56
352	NASRATPUR TO BARASGAON	MoRTH	07/2016	09/2019	12/2023	406.54	51
353	NALDURG TO AKKALKOT	MoRTH	02/2018	12/2019	12/2023	274.5	48
354	KARWANDI TO RAJURI	MoRTH	03/2018	12/2019	11/2023	276.95	47
355	PALPHATA TO PHULAMBARI	MoRTH	03/2018	12/2019	09/2023	227.19	45
356	CHIKALI TO DHAD	MoRTH	03/2018	12/2019	03/2024	189.46	51
357	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	MoRTH	03/2018	12/2019	12/2023	336.21	48
358	WADIGODRI TO DHANGRIPIMPRI	MoRTH	03/2018	02/2020	09/2023	194.23	43
359	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	MoRTH	03/2018	02/2020	08/2023	217.14	42
360	PARBHANI TO GANGKHED	MoRTH	03/2018	12/2019	08/2023	238.19	44
361	LATUR TO PANGAON	MoRTH	03/2018	12/2019	08/2023	336.47	44
362	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	MoRTH	01/2018	05/2020	08/2023	283.15	39
363	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	MoRTH	03/2018	07/2020	06/2024	626.76	47
364	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365	MoRTH	03/2018	07/2019	07/2023	192.67	48
365	AKOLA TO AKOT	MoRTH	01/2017	06/2019	08/2023	313.95	50
366	AJANTHA TO BULDHANA	NHIDCL	02/2017	07/2019	09/2023	401	50
367	DIGRAS DARWAH KARANJA	MoRTH	01/2017	06/2019	12/2023	391.06	54
368	MORSHI TO ACHALPUR	MoRTH	01/2017	06/2019	12/2023	341.16	54
369	DAHEGAON TO KUHI	MoRTH	01/2017	06/2019	09/2023	228.89	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
370	AMDI TO SAONER	MoRTH	01/2017	06/2019	08/2023	396.91	50
371	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	NHAI	02/2019	01/2022	08/2023	594.75	19
372	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	MoRTH	08/2020	02/2021	08/2023	302.62	30
373	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	MoRTH	08/2020	03/2021	03/2024	222.61	36
374	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	MoRTH	03/2019	12/2019	11/2024	423.15	59
375	JORAM - KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	NHIDCL	08/2020	04/2022	07/2023	294.04	15
376	JORAM - KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	NHIDCL	08/2020	04/2022	07/2023	199.03	15
377	JORAM - KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	NHIDCL	08/2020	04/2022	11/2023	184.88	19
378	KHELLANI-KHANABAL PKG-2	NHIDCL	07/2021	02/2023	10/2024	512.43	20
379	KHELLANI-KHANABAL PKG-4	NHIDCL	07/2021	08/2023	09/2024	859.67	13
380	KHELLANI-KHANABAL PKG-5	NHIDCL	07/2021	02/2023	01/2024	497.09	11
381	GOHA-KHELLANI PKG-3	NHIDCL	02/2021	03/2023	10/2023	431.28	7
382	SENAPATI- IMPHAL PKG-5B	NHIDCL	03/2021	01/2023	05/2024	211.7	16
383	IMPHAL - KHONGSANG PKG-3	NHIDCL	07/2021	03/2023	09/2023	467	6
384	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II	MoRTH	08/2020	12/2022	09/2023	216.72	9
385	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I.	MoRTH	12/2020	10/2023	06/2024	379.23	8
386	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II.	MoRTH	12/2020	10/2023	06/2024	339.65	8
387	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI	NHAI	12/2020	01/2024	03/2025	989.66	14
388	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH-	NHAI	02/2021	04/2024	11/2024	1269.96	7
389	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD	MoRTH	07/2018	02/2024	09/2024	1948.25	7
390	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT	MoRTH	04/2021	09/2023	12/2024	309.48	15
391	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W	MoRTH	03/2021	09/2023	03/2024	185.09	6
392	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA	NHAI	03/2021	11/2021	04/2024	1100.88	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	TOWN						
393	4L OF ADDAHOLE TO BANTWAL CROSS SECTION	NHAI	03/2021	10/2021	09/2023	317.9	23
394	MARAM - PEREN PKG-3	NHIDCL	08/2021	05/2023	11/2023	467.41	6
395	KEIFANG - TUVAI PKG-1	NHIDCL	09/2021	05/2023	04/2024	492.94	11
396	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06	MoRTH	08/2020	02/2022	01/2024	302.88	23
397	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH	MoRTH	11/2021	02/2022	12/2023	223.35	22
398	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR	MoRTH	02/2022	08/2022	08/2024	184.15	24
399	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6	MoRTH	02/2022	08/2022	10/2024	191.33	26
400	MOPA AIRPORT	MoRTH	12/2021	04/2022	10/2023	1183.16	18
401	REPANPALLI TO SIRONCHA	MoRTH	03/2022	06/2022	06/2024	282.07	24
402	INTEGRATED STRUCTURE WITH DEVELOPMENT OF OTHER ALLIED STRUCTURES ON BOTH SIDES OF CHANDNI CHOWK JUNC	NHAI	02/2019	02/2022	08/2023	397.6	18
403	TUNNEL AT KHAMBATI Ghat SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0	NHAI	02/2019	02/2022	12/2023	493	22
404	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG)	NHAI	09/2021	09/2023	03/2024	624.45	6
405	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG)	NHAI	09/2021	09/2023	03/2024	667.66	6
406	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY	NHAI	03/2021	02/2024	08/2024	2919.96	6
407	CONSTRUCTION OF FOUR LANE PINJORE BYPASS FROM KM 0.00 TO 7.70 ON EPC MODE.	MoRTH	12/2016	12/2017	09/2023	170.27	69
408	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH	NHAI	08/2022	12/2022	06/2024	175	18
409	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA	NHAI	11/2019	10/2022	07/2023	1272.97	9
410	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF	NHAI	11/2021	07/2023	03/2024	1302.72	8
411	BALANCE WORK OF RANCHI-MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG-	NHAI	01/2019	12/2020	12/2023	466.55	36
412	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4.	NHAI	03/2018	12/2022	02/2024	440.16	14
413	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS	NHAI	02/2019	03/2021	09/2023	166.9	30
414	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH-383	NHAI	06/2018	03/2022	04/2024	1103.86	25
415	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A	NHAI	12/2018	03/2022	07/2024	854.94	28

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	(MADURAI RING ROAD)						
416	4L MISSING LINK (OF REWA BYPASS) FROM JN. WITH NH 30 NEAR BELA TO JN. WITH MPRDC RING ROAD (NEAR SIL	NHAI	02/2021	01/2023	12/2023	197.87	11
417	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI	NHAI	07/2019	10/2020	08/2023	157.05	34
418	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000	NHAI	08/2020	03/2022	08/2023	200	17
419	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR	NHAI	03/2020	06/2022	12/2023	210.37	18
420	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K	NHAI	03/2020	03/2023	10/2023	510.97	7
421	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION	NHAI	09/2020	01/2023	03/2025	688	26
422	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G	NHAI	09/2020	03/2023	12/2023	939.43	9
423	2ND FLYOVER (LCW) PARALLEL TO EXISTING FLYOVER IN KISHANGANJ TOWN.	NHAI	03/2018	06/2020	08/2023	150.21	38
424	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091	NHAI	10/2018	02/2021	12/2023	707.9	34
425	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48	NHAI	01/2019	05/2021	02/2024	654.26	33
426	4L OF SHAMLI TO MUZAFFARNAGAR SECTION OF NH-709AD, PKG-II	NHAI	06/2020	10/2022	07/2023	1621.07	9
427	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER	NHAI	01/2018	02/2023	08/2023	1916.38	6
428	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II	NHAI	05/2019	11/2022	12/2023	779.17	13
429	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA	NHAI	08/2018	12/2021	12/2024	622.04	36
430	BALANCE 4 LANING WORK OF RAIGANJ DALKHOLA SECTION OF NH34 FROM KM 398.000 TO KM 452.750 (PACKAGE V)	NHAI	12/2018	09/2021	12/2023	1548.07	27
431	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272	NHAI	12/2018	02/2023	08/2023	2375.87	6
432	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF	NHAI	08/2019	04/2023	11/2023	323.51	7
433	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21)	NHAI	03/2018	09/2022	12/2023	2507	15
434	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. 0	NHAI	01/2018	10/2021	11/2023	2067.67	25
435	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A	NHAI	11/2018	09/2021	08/2023	2312.26	23
436	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN	NHAI	11/2018	09/2021	08/2023	2252.75	23
437	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA	NHAI	11/2018	09/2021	08/2023	1935.61	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
438	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II)	NHAI	03/2021	09/2022	12/2023	536.03	15
439	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III)	NHAI	03/2021	09/2022	12/2023	485.75	15
440	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J	NHAI	02/2021	10/2023	04/2024	1166.96	6
441	4L OF AKOLA - MEDSHI FROM KM. 0.00 TO KM. 47.70 OF NH-161 INCLUDING BYPASSES AT PATUR AND MEDSHI	NHAI	12/2019	11/2022	09/2023	1393.95	10
442	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794)	NHAI	12/2019	09/2022	11/2023	1654.07	14
443	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81	NHAI	02/2019	02/2022	10/2023	927.77	20
444	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66	NHAI	10/2020	04/2024	05/2025	3219.47	13
445	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100	NHAI	03/2021	03/2023	12/2023	1065.06	9
446	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN	NHAI	10/2019	10/2021	01/2024	1225.24	27
447	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU	NHAI	03/2021	03/2024	12/2024	1259	9
448	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU	NHAI	07/2020	12/2023	06/2024	2271.86	6
449	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA	NHAI	07/2020	08/2023	06/2024	1710.3	10
450	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG II) [KURANKHED TO SHELAD FROM KM. 220.00 TO KM. 270.00]	NHAI	11/2019	02/2023	09/2023	633.7	7
451	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI-MOTIHARI-RAXAUL SECTION OF NH-28A FRO	NHAI	12/2018	10/2020	09/2023	333.6	35
452	BALANCE WORK OF 2L PS OF TINDIVANAM KRISHNAGIRI FROM KM 37.600 TO 219.782	NHAI	05/2019	07/2021	08/2023	602.57	25
453	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE	NHAI	03/2022	03/2023	10/2023	162.73	7
454	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	02/2022	10/2024	950.64	32
455	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	09/2020	06/2024	1176.37	45
456	JUNAGADH BYPASS	NHAI	10/2017	04/2021	08/2023	232.49	28
457	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	05/2020	11/2023	1124.11	42
458	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	08/2020	06/2024	1227.87	46
459	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	MORTH	01/2014	11/2014	05/2024	195.45	114
460	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	MORTH	12/2019	04/2022	02/2024	282.41	22

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
461	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	MoRTH	10/2014	02/2017	10/2023	295.47	80
462	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MoRTH	03/2015	11/2015	09/2023	165.67	94
463	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	12/2023	511.83	76
464	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	07/2024	294.17	102
465	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	12/2021	08/2023	252	20
466	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	NHAI	03/2018	10/2022	07/2023	505.35	9
467	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	NHAI	03/2018	11/2020	07/2023	628.71	32
468	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	NHAI	03/2018	04/2021	09/2023	806.11	29
469	SIX / FOUR LANING OF NH 5 (NEW NH 16) FROM PUINTOLA TO TANGI (KM. 284.000 TO KM. 355.000)	NHAI	03/2018	12/2020	10/2023	538.41	34
470	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	MoRTH	12/2017	11/2020	12/2023	867.97	37
471	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	MoRTH	10/2018	11/2020	09/2023	400.76	34
472	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	MoRTH	08/2017	09/2020	10/2023	962.43	37
473	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	NHIDCL	08/2020	04/2022	05/2024	301.06	25
474	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	NHIDCL	09/2020	05/2022	03/2024	353.9	22
475	4-LANING OF HAPACHARA - TULUNGIA SECTION	NHIDCL	03/2020	12/2022	08/2023	220.2	8
476	2-LANING FROM MANU-SIMLUNG (PKG I)	NHIDCL	03/2020	01/2022	08/2023	247.76	19
477	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	NHIDCL	08/2020	04/2022	07/2024	208.84	27
478	2-LANING FROM MANU-SIMLUNG (PKG III)	NHIDCL	06/2020	01/2022	07/2023	347.36	18
479	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	NHIDCL	03/2019	04/2022	01/2024	402.94	21
480	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	NHIDCL	08/2020	04/2023	12/2023	295.97	8
481	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	NHIDCL	03/2020	06/2022	12/2023	242.97	18
482	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	NHIDCL	09/2020	10/2022	07/2024	277.44	21
483	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	NHIDCL	08/2020	04/2022	03/2024	202.36	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
484	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	NHIDCL	09/2020	04/2022	08/2023	315.63	16
485	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	NHIDCL	09/2020	04/2022	07/2023	257.15	15
486	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	NHIDCL	08/2020	04/2023	01/2024	311	9
487	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	NHIDCL	07/2020	04/2023	10/2023	345.38	6
488	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	NHIDCL	06/2020	01/2022	01/2024	277.5	24
489	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM 20.300 OF 7.450 KM LENGTH ON GOHA-KHEL	NHIDCL	07/2020	04/2022	03/2024	228.39	23
490	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	NHIDCL	03/2020	07/2022	07/2023	154.51	12
491	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	NHIDCL	07/2020	04/2022	01/2024	210.79	21
492	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	NHIDCL	03/2020	07/2022	08/2023	178.43	13
493	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	NHIDCL	08/2020	04/2022	08/2023	379.39	16
494	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	NHIDCL	09/2020	10/2022	10/2023	275.02	12
495	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	NHIDCL	03/2020	07/2022	12/2023	206.88	17
496	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	NHIDCL	03/2020	06/2022	08/2023	320.97	14
497	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	NHIDCL	03/2020	07/2022	12/2023	292.24	17
498	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	NHIDCL	03/2020	06/2022	12/2023	355.79	18
499	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	NHIDCL	03/2020	07/2022	10/2023	281.78	15
500	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	NHIDCL	03/2020	06/2022	12/2023	361.53	18
501	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	NHIDCL	04/2020	12/2021	03/2024	330.8	27
502	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	NHAI	09/2018	01/2020	07/2024	597.67	54
503	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	NHAI	10/2013	12/2020	12/2023	649.9	36
504	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	NHAI	10/2013	11/2020	12/2023	446.97	37
505	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	NHAI	10/2013	11/2020	12/2023	464.09	37
506	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	NHAI	10/2020	03/2023	01/2024	724.6	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
507	KAILASHAHAR TO KHOWAI PKG-4	NHIDCL	11/2020	06/2022	10/2023	159.13	16
508	TADADEGE - HENKAR	NHIDCL	02/2021	03/2023	06/2024	550.45	15
509	LADDA - BASAI	NHIDCL	02/2021	04/2023	02/2024	445.96	10
510	2-LANING FROM JOLAIBARI - BELONIA	NHIDCL	06/2020	01/2022	12/2023	201.99	23
511	DOGINALA - GAU	NHIDCL	12/2020	09/2022	08/2023	242.3	11
512	DEMBUEN - BRUNI	NHIDCL	12/2020	03/2023	11/2023	606.63	8
513	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	NHIDCL	09/2020	05/2022	04/2024	183.31	23
514	KHELLANI-KHANABAL PKG-1	NHIDCL	03/2021	09/2022	10/2023	486.45	13
515	KHELLANI-KHANABAL PKG-6	NHIDCL	02/2021	09/2022	08/2023	285.28	11
516	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	NHIDCL	09/2020	05/2023	08/2024	262.84	15
517	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	NHIDCL	08/2020	05/2022	11/2024	292.8	30
518	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	NHIDCL	03/2020	06/2022	03/2024	261.13	21
519	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	NHIDCL	10/2020	11/2023	05/2024	493.42	6
520	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	NHIDCL	10/2020	12/2023	09/2024	816.79	9
521	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	NHIDCL	10/2020	04/2022	01/2024	157.86	21
522	KHELLANI-KHANABAL PKG-3	NHIDCL	03/2021	12/2022	11/2023	398.51	11
523	KARGIL-ZANSKR PACKAGE-1	NHIDCL	03/2021	01/2023	11/2023	384.23	10
524	KARGIL-ZANSKR PACKAGE-2	NHIDCL	03/2021	01/2023	11/2023	404.89	10
525	KARGIL-ZANSKR PACKAGE-3	NHIDCL	08/2020	01/2023	10/2023	381.01	9
526	KARGIL-ZANSKR PACKAGE-8	NHIDCL	03/2021	01/2023	08/2023	398.37	7
527	MARIAM - PEREN PKG-1A	NHIDCL	02/2021	12/2022	10/2023	226.32	10
528	MARIAM - PEREN (PKG 1B)	NHIDCL	02/2021	12/2022	10/2023	188.36	10
529	MARIAM - PEREN PKG-2B	NHIDCL	02/2021	12/2022	08/2023	232.26	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
530	IMPHAL - MOREH PACKAGE- 3	NHIDCL	03/2021	12/2022	08/2023	259.31	8
531	IMPHAL - KHONGSANG PKG-2	NHIDCL	03/2021	12/2022	11/2023	195.14	11
532	DULTE- KWALKULH - CHAMPAI PKG.1	NHIDCL	03/2021	12/2022	11/2023	374.39	11
533	DULTE- KWALKULH - CHAMPAI PKG.2	NHIDCL	03/2021	12/2022	01/2024	233.25	13
534	DULTE- KWALKULH - CHAMPAI PKG.3	NHIDCL	03/2021	06/2023	01/2024	674.71	7
535	TLABUNG - LUNGLEI PKG-A	NHIDCL	03/2021	12/2022	12/2024	698.44	24
536	TLABUNG - LUNGLEI PKG-B	NHIDCL	03/2021	01/2023	12/2024	740.58	23
537	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	NHIDCL	03/2021	12/2022	11/2023	260.21	11
538	MANU-SIMLUNG (PKG 4)	NHIDCL	03/2021	12/2022	11/2023	354.79	11
539	DABOKA KATHKATI PACKAGE-5	NHIDCL	03/2021	01/2023	10/2023	288.85	9
540	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	NHIDCL	03/2021	12/2022	10/2023	636.42	10
541	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK	MoRTH	02/2017	08/2017	08/2023	294.28	72
542	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	NHAI	10/2019	08/2023	12/2024	1101.99	16
543	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	NHAI	02/2019	01/2022	08/2023	731.89	19
544	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	NHAI	11/2019	01/2024	07/2024	1601.1	6
545	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	NHAI	11/2019	07/2021	07/2023	716	24
546	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI	NHAI	09/2021	09/2022	09/2024	517.05	24
547	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP	NHAI	09/2021	09/2022	09/2024	622	24
548	4L OF KM 0.00 TO KM 42.00 OF OFDOBBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALO	NHAI	01/2020	04/2021	12/2023	1307	32
549	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352	NHAI	07/2020	07/2022	11/2023	899	16
550	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI	NHAI	07/2020	07/2022	11/2023	817	16
551	4 LANING OF PATHRAPALI TO KATGHORA FROM KM.53.300 TO KM.92.600	NHAI	11/2019	12/2022	08/2023	865.1	8
552	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209	NHAI	01/2019	01/2023	02/2024	1051.69	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
553	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83)	NHAI	01/2019	12/2022	02/2024	1409.38	14
554	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83)	NHAI	01/2019	10/2022	12/2023	1518.53	14
555	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S	NHAI	09/2020	03/2023	11/2023	2334.68	8
556	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16	NHAI	02/2019	03/2023	03/2024	757.45	12
557	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	06/2024	2848	123
558	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	12/2023	998.79	124
559	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	12/2023	1047	114
560	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	07/2023	1655.01	83
561	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	09/2016	12/2023	1665	87
562	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0)	NHAI	11/2019	02/2021	08/2023	1226.88	30
563	8L OF GUDUVANCHERY (KM 38.00) - MARAIMALAI NAGAR (KM 42.00) - SINGAPERUMAL KOIL (47.00) - CHETTIPU	NHAI	12/2020	02/2022	08/2023	230.69	18
564	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	08/2023	946	62
565	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	11/2023	649.5	56
566	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	08/2023	1083	62
567	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	NHAI	12/2015	04/2019	03/2024	1041.1	59
568	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	07/2023	2136.97	55
569	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	08/2023	322.09	64
570	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	NHAI	12/2015	12/2019	12/2023	1167.45	48
571	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM	NHAI	03/2016	10/2019	07/2023	1396.74	45
572	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	07/2023	1587.49	51
573	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	12/2024	701.4	69
574	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	02/2024	899	58
575	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2023	546	53

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
576	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	NHAI	03/2016	10/2019	03/2024	720	53
577	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	03/2024	591.66	56
578	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00	NHAI	03/2016	07/2020	02/2024	1408	43
579	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	07/2023	804.97	61
580	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	NHAI	05/2016	08/2019	08/2023	998.18	48
581	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	NHAI	05/2016	09/2019	10/2023	723.64	49
582	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	NHAI	05/2016	08/2019	10/2023	763.08	50
583	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MoRTH	02/2016	05/2016	07/2023	178.85	86
584	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MoRTH	01/2014	10/2016	11/2023	1408.85	85
585	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	NHAI	07/2016	07/2020	12/2023	829.97	41
586	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	05/2025	1167.42	74
587	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	NHAI	09/2016	07/2020	06/2024	1273.71	47
588	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	12/2023	2510.04	52
589	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	05/2024	950.69	57
590	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	NHAI	11/2016	07/2021	12/2023	1064.88	29
591	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	07/2023	400.25	52
592	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	12/2023	446.17	57
593	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	12/2020	10/2023	1251.11	34
594	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	05/2024	848.45	50
595	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	07/2024	744.64	52
596	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	08/2023	754.54	41
597	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2024	672.89	48
598	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH	NHIDCL	02/2017	04/2022	07/2023	167.28	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	713) ON EPC BASIS FROM EXI						
599	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	09/2019	09/2023	373.07	48
600	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2019	09/2023	396.52	49
601	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	09/2023	894	41
602	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	03/2024	2485.93	45
603	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	NHAI	12/2017	02/2020	10/2023	950.27	44
604	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWA (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	NHAI	12/2017	12/2020	02/2024	1308.73	38
605	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	NHAI	12/2017	07/2020	12/2023	686.65	41
606	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	NHAI	12/2017	07/2021	08/2023	1471.75	25
607	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	NHAI	12/2017	06/2019	08/2023	328.67	50
608	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	NHAI	01/2018	12/2021	03/2024	573.7	27
609	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	NHAI	01/2018	11/2021	11/2023	1155.16	24
610	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	NHAI	01/2018	08/2022	03/2024	633.68	19
611	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	NHAI	01/2018	08/2021	10/2023	614.48	26
612	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	NHAI	01/2018	09/2020	12/2023	686.65	39
613	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	NHAI	01/2018	06/2021	12/2023	503.88	30
614	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	11/2020	12/2023	274.31	37
615	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	11/2020	04/2024	403.36	41
616	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	11/2020	04/2024	417.24	41
617	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	01/2022	03/2024	262.97	26
618	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	NHIDCL	03/2017	12/2019	01/2024	409.85	49
619	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	09/2020	06/2024	391	45
620	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) 0	NHIDCL	03/2018	09/2020	01/2024	234.27	40

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
621	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	NHIDCL	02/2017	09/2020	09/2023	387	36
622	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	11/2022	12/2023	500.09	13
623	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2022	08/2023	285.68	11
624	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	12/2021	12/2023	215.79	24
625	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	10/2022	10/2023	272.89	12
626	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	NHIDCL	03/2018	09/2018	03/2024	323.98	66
627	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	NHIDCL	03/2017	04/2022	12/2023	375.8	20
628	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	NHIDCL	11/2017	10/2020	08/2023	290.05	34
629	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	NHIDCL	04/2017	09/2021	07/2023	553.51	22
630	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	MORTH	05/2018	05/2020	12/2023	248	43
631	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	02/2023	09/2024	1424.77	19
632	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU	NHAI	03/2018	09/2022	03/2024	841.57	18
633	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	NHAI	02/2018	04/2021	08/2023	741.86	28
634	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	NHAI	03/2018	12/2021	12/2023	1117.84	24
635	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	NHAI	03/2018	11/2021	03/2024	2140.93	28
636	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	NHAI	03/2018	12/2020	12/2024	314.43	48
637	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	NHAI	03/2018	02/2023	08/2023	828.29	6
638	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	NHAI	03/2018	10/2021	03/2024	1161.39	29
639	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	NHAI	03/2018	07/2021	09/2024	1162.92	38
640	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	NHAI	03/2018	05/2021	01/2024	478.74	32
641	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	NHIDCL	03/2018	07/2022	05/2024	1383.78	22
642	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	01/2024	519.09	9
643	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND	NHIDCL	04/2017	07/2023	02/2024	640.07	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	GEOMETRIC IMPROVEMENTS FRO						
644	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	06/2023	01/2024	642.96	7
645	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	01/2024	473.18	9
646	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	01/2024	537.82	9
647	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	06/2023	02/2024	518.53	8
648	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2023	05/2024	428.11	8
649	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOR ROAD SECTION OF NH-144A FROM GANESH VIHA	NHIDCL	03/2018	07/2021	08/2023	253.44	25
650	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MoRTH	03/2016	11/2018	12/2023	271.17	61
651	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	12/2023	169.63	69
652	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	12/2023	426.18	39
653	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	MoRTH	03/2018	10/2020	03/2024	254.3	41
654	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	09/2023	06/2024	160.27	9
655	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	09/2021	02/2024	236.78	29
656	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	08/2023	205.05	77
657	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	12/2023	214.69	69
658	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	08/2023	249.05	61
659	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	NHIDCL	10/2017	06/2020	12/2023	818	42
660	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	NHIDCL	03/2019	03/2022	10/2023	306.28	19
661	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	12/2023	1069.59	50
662	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	11/2023	170.57	36
663	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	MoRTH	08/2016	02/2017	10/2023	287.7	80
664	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	MoRTH	09/2016	02/2017	09/2023	295.67	79
665	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (MAYAGARH TO KHURDA) IN THE STATE OF ODISHA	MoRTH	12/2016	08/2018	10/2023	223.5	62
666	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN	MoRTH	12/2016	04/2018	09/2023	206.88	65

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	THE STATE OF ODISHA						
667	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	MoRTH	03/2018	08/2018	09/2023	214.23	61
668	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	MoRTH	03/2018	08/2018	09/2023	199.16	61
669	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	NHIDCL	12/2016	01/2020	08/2023	200.44	43
670	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	NHIDCL	03/2017	03/2022	03/2024	1718.59	24
671	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	NHIDCL	09/2016	12/2019	09/2023	568.92	45
672	WADI TO ASOLA	MoRTH	01/2017	09/2019	08/2023	363.82	47
673	WAKAN PALI KHOPOLI	MoRTH	01/2017	05/2019	10/2023	376.19	53
674	MAHAD TO RAIGAD FORT	MoRTH	07/2018	05/2020	12/2023	237.4	43
675	SHIROD SHAHPURER TO NANDED	MoRTH	01/2017	07/2019	08/2023	211.34	49
676	RALEGAON TO RAMTIRTH	MoRTH	01/2017	07/2019	08/2023	210.81	49
677	MEHKAR TO AJISPUR	MoRTH	01/2017	07/2019	08/2023	232.77	49
678	KARAD TO VITA	MoRTH	01/2018	12/2019	10/2023	344.85	46
679	VITA TO NAGAJ	MoRTH	03/2018	12/2019	12/2023	304.58	48
680	JALKOT TO TOGRI	MoRTH	07/2018	08/2020	12/2023	299.92	40
681	KOTHARI TO DHANORA	MoRTH	09/2018	08/2020	09/2023	301.38	37
682	OSMANNAGAR TO KUNDRAL	MoRTH	09/2017	08/2020	12/2023	344.25	40
683	PUNE TO MALE VILLAGE	MoRTH	03/2018	12/2019	08/2023	228.31	44
684	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	MoRTH	03/2018	12/2019	08/2023	256.15	44
685	HIMAYATNAGAR TO PHULSAWANGI	MoRTH	03/2018	12/2019	09/2023	294.87	45
686	JALGAON TO NANDURA	MoRTH	03/2018	12/2019	09/2023	177.84	45
687	SELDOH TO PANVAR	MoRTH	07/2018	05/2020	03/2024	404.33	46
688	BARASGAON TO RAHATEE	MoRTH	07/2016	09/2018	09/2023	289.11	60
689	SAKOLI TO BHANDARA	MoRTH	01/2017	06/2019	09/2023	362.96	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
690	PAITHAN TO SHIRUR	MoRTH	03/2017	06/2019	03/2024	341.8	57
691	SHIRUR TO KHARDA	MoRTH	02/2017	06/2019	03/2024	381.77	57
692	SILLOD TO FARDAPUR	MoRTH	02/2017	06/2019	10/2023	337.46	52
693	KUMBHARI PHTA TO DEULGAON RAJA	MoRTH	02/2017	06/2019	12/2023	406.51	54
694	KANTE TO WAKED	MoRTH	03/2016	11/2019	12/2023	1230.02	49
695	PARLI PIMPLA DAHIGUDA	MoRTH	02/2017	06/2019	08/2023	205.72	50
696	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO	MoRTH	03/2020	10/2022	12/2023	255.23	14
697	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	NHAI	03/2018	01/2022	01/2024	2120.4	24
698	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER	NHAI	03/2018	11/2021	11/2023	1294.47	24
699	JORAM - KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	NHIDCL	08/2020	04/2022	07/2023	228.71	15
700	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	NHAI	03/2018	11/2021	11/2023	998.7	24

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
701	JAL MARG VIKAS PROJECT	IWAI	01/2018	03/2023	12/2026	5369.18	45

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
702	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	SAIL	11/2020	12/2023	04/2025	542.24	16
703	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	SAIL	11/2020	05/2023	02/2024	377.18	9
704	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	09/2025	1034.01	95
705	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	08/2023	15525	99
706	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	NMDC	11/2015	06/2023	05/2025	2907	23

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
707	SETTING UP PHYSICAL INFRASTRUCTURE	CPWD FOR TELECOM	10/2014	03/2018	12/2023	248.2	69

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
708	FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	09/2023	13334	98
709	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	BSNL	03/2020	06/2021	12/2023	461.42	30

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
710	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	CPWD	05/2019	09/2020	02/2024	299.97	41
711	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI	CPWD	01/2022	11/2024	05/2025	646.52	6
712	KANPUR METRO RAIL PROJECT	LMRCL	05/2019	03/2024	06/2026	11076.48	27
713	AGRA METRO RAIL PROJECT	LMRCL	05/2019	03/2024	12/2025	8379.62	21
714	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2021	03/2025	26405.14	49
715	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	12/2023	23136	45
716	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	12/2023	11420	25
717	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	12/2023	10773	60
718	BHOPAL METRO RAIL	MPMRCL	11/2018	02/2023	12/2026	6941.4	46
719	INDORE METRO RAIL	MPMRCL	11/2018	02/2023	12/2026	7500.8	46
720	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	06/2024	1180	35
721	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	CPWD	10/2016	03/2022	06/2024	1128	27
722	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	DMRC	07/2019	03/2025	03/2026	24948.65	12
723	AHMEDABAD METRO RAIL PROJECT PHASE II	MEGA	03/2019	03/2024	12/2024	5384.17	9
724	SURAT METRO RAIL PROJECT	MEGA	03/2019	03/2024	03/2025	12020.32	12

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
725	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	BUIDCO	08/2017	06/2022	03/2024	824	21
726	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	BUIDCO	08/2017	06/2022	03/2024	578.89	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
727	INTERCEPTION AND DIVERSION WITH STP AT BALLY	KMDA	10/2017	12/2021	03/2024	164.93	27
728	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	KMDA	01/2018	12/2021	09/2023	172.1	21
729	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	KMDA	08/2017	12/2021	08/2023	185.22	20
730	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	KMDA	05/2018	02/2022	06/2024	160	28
731	SEWER NETWORKS, SPS AND STP, MUNGER	BUIDCO	03/2018	10/2021	12/2023	294.02	26
732	SEWER NETWORKS SPS AND STP HAJIPUR	BUIDCO	03/2018	08/2021	08/2023	305.19	24
733	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	03/2024	10151.04	48
734	FARRUKHABAD I AND D AND STP WORKS HAM	UPJalNigam	10/2017	03/2022	04/2024	213.62	25
735	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	UPJalNigam	03/2018	09/2021	09/2023	967.23	24
736	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	UPJalNigam	03/2019	08/2021	03/2024	271.39	31
737	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	KMDA	08/2017	09/2022	12/2026	307.12	51
738	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	KMDA	03/2018	06/2022	03/2024	165.16	21
739	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	KMDA	05/2018	02/2022	03/2024	198.43	25
740	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	KMDA	12/2018	04/2022	12/2024	234.31	32
741	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR	KMDA	03/2019	04/2022	12/2024	287.53	32
742	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	KMDA	01/2019	04/2022	12/2024	384.96	32
743	I AND D AND STP AT CHAPRA	BUIDCO	11/2018	12/2020	08/2023	236.15	32
744	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	42
745	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	BPB	03/2017	12/2019	12/2023	233.57	48
746	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	04/2024	298.12	33
747	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	UPJalNigam	02/2019	06/2022	04/2024	681.78	22
748	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	09/2023	239.11	19
749	CONSTRUCTION OF 564 MLD 124 MGD WASTE	DJB	03/2017	12/2022	09/2023	665.78	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD - 10MG/L						

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(JULY 2023)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	7670	4178
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	19220	7761
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	480.33	640	159.67
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	1383	3291.81	1908.81

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	HURA - C OC (3 MTY)	ECL	10/2015	03/2022	359.69	859.41	499.72
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	17237	19406.12	2169.12
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
10	ANANTA OCP EXPANSION PH III	MCL	08/2008	03/2012	228.08	398.14	170.06
11	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	8990	3082.89

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
12	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	CPWD EDUCATION	01/2018	04/2023	676	1085.04	409.04

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	4773	5401	628

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MH	10/2013	10/2019	1219.21	1900	680.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

MINES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	4103	5055	952
16	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	355	581	226
17	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	534	667.23	133.23

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
19	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
20	BARAUNI-GUWAHATI PIPELINE	GAIL	06/2018	12/2021	3308	3992	684
21	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	661.21	117.3
22	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	206.63	340.76	134.13
23	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
24	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
25	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	1740	2433.15	693.15
26	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
27	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	02/2022	1945	2251	306
28	60 KTA POLYPROPYLENE PROJECT	GAIL	03/2019	04/2024	910.56	1299.02	388.46
29	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	IOCL	10/2020	12/2023	1398	1587	189
30	DEVANGONTHI MARKETING TERMINAL	MANGALORE RE	06/2020	06/2023	200	304	104
31	NUMALIGARH REFINERY EXPANSION PROJECT 6 MTPA REFINERY	NRL	01/2019	10/2024	12366	18968	6602
32	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	2281.94	3219.94	938
33	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
34	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1732	1054
35	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

POWER								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
36	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	11134.54	7214.95	
37	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	17007	2640.42	
38	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	21247.54	14962.21	
39	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	7103	4124.52	
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77	
41	BIKANER SOLAR POWER PROJECT	SJVN	04/2022	05/2024	5491.89	6023.89	532	
42	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	529.68	679	149.32	
43	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	1272.29	623.96	
44	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	1931.39	2635.55	704.16	
45	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67	
46	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9	
47	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10998	399.02	
48	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14	
49	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4825.6	3168.6	
50	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1803	421.16	
RAILWAYS								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
51	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2500.98	1455.78	
52	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57	
53	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	3032.46	2607.86	
54	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	433	299.59	
55	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29	
56	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	3118.34	2393.65	
57	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	3620.28	3037.45	

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
58	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	9362.06	6968.59
59	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
60	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	1160.48	3014	1853.52
61	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4834.54	1921.03
62	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	6021	2517.31
63	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	3168.29	3445.48	277.19
64	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	986.3	1649.31	663.01
65	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
66	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	318.24	1095.12	776.88
67	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
68	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
69	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2404.03	341.73
70	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
71	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	3122.35	833.65
72	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3300	1173
73	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4805.17	2533.67
74	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
75	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	1640.04	1873.1	233.06
76	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	1347.26	1793.63	446.37
77	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	10442.41	5567.83
78	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	830	535
79	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1960	345.41

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
80	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
81	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
82	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	1160	1440	280
83	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
84	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
85	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2053.39	1932.69
86	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
87	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	1187.49	772.65
88	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	401.65	160.13
89	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	632.63	390.41
90	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	8324.28	7417.82
91	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	708.73	139.1
92	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2647.51	849.51
93	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	783.83	235.83
94	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1700	1327.86
95	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
96	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
97	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
98	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	24659	8443
99	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1457.79	530.78
100	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	943.6	1500	556.4
101	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1339	339
102	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	3029.04	1304.84

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
103	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	2063.03	2909	845.97
104	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	4059.65	1827.33
105	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
106	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	390.39	513.92	123.53
107	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	3055	3438.39	383.39
108	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	826.18	181.4
109	ANUPPUR-KATNI	SECR	04/2015	12/2021	1370	1680	310
110	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
111	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
112	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1510	1180.61
113	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
114	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
115	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	1177.96	1500.95	322.99
116	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	800	197.5
117	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.14	1212
118	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
119	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	150	341.66	191.66
120	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	760	1536	776
121	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	WR	03/2012	N.A.	248.26	528.49	280.23
122	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	WR	03/2012	N.A.	217.38	393.62	176.24
123	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	242.28	122.55
124	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3544.25	1635.74
125	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
126	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	2478.23	2938	459.77
127	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1552.26	609.31
128	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
129	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
130	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
131	PUNE-MIRAJ-LONDA (467 KM)	CR	02/2015	03/2024	3627.47	6409.38	2781.91
132	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	1272.19	1384.72	112.53
133	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	1763.93	2445.3	681.37
134	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	1295.42	2560	1264.58
135	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	51219	39630
136	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1110	785.27
137	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
138	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
139	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	14322.79	9868.62
140	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1304.62	919.42
142	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2650	2117.13
143	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6663	4336.48
144	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
145	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	7876.92	6537.44
146	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	970	559.92
147	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2017.96	1567.96
148	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	37012.26	34512.26

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
149	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	8964.35	5012.37
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
151	MUNEERABAD-MAHABOONAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3381.68	1658.68
152	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	2315	5174.3	2859.3
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	MORTH	01/2014	11/2014	195.45	385.97	190.52
154	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	454.89	814.56	359.67
155	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
156	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
157	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
158	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
159	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1414.01	331.01
160	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	667	3006.53	2339.53
161	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER	NHAI	03/2018	11/2021	1294.47	1588.4	293.93
162	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	NHAI	03/2018	11/2021	998.7	1358.32	359.62
163	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	NHIDCL	09/2020	05/2023	262.84	414.2	151.36
164	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	NHIDCL	09/2020	05/2022	183.31	439.56	256.25
165	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	NHAI	11/2019	02/2021	1226.88	1569.68	342.8
166	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	624.98	731.5	106.52
167	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	12/2022	217.96	884	666.04
168	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	11/2022	656.98	840	183.02
169	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	NHAI	11/2017	07/2021	2159	2262	103
170	BALANCE WORK OF TWO LANING WITH PAVED	NHAI	12/2018	10/2020	333.6	461.41	127.81

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	SHOULDER OF PIPRAKOTHI-MOTIHARI- RAXAUL SECTION OF NH-28A FRO						
171	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN	NHAI	10/2019	10/2021	1225.24	1676.11	450.87
172	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0	NHAI	10/2021	10/2023	1331.77	2508.79	1177.02
173	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100	NHAI	03/2021	03/2023	1065.06	1577.92	512.86
174	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66	NHAI	10/2020	04/2024	3219.47	3713.14	493.67
175	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH	NHAI	02/2021	07/2024	3375.31	3790.17	414.86
176	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM	NHAI	01/2021	07/2024	4265.42	4708.42	443
177	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX.	NHAI	06/2021	03/2025	2595	3994.6	1399.6
178	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX	NHAI	06/2021	02/2025	3606	3923.82	317.82
179	6L KORLAM-KANTAKAPALLE SECTION OF NH-130CD ROAD FROM KM 421.100 TO KM 445.100 (PKG-3)	NHAI	02/2021	02/2024	772.7	980.51	207.81
180	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1)	NHAI	02/2021	03/2024	922.5	1128.68	206.18
181	6L JAKKUVA - KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2)	NHAI	02/2021	03/2024	663.6	768	104.4
182	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81	NHAI	02/2019	02/2022	927.77	1603	675.23
183	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP	NHAI	03/2020	01/2024	1863.09	2238	374.91
184	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE	NHAI	12/2020	10/2024	1075.27	1307	231.73
185	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP	NHAI	11/2020	10/2024	1137.74	1289	151.26
186	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I)	NHAI	02/2021	12/2024	1484.83	1768	283.17
187	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III)	NHAI	03/2021	01/2025	1102.63	1303	200.37
188	6L OF PONDAVAKKAM TO KANNIGAIPAIR FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV)	NHAI	02/2021	01/2025	818.73	1105	286.27
189	4L OF HP/PUNJAB B04L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154)	NHAI	03/2021	05/2024	1002.11	1358	355.89
190	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF	NHAI	03/2021	12/2024	1322.95	1442.47	119.52
191	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80	NHAI	03/2018	03/2023	1241.38	2122.64	881.26
192	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361	NHAI	03/2018	03/2021	1169.04	1693.95	524.91

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
193	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA	NHAI	07/2020	08/2023	1710.3	1927	216.7
194	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU	NHAI	07/2020	12/2023	2271.86	3916	1644.14
195	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU	NHAI	03/2021	03/2024	1259	1910	651
196	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21)	NHAI	03/2018	09/2022	2507	3030.73	523.73
197	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE	NHAI	02/2020	01/2023	808.31	958	149.69
198	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545 IN TH	NHAI	10/2019	03/2023	1936.68	2458.03	521.35
199	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272	NHAI	12/2018	02/2023	2375.87	2566.8	190.93
200	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700	NHAI	03/2020	09/2024	2193.23	2314	120.77
201	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER	NHAI	01/2018	02/2023	1916.38	2078	161.62
202	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U	NHAI	10/2019	11/2023	1779.83	2200	420.17
203	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48	NHAI	01/2019	05/2021	654.26	821	166.74
204	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000	NHAI	02/2019	05/2024	1008.99	1361	352.01
205	BANGALORE CHENNAI EXPRESSWAY PHASE-III - PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1	NHAI	10/2020	05/2024	1023.91	1285	261.09
206	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT	NHAI	02/2021	07/2024	2948.31	3392	443.69
207	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2	NHAI	12/2020	07/2024	843.48	966	122.52
208	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH	NHAI	08/2020	03/2024	1034	1589	555
209	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS]	NHAI	09/2020	10/2023	748.99	903	154.01
210	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98	NHAI	09/2020	03/2024	755.26	1039	283.74
211	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP	NHAI	11/2020	12/2023	1690.23	2010.17	319.94
212	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP	NHAI	09/2021	09/2022	622	817.91	195.91
213	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI	NHAI	09/2021	09/2022	517.05	655.06	138.01
214	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	NHAI	03/2018	10/2020	1872.68	2756.09	883.41
215	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	NHAI	03/2018	01/2022	2120.4	2565.63	445.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
216	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	186.96	322.24	135.28
217	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MORTH	01/2017	01/2018	576.48	686.13	109.65
218	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2023	428.11	777.5	349.39
219	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2024	404.29	723.8	319.51
220	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU	NHAI	03/2018	09/2022	841.57	1619.48	777.91
221	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	02/2023	1424.77	1862.77	438
222	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	NHAI	01/2018	06/2021	503.88	609.03	105.15
223	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	NHAI	01/2018	09/2021	999	1152.7	153.7
224	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	NHAI	01/2018	09/2020	686.65	1015.16	328.51
225	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	NHAI	01/2018	08/2021	614.48	757.12	142.64
226	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	NHAI	01/2018	12/2021	573.7	726.99	153.29
227	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	05/2020	1124.11	1503.86	379.75
228	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	11/2020	476.56	780.37	303.81
229	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	02/2022	950.64	1168.33	217.69
230	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	672.89	830.31	157.42
231	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	1007	262.36
232	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	12/2020	1251.11	1361	109.89
233	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
234	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	1408.85	2138.16	729.31
235	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	11/2013	07/2016	683.83	828.45	144.62
236	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00	NHAI	03/2016	07/2020	1408	1659.12	251.12
237	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	899	1381.45	482.45
238	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	3063.99	1476.5

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	09/2016	1665	2360.65	695.65
240	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	06/2023	518.53	902.2	383.67
241	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	537.82	820.42	282.6
242	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	473.18	667.06	193.88
243	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	06/2023	642.96	1139.85	496.89
244	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	519.09	775.47	256.38
245	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	NHAI	03/2018	05/2021	478.74	1136.83	658.09
246	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	NHAI	03/2018	12/2020	1484.3	2182.41	698.11
247	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	NHAI	03/2018	10/2021	1161.39	1404	242.61
248	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	NHAI	03/2018	09/2023	633.55	736.33	102.78
249	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	1027.53	2628.31	1600.78
250	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	1655.01	2639	983.99
251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	675	780.77	105.77
252	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	946	1046.56	100.56
253	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	588.95	873.91	284.96

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
254	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23840	8315
255	SCREENING PLANT-III AT KIRANDUL	NMDC	03/2021	08/2024	2092.97	2221.86	128.89

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
256	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
257	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	18380	3780
258	PATNA METRO RAIL CORPORATION LIMITED	PATNA METRO	02/2019	06/2024	13365.77	13925.5	559.73

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
259	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12925.22	2152.22
260	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	11420	13656.22	2236.22
261	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	38585	40180.91	1595.91
262	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	23136	37276	14140
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
263	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83
264	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	254.13	413.29	159.16
265	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	KMDA	08/2017	09/2022	307.12	653.67	346.55
266	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	225.77	398.9	173.13
267	SAIDPUR SEWER NETWORK PATNA	BUIDCO	04/2015	01/2021	268.63	431.21	162.58

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	1,2320.00	1,7079.00	4759	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	03/2024	1,1459.00	1,9220.00	7761	99
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	12/2024	3492.00	7670.00	4178	171

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	03/2024	480.33	640.00	159.67	30
5	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2024	1383.00	3291.81	1908.81	39

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
7	HURA - C OC (3 MTY)	ECL	10/2015	03/2022	03/2029	359.69	859.41	499.72	84
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	12/2023	1,7237.00	1,9406.12	2169.12	25

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	CPWD EDUCATION	01/2018	04/2023	12/2023	676.00	1085.04	409.04	8

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	09/2023	4773.00	5401.00	628	45

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT	CPWD FOR MHA	10/2013	10/2019	12/2023	1219.21	1900.00	680.79	50

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

490

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	NEW DELHI								

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	11/2023	534.00	667.23	133.23	46
13	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	03/2025	4103.00	5055.00	952	47
14	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	09/2025	355.00	581.00	226	58

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFIN	06/2020	06/2023	01/2024	200.00	304.00	104	7
16	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	10/2023	206.63	340.76	134.13	44
17	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2025	1112.00	1507.24	395.24	68
18	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2024	1740.00	2433.15	693.15	42
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2026	3190.69	3375.90	185.21	97
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	11/2024	2915.00	5909.00	2994	143
21	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	01/2026	678.00	1732.00	1054	107
22	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	04/2024	2,0928.00	2,6264.00	5336	45
23	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	03/2024	823.27	1137.79	314.52	12
24	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	02/2022	12/2023	1945.00	2251.00	306	22
25	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	03/2024	4497.00	6025.00	1528	63
26	DEVELOPMENT OF SURFACE	OIL	01/2018	02/2020	09/2023	543.91	661.21	117.3	43

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

491

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA								
27	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	12/2023	3228.80	3976.67	747.87	21
28	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2025	2281.94	3219.94	938	31
29	BARAUNI-GUWAHATI PIPELINE	GAIL	06/2018	12/2021	10/2023	3308.00	3992.00	684	22

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
30	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	11/2023	529.68	679.00	149.32	60
31	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	01/2024	5111.33	6700.00	1588.67	61
32	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2024	8692.97	2,1312.11	12619.1	153
33	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	06/2026	2491.58	3860.35	1368.77	156
34	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	06/2024	1,4366.58	1,7007.00	2640.42	60
35	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	05/2025	6285.33	2,1247.54	14962.2	176
36	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	03/2024	1931.39	2635.55	704.16	49
37	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2024	3919.59	1,1134.54	7214.95	174
38	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2024	2978.48	7103.00	4124.52	141
39	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	09/2026	1381.84	1803.00	421.16	84
40	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2024	1657.00	4825.60	3168.6	100
41	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	08/2023	1,0598.98	1,0998.00	399.02	33
42	COMPREHENSIVE SCHEME FOR THE	PGCIL	12/2014	12/2018	12/2024	4754.42	9129.32	4374.9	72

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

492

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
43	STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P NAITWAR MORI HEP	SJVN	10/2017	12/2021	08/2023	648.33	1272.29	623.96	20

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
44	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	08/2023	390.39	513.92	123.53	20
45	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	03/2026	1876.00	2081.27	205.27	36
46	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	12/2025	3631.00	3887.48	256.48	45
47	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2025	701.61	810.02	108.41	76
48	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2026	2232.32	4059.65	1827.33	48
49	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	01/2025	2063.03	2909.00	845.97	46
50	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	03/2024	1724.20	3029.04	1304.84	36
51	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2023	943.60	1500.00	556.4	21
52	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2024	927.01	1457.79	530.78	60
53	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
54	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2024	2478.23	2938.00	459.77	27
55	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2024	582.13	1247.64	665.51	30
56	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2024	1908.51	3544.25	1635.74	21
57	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	08/2023	760.00	1536.00	776	41
58	NANPARA - NEPALGANJ GAUGE	NER	04/2017	04/2017	12/2024	150.00	341.66	191.66	92

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

493

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	CONVERSION.								
59	CHANDIGARH-BADDI	NR	04/2007	03/2023	06/2025	328.14	1540.14	1212	27
60	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	03/2024	1177.96	1500.95	322.99	51
61	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	12/2024	744.04	1215.54	471.5	45
62	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450.00	2017.96	1567.96	148
63	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	01/2024	2500.00	3,7012.26	34512.3	254
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2026	3951.98	8964.35	5012.37	120
65	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
66	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2024	318.24	1095.12	776.88	144
67	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2024	1160.00	1440.00	280	48
68	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	02/2024	600.00	701.81	101.81	47
69	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	12/2024	1614.59	1960.00	345.41	69
70	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2025	548.00	783.83	235.83	60
71	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	3118.34	2393.65	73
72	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	02/2024	2393.47	9362.06	6968.59	119
73	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	3014.00	1853.52	180
74	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	07/2025	2913.51	4834.54	1921.03	112
75	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2026	3503.69	6021.00	2517.31	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

494

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
76	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	03/2024	3168.29	3445.48	277.19	12
77	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	03/2026	986.30	1649.31	663.01	120
78	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127.00	3300.00	1173	12
79	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2026	2271.50	4805.17	2533.67	60
80	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2027	1045.20	2500.98	1455.78	216
81	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2024	1188.91	1619.48	430.57	60
82	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	12/2025	424.60	3032.46	2607.86	57
83	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	07/2023	133.41	433.00	299.59	172
84	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
85	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
86	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2026	2923.13	3791.66	868.53	213
87	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2025	4454.17	1,4322.79	9868.62	168
88	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2023	495.74	734.01	238.27	126
89	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2650.00	2117.13	60
90	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	6663.00	4336.48	132
91	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	7876.92	6537.44	96
92	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	09/2023	410.08	970.00	559.92	55

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

495

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
93	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	01/2024	1798.00	2647.51	849.51	58
94	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	12/2024	242.22	632.63	390.41	57
95	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	10/2024	414.84	1187.49	772.65	55
96	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2053.39	1932.69	105
97	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
98	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	10/2023	1295.42	2560.00	1264.58	19
99	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2024	1763.93	2445.30	681.37	55
100	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	12/2024	1272.19	1384.72	112.53	33
101	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2024	295.00	830.00	535	61
102	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	12/2023	4874.58	1,0442.41	5567.83	93
103	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	12/2026	1347.26	1793.63	446.37	57
104	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	12/2025	1640.04	1873.10	233.06	45
105	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
106	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2026	644.78	826.18	181.4	108
107	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2024	1370.00	1680.00	310	36
108	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	10/2024	1973.00	2135.34	162.34	43
109	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	1185.73	454.09	36

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

496

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
110	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2025	229.00	1096.00	867	48
111	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2023	3055.00	3438.39	383.39	63

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
112	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	NHAI	03/2018	10/2020	09/2024	1872.68	2756.09	883.41	47
113	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	NHAI	03/2018	01/2022	01/2024	2120.40	2565.63	445.23	24
114	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81	NHAI	02/2019	02/2022	10/2023	927.77	1603.00	675.23	20
115	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI	NHAI	09/2021	09/2022	09/2024	517.05	655.06	138.01	24
116	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP	NHAI	09/2021	09/2022	09/2024	622.00	817.91	195.91	24
117	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	06/2024	2848.00	3379.45	531.45	123
118	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	07/2023	1655.01	2639.00	983.99	83
119	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	09/2016	12/2023	1665.00	2360.65	695.65	87
120	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	NHAI	11/2019	02/2021	08/2023	1226.88	1569.68	342.8	30
121	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	05/2024	950.69	1108.00	157.31	57
122	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	12/2020	10/2023	1251.11	1361.00	109.89	34
123	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66	NHAI	10/2020	04/2024	05/2025	3219.47	3713.14	493.67	13
124	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100	NHAI	03/2021	03/2023	12/2023	1065.06	1577.92	512.86	9
125	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN	NHAI	10/2019	10/2021	01/2024	1225.24	1676.11	450.87	27

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

497

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
126	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU	NHAI	03/2021	03/2024	12/2024	1259.00	1910.00	651	9
127	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU	NHAI	07/2020	12/2023	06/2024	2271.86	3916.00	1644.14	6
128	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA	NHAI	07/2020	08/2023	06/2024	1710.30	1927.00	216.7	10
129	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI-MOTIHARI- RAXAUL SECTION OF NH-28A FRO	NHAI	12/2018	10/2020	09/2023	333.60	461.41	127.81	35
130	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	02/2022	10/2024	950.64	1168.33	217.69	32
131	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	05/2020	11/2023	1124.11	1503.86	379.75	42
132	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	MORTH	01/2014	11/2014	05/2024	195.45	385.97	190.52	114
133	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	NHIDCL	09/2020	05/2022	04/2024	183.31	439.56	256.25	23
134	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	NHIDCL	09/2020	05/2023	08/2024	262.84	414.20	151.36	15
135	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48	NHAI	01/2019	05/2021	02/2024	654.26	821.00	166.74	33
136	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER	NHAI	01/2018	02/2023	08/2023	1916.38	2078.00	161.62	6
137	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272	NHAI	12/2018	02/2023	08/2023	2375.87	2566.80	190.93	6
138	DWARKA EXPRESSWAY FROM KM - 0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21)	NHAI	03/2018	09/2022	12/2023	2507.00	3030.73	523.73	15
139	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	07/2024	744.64	1007.00	262.36	52
140	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2024	672.89	830.31	157.42	48
141	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	NHAI	01/2018	12/2021	03/2024	573.70	726.99	153.29	27
142	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	NHAI	01/2018	08/2021	10/2023	614.48	757.12	142.64	26
143	REHABILITATION AND UPGRADATION	NHAI	01/2018	09/2020	12/2023	686.65	1015.16	328.51	39

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

498

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON								
144	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	NHAI	01/2018	06/2021	12/2023	503.88	609.03	105.15	30
145	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	02/2023	09/2024	1424.77	1862.77	438	19
146	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU	NHAI	03/2018	09/2022	03/2024	841.57	1619.48	777.91	18
147	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	08/2023	946.00	1046.56	100.56	62
148	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	08/2023	1083.00	1414.01	331.01	62
149	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	07/2023	1587.49	3063.99	1476.5	51
150	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	02/2024	899.00	1381.45	482.45	58
151	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00	NHAI	03/2016	07/2020	02/2024	1408.00	1659.12	251.12	43
152	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MoRTH	01/2014	10/2016	11/2023	1408.85	2138.16	729.31	85
153	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	NHAI	03/2018	10/2021	03/2024	1161.39	1404.00	242.61	29
154	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	NHAI	03/2018	05/2021	01/2024	478.74	1136.83	658.09	32
155	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	01/2024	519.09	775.47	256.38	9
156	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	06/2023	01/2024	642.96	1139.85	496.89	7
157	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	01/2024	473.18	667.06	193.88	9
158	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	04/2023	01/2024	537.82	820.42	282.6	9
159	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	06/2023	02/2024	518.53	902.20	383.67	8
160	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER	NHIDCL	04/2017	09/2023	05/2024	428.11	777.50	349.39	8

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

499

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JULY 2023)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO								
161	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	11/2022	08/2023	656.98	840.00	183.02	9
162	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	12/2022	08/2023	217.96	884.00	666.04	8
163	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	12/2023	624.98	731.50	106.52	86
164	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER	NHAI	03/2018	11/2021	11/2023	1294.47	1588.40	293.93	24
165	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	NHAI	03/2018	11/2021	11/2023	998.70	1358.32	359.62	24

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
166	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	08/2023	1,5525.00	2,3840.00	8315	99

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
167	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	12/2023	1,0773.00	1,2925.22	2152.22	60
168	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	12/2023	1,1420.00	1,3656.22	2236.22	25
169	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	12/2023	2,3136.00	3,7276.00	14140	45

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
170	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	KMDA	08/2017	09/2022	12/2026	307.12	653.67	346.55	51
171	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	413.29	159.16	42
172	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	03/2024	1,0151.04	5,5548.87	45397.8	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

500

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 1000 Crore and above					(July 2023)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year)		Cost Overruns (%)	T.O.R.s (in months)
					Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9
	<u>POWER</u>							
	<u>Power Grid Corporation Of India Limited</u>							
1	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - PPP (BOT) - [N18000327]	03/2019	1,326.00 -	1,326.00	03/2023 -	09/2023	.00	6
	Total		1,326.00 -	1,326.00				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
2	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - PPP BOT (Hybrid Annuity) - [N24001589]	09/2020	755.26 -	1,039.00	03/2024 -	03/2024	37.57	0
3	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	12/2023	.00	114
4	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 - PPP BOT (Hybrid Annuity) - [N24001601]	01/2019	1,051.69 -	1,051.69	01/2023 -	02/2024	.00	13
5	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V - PPP BOT (Hybrid Annuity) - [N24001514]	01/2021	1,060.29 -	1,060.29	01/2024 -	12/2023	.00	-1
6	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) - PPP BOT (Hybrid Annuity) - [N24001553]	03/2022	1,092.90 -	1,092.90	02/2025 -	02/2025	.00	0
7	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. - PPP BOT (Hybrid Annuity) - [N24001706]	03/2021	1,097.18 1,097.00	1,097.00	01/2024 -	01/2024	-.02	0
8	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) - PPP BOT (Hybrid Annuity) - [N24001507]	11/2022	1,124.00 -	1,124.00	05/2024 -	05/2024	.00	0
9	6L ALURU - JAKKUBA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - PPP BOT (Hybrid Annuity) - [N24001838]	02/2021	922.50 -	1,128.68	03/2024 -	06/2024	22.35	3
10	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E - PPP BOT (Hybrid Annuity) - [N24001707]	03/2021	1,143.46 1,143.00	1,143.00	01/2024 -	01/2024	-.04	0
11	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N - PPP BOT (Hybrid Annuity) - [N24001640]	03/2021	1,229.38 -	1,229.38	11/2024 -	11/2024	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 1000 Crore and above (July 2023)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM - PPP BOT (Hybrid Annuity) - [N24001694]	02/2019	1,243.57 -	1,243.57	12/2023 -	12/2023	.00	0
13	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) - PPP BOT (Hybrid Annuity) - [N24001504]	05/2022	1,260.00 -	1,260.00	05/2024 -	05/2024	.00	0
14	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 - PPP BOT (Hybrid Annuity) - [N24001696]	02/2019	1,291.37 -	1,291.37	08/2023 -	08/2023	.00	0
15	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO - PPP BOT (Hybrid Annuity) - [N24001634]	01/2021	1,306.95 -	1,306.95	12/2023 -	12/2023	.00	0
16	4L OF KM 0.00 TO KM 42.00 OF OFDOBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALO - PPP BOT (Hybrid Annuity) - [N24001509]	01/2020	1,307.00 -	1,307.00	04/2021 -	12/2023	.00	32
17	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 - PPP BOT (Hybrid Annuity) - [N24001522]	01/2021	1,307.95 -	1,307.95	01/2024 -	01/2024	.00	0
18	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP - PPP BOT (Hybrid Annuity) - [N24001534]	12/2020	1,334.04 -	1,334.00	01/2024 -	03/2024	-.00	2
19	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D - PPP BOT (Hybrid Annuity) - [N24001756]	10/2020	1,352.56 -	1,352.56	10/2024 -	10/2024	.00	0
20	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - PPP BOT (Hybrid Annuity) - [N24001721]	02/2019	1,008.99 -	1,361.00	05/2024 -	05/2024	34.89	0
21	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA - PPP BOT (Hybrid Annuity) - [N24001593]	11/2021	1,368.19 -	1,368.19	09/2024 -	09/2024	.00	0
22	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA – RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR - PPP BOT (Hybrid Annuity) - [N24001636]	05/2021	1,368.91 -	1,368.91	12/2024 -	12/2024	.00	0
23	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF - PPP BOT (Annuity) - [N24001526]	08/2021	1,377.79 -	1,377.79	10/2024 -	10/2024	.00	0
24	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) - PPP BOT (Hybrid Annuity) - [N24001602]	01/2019	1,409.38 -	1,409.38	12/2022 -	02/2024	.00	14
25	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE - PPP BOT (Hybrid Annuity) - [N24001680]	03/2021	1,409.68 -	1,409.68	10/2024 -	10/2024	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 1000 Crore and above (July 2023)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
26	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F - PPP BOT (Hybrid Annuity) - [N24001633]	12/2020	1,430.88 -	1,430.88	12/2023 -	12/2023	.00	0
27	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF - PPP BOT (Hybrid Annuity) - [N24001808]	03/2021	1,322.95 -	1,442.47	12/2024 -	12/2024	9.03	0
28	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) - PPP BOT (Hybrid Annuity) - [N24001508]	11/2022	1,450.00 -	1,450.00	10/2024 -	10/2024	.00	0
29	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA - PPP BOT (Hybrid Annuity) - [N24001588]	12/2021	1,470.73 -	1,470.73	01/2025 -	01/2025	.00	0
30	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGE NEAR TO MANEWAL (LUDHIANA - PPP BOT (Hybrid Annuity) - [N24001630]	07/2021	1,501.02 -	1,501.02	02/2025 -	02/2025	.00	0
31	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) - PPP BOT (Hybrid Annuity) - [N24001603]	01/2019	1,518.53 -	1,518.53	10/2022 -	12/2023	.00	14
32	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) - PPP BOT (Hybrid Annuity) - [N24001505]	03/2022	1,549.02 -	1,549.02	03/2024 -	03/2024	.00	0
33	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88 -	1,569.68	02/2021 -	08/2023	27.94	30
34	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10 -	1,601.10	01/2024 -	07/2024	.00	6
35	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR - PPP BOT (Hybrid Annuity) - [N24001557]	03/2022	1,636.15 -	1,636.15	11/2024 -	11/2024	.00	0
36	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 - PPP BOT (Hybrid Annuity) - [N24001675]	11/2022	1,732.73 -	1,732.73	05/2025 -	05/2025	.00	0
37	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM - PPP BOT (Hybrid Annuity) - [N24001632]	01/2021	1,741.86 -	1,741.86	05/2024 -	05/2024	.00	0
38	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) - PPP (BOT) - [N24001493]	12/2022	1,749.86 -	1,749.86	12/2024 -	12/2024	.00	0
39	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 - PPP BOT (Hybrid Annuity) - [N24001693]	09/2021	1,751.18 -	1,751.18	10/2024 -	10/2024	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 1000 Crore and above (July 2023)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
40	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K - PPP BOT (Hybrid Annuity) - [N24001637]	03/2021	1,754.84 -	1,754.84	01/2025 -	01/2025	.00	0
41	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 - PPP BOT (Hybrid Annuity) - [N24001547]	03/2022	1,909.98 -	1,909.98	01/2026 -	01/2026	.00	0
42	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 - PPP BOT (Hybrid Annuity) - [N24001550]	09/2021	1,821.72 -	1,917.32	09/2024 -	09/2024	5.25	0
43	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - PPP BOT (Hybrid Annuity) - [N24001533]	11/2020	1,690.23 -	2,010.17	12/2023 -	03/2024	18.93	3
44	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 - PPP BOT (Hybrid Annuity) - [N24001628]	11/2021	2,155.95 -	2,155.95	02/2025 -	02/2025	.00	0
45	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA - PPP (BOT) - [N24001748]	03/2021	2,200.93 -	2,200.93	09/2024 -	09/2024	.00	0
46	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00 -	2,262.00	07/2021 -	05/2023	4.77	22
47	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 - PPP (BOT) - [N24001747]	03/2020	2,193.23 -	2,314.00	09/2024 -	09/2024	5.51	0
48	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S - PPP BOT (Hybrid Annuity) - [N24001710]	09/2020	2,334.68 2,335.00	2,335.00	03/2023 -	11/2023	.01	8
49	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	2,360.65	09/2016 -	12/2023	41.78	87
50	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	2,639.00	08/2016 -	07/2023	59.46	83
51	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B - PPP BOT (Hybrid Annuity) - [N24001552]	10/2021	2,714.95 -	2,714.95	09/2024 -	09/2024	.00	0
52	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 - PPP BOT (Hybrid Annuity) - [N24001676]	12/2022	2,718.46 -	2,718.46	06/2025 -	06/2025	.00	0
53	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) - PPP BOT (Hybrid Annuity) - [N24001506]	02/2022	2,747.00 -	2,747.00	02/2024 -	02/2024	.00	0
54	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 - PPP BOT (Hybrid Annuity) - [N24001551]	10/2021	3,044.02 -	3,044.02	09/2024 -	09/2024	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 1000 Crore and above (July 2023)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
55	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	06/2024	18.66	123
	Total		86,165.93 -	90,320.22				
	Grand Total		87,491.93	91,646.22				

List of projects original without Date of Commissioning

Costing Rs. 1000 Crore and above						(July 2023)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
1	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	1,323.75	-	03/2024	-	0/0
2	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,700.00	2,044.95	-	03/2024	-	0/0
3	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	1,510.00	2,102.69	-	03/2024	-	0/0
4	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,822.92	-	12/2024	-	0/0
5	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	834.76	-	12/2025	-	0/0
	<u>South Western Railway</u>								
6	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 2,404.03	2,404.03	1,161.58	-	12/2025	-	2/2
7	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,801.01	126.80	-	12/2026	-	0/0
8	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	5,174.30	159.49	-	03/2030	-	0/0
	<u>Southern Railway</u>								
9	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	1,431.90	2,095.35	-	03/2025	-	0/0
10	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	1,339.00	.93	-	03/2025	-	0/0
	Total		11,905.47 -	20,658.06	11,673.22				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
11	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	1,101.58	608.53	-	12/2023	-	0/0
12	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	1,478.40	621.30	-	06/2024	-	0/0
	Total		2,579.98 -	2,579.98	1,229.83				0/0
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								

Costing Rs. 1000 Crore and above (July 2023)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
13	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	1,832.74	- -	09/2023	-	2/9
	Total		2,694.00 -	2,694.00	1,832.74				2/9
	Grand Total		17,179.45	25,932.04	14,735.79				4/11

List of projects without Date of Commissioning

Costing Rs. 1000 Crore and above				(July 2023)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Neyveli Lignite Corporation</u>				
1	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	09/2020
2	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	09/2020
3	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	12/2015 -	02/2021
	Total		10,216.01 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
4	CBR 9 MMTPA PROJECT - [N16000434]CPCL,TAMIL NADU	01/2021	31,580.00 31,580.00	06/2025 -	-
	Total		31,580.00 -		
	<u>POWER</u>				
	<u>National Thermal Power Corporation</u>				
5	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	08/2017
	Total		1,527.00 -		
	<u>RAILWAYS</u>				
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
6	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020
7	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
8	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	03/2020 -	03/2023
9	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	03/2012 -	06/2023
	<u>East Coast Railway</u>				
10	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	09/2022
11	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 02/2023	02/2023
	<u>Kolkata Metro Rail Corporation Limited</u>				

Costing Rs. 1000 Crore and above					(July 2023)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
12	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	03/2016
	<u>North East Frontier Railway</u>				
13	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	-
14	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
15	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 10/2023	05/2023
	<u>South Central Railway</u>				
16	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2000
17	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	03/2021 -	03/2021
	Total		41,961.66 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
18	KALMATH TO ZARAP - [N24001137]MoRTH, MAHARASHTRA	09/2016	1,338.13 2,617.44	03/2020 -	01/2023
19	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH, MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	02/2023
20	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH, MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	02/2023
21	WAKED TO TALEGAON - [N24001135]MoRTH, MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	02/2023
22	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH, ARUNACHAL PRADESH	09/2011	1,979.00 -	- 12/2021	05/2023
23	INDAPUR TO VADPALE - [N24001114]MoRTH, MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	06/2023
24	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH, BIHAR	02/2019	2,926.42 -	- 09/2024	-
	<u>National Highways Authority Of India</u>				
25	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA	01/2018	953.09 1,014.08	05/2020 -	05/2023
26	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	12/2020 08/2023	05/2023
27	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 2,262.00	07/2021 04/2023	05/2023
28	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL - [N24001566]NHAI, RAJASTHAN	11/2019	1,640.10 -	05/2023 08/2023	05/2023

Costing Rs. 1000 Crore and above					(July 2023)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
29	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) - [N24001780]NHAI,HARYANA	01/2018	2,228.00 -	11/2020 08/2023	05/2023
30	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,950.04	06/2018 07/2023	06/2023
31	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,192.10	06/2018 07/2023	06/2023
32	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	03/2017 05/2021	06/2023
33	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 1,152.70	09/2021 -	06/2023
34	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	03/2021 06/2023	06/2023
35	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M - [N24001573]NHAI,RAJASTHAN	11/2019	1,658.06 -	12/2022 08/2023	06/2023
36	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A - [N24001690]NHAI,KARNATAKA	01/2021	1,167.52 1,157.00	01/2023 12/2023	06/2023
37	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805]NHAI,MAHARASHTRA	03/2018	1,169.04 -	03/2021 -	06/2023
38	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806]NHAI,MAHARASHTRA	03/2018	1,241.38 -	03/2023 -	06/2023
	Total		29,890.74 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
39	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	12/2015
40	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	02/2021
	<u>Delhi Metro Rail Corporation</u>				
41	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	08/2021
	<u>Kochi Metro Rail Corporation Ltd</u>				
42	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	09/2020
	Total		62,136.79 -		
	Grand Total		1,77,312.20		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 1000 Crore and above						(July 2023)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 6,840.00	7,670.00	6,569.75	09/2010 10/2022	12/2024	171	26
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	38,740.00	11/2020 -	11/2023	36	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	16,576.00	12/2016 -	12/2023	84	-
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 19,220.00	19,220.00	20,460.00	12/2015 -	03/2024	99	-
	Total		67,120.00 -	83,818.00	82,345.75				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	3,291.81	769.80	09/2021 -	12/2024	39	-
6	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	466.96	10/2022 -	12/2024	26	-
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	365.49	03/2021 -	03/2025	48	-
8	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	1,335.88	02/2022 -	12/2025	46	-
	Total		6,208.90 -	8,207.71	2,938.13				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
9	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	582.15	03/2019 -	04/2025	73	-
	<u>Eastern Coal Fields Limited</u>								
10	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,146.48	713.53	08/2019 -	08/2024	60	-
	<u>Mahanadi Coal Fields Limited</u>								
11	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	779.83	03/2021 -	03/2026	60	-
	<u>Neyveli Lignite Corporation</u>								
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	19,406.12	15,652.81	11/2021 -	12/2023	25	-
	<u>Northern Coal Fields Limited</u>								

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
13	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	1,011.43	03/2022 -	08/2023	17	-
14	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	1,447.90	03/2021 -	10/2023	31	-
	<u>South-Eastern Coal Fields Limited</u>								
15	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATTISGARH	06/2010	11,816.40 -	11,816.40	5,887.31	03/2023 -	03/2025	24	-
16	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATTISGARH	08/2013	7,612.33 -	7,612.33	4,109.56	03/2023 -	03/2025	24	-
17	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATTISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	-
18	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATTISGARH	11/2014	1,624.59 -	1,624.59	49.60	03/2023 -	03/2031	96	-
	Total		48,471.28 -	53,125.15	30,234.12				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
19	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	4,103.00 5,055.00	5,055.00	2,259.22	04/2021 12/2022	03/2025	47	27
20	POTTANGI BAUXITE MINES - [N10000016]NALCO,ODISHA	05/2018	1,437.00 1,381.00	1,381.00	603.12	12/2024 03/2025	05/2025	5	2
	Total		5,540.00 -	6,436.00	2,862.34				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
21	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATTISGARH	01/2010	15,525.00 23,840.00	23,840.00	23,131.35	05/2015 06/2023	08/2023	99	2
22	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATTISGARH	11/2015	2,907.00 -	2,907.00	1,362.32	06/2023 07/2024	05/2025	23	10
	<u>Steel Authority Of India Limited (Sail)</u>								
23	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	843.97	10/2017 12/2021	09/2025	95	45
	Total		19,466.01 -	27,781.01	25,337.64				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
24	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	867.50	08/2022 06/2023	10/2024	26	16
25	KOCHI SALEM LPG PIPELINE PROJECT - [N160000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	1,094.66	06/2019 02/2024	02/2025	68	12
26	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442]BPCL,MAHARASHTRA	04/2021	1,164.69 -	1,164.69	169.72	06/2024 -	07/2025	13	-
	<u>Hindustan Petroleum Corporation Limited</u>								
27	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	23,860.04	07/2020 07/2022	04/2024	45	21
	<u>Indian Oil Corporation Limited</u>								

Costing Rs. 1000 Crore and above

(July 2023)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
28	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	1,119.42	10/2021 04/2023	07/2023	21	3
29	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	1,329.13	08/2020 07/2023	11/2023	39	4
30	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 2,251.00	2,251.00	2,005.03	02/2022 04/2023	12/2023	22	8
31	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL	03/2018	3,712.00 3,696.00	3,696.00	2,852.90	09/2022 06/2023	12/2023	15	6
32	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 1,587.00	1,587.00	726.79	12/2023 -	02/2024	2	-
33	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	5,303.14	12/2018 11/2023	03/2024	63	4
34	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	1,614.00	513.56	08/2023 -	03/2024	7	-
35	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,219.94	3,219.94	1,122.50	12/2022 07/2023	07/2025	31	24
36	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	13,805.00	3,776.82	01/2024 -	07/2025	18	-
	<u>Oil & Natural Gas Corporation Limited</u>								
37	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,897.83	04/2018 12/2023	05/2026	97	29
	Total		60,188.82 -	69,050.27	47,639.04				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
38	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	4,287.59	1,168.94	08/2024 -	03/2026	19	-
39	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	3,194.18	04/2020 07/2025	09/2026	77	14
	<u>National Thermal Power Corporation</u>								
40	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,998.00	10,831.04	11/2020 07/2022	08/2023	33	13
41	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	17,007.00	14,880.63	06/2019 10/2022	06/2024	60	20
42	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	21,304.21	10/2011 07/2023	07/2024	153	12
43	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	7,103.00	5,911.37	03/2013 12/2021	12/2024	141	36
44	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	18,668.00	11,484.39	03/2023 -	03/2025	24	-

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
45	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,803.00	909.90	09/2019 12/2024	09/2026	84	21
	<u>Power Grid Corporation Of India Limited</u>								
46	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]PGCIL,RAJASTHAN	03/2021	1,340.81 -	1,340.81	1,087.22	12/2022 -	07/2023	7	-
47	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]PGCIL,ASSAM	03/2019	1,326.00 -	1,326.00	1,367.92	03/2023 -	09/2023	6	-
48	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN	05/2021	1,184.88 -	1,184.88	712.85	09/2022 -	12/2023	15	-
49	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	4,578.01	12/2018 -	01/2024	61	-
50	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	2,635.55	1,952.75	02/2020 -	03/2024	49	-
51	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	1,562.00	805.08	12/2022 -	03/2024	15	-
52	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	1,006.00	791.18	12/2022 -	03/2024	15	-
53	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332]PGCIL,MULTI STATE	05/2022	1,666.00 -	1,666.00	511.39	11/2023 -	03/2024	4	-
54	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337]PGCIL,MULTI STATE	07/2022	4,546.26 -	4,546.26	633.23	06/2023 -	06/2024	12	-
55	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	5,600.77	12/2018 -	12/2024	72	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
56	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	1,272.29	1,172.12	12/2021 -	08/2023	20	-
57	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR	03/2019	10,439.09 -	10,439.09	8,067.59	01/2024 -	03/2024	2	-
	<u>Thdc India Limited</u>								
58	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	4,825.60	5,601.35	02/2016 06/2022	06/2024	100	24
59	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	7,902.37	09/2023 -	08/2024	11	-
60	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	3,163.57	06/2013 -	06/2026	156	-
	Total		1,19,841.07 -	1,51,874.39	1,13,632.06				

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Cpwd For Health</u>								
61	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	1,404.00	95.63	09/2023 -	10/2023	1	-
	<u>HII Infra Tech Services Limited</u>								
62	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR - [N21000031]HITES,TELANGANA	12/2018	1,110.55 -	1,110.55	269.09	07/2024 -	10/2024	3	-
	Total		2,514.55 -	2,514.55	364.72				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
63	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	3,445.48	1,666.35	03/2023 -	03/2024	12	-
64	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,805.17	3,491.85	03/2021 03/2025	03/2026	60	12
65	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	2,081.27	1,335.69	03/2023 03/2025	03/2026	36	12
	<u>East Central Railways</u>								
66	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	1,160.75	03/2020 -	12/2023	45	-
67	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	2,445.51	03/2020 -	03/2024	48	-
68	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	965.84	03/2021 -	03/2024	36	-
69	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	950.34	03/2021 -	12/2024	45	-
	<u>East Coast Railway</u>								
70	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATTISGARH	12/2012	1,160.00 -	1,440.00	1,058.66	03/2020 -	03/2024	48	-
71	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	790.93	03/2022 -	03/2024	24	-
72	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	1,052.09	12/2018 -	02/2025	74	-
73	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	980.13	06/2021 -	03/2025	45	-
74	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	2,904.31	03/2009 -	12/2026	213	-
	<u>Eastern Railways</u>								
75	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	1,141.34	03/2019 12/2009	03/2024	60	171
76	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	980.46	03/2022 -	03/2025	36	-
	<u>Indian Railway Construction Company Limited</u>								
77	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]JRCON,CHHATTISGARH	04/2013	3,055.00 -	3,438.39	2,976.72	09/2018 -	12/2023	63	-

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	5,200.00	-	03/2020 -	12/2025	69	-
	<u>North Central Railway</u>								
79	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 2,001.00	2,001.00	1,118.80	03/2021 -	12/2023	33	-
80	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	1,024.32	03/2022 -	12/2024	33	-
81	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	60.37	03/2023 -	03/2026	36	-
	<u>North East Frontier Railway</u>								
82	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	7,876.92	3,290.96	12/2015 -	12/2023	96	-
83	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	2,647.51	1,999.72	03/2019 -	01/2024	58	-
84	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	9,362.06	6,591.01	03/2014 -	02/2024	119	-
85	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,650.00	1,761.52	03/2019 -	03/2024	60	-
86	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	1,187.49	349.63	03/2020 -	10/2024	55	-
87	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,663.00	2,556.74	03/2015 -	03/2026	132	-
88	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	4,059.65	2,898.81	03/2022 -	03/2026	48	-
	<u>North Eastern Railway</u>								
89	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	2,560.00	2,121.53	03/2022 -	10/2023	19	-
90	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,500.95	1,119.47	12/2019 -	03/2024	51	-
	<u>Northern Railway</u>								
91	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 37,012.26	37,012.26	36,017.83	11/2002 12/2023	01/2024	254	1
92	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024	148	-
	<u>National High Speed Rail Corporation Limited</u>								
93	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	1,08,000.00	46,912.58	12/2023 -	08/2027	44	-
	<u>Rail Vikas Nigam Ltd.</u>								
94	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,846.81	03/2020 -	08/2023	41	-
95	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,556.55	03/2022 -	10/2023	19	-
96	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,500.00	1,251.40	03/2022 -	12/2023	21	-
97	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	3,300.00	3,204.74	03/2023 -	03/2024	12	-
98	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,457.79	1,491.77	03/2019 -	03/2024	60	-

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
99	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,587.43	03/2023 -	12/2024	21	-
100	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	24,659.00	14,020.06	12/2024 -	03/2025	3	-
101	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,834.54	3,020.54	03/2016 -	07/2025	112	-
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	355.80	03/2014 -	12/2025	141	-
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	8,964.35	5,943.37	03/2016 -	03/2026	120	-
104	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	3,674.36	12/2024 -	12/2026	24	-
	<u>South Central Railway</u>								
105	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,909.00	2,909.00	2,355.36	03/2021 -	01/2025	46	-
106	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	3,014.00	1,071.53	03/2010 -	03/2025	180	-
107	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	1,533.64	03/2023 -	03/2025	24	-
108	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	2,728.66	03/2022 -	12/2025	45	-
109	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,500.98	1,129.92	03/2009 -	03/2027	216	-
	<u>South East Central Railway</u>								
110	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATTISGARH	04/2015	1,973.00 2,135.34	2,135.34	1,488.70	03/2021 12/2023	10/2024	43	10
111	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 2,753.05	3,544.25	2,238.21	03/2023 12/2023	12/2024	21	12
112	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,680.00	1,171.79	12/2021 12/2023	12/2024	36	12
113	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	230.25	12/2021 -	12/2025	48	-
	<u>South Eastern Railway</u>								
114	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 3,029.04	3,029.04	1,693.74	03/2021 -	03/2024	36	-
115	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	1,148.32	05/2023 -	02/2025	21	-
	<u>South Western Railway</u>								
116	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,960.00	1,887.40	03/2019 -	12/2024	69	-
117	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 1,378.00	1,649.31	363.80	03/2016 -	03/2026	120	-
118	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	722.55	12/2018 -	03/2026	87	-
	<u>Southern Railway</u>								

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
119	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,118.34	1,877.71	02/2019 -	03/2025	73	-
	<u>West Central Railway</u>								
120	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 2,938.00	2,938.00	1,279.35	03/2022 -	06/2024	27	-
121	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	990.59	03/2022 -	09/2024	30	-
122	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	2,020.86	03/2020 -	10/2024	55	-
123	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	202	-
	<u>Western Railway</u>								
124	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.03	1,095.12	201.24	03/2012 -	03/2024	144	-
	Total		2,30,722.02 -	3,43,193.82	1,99,083.27				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
125	MOPA AIRPORT - [N24001458]MoRTH,GOA	12/2021	1,183.16 -	1,183.16	485.75	04/2022 -	10/2023	18	-
126	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	2,138.16	1,560.46	10/2016 -	11/2023	85	-
127	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	739.08	10/2019 -	12/2023	50	-
128	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	1,230.02	791.80	11/2019 -	12/2023	49	-
129	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH	07/2018	1,948.25 -	1,948.25	640.55	02/2024 -	09/2024	7	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
130	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 1,139.85	1,139.85	528.71	06/2023 12/2023	01/2024	7	1
131	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 1,718.59	1,718.59	656.26	03/2022 12/2023	03/2024	24	3
132	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	542.67	07/2022 07/2022	05/2024	22	22
	<u>National Highways Authority Of India</u>								
133	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 2,639.00	2,639.00	1,771.52	08/2016 06/2023	07/2023	83	1

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
134	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 4,041.80	1,396.74	3,738.01	10/2019 05/2023	07/2023	45	2
135	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 3,150.00	3,063.99	2,938.25	04/2019 12/2022	07/2023	51	7
136	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29 - [N24001517]NHAI,GUJARAT	09/2020	1,523.77 -	1,523.77	963.02	04/2023 -	07/2023	3	-
137	4L OF SHAMLI TO MUZAFFARNAGAR SECTION OF NH-709AD, PKG-II - [N24001742]NHAI,UTTAR PRADESH	06/2020	1,621.07 -	1,621.07	977.49	10/2022 -	07/2023	9	-
138	FOUR LANNING OF JAGDISHPUR-FAIZABAD SECTION FROM KM 47.930 TO KM 107.680 OF NH-330A - [N24001816]NHAI,UTTAR PRADESH	03/2021	1,980.00 -	1,980.00	1,043.39	03/2023 -	07/2023	4	-
139	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,471.75	1,471.75	1,439.30	07/2021 07/2023	08/2023	25	1
140	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	1,188.00	02/2022 11/2022	08/2023	18	9
141	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	1,169.00	05/2020 03/2023	08/2023	39	5
142	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755]NHAI,UTTAR PRADESH	10/2019	1,936.68 -	2,458.03	1,380.90	03/2023 -	08/2023	5	-
143	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A - [N24001782]NHAI,HARYANA	11/2018	2,312.26 -	2,312.26	1,361.51	09/2021 -	08/2023	23	-
144	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN - [N24001783]NHAI,HARYANA	11/2018	2,252.75 -	2,252.75	1,223.07	09/2021 -	08/2023	23	-
145	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA - [N24001784]NHAI,HARYANA	11/2018	1,935.61 -	1,935.61	856.41	09/2021 -	08/2023	23	-
146	ALIGARH-KANPUR SECTION PACKAGEV FROM MITRASEN-KANPUR - [N24001740]NHAI,UTTAR PRADESH	10/2019	2,325.28 -	2,325.28	1,836.49	09/2023 -	10/2023	1	-
147	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826]NHAI,UTTAR PRADESH	02/2019	927.77 -	1,603.00	1,104.18	02/2022 -	10/2023	20	-
148	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]NHAI,TAMIL NADU	03/2018	998.70 1,358.32	1,358.32	785.96	11/2021 -	11/2023	24	-

Costing Rs. 1000 Crore and above

(July 2023)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
149	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429]NHAI,TAMIL NADU	03/2018	1,294.47 1,588.40	1,588.40	605.20	11/2021 -	11/2023	24	-
150	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781]NHAI,DELHI	01/2018	2,067.67 -	2,160.00	1,496.49	10/2021 -	11/2023	25	-
151	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,182.94	589.65	12/2019 -	12/2023	48	-
152	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	2,360.65	4,657.47	09/2016 -	12/2023	87	-
153	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	783.15	08/2019 -	12/2023	52	-
154	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 504.09	1,015.16	355.84	09/2020 -	12/2023	39	-
155	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) - [N24001603]NHAI,TAMIL NADU	01/2019	1,518.53 -	1,518.53	844.56	10/2022 -	12/2023	14	-
156	BALANCE 4 LANING WORK OF RAIGANJ DALKHOLA SECTION OF NH34 FROM KM 398.000 TO KM 452.750 (PACKAGE V) - [N24001751]NHAI,WEST BENGAL	12/2018	1,548.07 -	1,548.07	1,086.32	09/2021 -	12/2023	27	-
157	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779]NHAI,DELHI	03/2018	2,507.00 -	3,030.73	1,155.70	09/2022 -	12/2023	15	-
158	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	1,136.83	1,016.30	05/2021 11/2022	01/2024	32	14
159	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430]NHAI,TAMIL NADU	03/2018	2,120.40 2,565.63	2,565.63	1,147.79	01/2022 -	01/2024	24	-
160	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP - [N24001824]NHAI,ANDHRA PRADESH	03/2020	1,863.09 -	2,238.00	894.15	01/2024 01/2022	01/2024	0	24
161	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	309.04	12/2020 -	02/2024	38	-
162	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) - [N24001602]NHAI,TAMIL NADU	01/2019	1,409.38 -	1,409.38	520.63	12/2022 -	02/2024	14	-
163	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH - [N24001660]NHAI,KERALA	08/2020	2,714.60 3,319.41	2,714.60	1,414.01	02/2024 11/2021	02/2024	0	27
164	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	1,433.11	06/2020 -	03/2024	45	-

Costing Rs. 1000 Crore and above

(July 2023)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
165	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU - [N24000788]NHAI, WEST BENGAL	03/2018	841.57 1,619.48	1,619.48	1,368.06	09/2022 12/2022	03/2024	18	15
166	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	2,140.93	1,912.14	11/2021 -	03/2024	28	-
167	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533]NHAI, HARYANA	11/2020	1,690.23 -	2,010.17	1,067.66	12/2023 -	03/2024	3	-
168	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF - [N24001596]NHAI, JHARKHAND	11/2021	1,302.72 -	1,302.72	521.32	07/2023 -	03/2024	8	-
169	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH-383 - [N24001605]NHAI, TAMIL NADU	06/2018	1,103.86 -	1,103.86	295.97	03/2022 -	04/2024	25	-
170	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ - [N24001663]NHAI, KERALA	06/2020	3,041.65 3,799.76	3,041.65	1,795.19	04/2024 10/2021	04/2024	0	30
171	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ - [N24001664]NHAI, KERALA	06/2020	1,746.45 2,377.88	1,746.45	879.34	04/2024 10/2021	04/2024	0	30
172	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799]NHAI, MAHARASHTRA	02/2021	1,166.96 -	1,251.00	755.96	10/2023 -	04/2024	6	-
173	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH - [N24001662]NHAI, KERALA	05/2020	1,981.07 2,430.53	1,981.07	1,121.13	05/2024 11/2021	05/2024	0	30
174	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	3,379.45	3,656.21	03/2014 -	06/2024	123	-
175	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	1,264.66	07/2020 -	06/2024	47	-
176	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788]NHAI, GUJARAT	07/2020	2,271.86 -	3,916.00	426.80	12/2023 -	06/2024	6	-
177	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789]NHAI, GUJARAT	07/2020	1,710.30 -	1,927.00	265.19	08/2023 -	06/2024	10	-
178	6L ALURU - JAKKUA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838]NHAI, ANDHRA PRADESH	02/2021	922.50 -	1,128.68	435.46	03/2024 -	06/2024	3	-
179	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	1,007.00	257.01	03/2020 07/2022	07/2024	52	24

Costing Rs. 1000 Crore and above

(July 2023)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
180	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	1,601.10	738.85	01/2024 -	07/2024	6	-
181	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 1,862.77	1,862.77	465.92	02/2023 -	09/2024	19	-
182	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	1,182.87	160.20	07/2021 -	09/2024	38	-
183	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431]NHAI,TAMIL NADU	03/2018	1,872.68 2,661.51	2,756.09	848.82	10/2020 -	09/2024	47	-
184	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	1,168.33	729.78	02/2022 08/2023	10/2024	32	14
185	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786]NHAI,GUJARAT	03/2021	1,259.00 -	1,910.00	60.25	03/2024 -	12/2024	9	-
186	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A - [N24001823]NHAI,ANDHRA PRADESH	01/2022	1,852.12 -	1,787.00	255.61	01/2025 01/2023	01/2025	0	24
	Total		98,907.48 -	1,13,765.89	67,312.72				
	<u>SHIPPING AND PORTS</u>								
	<u>Inland Waterways Authority Of India</u>								
187	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	5,369.18 4,633.10	5,362.27	2,498.52	03/2023 -	12/2026	45	-
	Total		5,369.18 -	5,362.27	2,498.52				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
188	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	21,913.00	07/2015 12/2022	09/2023	98	9
	Total		13,334.00 -	13,334.00	21,913.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
189	AHMEDABAD METRO RAIL PROJECT PHASE I - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,925.22	11,786.54	12/2018 -	12/2023	60	-
190	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17 -	5,384.17	1,428.76	03/2024 -	12/2024	9	-
191	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	12,020.32	2,396.13	03/2024 -	03/2025	12	-
	<u>Bangalore Metro Rail Corporation Limited</u>								

Costing Rs. 1000 Crore and above

(July 2023)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
192	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	20,936.29	02/2021 -	03/2025	49	-
	<u>Central Public Works Department</u>								
193	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	36.69	07/2021 -	06/2024	35	-
	<u>Delhi Metro Rail Corporation</u>								
194	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	24,948.65	7,812.66	03/2025 -	03/2026	12	-
	<u>Lucknow Metro Rail Corporation Limited</u>								
195	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	2,611.47	03/2024 -	12/2025	21	-
196	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	5,323.53	03/2024 -	06/2026	27	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
197	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	37,276.00	24,123.86	03/2020 -	12/2023	45	-
	<u>Patna Metro Rail Corporation</u>								
198	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR	02/2019	13,365.77 -	13,925.50	1,353.32	06/2024 -	09/2024	3	-
	Total		1,36,669.15 -	1,53,441.90	77,809.25				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
199	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	21,727.98	03/2020 -	03/2024	48	-
	Total		10,151.04 -	55,548.87	21,727.98				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								
200	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 1,735.25	1,900.00	1,583.95	10/2019 -	12/2023	50	-
	Total		1,219.21 -	1,900.00	1,583.95				
	<u>DPIIT</u>								
	<u>Iicc For Dpiit</u>								
201	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,401.00	4,071.81	12/2019 -	09/2023	45	-
	Total		4,773.00 -	5,401.00	4,071.81				
	Grand Total		8,30,495.71	10,94,754.83	7,01,354.30				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 1000 Crore and above					(July 2023)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	7,670.00	09/2010	12/2024	119.64	171
	Total		3,492.00	7,670.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	03/2021	03/2025	7.88	48
3	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00	3,291.81	09/2021	12/2024	138.02	39
	Total		2,525.00	4,523.81				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
4	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	08/2019	08/2024	93.35	60
	<u>Neyveli Lignite Corporation</u>							
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11	8,990.00	12/2015	02/2021	52.19	62
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00	19,406.12	11/2021	12/2023	12.58	25
	Total		25,805.84	33,542.60				
	<u>DPIIT</u>							
	<u>licc For Dpiit</u>							
7	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00	5,401.00	12/2019	09/2023	13.16	45
	Total		4,773.00	5,401.00				
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							

Costing Rs. 1000 Crore and above

(July 2023)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
8	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,900.00	10/2019 -	12/2023	55.84	50
	Total		1,219.21 -	1,900.00				
	<u>PETROLEUM</u>							
	<u>Numaligarh Refinery Limited</u>							
9	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379	01/2019	12,366.00 -	18,968.00	10/2024 -	10/2024	53.39	0
	Total		12,366.00 -	18,968.00				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
10	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 -	1,803.00	09/2019 -	09/2026	30.48	84
11	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	7,103.00	03/2013 -	12/2024	138.48	141
12	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	01/2016	10,598.98 -	10,998.00	11/2020 -	08/2023	3.76	33
13	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	17,007.00	06/2019 -	06/2024	18.38	60
	<u>Power Grid Corporation Of India Limited</u>							
14	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	08/2017	1,931.39 -	2,635.55	02/2020 -	03/2024	36.46	49
15	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,700.00	12/2018 -	01/2024	31.08	61
16	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,129.32	12/2018 -	12/2024	92.02	72
	<u>Satluj Jal Vidyut Nigam Limited</u>							
17	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	1,272.29	12/2021 -	08/2023	96.24	20
18	BIKANER SOLAR POWER PROJECT - [N18000335	04/2022	5,491.89 532.00	6,023.89	05/2024 -	05/2024	9.69	0
	<u>Thdc India Limited</u>							
19	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	4,825.60	02/2016 -	06/2024	191.23	100
	Total		48,920.24 -	67,497.65				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							

Costing Rs. 1000 Crore and above					(July 2023)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
20	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,384.72	03/2022 -	12/2024	8.85	33
21	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2026	10.94	36
22	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	03/2023 -	03/2024	8.75	12
23	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,805.17	03/2021 -	03/2026	111.54	60
24	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	6,409.38	03/2024 -	03/2024	76.69	0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
25	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	- -	-	341.96	0
	<u>East Central Railways</u>							
26	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,110.00	03/2012 -	06/2023	241.82	135
27	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,510.00	- -	03/2024	358.42	0
28	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,700.00	- -	03/2024	356.82	0
	<u>East Coast Railway</u>							
29	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,440.00	03/2020 -	03/2024	24.14	48
30	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2025	137.80	45
	<u>Eastern Railways</u>							
31	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2024	36.22	60
32	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
33	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	04/2013	3,055.00 -	3,438.39	09/2018 -	12/2023	12.55	63
	<u>Metropolitan Rapid Transport Projects</u>							
34	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135]	03/2013	4,874.58 -	10,442.41	03/2016 -	12/2023	114.22	93
	<u>North Central Railway</u>							
35	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
36	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	1,187.49	03/2020 -	10/2024	186.25	55

Costing Rs. 1000 Crore and above

(July 2023)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
37	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,304.62	03/2019 -	-	238.69	0
38	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING [N22000183]	04/2013	1,798.00 -	2,647.51	03/2019 -	01/2024	47.25	58
39	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,650.00	03/2019 -	03/2024	397.31	60
40	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	4,059.65	03/2022 -	03/2026	81.86	48
41	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	03/2015 -	03/2026	186.39	132
42	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	7,876.92	12/2015 -	12/2023	488.06	96
43	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	8,324.28	03/2021 -	-	818.33	0
44	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	9,362.06	03/2014 -	02/2024	291.15	119
45	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.79	03/2011 -	03/2025	221.56	168
	<u>North Eastern Railway</u>							
46	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]	04/2016	1,177.96 -	1,500.95	12/2019 -	03/2024	27.42	51
47	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	2,560.00	03/2022 -	10/2023	97.62	19
	<u>Northern Railway</u>							
48	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	07/2012 -	11/2024	348.44	148
	<u>Rail Vikas Nigam Ltd.</u>							
49	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,457.79	03/2019 -	03/2024	57.26	60
50	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,500.00	03/2022 -	12/2023	58.97	21
51	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,536.00	03/2020 -	08/2023	102.11	41
52	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,552.26	03/2019 -	05/2023	64.62	50
53	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
54	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,300.00	03/2023 -	03/2024	55.15	12
55	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
56	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0

Costing Rs. 1000 Crore and above

(July 2023)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
57	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,834.54	03/2016 -	07/2025	65.94	112
58	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	12/2026 -	03/2025	127.62	-21
59	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	8,964.35	03/2016 -	03/2026	126.83	120
60	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	24,659.00	12/2024 -	03/2025	52.07	3
	<u>South Central Railway</u>							
61	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2025	5.16	24
62	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,500.98	03/2009 -	03/2027	139.28	216
63	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	1,160.48 -	3,014.00	03/2010 -	03/2025	159.72	180
64	NADIKUDE-SRI KALAHASTI - [N22000286	04/2011	2,288.70 -	3,122.35	03/2021 -	03/2021	36.42	0
65	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,381.68	03/2000 -	03/2000	96.27	0
66	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	03/2022 -	12/2025	7.06	45
	<u>South East Central Railway</u>							
67	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	12/2021 -	12/2025	378.60	48
68	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,680.00	12/2021 -	12/2024	22.63	36
69	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,544.25	03/2023 -	12/2024	85.71	21
	<u>South Western Railway</u>							
70	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 -	1,649.31	03/2016 -	03/2026	67.22	120
71	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,960.00	03/2019 -	12/2024	21.39	69
72	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	2,315.00 -	5,174.30	- -	03/2030	123.51	0
	<u>Southern Railway</u>							
73	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400	02/2015	1,000.00 -	1,339.00	- -	03/2025	33.90	0
74	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,053.39	03/2019 -	12/2027	1,601.23	105
75	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	3,118.34	02/2019 -	03/2025	330.30	73
76	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	3,620.28	- -	12/2025	521.16	0
	<u>West Central Railway</u>							

Costing Rs. 1000 Crore and above

(July 2023)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
77	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	03/2022 -	09/2024	114.32	30
78	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	3,032.46	03/2021 -	12/2025	614.19	57
79	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>							
80	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123	04/2008	318.24 -	1,095.12	03/2012 -	03/2024	244.12	144
81	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	6,021.00	03/2022 -	03/2026	71.85	48
	Total		1,26,718.29 -	2,89,900.39				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
82	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	12/2023	.00	49
83	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	02/2023	.00	39
84	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	- -	05/2023	2.93	0
	<u>National Highways Authority Of India</u>							
85	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	1,007.00	03/2020 -	07/2024	35.23	52
86	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736	01/2018	686.65 -	1,015.16	09/2020 -	12/2023	47.84	39
87	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 - [N24001589	09/2020	755.26 -	1,039.00	03/2024 -	03/2024	37.57	0
88	6L OF PONDAVAKKAM TO KANNIGAIPAIR FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) - [N24001818	02/2021	818.73 -	1,105.00	01/2025 -	01/2025	34.97	0
89	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	08/2019 -	05/2024	16.55	57
90	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B - [N24001796	03/2022	1,013.33 -	1,111.33	10/2024 -	10/2024	9.67	0
91	6L ALURU - JAKKUBA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) - [N24001838	02/2021	922.50 -	1,128.68	03/2024 -	06/2024	22.35	3
92	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 -	1,136.83	05/2021 -	01/2024	137.46	32

Costing Rs. 1000 Crore and above								
(July 2023)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
93	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A - [N24001690	01/2021	1,167.52 1,658.00	1,167.52	01/2023 -	06/2023	.00	5
94	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 -	1,168.33	02/2022 -	10/2024	22.90	32
95	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507	12/2015	1,167.45 -	1,182.94	12/2019 -	12/2023	1.33	48
96	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J - [N24001799	02/2021	1,166.96 -	1,251.00	10/2023 -	04/2024	7.20	6
97	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 - [N24001720	10/2020	1,023.91 -	1,285.00	05/2024 -	05/2024	25.50	0
98	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP - [N24001821	11/2020	1,137.74 -	1,289.00	10/2024 -	10/2024	13.29	0
99	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) - [N24001819	03/2021	1,102.63 -	1,303.00	01/2025 -	01/2025	18.17	0
100	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE - [N24001822	12/2020	1,075.27 -	1,307.00	10/2024 -	10/2024	21.55	0
101	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) - [N24001812	03/2021	1,002.11 -	1,358.00	05/2024 -	05/2024	35.51	0
102	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 - [N24001721	02/2019	1,008.99 -	1,361.00	05/2024 -	05/2024	34.89	0
103	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 -	1,361.00	12/2020 -	10/2023	8.78	34
104	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT - [N24001785	03/2022	1,373.06 -	1,373.06	06/2025 -	06/2025	.00	0
105	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH - [N24001595	08/2020	1,034.00 -	1,589.00	03/2024 -	03/2024	53.68	0
106	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 - [N24001826	02/2019	927.77 -	1,603.00	02/2022 -	10/2023	72.78	20
107	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361 - [N24001805	03/2018	1,169.04 -	1,693.95	03/2021 -	06/2023	44.90	27
108	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) - [N24001820	02/2021	1,484.83 -	1,768.00	12/2024 -	12/2024	19.07	0
109	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU - [N24001786	03/2021	1,259.00 -	1,910.00	03/2024 -	12/2024	51.71	9

Costing Rs. 1000 Crore and above							(July 2023)	
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
110	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA - [N24001789	07/2020	1,710.30 -	1,927.00	08/2023 -	06/2024	12.67	10
111	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP - [N24001533	11/2020	1,690.23 -	2,010.17	12/2023 -	03/2024	18.93	3
112	TUMKUR - NELAMANGALA(6L) - [N24001681	08/2022	2,032.15 1,351.00	2,032.15	08/2025 -	08/2025	.00	0
113	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER - [N24001743	01/2018	1,916.38 -	2,078.00	02/2023 -	08/2023	8.43	6
114	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80 - [N24001806	03/2018	1,241.38 -	2,122.64	03/2023 -	06/2023	70.99	3
115	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O - [N24001781	01/2018	2,067.67 -	2,160.00	10/2021 -	11/2023	4.47	25
116	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835	03/2018	1,484.30 -	2,182.41	12/2020 -	05/2023	47.03	29
117	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U - [N24001739	10/2019	1,779.83 -	2,200.00	11/2023 -	11/2023	23.61	0
118	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP - [N24001824	03/2020	1,863.09 -	2,238.00	01/2024 -	01/2024	20.12	0
119	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	09/2016 -	12/2023	41.78	87
120	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH - [N24001755	10/2019	1,936.68 -	2,458.03	03/2023 -	08/2023	26.92	5
121	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431	03/2018	1,872.68 -	2,756.09	10/2020 -	09/2024	47.17	47
122	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) - [N24001779	03/2018	2,507.00 -	3,030.73	09/2022 -	12/2023	20.89	15
123	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	03/2014 -	06/2024	18.66	123
124	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT - [N24001719	02/2021	2,948.31 -	3,392.00	07/2024 -	07/2024	15.05	0
125	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH - [N24001659	02/2021	3,375.31 -	3,790.17	07/2024 -	07/2024	12.29	0
126	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU - [N24001788	07/2020	2,271.86 -	3,916.00	12/2023 -	06/2024	72.37	6
127	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH - 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX - [N24001655	06/2021	3,606.00 -	3,923.82	02/2025 -	02/2025	8.81	0

Costing Rs. 1000 Crore and above

(July 2023)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
128	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. - [N24001656	06/2021	2,595.00 -	3,994.60	03/2025 -	03/2025	53.93	0
129	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM - [N24001658	01/2021	4,265.42 -	4,708.42	07/2024 -	07/2024	10.39	0
	Total		76,156.65 -	94,147.52				
	<u>SHIPPING AND PORTS</u>							
	<u>Inland Waterways Authority Of India</u>							
130	JAL MARG VIKAS PROJECT - [N25000072	01/2018	5,369.18 -	5,362.27	03/2023 -	12/2026	-13	45
	Total		5,369.18 -	5,362.27				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
131	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	12/2018 -	12/2023	19.98	60
	<u>Chennai Metro Rail Ltd</u>							
132	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	18,380.00	12/2015 -	12/2015	25.89	0
	<u>Delhi Metro Rail Corporation</u>							
133	DELHI MRTS PHASE-III - [N28000056	09/2011	38,585.00 -	40,180.91	03/2016 -	08/2021	4.14	65
	<u>Kochi Metro Rail Corporation Ltd</u>							
134	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	07/2017 -	09/2020	20.00	38
	<u>Mumbai Metro Rail Corporation Ltd</u>							
135	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	37,276.00	03/2020 -	12/2023	61.12	45
	<u>Patna Metro Rail Corporation</u>							
136	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 -	13,925.50	06/2024 -	09/2024	4.19	3
	Total		1,05,641.56 -	1,28,905.77				
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
137	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	03/2020 -	03/2024	447.22	48
	Total		10,151.04 -	55,548.87				
	Grand Total		4,23,138.01	7,13,367.88				

North East Projects Costing Rs.150 crore and above (as on					31.07.2023)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (12/2023) [12/2023]	645.63 (-) [645.63]	636.43 (0.00) [16]
	<u>Power</u>				
2	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH	2/2023	2/2032 (-) [2/2032]	31,876.39 (-) [31,876.39]	2,177.22 (0.00) [0]
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (5/2025) [5/2025]	6,285.33 (21,247.54) [21,247.54]	18,903.19 (14,962.21) [176]
	<u>Road Transport And Highways</u>				
4	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	3/2027 (-) [3/2027]	496.47 (-) [496.47]	103.90 (0.00) [0]
5	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	3/2027 (-) [3/2027]	437.60 (-) [437.60]	210.88 (0.00) [0]
6	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	263.61 (0.00) [0]
7	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	334.89 (0.00) [0]
8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	3/2027 (-) [3/2027]	403.68 (-) [403.68]	346.74 (0.00) [0]
9	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	3/2027 (-) [3/2027]	543.05 (-) [543.05]	414.11 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	3/2027 (-) [3/2027]	450.65 (-) [450.65]	272.11 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	3/2027 (-) [3/2027]	486.70 (-) [486.70]	415.54 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	3/2027 (-) [3/2027]	560.39 (-) [560.39]	531.18 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	3/2027 (-) [3/2027]	394.27 (-) [394.27]	412.07 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	3/2027 (-) [3/2027]	421.48 (-) [421.48]	349.87 (0.00) [0]
15	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM	12/2016	1/2020 (1/2022)	200.44 (200.44)	146.43 (0.00)

	120.		[8/2023]	[200.44]	[43]
16	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	12/2019 (3/2023) [9/2023]	568.92 (568.92) [568.92]	493.58 (0.00) [45]
17	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	3/2022 (12/2023) [3/2024]	1,718.59 (1,718.59) [1,718.59]	656.26 (0.00) [24]
18	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (5/2024) [5/2024]	301.06 (-) [301.06]	96.33 (0.00) [25]
19	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (10/2022) [3/2024]	353.90 (-) [353.90]	41.82 (0.00) [22]
20	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2022 (7/2023) [7/2023]	167.28 (229.70) [167.28]	138.66 (0.00) [15]
21	DEMBUEN - BRUNI	12/2020	3/2023 (-) [11/2023]	606.63 (606.63) [606.63]	270.03 (0.00) [8]
22	DOGINALA - GAU	12/2020	9/2022 (-) [8/2023]	242.30 (-) [242.30]	21.47 (0.00) [11]
23	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (7/2023) [7/2023]	228.71 (-) [228.71]	90.14 (0.00) [15]
24	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (7/2023) [7/2023]	294.04 (-) [294.04]	129.38 (0.00) [15]
25	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (7/2023) [7/2023]	199.03 (-) [199.03]	101.66 (0.00) [15]
26	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (11/2023) [11/2023]	184.88 (-) [184.88]	71.91 (0.00) [19]
27	LADDA - BASAI	2/2021	4/2023 (-) [2/2024]	445.96 (-) [445.96]	75.67 (0.00) [10]
28	TADADEGE - HENKAR	2/2021	3/2023 (-) [6/2024]	550.45 (-) [550.45]	61.12 (0.00) [15]
29	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	11/2023 (11/2023) [11/2023]	180.57 (244.10) [180.57]	96.11 (0.00) [0]
30	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	5/2023 (5/2023) [5/2023]	256.66 (-) [256.66]	0.00 (0.00) [0]
31	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (12/2021) [5/2023]	1,979.00 (-) [2,036.90]	1,253.04 (57.90) [0]
32	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	3/2027 (-) [3/2027]	182.55 (-) [182.55]	72.99 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
33	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2025]	1,142.00 (-) [1,232.00]	365.49 (90.00) [48]
	<u>Health And Family Welfare</u>				
34	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (12/2022) [10/2023]	875.00 (890.14) [860.00]	684.50 (-15.00) [29]

	Petroleum				
35	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA	6/2022	10/2025 (-) [10/2025]	768.00 (-) [768.00]	1.39 (0.00) [0]
36	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM	3/2023	3/2026 (3/2026) [3/2026]	156.36 (156.36) [156.36]	0.36 (0.00) [0]
37	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (3/2023) [9/2023]	543.91 (-) [661.21]	439.99 (117.30) [43]
38	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	236.12 (0.00) [0]
39	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [7/2024]	218.38 (-) [218.38]	66.27 (0.00) [17]
40	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	6,125.60 (6,602.00) [0]
41	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	5,608.65 (-1,170.00) [0]
42	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING	12/2020	7/2024 (-) [3/2024]	430.76 (-) [430.76]	118.55 (0.00) [-4]
43	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM	3/2022	7/2026 (-) [9/2026]	277.00 (-) [277.00]	35.19 (0.00) [2]
44	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM	3/2023	12/2026 (-) [12/2026]	384.04 (-) [384.04]	0.35 (0.00) [0]
45	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT	6/2021	12/2024 (-) [12/2024]	860.00 (-) [860.00]	101.03 (0.00) [0]
	Power				
46	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C	3/2019	3/2023 (-) [9/2023]	1,326.00 (-) [1,326.00]	1,367.92 (0.00) [6]
	Railways				
47	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2026]	2,232.32 (-) [4,059.65]	2,898.81 (1,827.33) [48]
48	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [0/0]	385.20 (-) [1,304.62]	1,104.78 (919.42) [0]
	Road Transport And Highways				
49	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [3/2024]	261.13 (-) [261.13]	51.90 (0.00) [21]
50	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2023]	217.50 (-) [217.50]	48.14 (0.00) [0]
51	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [6/2023]	216.49 (241.52) [216.49]	101.02 (0.00) [0]
52	4 LANING FROM JAMUGURI TO BISWANATH CHARALI FROM KM 182 TO KM 208 OF NH-52	1/1991	6/2019 (6/2019) [4/2023]	520.01 (-) [520.01]	277.79 (0.00) [0]
53	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (2/2022) [6/2023]	588.95 (811.28) [873.91]	647.07 (284.96) [0]

54	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (7/2021) [5/2023]	289.99 (-) [289.99]	216.08 (0.00) [0]
55	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	12/2021 (12/2019) [8/2023]	252.00 (330.30) [330.30]	146.28 (78.30) [20]
56	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	8/2023 (-) [11/2023]	437.39 (-) [437.39]	224.61 (0.00) [3]
57	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [7/2024]	294.17 (-) [294.17]	248.08 (0.00) [102]
58	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	1,340.72 (0.00) [0]
59	4-LANING OF DERGAON TOWN	3/2020	6/2022 (-) [6/2023]	287.63 (-) [287.63]	383.88 (0.00) [0]
60	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [8/2023]	220.20 (-) [220.20]	168.60 (0.00) [8]
61	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146	12/2021	8/2024 (-) [8/2024]	300.00 (-) [300.00]	223.00 (0.00) [0]
62	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI	3/2022	6/2024 (-) [6/2024]	457.72 (-) [457.72]	33.65 (0.00) [0]
63	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH	8/2022	12/2022 (-) [6/2024]	175.00 (-) [175.00]	66.50 (0.00) [18]
64	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23	3/2022	1/2026 (-) [1/2026]	1,909.98 (-) [1,909.98]	22.90 (0.00) [0]
65	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	76.97 (0.00) [0]
66	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA	3/2022	4/2025 (-) [4/2025]	535.03 (-) [535.03]	0.00 (0.00) [0]
67	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [5/2023]	335.88 (-) [335.88]	211.73 (0.00) [0]
68	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [6/2023]	260.07 (-) [260.07]	284.93 (0.00) [0]
69	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [10/2023]	288.85 (-) [288.85]	110.33 (0.00) [9]
70	DABOKA KATHKATI PACKAGE-6	9/2021	7/2024 (-) [7/2024]	625.64 (-) [625.64]	265.02 (0.00) [0]
71	DABOKA KATHKATI PACKAGE-7	11/2021	7/2024 (-) [7/2024]	204.10 (-) [204.10]	54.66 (0.00) [0]
72	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1	3/2022	7/2024 (-) [7/2024]	215.27 (-) [215.27]	50.37 (0.00) [0]
73	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2	4/2022	7/2024 (-) [1/2024]	170.95 (-) [170.95]	22.38 (0.00) [-6]
74	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3	1/2023	5/2025	458.59	0.00

			(-) [5/2025]	(-) [458.59]	(0.00) [0]
75	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	6/2020 (6/2020) [12/2023]	818.00 (887.68) [818.00]	659.65 (0.00) [42]
76	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	3/2024 (-) [3/2024]	463.49 (-) [463.49]	284.31 (0.00) [0]
77	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [6/2023]	829.00 (-) [829.00]	819.58 (0.00) [0]
78	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [6/2023]	454.89 (814.56) [814.56]	498.86 (359.67) [0]
79	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2	3/2022	1/2025 (-) [1/2025]	909.02 (-) [909.02]	72.25 (0.00) [0]
80	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	508.56 (0.00) [0]
81	JOGIGHOPA BRIDGE	8/2021	11/2024 (-) [11/2024]	746.76 (-) [746.76]	144.33 (0.00) [0]
82	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	8/2023 (-) [8/2023]	1,049.51 (-) [1,049.51]	293.67 (0.00) [0]
83	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH	7/2017	4/2020 (-) [6/2023]	442.23 (-) [442.23]	192.31 (0.00) [0]
84	SRIRAMPUR - DHUBRI PKG-1	3/2022	2/2025 (-) [2/2025]	613.89 (-) [613.89]	0.00 (0.00) [0]
85	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [10/2023]	636.42 (-) [418.49]	544.79 (-217.93) [10]
86	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	36.36 (0.00) [0]
87	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (820.56) [761.54]	425.77 (0.00) [0]
88	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [7/2024]	208.84 (-) [208.84]	90.92 (0.00) [27]
	<u>MANIPUR</u>				
	<u>Civil Aviation</u>				
89	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX	11/2021	7/2024 (12/2024) [12/2024]	499.00 (-) [499.00]	83.88 (0.00) [5]
	<u>Railways</u>				
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (3/2025) [3/2025]	4,454.17 (12,264.15) [14,322.79]	13,763.33 (9,868.62) [168]
	<u>Road Transport And Highways</u>				
91	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [5/2023]	167.95 (-) [167.95]	84.16 (0.00) [0]
92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [5/2023]	292.24 (-) [292.24]	127.86 (0.00) [0]
93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-	6/2020	8/2022	365.53	142.51

	102B (PKG- 2B)		(-) [5/2023]	(-) [365.53]	(0.00) [0]
94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [5/2023]	167.95 (204.12) [167.95]	77.72 (0.00) [0]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [5/2023]	177.76 (-) [177.76]	70.23 (0.00) [0]
96	AKASH BRIDGE - JESSAMI SECTION PKG-2	3/2022	2/2025 (-) [2/2025]	152.11 (-) [152.11]	0.00 (0.00) [0]
97	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [8/2023]	673.27 (-) [673.27]	281.57 (0.00) [-2]
98	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM	9/2021	2/2024 (-) [2/2024]	310.76 (-) [310.76]	66.01 (0.00) [0]
99	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [11/2023]	195.14 (-) [195.14]	34.94 (0.00) [11]
100	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [9/2023]	467.00 (-) [467.00]	139.15 (0.00) [6]
101	IMPHAL - KHONGSANG PKG-4	8/2021	12/2023 (-) [12/2023]	579.63 (-) [579.63]	53.90 (0.00) [0]
102	IMPHAL - KHONGSANG PKG-5	12/2021	5/2024 (-) [5/2024]	410.68 (-) [410.68]	40.52 (0.00) [0]
103	IMPHAL - KHONGSANG PKG-6	12/2021	2/2025 (-) [2/2025]	504.76 (-) [504.76]	16.43 (0.00) [0]
104	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [5/2023]	277.99 (-) [277.99]	123.86 (0.00) [0]
105	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [8/2023]	259.31 (-) [259.31]	136.05 (0.00) [8]
106	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	22.08 (0.00) [0]
107	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
108	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [8/2023]	379.39 (-) [379.39]	186.51 (0.00) [16]
109	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [3/2023]	471.00 (-) [471.00]	319.81 (0.00) [0]
110	MARAM - PEREN PKG-3	8/2021	5/2023 (-) [11/2023]	467.41 (-) [467.41]	126.80 (0.00) [6]
111	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [10/2023]	188.36 (-) [188.36]	81.38 (0.00) [10]
112	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	126.78 (0.00) [0]
113	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-)	226.32 (-)	47.15 (0.00)

			[10/2023]	[226.32]	[10]
114	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [8/2023]	232.26 (-) [232.26]	147.43 (0.00) [8]
115	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [5/2024]	211.70 (-) [211.70]	1.64 (0.00) [16]
116	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	52.65 (0.00) [0]
117	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	197.54 (0.00) [0]
118	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [4/2023]	234.08 (-) [234.08]	111.25 (0.00) [0]
119	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [4/2023]	198.77 (-) [198.77]	53.84 (0.00) [0]
120	TAMENGLONG - MAHUR PKG-5	8/2021	5/2023 (-) [5/2023]	477.86 (-) [477.86]	68.12 (0.00) [0]
121	TAMENGLONG - MAHUR PKG-6	9/2021	5/2023 (-) [5/2023]	311.18 (-) [311.18]	121.73 (0.00) [0]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
122	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (12/2023) [12/2023]	484.32 (429.70) [429.70]	262.25 (-54.62) [111]
	<u>Doner</u>				
123	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [9/2017]	151.33 (-) [151.33]	148.33 (0.00) [0]
	<u>Railways</u>				
124	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [8,324.28]	269.80 (7,417.82) [0]
	<u>Road Transport And Highways</u>				
125	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	181.82 (0.00) [0]
126	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	3/2022 (-) [10/2023]	306.28 (-) [306.28]	196.84 (0.00) [19]
127	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	45.46 (0.00) [0]
128	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [9/2023]	525.68 (-) [525.68]	357.03 (0.00) [-3]
129	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [7/2023]	445.51 (-) [445.51]	191.35 (0.00) [-5]
130	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2	11/2021	6/2024 (-) [6/2024]	283.50 (261.40) [283.50]	96.86 (0.00) [0]
131	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [11/2023]	260.21 (-) [260.21]	149.15 (0.00) [11]
132	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4	10/2020	4/2022	157.86	102.41

	(KANAI-RONGARA)		(-) [1/2024]	(-) [157.86]	(0.00) [21]
133	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06	8/2020	2/2022 (1/2024) [1/2024]	302.88 (-) [302.88]	91.62 (0.00) [23]
134	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM	9/2021	5/2024 (-) [5/2024]	359.86 (-) [359.86]	169.42 (0.00) [0]
135	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	9/2021 (9/2021) [7/2023]	553.51 (610.09) [553.51]	290.35 (0.00) [22]
	<u>MIZORAM</u>				
	<u>Railways</u>				
136	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [2/2024]	2,393.47 (5,021.45) [9,362.06]	6,591.01 (6,968.59) [119]
	<u>Road Transport And Highways</u>				
137	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2023) [6/2023]	195.04 (434.65) [377.99]	415.11 (182.95) [0]
138	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (6/2023) [6/2023]	186.96 (-) [322.24]	312.50 (135.28) [0]
139	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2023) [6/2023]	193.69 (374.59) [327.92]	364.32 (134.23) [0]
140	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (7/2023) [10/2023]	275.02 (-) [275.02]	166.23 (0.00) [12]
141	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (8/2023) [12/2023]	206.88 (219.33) [278.98]	227.33 (72.10) [17]
142	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (8/2023) [12/2023]	292.24 (331.17) [331.17]	235.26 (38.93) [17]
143	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (7/2023) [10/2023]	281.78 (253.41) [253.41]	228.20 (-28.37) [15]
144	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (11/2023) [11/2023]	374.39 (374.39) [374.39]	267.81 (0.00) [11]
145	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (7/2023) [1/2024]	233.25 (233.25) [233.25]	153.10 (0.00) [13]
146	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (1/2024) [1/2024]	674.71 (674.71) [674.71]	521.28 (0.00) [7]
147	KEIFANG - TUVAI PKG-1	9/2021	5/2023 (2/2024) [4/2024]	492.94 (492.94) [492.94]	230.26 (0.00) [11]
148	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (10/2023) [12/2024]	698.44 (698.45) [698.45]	227.20 (0.01) [24]
149	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (11/2023) [12/2024]	740.58 (740.58) [740.58]	104.66 (0.00) [23]
150	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2023 (1/2024) [1/2024]	519.09 (775.47) [775.47]	532.37 (256.38) [9]
151	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC	4/2017	6/2023 (12/2023)	642.96 (1,139.85)	528.71 (496.89)

	IMPROVEMENTS FRO		[1/2024]	[1,139.85]	[7]
152	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2023 (10/2023) [1/2024]	537.82 (820.42) [820.42]	619.87 (282.60) [9]
153	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2024 (7/2024) [7/2024]	404.29 (723.80) [723.80]	452.54 (319.51) [3]
154	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2023 (5/2024) [5/2024]	428.11 (777.50) [777.50]	437.46 (349.39) [8]
155	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	6/2023 (2/2024) [2/2024]	518.53 (902.20) [902.20]	623.42 (383.67) [8]
156	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2023 (11/2023) [1/2024]	473.18 (667.06) [667.06]	465.49 (193.88) [9]
157	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	7/2023 (2/2024) [2/2024]	640.07 (1,134.72) [640.07]	965.74 (0.00) [7]
158	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (6/2023) [6/2023]	624.41 (1,109.88) [992.67]	1,021.46 (368.26) [0]
	NAGALAND				
	Railways				
159	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	2,556.74 (4,336.48) [132]
	Road Transport And Highways				
160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2022 (1/2023) [8/2023]	285.68 (-) [285.68]	155.93 (0.00) [11]
161	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2020 (8/2022) [9/2023]	387.00 (-) [387.00]	384.58 (0.00) [36]
162	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	11/2022 (6/2023) [12/2023]	500.09 (583.31) [500.09]	299.49 (0.00) [13]
163	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (3/2023) [8/2023]	320.97 (-) [320.97]	168.47 (0.00) [14]
164	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (2/2023) [12/2023]	355.79 (-) [355.79]	109.24 (0.00) [18]
165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (6/2023) [12/2023]	361.53 (-) [361.53]	112.55 (0.00) [18]
166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (3/2023) [3/2023]	330.78 (-) [330.78]	199.02 (0.00) [0]
167	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (12/2022) [3/2024]	330.80 (-) [330.80]	83.11 (0.00) [27]
168	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (10/2022) [6/2023]	278.95 (-) [278.95]	161.69 (0.00) [0]
169	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (9/2022) [0/0]	206.53 (-) [206.53]	98.69 (0.00) [0]
170	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5-LEGGED J	3/2022	12/2024 (-) [12/2024]	605.36 (-) [605.36]	82.51 (0.00) [0]

171	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (2/2023) [2/2023]	217.35 (-) [217.35]	197.79 (0.00) [0]
172	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (2/2023) [7/2023]	257.15 (-) [257.15]	124.52 (0.00) [15]
173	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [3/2024]	202.36 (-) [202.36]	62.66 (0.00) [23]
174	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [7/2024]	277.44 (-) [277.44]	134.18 (0.00) [21]
175	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	12/2021 (3/2023) [3/2023]	315.03 (-) [315.03]	212.85 (0.00) [0]
176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	12/2021 (3/2023) [4/2023]	240.64 (255.58) [240.64]	172.36 (0.00) [0]
177	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	12/2021 (8/2022) [12/2023]	215.79 (-) [215.79]	97.45 (0.00) [24]
178	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	10/2022 (10/2022) [10/2023]	272.89 (-) [272.89]	145.48 (0.00) [12]
179	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (6/2023) [3/2024]	323.98 (-) [323.98]	70.01 (0.00) [66]
180	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	9/2019 (9/2019) [9/2023]	373.07 (489.01) [387.00]	377.90 (13.93) [48]
181	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2019 (8/2019) [9/2023]	396.52 (519.72) [396.52]	330.51 (0.00) [49]
182	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2022 (8/2022) [1/2023]	429.52 (562.98) [429.52]	267.69 (0.00) [0]
183	MERANGKONG-TAMLU-MON (MTM) PKG-5	7/2021	12/2023 (-) [3/2024]	161.73 (-) [161.73]	32.41 (0.00) [3]
184	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [0/0]	207.33 (-) [207.33]	0.00 (0.00) [0]
185	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (2/2023) [6/2023]	258.52 (-) [258.52]	57.58 (0.00) [0]
186	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [8/2023]	315.63 (-) [315.63]	42.64 (0.00) [16]
187	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I	6/2020	9/2024 (9/2024) [9/2024]	252.19 (-) [252.19]	0.28 (0.00) [0]
188	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (5/2023) [5/2023]	237.51 (-) [237.51]	200.01 (0.00) [0]
189	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N	3/2021	7/2024 (7/2024) [7/2024]	297.24 (-) [297.24]	44.41 (0.00) [0]
190	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO	3/2021	2/2024 (2/2024) [2/2024]	226.44 (-) [226.44]	50.91 (0.00) [0]
	SIKKIM				

	<u>Department Of Higher Education</u>				
191	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM	8/2020	1/2025 (-) [12/2024]	314.06 (-) [303.55]	15.70 (-10.51) [-1]
	<u>Power</u>				
192	RANGIT IV HE PROJECT	3/2021	5/2024 (8/2024) [8/2024]	938.29 (938.29) [938.29]	658.71 (0.00) [3]
193	TEESTA VI HE PROJECT	3/2019	3/2024 (8/2026) [8/2026]	5,748.04 (-) [5,748.04]	2,643.25 (0.00) [29]
	<u>Railways</u>				
194	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [7,876.92]	3,290.96 (6,537.44) [96]
	<u>Road Transport And Highways</u>				
195	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (9/2023) [9/2023]	230.45 (244.91) [244.91]	190.66 (14.46) [5]
196	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [5/2024]	493.42 (478.79) [478.79]	230.22 (-14.63) [6]
197	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [1/2024]	311.00 (273.78) [273.78]	200.01 (-37.22) [9]
198	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [10/2023]	345.38 (395.59) [395.59]	300.58 (50.21) [6]
199	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [4/2024]	183.31 (439.56) [439.56]	322.34 (256.25) [23]
200	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [8/2024]	262.84 (414.20) [414.20]	185.56 (151.36) [15]
201	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOL TO BURTUK (L=23.316KM)	10/2021	5/2024 (5/2024) [5/2024]	385.15 (-) [385.15]	81.83 (0.00) [0]
202	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	4/2022 (5/2022) [12/2023]	375.80 (-) [375.80]	270.63 (0.00) [20]
203	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	10/2020 (8/2023) [8/2023]	290.05 (-) [290.05]	218.36 (0.00) [34]
204	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (9/2024) [9/2024]	816.79 (786.60) [786.60]	204.88 (-30.19) [9]
205	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [1/2024]	402.94 (-) [402.94]	188.53 (0.00) [21]
206	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (8/2023) [12/2023]	295.97 (-) [295.97]	190.56 (0.00) [8]
207	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [12/2023]	242.97 (-) [242.97]	204.16 (0.00) [18]
208	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (10/2023) [11/2024]	292.80 (-) [292.80]	94.56 (0.00) [30]
209	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	117.90 (0.00) [0]

210	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (2/2024) [2/2024]	410.60 (379.30) [379.30]	147.62 (-31.30) [0]
	<u>TRIPURA</u>				
	<u>Petroleum</u>				
211	CREATION OF GAS DEHYDRATION FACILITIES	3/2022	5/2024 (-) [5/2024]	209.33 (-) [209.33]	20.50 (0.00) [0]
212	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT	6/2022	8/2025 (-) [8/2025]	656.00 (-) [656.00]	98.04 (0.00) [0]
	<u>Railways</u>				
213	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022) [9/2022]	569.63 (-) [708.73]	380.92 (139.10) [0]
	<u>Road Transport And Highways</u>				
214	2 LANING FROM MANU-SIMLUNG PKG-2	2/2022	1/2025 (-) [1/2025]	456.88 (-) [456.88]	11.22 (0.00) [0]
215	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (6/2023) [12/2023]	201.99 (-) [201.99]	117.12 (0.00) [23]
216	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (10/2022) [8/2023]	247.76 (251.89) [251.89]	137.58 (4.13) [19]
217	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (4/2023) [7/2023]	347.36 (-) [347.36]	224.48 (0.00) [18]
218	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (10/2022) [6/2023]	173.17 (-) [173.17]	64.05 (0.00) [0]
219	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (3/2023) [4/2023]	165.54 (-) [210.54]	85.02 (45.00) [0]
220	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (4/2023) [5/2023]	280.91 (296.48) [296.48]	202.06 (15.57) [0]
221	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (6/2023) [10/2023]	159.13 (171.50) [171.50]	67.62 (12.37) [16]
222	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (4/2023) [4/2023]	332.14 (-) [332.14]	148.07 (0.00) [0]
223	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (6/2023) [11/2023]	354.79 (-) [354.79]	33.27 (0.00) [11]
224	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR- KURTI BRID	3/2020	7/2022 (8/2023) [8/2023]	178.43 (-) [208.74]	77.89 (30.31) [13]
225	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (3/2023) [7/2023]	154.51 (-) [154.51]	73.74 (0.00) [12]
226	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (6/2023) [1/2024]	277.50 (302.02) [302.02]	201.23 (24.52) [24]
227	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (5/2023) [5/2023]	197.67 (236.18) [236.18]	211.12 (38.51) [0]
	Total			1,72,552.26 (70,659.62) [2,35,380.33]	1,12,286.77 (62,828.07)

Details of Central Sector Projects Costing Rs.150 crore and above (as on)					31.07.2023)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ANDAMAN AND NICOBAR ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (5/2023) [6/2023]	417.23 (707.73) [707.73]	674.47 (290.50) [0]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2019 (3/2023) [1/2024]	409.85 (-) [409.85]	207.65 (0.00) [49]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [9/2023]	401.00 (401.00) [401.00]	260.08 (0.00) [50]
4	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	1/2022 (-) [3/2024]	262.97 (-) [262.97]	92.73 (0.00) [26]
5	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	214.90 (-19.34) [0]
6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	9/2020 (1/2023) [6/2024]	391.00 (-) [391.00]	170.37 (0.00) [45]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	9/2020 (11/2022) [1/2024]	234.27 (-) [234.27]	124.29 (0.00) [40]
8	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (4/2023) [4/2023]	237.80 (-) [238.00]	109.61 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
9	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [6/2024]	611.80 (-) [611.80]	217.58 (0.00) [15]
10	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (12/2021) [10/2023]	177.10 (-) [177.10]	142.52 (0.00) [44]
	<u>Department Of Higher Education</u>				
11	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	9/2019	9/2022 (-) [12/2023]	588.72 (-) [588.72]	457.26 (0.00) [15]
12	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [4/2023]	655.34 (-) [655.34]	366.21 (0.00) [0]
	<u>Petroleum</u>				
13	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS	3/2022	3/2030 (-) [3/2030]	1,420.00 (-) [1,420.00]	25.37 (0.00) [0]
14	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	8/2027 (3/2030) [3/2030]	2,880.00 (-) [2,880.00]	206.83 (0.00) [31]

15	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (5/2023) [5/2023]	466.00 (-) [466.00]	415.73 (0.00) [0]
16	CREATION OF GDU AND DPD FACILITIES AT RAJAHMUNDY	3/2022	5/2024 (-) [5/2024]	211.22 (-) [211.22]	6.03 (0.00) [0]
17	DEVELOPMENT OF NELP BLOCK KG-ONN-2003/1 NAGAYALANKA FIELD-PH II	3/2022	6/2023 (-) [11/2023]	284.79 (-) [284.79]	201.63 (0.00) [5]
18	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY	9/2021	6/2024 (-) [6/2024]	160.00 (-) [160.00]	0.43 (0.00) [0]
19	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (5/2024) [5/2024]	34,012.00 (-) [34,012.00]	25,464.83 (0.00) [47]
20	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (6/2023) [2/2024]	167.00 (-) [167.00]	77.46 (0.00) [19]
21	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [3/2025]	355.00 (-) [355.00]	198.26 (0.00) [35]
22	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [4/2024]	332.61 (332.61) [332.61]	214.55 (0.00) [17]
23	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (7/2023) [10/2023]	196.26 (196.26) [196.26]	141.51 (0.00) [39]
24	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [4/2024]	20,928.00 (26,264.00) [26,264.00]	23,860.04 (5,336.00) [45]
<u>Railways</u>					
25	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [12/2025]	3,631.00 (-) [3,887.48]	2,728.66 (256.48) [45]
26	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2027]	1,045.20 (-) [2,500.98]	1,129.92 (1,455.78) [216]
27	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [9/2022]	2,499.71 (-) [2,499.71]	907.91 (0.00) [0]
28	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [3/2019]	234.50 (-) [235.00]	14.14 (0.50) [0]
29	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2021]	2,288.70 (-) [3,122.35]	1,267.65 (833.65) [0]
30	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	5,013.33 (302.42) [0]
<u>Road Transport And Highways</u>					
31	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A	1/2022	1/2025 (1/2023) [1/2025]	1,852.12 (-) [1,787.00]	255.61 (-65.12) [0]
32	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67	5/2022	7/2025 (-) [7/2025]	1,063.72 (-) [1,063.72]	170.67 (0.00) [0]
33	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	6/2019 (5/2023) [8/2023]	328.67 (416.07) [416.07]	333.18 (87.40) [50]
34	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (8/2023) [8/2023]	1,226.88 (1,569.68) [1,569.68]	1,054.39 (342.80) [30]

35	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	1/2024 (-) [7/2024]	1,601.10 (-) [1,601.10]	738.85 (0.00) [6]
36	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA	1/2023	11/2025 (-) [11/2025]	956.14 (-) [956.14]	18.72 (0.00) [0]
37	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA	12/2022	9/2025 (-) [9/2025]	912.94 (-) [912.94]	59.28 (0.00) [0]
38	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK	2/2023	10/2025 (-) [10/2025]	909.02 (-) [909.02]	27.25 (0.00) [0]
39	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000	2/2023	10/2025 (-) [10/2025]	1,253.24 (-) [1,253.24]	68.47 (0.00) [0]
40	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM.	12/2022	10/2025 (-) [10/2025]	1,058.90 (-) [1,058.90]	28.23 (0.00) [0]
41	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5	12/2022	11/2025 (-) [11/2025]	750.81 (-) [750.81]	22.03 (0.00) [0]
42	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH	12/2022	11/2025 (-) [11/2025]	992.89 (-) [992.89]	28.26 (0.00) [0]
43	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM.	2/2023	10/2025 (-) [10/2025]	1,200.42 (-) [1,200.42]	56.79 (0.00) [0]
44	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1)	2/2021	3/2024 (-) [6/2024]	922.50 (-) [1,128.68]	435.46 (206.18) [3]
45	6L JAKKUVA – KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2)	2/2021	3/2024 (-) [6/2024]	663.60 (-) [768.00]	241.99 (104.40) [3]
46	6L KANTAKAPALLE – SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4)	2/2021	10/2024 (-) [10/2024]	824.29 (-) [924.00]	306.38 (99.71) [0]
47	6L KORLAM-KANTAKAPALLE SECTION OF NH-130CD ROAD FROM KM 421.100 TO KM 445.100 (PKG-3)	2/2021	2/2024 (-) [2/2024]	772.70 (-) [980.51]	321.87 (207.81) [0]
48	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16	2/2019	3/2023 (-) [3/2024]	757.45 (-) [757.45]	261.31 (0.00) [12]
49	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV)	2/2021	1/2025 (-) [1/2025]	818.73 (-) [1,105.00]	73.20 (286.27) [0]
50	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I)	2/2021	12/2024 (-) [12/2024]	1,484.83 (-) [1,768.00]	383.07 (283.17) [0]
51	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III)	3/2021	1/2025 (-) [1/2025]	1,102.63 (-) [1,303.00]	212.43 (200.37) [0]
52	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE	12/2020	10/2024 (-) [10/2024]	1,075.27 (-) [1,307.00]	384.53 (231.73) [0]
53	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP	11/2020	10/2024 (-) [10/2024]	1,137.74 (-) [1,289.00]	321.70 (151.26) [0]
54	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2023) [5/2023]	263.45 (263.45) [263.45]	168.59 (0.00) [0]
55	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI	9/2021	9/2022 (9/2024) [9/2024]	517.05 (-) [655.06]	174.28 (138.01) [24]

56	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP	9/2021	9/2022 (9/2024) [9/2024]	622.00 (-) [817.91]	116.11 (195.91) [24]
57	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (11/2022) [11/2022]	429.43 (-) [373.05]	376.80 (-56.38) [0]
58	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	12/2020 (12/2022) [12/2024]	314.43 (-) [348.72]	85.61 (34.29) [48]
59	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (6/2023) [6/2023]	350.61 (411.18) [411.18]	340.08 (60.57) [0]
60	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (12/2019) [1/2021]	333.21 (-) [353.43]	342.71 (20.22) [0]
61	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (2/2023) [2/2023]	576.48 (686.13) [686.13]	635.78 (109.65) [0]
62	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (11/2022) [11/2022]	348.95 (355.69) [355.69]	300.51 (6.74) [0]
63	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	3/2020	3/2021 (11/2022) [11/2022]	207.79 (-) [207.79]	171.92 (0.00) [0]
64	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (10/2022) [10/2022]	386.09 (288.76) [288.76]	258.28 (-97.33) [0]
65	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (11/2022) [11/2022]	290.15 (-) [236.16]	204.32 (-53.99) [0]
66	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (5/2024) [5/2024]	195.45 (385.97) [385.97]	187.74 (190.52) [114]
67	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (2/2023) [2/2023]	995.09 (995.00) [995.09]	643.54 (0.00) [0]
68	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (10/2022) [10/2022]	444.84 (459.37) [459.37]	419.80 (14.53) [0]
69	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (10/2022) [10/2022]	376.25 (414.44) [414.44]	399.50 (38.19) [0]
70	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (10/2022) [10/2022]	289.67 (285.29) [285.29]	254.19 (-4.38) [0]
71	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (-) [11/2018]	504.19 (504.00) [504.19]	517.57 (0.00) [0]
72	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (5/2021) [5/2021]	271.45 (-) [271.45]	240.72 (0.00) [0]
73	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (7/2022) [7/2022]	319.28 (-) [319.28]	245.47 (0.00) [0]
74	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600	3/2015	9/2015 (8/2017) [5/2018]	309.01 (-) [309.01]	309.01 (0.00) [0]
75	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (1/2022) [2/2022]	372.68 (-) [309.37]	274.76 (-63.31) [0]
76	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (5/2022) [5/2022]	228.32 (-) [202.83]	175.29 (-25.49) [0]

77	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (12/2021) [12/2021]	418.03 (386.99) [386.99]	365.73 (-31.04) [0]
78	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	8/2020	3/2021 (3/2024) [3/2024]	222.61 (-) [222.61]	75.90 (0.00) [36]
79	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP	3/2020	1/2024 (1/2022) [1/2024]	1,863.09 (-) [2,238.00]	894.15 (374.91) [0]
80	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (7/2024) [7/2024]	597.67 (641.90) [641.90]	610.69 (44.23) [54]
81	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	6/2020	5/2021 (11/2022) [12/2022]	221.40 (-) [221.40]	166.34 (0.00) [0]
<u>Water Resources</u>					
82	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (-) [3/2024]	10,151.04 (-) [55,548.87]	21,727.98 (45,397.83) [48]
<u>ARUNACHAL PRADESH</u>					
<u>Civil Aviation</u>					
83	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (12/2023) [12/2023]	645.63 (-) [645.63]	636.43 (0.00) [16]
<u>Power</u>					
84	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH	2/2023	2/2032 (-) [2/2032]	31,876.39 (-) [31,876.39]	2,177.22 (0.00) [0]
85	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (5/2025) [5/2025]	6,285.33 (21,247.54) [21,247.54]	18,903.19 (14,962.21) [176]
<u>Road Transport And Highways</u>					
86	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	3/2027 (-) [3/2027]	496.47 (-) [496.47]	103.90 (0.00) [0]
87	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	3/2027 (-) [3/2027]	437.60 (-) [437.60]	210.88 (0.00) [0]
88	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	263.61 (0.00) [0]
89	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	334.89 (0.00) [0]
90	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	3/2027 (-) [3/2027]	403.68 (-) [403.68]	346.74 (0.00) [0]
91	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	3/2027 (-) [3/2027]	543.05 (-) [543.05]	414.11 (0.00) [0]
92	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	3/2027 (-) [3/2027]	450.65 (-) [450.65]	272.11 (0.00) [0]
93	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	3/2027 (-) [3/2027]	486.70 (-) [486.70]	415.54 (0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	3/2027 (-) [3/2027]	560.39 (-) [560.39]	531.18 (0.00) [0]
95	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	3/2027 (-) [3/2027]	394.27 (-) [394.27]	412.07 (0.00) [0]

96	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	3/2027 (-) [3/2027]	421.48 (-) [421.48]	349.87 (0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	1/2020 (1/2022) [8/2023]	200.44 (200.44) [200.44]	146.43 (0.00) [43]
98	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	12/2019 (3/2023) [9/2023]	568.92 (568.92) [568.92]	493.58 (0.00) [45]
99	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	3/2022 (12/2023) [3/2024]	1,718.59 (1,718.59) [1,718.59]	656.26 (0.00) [24]
100	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (5/2024) [5/2024]	301.06 (-) [301.06]	96.33 (0.00) [25]
101	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (10/2022) [3/2024]	353.90 (-) [353.90]	41.82 (0.00) [22]
102	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2022 (7/2023) [7/2023]	167.28 (229.70) [167.28]	138.66 (0.00) [15]
103	DEMBUEN - BRUNI	12/2020	3/2023 (-) [11/2023]	606.63 (606.63) [606.63]	270.03 (0.00) [8]
104	DOGINALA - GAU	12/2020	9/2022 (-) [8/2023]	242.30 (-) [242.30]	21.47 (0.00) [11]
105	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (7/2023) [7/2023]	228.71 (-) [228.71]	90.14 (0.00) [15]
106	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (7/2023) [7/2023]	294.04 (-) [294.04]	129.38 (0.00) [15]
107	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (7/2023) [7/2023]	199.03 (-) [199.03]	101.66 (0.00) [15]
108	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (11/2023) [11/2023]	184.88 (-) [184.88]	71.91 (0.00) [19]
109	LADDA - BASAI	2/2021	4/2023 (-) [2/2024]	445.96 (-) [445.96]	75.67 (0.00) [10]
110	TADADEGE - HENKAR	2/2021	3/2023 (-) [6/2024]	550.45 (-) [550.45]	61.12 (0.00) [15]
111	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	11/2023 (11/2023) [11/2023]	180.57 (244.10) [180.57]	96.11 (0.00) [0]
112	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	5/2023 (5/2023) [5/2023]	256.66 (-) [256.66]	0.00 (0.00) [0]
113	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (12/2021) [5/2023]	1,979.00 (-) [2,036.90]	1,253.04 (57.90) [0]
114	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	3/2027 (-) [3/2027]	182.55 (-) [182.55]	72.99 (0.00) [0]
	ASSAM				
	Civil Aviation				
115	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2025]	1,142.00 (-) [1,232.00]	365.49 (90.00) [48]

	<u>Health And Family Welfare</u>				
116	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (12/2022) [10/2023]	875.00 (890.14) [860.00]	684.50 (-15.00) [29]
	<u>Petroleum</u>				
117	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA	6/2022	10/2025 (-) [10/2025]	768.00 (-) [768.00]	1.39 (0.00) [0]
118	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM	3/2023	3/2026 (3/2026) [3/2026]	156.36 (156.36) [156.36]	0.36 (0.00) [0]
119	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (3/2023) [9/2023]	543.91 (-) [661.21]	439.99 (117.30) [43]
120	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	236.12 (0.00) [0]
121	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [7/2024]	218.38 (-) [218.38]	66.27 (0.00) [17]
122	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	6,125.60 (6,602.00) [0]
123	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	5,608.65 (-1,170.00) [0]
124	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING	12/2020	7/2024 (-) [3/2024]	430.76 (-) [430.76]	118.55 (0.00) [-4]
125	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM	3/2022	7/2026 (-) [9/2026]	277.00 (-) [277.00]	35.19 (0.00) [2]
126	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM	3/2023	12/2026 (-) [12/2026]	384.04 (-) [384.04]	0.35 (0.00) [0]
127	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT	6/2021	12/2024 (-) [12/2024]	860.00 (-) [860.00]	101.03 (0.00) [0]
	<u>Power</u>				
128	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C	3/2019	3/2023 (-) [9/2023]	1,326.00 (-) [1,326.00]	1,367.92 (0.00) [6]
	<u>Railways</u>				
129	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2026]	2,232.32 (-) [4,059.65]	2,898.81 (1,827.33) [48]
130	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [0/0]	385.20 (-) [1,304.62]	1,104.78 (919.42) [0]
	<u>Road Transport And Highways</u>				
131	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [3/2024]	261.13 (-) [261.13]	51.90 (0.00) [21]
132	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2023]	217.50 (-) [217.50]	48.14 (0.00) [0]
133	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [6/2023]	216.49 (241.52) [216.49]	101.02 (0.00) [0]
134	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	6/2019 (6/2019) [4/2023]	520.01 (-) [520.01]	277.79 (0.00) [0]

135	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (2/2022) [6/2023]	588.95 (811.28) [873.91]	647.07 (284.96) [0]
136	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (7/2021) [5/2023]	289.99 (-) [289.99]	216.08 (0.00) [0]
137	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	12/2021 (12/2019) [8/2023]	252.00 (330.30) [330.30]	146.28 (78.30) [20]
138	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	8/2023 (-) [11/2023]	437.39 (-) [437.39]	224.61 (0.00) [3]
139	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [7/2024]	294.17 (-) [294.17]	248.08 (0.00) [102]
140	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	1,340.72 (0.00) [0]
141	4-LANING OF DERGAON TOWN	3/2020	6/2022 (-) [6/2023]	287.63 (-) [287.63]	383.88 (0.00) [0]
142	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [8/2023]	220.20 (-) [220.20]	168.60 (0.00) [8]
143	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146	12/2021	8/2024 (-) [8/2024]	300.00 (-) [300.00]	223.00 (0.00) [0]
144	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI	3/2022	6/2024 (-) [6/2024]	457.72 (-) [457.72]	33.65 (0.00) [0]
145	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH	8/2022	12/2022 (-) [6/2024]	175.00 (-) [175.00]	66.50 (0.00) [18]
146	BALANCE WORK OF 4L OF NARIMBANGLO-JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23	3/2022	1/2026 (-) [1/2026]	1,909.98 (-) [1,909.98]	22.90 (0.00) [0]
147	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	76.97 (0.00) [0]
148	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA	3/2022	4/2025 (-) [4/2025]	535.03 (-) [535.03]	0.00 (0.00) [0]
149	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [5/2023]	335.88 (-) [335.88]	211.73 (0.00) [0]
150	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [6/2023]	260.07 (-) [260.07]	284.93 (0.00) [0]
151	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [10/2023]	288.85 (-) [288.85]	110.33 (0.00) [9]
152	DABOKA KATHKATI PACKAGE-6	9/2021	7/2024 (-) [7/2024]	625.64 (-) [625.64]	265.02 (0.00) [0]
153	DABOKA KATHKATI PACKAGE-7	11/2021	7/2024 (-) [7/2024]	204.10 (-) [204.10]	54.66 (0.00) [0]
154	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1	3/2022	7/2024 (-) [7/2024]	215.27 (-) [215.27]	50.37 (0.00) [0]
155	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2	4/2022	7/2024 (-) [1/2024]	170.95 (-) [170.95]	22.38 (0.00) [-6]

156	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3	1/2023	5/2025 (-) [5/2025]	458.59 (-) [458.59]	0.00 (0.00) [0]
157	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	6/2020 (6/2020) [12/2023]	818.00 (887.68) [818.00]	659.65 (0.00) [42]
158	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	3/2024 (-) [3/2024]	463.49 (-) [463.49]	284.31 (0.00) [0]
159	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [6/2023]	829.00 (-) [829.00]	819.58 (0.00) [0]
160	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [6/2023]	454.89 (814.56) [814.56]	498.86 (359.67) [0]
161	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2	3/2022	1/2025 (-) [1/2025]	909.02 (-) [909.02]	72.25 (0.00) [0]
162	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	508.56 (0.00) [0]
163	JOGIGHOPA BRIDGE	8/2021	11/2024 (-) [11/2024]	746.76 (-) [746.76]	144.33 (0.00) [0]
164	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	8/2023 (-) [8/2023]	1,049.51 (-) [1,049.51]	293.67 (0.00) [0]
165	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH	7/2017	4/2020 (-) [6/2023]	442.23 (-) [442.23]	192.31 (0.00) [0]
166	SRIRAMPUR - DHUBRI PKG-1	3/2022	2/2025 (-) [2/2025]	613.89 (-) [613.89]	0.00 (0.00) [0]
167	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [10/2023]	636.42 (-) [418.49]	544.79 (-217.93) [10]
168	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	36.36 (0.00) [0]
169	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (820.56) [761.54]	425.77 (0.00) [0]
170	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [7/2024]	208.84 (-) [208.84]	90.92 (0.00) [27]
	BIHAR				
	Civil Aviation				
171	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [12/2024]	1,216.90 (-) [1,216.90]	466.96 (0.00) [26]
	Department Of Higher Education				
172	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (10/2023) [10/2023]	496.18 (496.00) [460.00]	396.27 (-36.18) [76]
173	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [8/2023]	375.00 (-) [375.00]	278.08 (0.00) [35]
	Petroleum				
174	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (12/2024) [12/2024]	14,810.00 (-) [14,810.00]	6,350.87 (0.00) [20]
175	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND	6/2019	12/2029	988.00	84.87

	KISHANGANJ DISTRICTS		(3/2030) [3/2030]	(-) [988.00]	(0.00) [3]
176	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	2/2028 (8/2029) [8/2029]	439.00 (-) [439.00]	195.43 (0.00) [18]
177	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	8/2027 (2/2029) [2/2029]	176.00 (-) [176.00]	135.37 (0.00) [18]
178	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	12/2029 (3/2030) [3/2030]	163.00 (-) [163.00]	62.69 (0.00) [3]
179	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	6/2019	2/2028 (8/2029) [8/2029]	347.00 (-) [347.00]	147.32 (0.00) [18]
180	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2/2028 (8/2029) [8/2029]	2,996.00 (-) [2,996.00]	517.47 (0.00) [18]
181	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2023]	359.25 (-) [359.25]	272.02 (0.00) [12]
182	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (6/2023) [12/2023]	199.36 (-) [199.36]	163.45 (0.00) [38]
183	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI	1/2022	9/2024 (-) [9/2024]	389.00 (-) [389.00]	16.42 (0.00) [0]
184	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (6/2023) [9/2023]	403.00 (-) [403.00]	250.14 (0.00) [13]
	<u>Power</u>				
185	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2024]	8,692.97 (21,312.11) [21,312.11]	21,304.21 (12,619.14) [153]
186	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [3/2024]	10,439.09 (-) [10,439.09]	8,067.59 (0.00) [2]
187	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION	5/2021	4/2023 (-) [8/2023]	179.29 (-) [179.29]	108.51 (0.00) [4]
	<u>Railways</u>				
188	ARARIA-SUPAUL (NL)	4/2008	/ (-) [12/2025]	1,605.17 (1,605.17) [1,605.17]	834.76 (0.00) [-]
189	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [3/2024]	329.39 (1,483.14) [1,510.00]	2,102.69 (1,180.61) [-]
190	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [12/2024]	528.65 (2,066.78) [2,066.78]	1,822.92 (1,538.13) [-]
191	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [6/2023]	324.73 (967.29) [1,110.00]	1,165.40 (785.27) [0]
192	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [3/2025]	548.00 (548.00) [783.83]	543.54 (235.83) [60]
193	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [3/2025]	162.87 (614.45) [614.45]	399.41 (451.58) [-]
194	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	1,346.62 (0.00) [0]
195	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	965.84

			(-) [3/2024]	(1,185.73) [1,185.73]	(454.09) [36]
196	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2024]	532.87 (2,132.03) [2,650.00]	1,761.52 (2,117.13) [60]
197	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [12/2023]	1,491.47 (-) [1,491.47]	1,160.75 (0.00) [45]
198	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [12/2024]	744.04 (1,215.54) [1,215.54]	950.34 (471.50) [45]
199	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [12/2024]	325.00 (735.20) [735.20]	520.72 (410.20) [-]
200	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2024]	372.14 (1,470.50) [1,700.00]	2,044.95 (1,327.86) [-]
201	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [12/2024]	380.00 (519.33) [519.33]	399.56 (139.33) [-]
Road Transport And Highways					
202	2ND FLYOVER (LCW) PARALLEL TO EXISTING FLYOVER IN KISHANGANJ TOWN.	3/2018	6/2020 (8/2023) [8/2023]	150.21 (150.00) [150.00]	148.40 (-0.21) [38]
203	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S	9/2020	3/2023 (11/2023) [11/2023]	2,334.68 (2,335.00) [2,335.00]	714.12 (0.32) [8]
204	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E	3/2021	1/2024 (-) [1/2024]	1,143.46 (1,143.00) [1,143.00]	268.70 (-0.46) [0]
205	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E.	3/2021	1/2024 (-) [1/2024]	1,097.18 (1,097.00) [1,097.00]	329.35 (-0.18) [0]
206	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (6/2023) [6/2023]	575.00 (-) [575.00]	519.82 (0.00) [0]
207	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III)	2/2023	2/2025 (-) [2/2025]	1,358.00 (-) [1,358.00]	0.65 (0.00) [0]
208	6 L OF AURANGABAD TO BIHAR-JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N	2/2022	5/2025 (-) [5/2025]	786.81 (787.00) [787.00]	0.00 (0.19) [0]
209	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G	9/2020	3/2023 (-) [12/2023]	939.43 (-) [939.43]	40.02 (0.00) [9]
210	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20	9/2020	4/2023 (-) [4/2023]	897.45 (-) [897.45]	1,030.28 (0.00) [0]
211	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20	9/2020	6/2024 (-) [6/2024]	2,156.22 (-) [2,156.22]	1,585.58 (0.00) [0]
212	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [12/2023]	464.09 (-) [464.09]	461.45 (0.00) [37]
213	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [12/2023]	649.90 (-) [649.90]	456.06 (0.00) [36]
214	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [12/2023]	446.97 (-) [446.97]	384.28 (0.00) [37]
215	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI-MOTIHARI- RAXAUL SECTION OF NH-28A FRO	12/2018	10/2020 (-) [9/2023]	333.60 (459.89) [461.41]	399.69 (127.81) [35]

216	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	10/2019	8/2023 (12/2024) [12/2024]	1,101.99 (-) [1,101.99]	563.96 (0.00) [16]
217	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH:	12/2021	9/2024 (-) [9/2024]	184.90 (185.00) [185.00]	79.79 (0.10) [0]
218	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3	3/2022	12/2024 (-) [12/2024]	312.58 (-) [312.58]	37.38 (0.00) [0]
219	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (9/2024) [0/0]	2,926.42 (-) [2,926.42]	787.79 (0.00) [0]
220	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [6/2024]	1,478.40 (-) [1,478.40]	621.30 (0.00) [-]
221	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	10/2024 (10/2024) [10/2024]	2,598.00 (-) [1,962.50]	1,012.87 (-635.50) [0]
222	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	11/2021 (-) [6/2023]	496.20 (-) [537.17]	282.48 (40.97) [0]
223	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (5/2022) [5/2022]	683.83 (828.45) [828.45]	768.65 (144.62) [0]
224	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (6/2023) [6/2023]	553.30 (587.41) [587.41]	583.48 (34.11) [0]
225	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (7/2023) [7/2023]	178.85 (225.06) [225.06]	227.48 (46.21) [86]
226	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	12/2019 (-) [12/2023]	1,167.45 (-) [1,182.94]	589.65 (15.49) [48]
227	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (8/2023) [8/2023]	322.09 (-) [322.09]	282.54 (0.00) [64]
228	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [11/2023]	1,408.85 (2,138.16) [2,138.16]	1,560.46 (729.31) [85]
229	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI	3/2021	3/2024 (-) [3/2024]	1,020.84 (-) [1,020.84]	84.78 (0.00) [0]
230	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C	3/2022	3/2024 (-) [3/2024]	1,485.66 (-) [1,485.66]	0.00 (0.00) [0]
231	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH	8/2022	8/2024 (-) [8/2024]	1,198.02 (-) [1,198.02]	0.00 (0.00) [0]
232	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU	4/2022	4/2024 (-) [4/2024]	1,769.50 (-) [1,769.50]	0.00 (0.00) [0]
233	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO	8/2020	7/2023 (-) [7/2023]	690.00 (-) [690.00]	594.41 (0.00) [0]
234	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (7/2022) [3/2024]	1,041.10 (567.00) [639.58]	530.28 (-401.52) [59]
235	PATNA-MUZZAFFARPUR	8/2010	2/2013 (6/2023) [6/2023]	671.30 (-) [671.30]	1,591.71 (0.00) [0]
236	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	12/2021 (12/2019) [3/2024]	573.70 (644.50) [726.99]	371.11 (153.29) [27]

237	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (5/2023) [5/2023]	319.68 (404.10) [404.10]	401.17 (84.42) [0]
238	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (12/2023) [12/2023]	675.00 (780.77) [780.77]	485.28 (105.77) [-]
239	SIX LANNING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	4/2024 (-) [3/2024]	895.39 (-) [895.39]	1,632.71 (0.00) [-1]
240	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	2/2022 (8/2023) [10/2024]	950.64 (1,161.00) [1,168.33]	729.78 (217.69) [32]
241	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO	12/2021	3/2024 (-) [3/2024]	552.55 (553.00) [553.00]	292.70 (0.45) [0]
242	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (3/2022) [3/2022]	153.24 (-) [153.24]	122.60 (0.00) [0]
243	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (3/2024) [3/2024]	672.89 (736.01) [830.31]	347.17 (157.42) [48]
<u>Urban Development</u>					
244	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [9/2024]	13,365.77 (-) [13,925.50]	1,353.32 (559.73) [3]
<u>Water Resources</u>					
245	I AND D AND STP AT CHAPRA	11/2018	12/2020 (-) [8/2023]	236.15 (-) [236.15]	110.63 (0.00) [32]
246	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (11/2020) [3/2024]	254.13 (413.29) [413.29]	59.00 (159.16) [42]
247	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [1/2021]	268.63 (-) [431.21]	478.03 (162.58) [0]
248	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (12/2019) [12/2019]	230.06 (-) [230.06]	188.78 (0.00) [0]
249	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [8/2023]	305.19 (-) [305.19]	282.74 (0.00) [24]
250	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (3/2018) [12/2023]	294.02 (350.79) [294.02]	212.03 (0.00) [26]
251	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (5/2017) [4/2021]	356.37 (364.00) [356.37]	290.70 (0.00) [0]
252	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [3/2024]	824.00 (734.09) [824.00]	198.83 (0.00) [21]
253	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [3/2024]	578.89 (453.83) [578.89]	45.41 (0.00) [21]
254	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [6/2020]	225.77 (-) [398.90]	360.57 (173.13) [0]
255	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (3/2017) [5/2021]	277.42 (253.98) [277.42]	328.54 (0.00) [0]
256	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (5/2017) [11/2020]	191.62 (-) [191.62]	117.30 (0.00) [0]

	<u>CHHATTISGARH</u>				
	<u>Coal</u>				
257	AMERA OC RCE	2/2015	3/2018 (-) [3/2026]	335.97 (-) [335.97]	49.00 (0.00) [96]
258	AMGAON OPENCAS T PROJECT RCE	7/2015	3/2020 (-) [3/2025]	316.10 (-) [316.10]	156.33 (0.00) [60]
259	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	721.14 (0.00) [0]
260	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (3/2025) [3/2025]	610.63 (-) [610.63]	482.80 (0.00) [36]
261	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	2,336.23 (0.00) [0]
262	DURGAPUR OPENCAS T PROJECT	2/2015	3/2023 (-) [3/2030]	916.24 (-) [916.24]	13.73 (0.00) [84]
263	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2025]	11,816.40 (-) [11,816.40]	5,887.31 (0.00) [24]
264	JAGANNATHPUR OC RCE (3.0 MTY)	7/2016	3/2020 (-) [3/2024]	459.49 (-) [459.49]	223.15 (0.00) [48]
265	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	198.08 (0.00) [0]
266	JHIRIA WEST OPENCAS T PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	15.69 (0.00) [0]
267	KARTALI (EAS T) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	9.22 (0.00) [144]
268	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2025]	7,612.33 (-) [7,612.33]	4,109.56 (0.00) [24]
269	MADANNAGAR OPENCAS T PROJECT	10/2015	3/2024 (-) [3/2027]	1,875.32 (-) [1,875.32]	0.00 (0.00) [36]
270	MAHAMAYA OPENCAS T PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	102.84 (0.00) [0]
271	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2031]	1,624.59 (-) [1,624.59]	49.60 (0.00) [96]
272	PORDA CHIMTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	39.19 (0.00) [0]
273	VIJAY WEST OPENCAS T PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	88.27 (0.00) [0]
	<u>Department Of Higher Education</u>				
274	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	640.70 (0.00) [0]
	<u>Petroleum</u>				
275	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	3/2021	3/2024 (3/2025) [3/2025]	456.00 (-) [456.00]	181.92 (0.00) [12]
	<u>Power</u>				

276	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII	3/2023	9/2024 (-) [9/2024]	271.69 (-) [271.69]	0.00 (0.00) [0]
277	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX	3/2023	3/2025 (-) [3/2025]	260.30 (-) [260.30]	0.00 (0.00) [0]
278	WESTERN REGION EXPANSION SCHEME XXV	2/2023	11/2023 (-) [3/2024]	385.84 (-) [385.84]	0.00 (0.00) [4]
	<u>Railways</u>				
279	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023) [10/2024]	1,973.00 (2,135.34) [2,135.34]	1,488.70 (162.34) [43]
280	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [12/2023]	3,055.00 (-) [3,438.39]	2,976.72 (383.39) [63]
281	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2024]	1,160.00 (-) [1,440.00]	1,058.66 (280.00) [48]
	<u>Road Transport And Highways</u>				
282	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH-130A	4/2020	3/2024 (-) [3/2024]	1,855.59 (1,869.85) [1,869.85]	187.36 (14.26) [0]
283	4 LANING OF CHAMPA-KORBA-CHHURI-KATGHORA SECTION OF NH 149B FROM KM.0.000 TO KM.38.200	2/2021	1/2024 (-) [1/2024]	999.97 (-) [999.97]	831.22 (0.00) [0]
284	4 LANING OF PATHRAPALI TO KATGHORA FROM KM.53.300 TO KM.92.600	11/2019	12/2022 (3/2023) [8/2023]	865.10 (-) [865.10]	655.41 (0.00) [8]
285	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299.	3/2018	1/2019 (-) [12/2023]	349.03 (-) [349.03]	277.34 (0.00) [59]
286	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA	11/2021	9/2024 (-) [9/2024]	1,368.19 (-) [1,368.19]	595.79 (0.00) [0]
287	DEVELOPMENT OF SIX LANE SARGI-BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA	12/2021	1/2025 (-) [1/2025]	1,470.73 (-) [1,470.73]	179.31 (0.00) [0]
288	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (-) [12/2023]	335.32 (-) [335.32]	321.06 (0.00) [78]
289	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (-) [12/2023]	476.20 (543.73) [543.73]	476.08 (67.53) [87]
290	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (-) [3/2015]	496.02 (-) [496.02]	240.11 (0.00) [0]
291	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (-) [3/2024]	497.14 (-) [572.66]	309.49 (75.52) [91]
292	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (-) [12/2023]	624.98 (731.50) [731.50]	539.88 (106.52) [86]
293	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (-) [12/2023]	452.94 (-) [435.61]	205.99 (-17.33) [89]
294	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (-) [8/2023]	423.79 (-) [423.79]	324.86 (0.00) [67]
295	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (-) [8/2023]	188.80 (-) [188.80]	131.38 (0.00) [51]

	Steel				
296	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (6/2023) [8/2023]	15,525.00 (23,840.00) [23,840.00]	23,131.35 (8,315.00) [99]
297	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (7/2024) [5/2025]	2,907.00 (-) [2,907.00]	1,362.32 (0.00) [23]
298	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [4/2025]	542.24 (-) [542.24]	160.15 (0.00) [16]
299	SCREENING PLANT-III AT KIRANDUL	3/2021	8/2024 (-) [8/2024]	2,092.97 (2,221.86) [2,221.86]	704.51 (128.89) [0]
	Urban Development				
300	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	5/2019	9/2020 (2/2024) [2/2024]	299.97 (299.97) [299.97]	150.93 (0.00) [41]
	DELHI				
	Civil Aviation				
301	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [8/2023]	303.80 (351.21) [351.21]	304.71 (47.41) [40]
	Commerce				
302	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [10/2020]	302.64 (-) [302.64]	30.00 (0.00) [0]
	Dpiit				
303	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [9/2023]	4,773.00 (-) [5,401.00]	4,071.81 (628.00) [45]
	Finance				
304	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA	7/2018	4/2022 (-) [4/2022]	228.50 (-) [220.27]	176.28 (-8.23) [0]
	Home Affairs				
305	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/2019	7/2022 (-) [5/2024]	277.35 (-) [290.33]	90.12 (12.98) [22]
306	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [12/2023]	1,219.21 (1,735.25) [1,900.00]	1,583.95 (680.79) [50]
	Railways				
307	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	133.78 (123.32) [-]
	Renewable Energy				
308	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (4/2022) [4/2022]	271.90 (366.12) [366.12]	329.49 (94.22) [0]
	Road Transport And Highways				
309	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O	1/2018	10/2021 (-) [11/2023]	2,067.67 (-) [2,160.00]	1,496.49 (92.33) [25]
310	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30	7/2020	10/2023 (-) [10/2023]	801.46 (-) [801.46]	382.03 (0.00) [0]
311	DEVELOPMENT OF 6L UER II [PACKAGE - III] (NANGLOI - NAJAFGARH ROAD TILL SECTOR 24 DWARKA) FROM KM. 2	7/2020	10/2023 (-) [10/2023]	1,069.27 (-) [1,069.27]	748.48 (0.00) [0]
312	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM	7/2020	10/2023 (-) [10/2023]	1,894.96 (-) [1,894.96]	741.88 (0.00) [0]

313	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-) 0.70	7/2020	10/2023 (-) [10/2023]	2,171.80 (-) [2,171.80]	958.13 (0.00) [0]
314	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21)	3/2018	9/2022 (-) [12/2023]	2,507.00 (-) [3,030.73]	1,155.70 (523.73) [15]
315	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR	6/2020	12/2024 (-) [12/2024]	1,479.22 (-) [1,479.22]	667.80 (0.00) [0]
	<u>Telecommunications</u>				
316	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	3/2018 (-) [12/2023]	248.20 (-) [248.20]	187.88 (0.00) [69]
	<u>Urban Development</u>				
317	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI	1/2022	11/2024 (5/2025) [5/2025]	646.52 (-) [646.52]	38.46 (0.00) [6]
318	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2026]	24,948.65 (-) [24,948.65]	7,812.66 (0.00) [12]
319	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (9/2021) [9/2021]	565.00 (-) [565.00]	520.56 (0.00) [0]
320	DELHI MRTS PHASE-III	9/2011	3/2016 (8/2021) [8/2021]	38,585.00 (-) [40,180.91]	40,217.45 (1,595.91) [0]
321	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [6/2024]	1,180.00 (-) [1,100.80]	36.69 (-79.20) [35]
322	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (6/2024) [6/2024]	1,128.00 (-) [1,128.00]	166.06 (0.00) [27]
323	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [9/2023]	2,694.00 (-) [2,694.00]	1,832.74 (0.00) [-]
	<u>Water Resources</u>				
324	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [5/2020]	344.81 (-) [344.81]	0.00 (0.00) [0]
325	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [3/2022]	515.07 (-) [515.07]	388.08 (0.00) [0]
326	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [9/2023]	665.78 (-) [665.78]	522.28 (0.00) [9]
327	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [6/2023]	211.79 (223.70) [211.79]	167.48 (0.00) [0]
328	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (9/2023) [9/2023]	239.11 (314.71) [239.11]	252.01 (0.00) [19]
	<u>GOA</u>				
	<u>Civil Aviation</u>				
329	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT.	11/2017	9/2021 (-) [6/2024]	255.69 (-) [255.69]	45.34 (0.00) [33]
	<u>Department Of Higher Education</u>				
330	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	8/2021 (-) [11/2023]	303.90 (334.45) [364.00]	295.00 (60.10) [27]
	<u>Road Transport And Highways</u>				
331	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM.	3/2015	/	184.05	136.74

	14/020 AND WIDENING OF EXISTING TWO LANE ROAD		(-) [12/2022]	(-) [184.05]	(0.00) [0]
332	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/	936.40	708.69
			(-) [0/0]	(-) [936.40]	(0.00) [0]
333	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/	298.33	399.84
			(12/2021) [12/2022]	(354.43) [298.33]	(0.00) [0]
334	KARASWADA TO BAMBOLIM	3/2017	12/2019	852.67	300.98
			(-) [1/2023]	(-) [852.67]	(0.00) [0]
335	MOPA AIRPORT	12/2021	4/2022	1,183.16	485.75
			(-) [10/2023]	(-) [1,183.16]	(0.00) [18]
336	PATRADEVI TO KARASWADA 4L	3/2017	5/2020	634.32	496.44
			(-) [3/2023]	(-) [634.32]	(0.00) [0]
337	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	464.36
			(-) [1/2023]	(-) [773.98]	(0.00) [0]
338	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	709.30
			(-) [1/2023]	(-) [819.95]	(0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
339	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11,459.00	20,460.00
			(-) [3/2024]	(19,220.00) [19,220.00]	(7,761.00) [99]
	<u>Civil Aviation</u>				
340	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1.	6/2022	12/2025	1,305.00	13.41
			(-) [12/2025]	(-) [636.45]	(-668.55) [0]
341	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022	1,405.00	1,008.10
			(12/2023) [12/2023]	(-) [1,405.00]	(0.00) [16]
342	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT.	8/2018	2/2021	353.25	254.94
			(-) [9/2023]	(-) [353.25]	(0.00) [31]
	<u>Petroleum</u>				
343	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023	5,251.00	3,116.31
			(11/2023) [11/2023]	(5,894.00) [5,251.00]	(0.00) [6]
344	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023	1,614.00	513.56
			(-) [3/2024]	(-) [1,614.00]	(0.00) [7]
345	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD	1/2022	11/2024	621.40	81.21
			(-) [11/2024]	(-) [621.40]	(0.00) [0]
346	CONSTRUCTION OF TWO PRODUCED WATER TREATMENT PLANTS (PWTP) AT BECHARAJI AND SOBHASAN INSTALLATION OF	7/2021	7/2024	320.20	22.53
			(-) [7/2024]	(-) [320.20]	(0.00) [0]
347	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT	1/2022	9/2024	328.00	12.15
			(-) [9/2024]	(-) [328.00]	(0.00) [0]
348	KALOL REDEVELOPMENT PROJECT	8/2022	3/2027	1,487.41	374.18
			(-) [3/2027]	(-) [1,487.41]	(0.00) [0]
349	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A	7/2021	7/2025	173.03	28.68
			(-) [7/2025]	(-) [173.03]	(0.00) [0]
350	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024	18,936.00	4,182.86
			(-)	(-)	(0.00)

			[8/2024]	[18,936.00]	[-1]
351	REDEVELOPMENT OF LINCH FIELD	4/2021	3/2025 (-) [3/2025]	631.03 (-) [631.03]	214.83 (0.00) [0]
352	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	1,018.19 (0.00) [0]
353	REDEVELOPMENT OF SOBHASAN COMPLEX	8/2021	2/2026 (-) [2/2026]	885.63 (-) [885.63]	275.75 (0.00) [0]
354	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (2/2024) [12/2023]	1,378.00 (-) [1,378.00]	885.65 (0.00) [12]
355	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT	5/2022	2/2025 (-) [2/2025]	249.43 (-) [249.43]	5.95 (0.00) [0]
356	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (12/2023) [12/2023]	225.54 (-) [247.90]	219.43 (22.36) [34]
	<u>Power</u>				
357	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	5/2021	9/2022 (3/2024) [3/2024]	674.92 (-) [674.92]	89.67 (0.00) [18]
358	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID)	11/2022	3/2024 (6/2024) [6/2024]	1,442.60 (-) [1,442.60]	80.60 (0.00) [3]
359	Bagodara Solar Power Project	5/2021	10/2022 (-) [12/2023]	339.35 (-) [339.35]	253.94 (0.00) [14]
360	DAYAPAR WIND ENERGY PROJECT 150MW	11/2021	5/2023 (6/2024) [6/2024]	937.80 (-) [937.80]	314.00 (0.00) [13]
361	DAYAPAR WIND ENERGY PROJECT 200MW	7/2022	3/2025 (3/2025) [3/2025]	1,316.02 (-) [1,316.02]	92.02 (0.00) [0]
362	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK	3/2023	12/2024 (-) [12/2024]	922.30 (-) [922.30]	0.00 (0.00) [0]
363	GUJARAT 200 MW (GUVNL TENDER)	1/2021	7/2022 (3/2024) [3/2024]	842.27 (-) [842.27]	93.82 (0.00) [20]
364	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA	3/2023	3/2025 (-) [3/2025]	1,167.55 (-) [1,167.55]	0.00 (0.00) [0]
365	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA	3/2023	3/2025 (-) [3/2025]	2,820.99 (-) [2,820.99]	0.00 (0.00) [0]
366	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK	3/2023	12/2024 (-) [12/2024]	966.79 (-) [966.79]	0.00 (0.00) [0]
367	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK)	9/2022	9/2024 (9/2024) [9/2024]	7,179.54 (-) [7,179.54]	545.46 (0.00) [0]
368	RAGHANESDA SOLAR POWER PROJECT	6/2022	12/2023 (-) [12/2023]	642.15 (-) [642.15]	203.25 (0.00) [0]
369	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT	3/2023	3/2025 (-) [3/2025]	815.12 (-) [815.12]	0.00 (0.00) [0]
	<u>Railways</u>				
370	ANAND GODHRA DOUBLING PROJECT 79 KMS	4/2017	3/2020 (12/2024)	692.25 (692.26)	116.70 (0.01)

			[12/2024]	[692.26]	[57]
371	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [3/2024]	318.24 (321.03) [1,095.12]	201.24 (776.88) [144]
372	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	4/2018	3/2024 (12/2024) [12/2024]	537.31 (537.31) [537.31]	191.29 (0.00) [9]
373	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (-) [10/2025]	844.10 (844.10) [844.10]	457.93 (0.00) [-]
374	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [3/2019]	343.00 (-) [343.00]	222.83 (0.00) [0]
375	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [3/2024]	248.26 (-) [528.49]	116.25 (280.23) [-]
Road Transport And Highways					
376	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	7/2020 (-) [12/2023]	829.97 (-) [829.97]	329.71 (0.00) [41]
377	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE	3/2022	3/2023 (-) [10/2023]	162.73 (-) [162.73]	54.00 (0.00) [7]
378	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III)	3/2021	9/2022 (-) [12/2023]	485.75 (-) [485.75]	207.82 (0.00) [15]
379	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II)	3/2021	9/2022 (-) [12/2023]	536.03 (-) [536.03]	350.00 (0.00) [15]
380	4L OF DHROL-BHADRA-PATIYA SECTION FROM 0.000 TO KM 13.600 AND BHADRA PATIYA - PIPALIYA SECTION FROM	5/2020	10/2023 (10/2023) [10/2023]	971.03 (-) [971.03]	411.77 (0.00) [0]
381	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU	3/2021	3/2024 (-) [12/2024]	1,259.00 (-) [1,910.00]	60.25 (651.00) [9]
382	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU	7/2020	12/2023 (-) [6/2024]	2,271.86 (-) [3,916.00]	426.80 (1,644.14) [6]
383	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA	7/2020	8/2023 (-) [6/2024]	1,710.30 (-) [1,927.00]	265.19 (216.70) [10]
384	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	10/2021 (3/2024) [3/2024]	1,161.39 (1,404.00) [1,404.00]	396.76 (242.61) [29]
385	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG	5/2020	12/2023 (-) [12/2023]	894.00 (-) [894.00]	437.91 (0.00) [0]
386	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0	5/2020	3/2024 (-) [3/2024]	690.30 (-) [690.30]	422.62 (0.00) [0]
387	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION	5/2020	1/2024 (-) [3/2024]	882.00 (-) [882.00]	319.15 (0.00) [2]
388	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB	5/2020	7/2023 (-) [9/2023]	691.52 (-) [691.52]	342.22 (0.00) [2]
389	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	11/2020 (9/2023) [9/2023]	400.76 (394.44) [394.44]	276.30 (-6.32) [34]
390	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT	6/2020	4/2023 (8/2023) [8/2023]	166.21 (-) [166.21]	89.45 (0.00) [4]

391	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	9/2020 (10/2023) [10/2023]	962.43 (978.93) [978.93]	818.30 (16.50) [37]
392	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26	9/2020	2/2024 (-) [2/2024]	1,542.02 (-) [1,542.02]	363.32 (0.00) [0]
393	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27	9/2020	2/2024 (-) [2/2024]	1,185.69 (-) [1,185.69]	432.47 (0.00) [0]
394	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28	9/2020	11/2023 (-) [11/2023]	1,198.55 (-) [1,198.55]	431.31 (0.00) [0]
395	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 29	9/2020	4/2023 (-) [7/2023]	1,523.77 (-) [1,523.77]	963.02 (0.00) [3]
396	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30	11/2019	9/2023 (-) [9/2023]	1,669.56 (-) [1,669.56]	575.33 (0.00) [0]
397	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31	11/2019	5/2024 (-) [5/2024]	1,604.06 (-) [1,604.06]	1,057.90 (0.00) [0]
398	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2020 (12/2023) [12/2023]	867.97 (913.49) [913.49]	778.14 (45.52) [37]
399	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	8/2019 (-) [8/2023]	998.18 (-) [998.18]	802.04 (0.00) [48]
400	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	9/2019 (-) [10/2023]	723.64 (-) [723.64]	551.69 (0.00) [49]
401	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	8/2019 (-) [10/2023]	763.08 (-) [763.08]	408.37 (0.00) [50]
402	JUNAGADH BYPASS	10/2017	4/2021 (6/2023) [8/2023]	232.49 (375.78) [290.69]	319.53 (58.20) [28]
403	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1)	2/2020	6/2023 (-) [8/2023]	606.51 (-) [657.00]	446.88 (50.49) [2]
404	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3)	2/2020	8/2023 (12/2023) [8/2023]	752.30 (-) [766.20]	392.85 (13.90) [0]
405	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4)	2/2020	3/2023 (-) [8/2023]	778.15 (-) [785.67]	429.03 (7.52) [5]
406	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	12/2020 (10/2023) [10/2023]	1,251.11 (-) [1,361.00]	563.93 (109.89) [34]
407	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (7/2023) [7/2023]	351.00 (270.00) [270.00]	215.52 (-81.00) [25]
408	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT	3/2022	6/2025 (-) [6/2025]	1,373.06 (1,085.00) [1,373.06]	202.38 (0.00) [0]
Urban Development					
409	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [12/2023]	10,773.00 (-) [12,925.22]	11,786.54 (2,152.22) [60]
410	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [12/2024]	5,384.17 (-) [5,384.17]	1,428.76 (0.00) [9]
411	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-)	12,020.32 (-)	2,396.13 (0.00)

			[3/2025]	[12,020.32]	[12]
	HARYANA				
	Home Affairs				
412	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)"	1/2020	10/2023 (3/2024) [3/2024]	166.98 (167.00) [166.98]	41.73 (0.00) [5]
	Petroleum				
413	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	4,702.23 (0.00) [0]
414	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (8/2022) [9/2023]	909.00 (-) [909.00]	810.76 (0.00) [32]
415	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (6/2023) [10/2023]	206.63 (340.76) [340.76]	274.27 (134.13) [44]
416	CITY GAS DISTRIBUTION NETWORK PROJECT AT ROHTAK	4/2018	6/2025 (-) [6/2025]	261.48 (-) [261.48]	137.28 (0.00) [0]
417	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	353.70 (0.00) [5]
418	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [12/2023]	164.69 (-) [164.69]	124.00 (0.00) [29]
419	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2023) [9/2023]	278.60 (-) [278.60]	186.05 (0.00) [27]
420	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (7/2023) [11/2023]	1,636.00 (-) [1,636.00]	1,329.13 (0.00) [39]
421	POLY BUTADIENE RUBBER PLANT AT PANIPAT	3/2022	3/2025 (-) [3/2025]	1,459.00 (2,102.79) [1,459.00]	69.74 (0.00) [0]
422	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	12/2021 (12/2023) [12/2023]	1,255.00 (-) [1,255.00]	776.69 (0.00) [24]
423	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2025]	2,281.94 (3,219.94) [3,219.94]	1,122.50 (938.00) [31]
	Power				
424	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA	1/2019	3/2022 (-) [9/2023]	267.33 (-) [267.33]	109.36 (0.00) [18]
	Railways				
425	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [12/2011]	287.00 (-) [893.45]	686.20 (606.45) [0]
	Road Transport And Highways				
426	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O	3/2022	2/2025 (-) [2/2025]	1,269.50 (-) [1,269.50]	35.00 (0.00) [0]
427	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K	3/2020	3/2023 (-) [10/2023]	510.97 (-) [510.97]	506.37 (0.00) [7]
428	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352	7/2020	7/2022 (11/2023) [11/2023]	899.00 (-) [947.00]	920.51 (48.00) [16]
429	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP	11/2020	12/2023 (-) [3/2024]	1,690.23 (-) [2,010.17]	1,067.66 (319.94) [3]
430	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM	11/2021	11/2023	694.00	1,212.57

	KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA		(11/2023) [11/2023]	(-) [694.00]	(0.00) [0]
431	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	12/2020 (8/2023) [5/2023]	1,484.30 (-) [2,182.41]	1,219.02 (698.11) [0]
432	CONSTRUCTION OF 8LANE DIVIDED CARRIAGEWAY STARTING AT SOHNA GURUGRAM ROAD NE 4 NEAR ALIPUR VILLAGE A	11/2018	9/2021 (-) [8/2023]	2,312.26 (-) [2,312.26]	1,361.51 (0.00) [23]
433	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN	11/2018	9/2021 (-) [8/2023]	2,252.75 (-) [2,252.75]	1,223.07 (0.00) [23]
434	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA	11/2018	9/2021 (-) [8/2023]	1,935.61 (-) [1,935.61]	856.41 (0.00) [23]
435	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F	12/2020	12/2023 (-) [12/2023]	1,430.88 (-) [1,430.88]	872.76 (0.00) [0]
436	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO	1/2021	12/2023 (-) [12/2023]	1,306.95 (-) [1,306.95]	761.02 (0.00) [0]
437	CONSTRUCTION OF FOUR LANE PINJORE BYPASS FROM KM 0.00 TO 7.70 ON EPC MODE.	12/2016	12/2017 (-) [9/2023]	170.27 (-) [170.27]	98.77 (0.00) [69]
438	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP	12/2020	1/2024 (3/2024) [3/2024]	1,334.04 (-) [1,334.00]	717.42 (-0.04) [2]
439	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU	12/2020	11/2023 (-) [11/2023]	1,524.03 (-) [1,524.03]	890.82 (0.00) [0]
440	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE	2/2020	1/2023 (-) [6/2023]	808.31 (-) [958.00]	734.96 (149.69) [0]
441	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM)	1/2018	11/2020 (8/2023) [5/2023]	2,228.00 (-) [2,228.00]	1,411.27 (0.00) [0]
442	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI	7/2020	7/2022 (-) [11/2023]	817.00 (-) [817.00]	851.73 (0.00) [16]
443	SIX LANNING OF MANDI DABWALI (PUNJAB/HARYANA BORDER)- CHAUTALA ROAD SECTION FROM PROPOSED MANDI DABW	1/2021	1/2024 (1/2024) [1/2024]	864.27 (864.00) [864.27]	327.36 (0.00) [0]
	HIMACHAL PRADESH				
	Department Of Higher Education				
444	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022 (1/2024) [1/2024]	392.51 (-) [446.43]	213.56 (53.92) [19]
	Health And Family Welfare				
445	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [8/2025]	260.00 (-) [260.00]	0.00 (0.00) [50]
	Petroleum				
446	CITY GAS DISTRIBUTION NETWORK PROJECT AT BILASPUR, HAMIRPUR AND UNA	4/2019	9/2030 (-) [9/2030]	427.94 (-) [427.94]	71.16 (0.00) [0]
	Power				
447	DHAULASIDH HYDROELECTRIC PROJECT (66 MW)	10/2020	11/2025 (-) [11/2025]	687.97 (-) [687.97]	433.34 (0.00) [0]
448	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	1,172.83 (0.00) [0]
449	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009	3,919.59	10,807.99

			(3/2024) [3/2024]	(11,134.54) [11,134.54]	(7,214.95) [174]
450	SUNNI DAM HYDRO ELECTRIC PROJECT	1/2023	4/2028 (-) [4/2028]	2,614.51 (-) [2,614.51]	496.15 (0.00) [0]
	<u>Railways</u>				
451	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [3/2025]	2,966.99 (-) [6,753.42]	3,955.01 (3,786.43) [-21]
	<u>Road Transport And Highways</u>				
452	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [3/2024]	2,485.93 (-) [2,485.93]	1,433.11 (0.00) [45]
453	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A	7/2021	9/2024 (-) [9/2024]	1,692.05 (-) [1,692.05]	598.25 (0.00) [0]
454	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154)	3/2021	5/2024 (-) [5/2024]	1,002.11 (1,247.93) [1,358.00]	28.69 (355.89) [0]
455	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB)	4/2021	6/2024 (-) [6/2024]	583.93 (-) [583.93]	33.42 (0.00) [0]
456	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP	2/2022	6/2024 (-) [6/2024]	190.60 (-) [163.00]	51.65 (-27.60) [0]
457	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU	5/2022	3/2024 (-) [3/2024]	469.95 (-) [280.00]	188.16 (-189.95) [0]
458	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	5/2021 (11/2022) [1/2024]	478.74 (-) [1,136.83]	1,016.30 (658.09) [32]
459	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	7/2020 (-) [6/2024]	1,273.71 (-) [1,273.71]	1,264.66 (0.00) [47]
460	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K	2/2021	9/2021 (-) [9/2021]	345.89 (-) [345.89]	193.34 (0.00) [0]
461	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K	8/2020	12/2024 (-) [12/2024]	371.93 (-) [371.93]	63.42 (0.00) [0]
462	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50.	8/2020	3/2021 (-) [3/2021]	242.80 (-) [242.80]	115.62 (0.00) [0]
463	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2	8/2020	4/2025 (-) [4/2025]	314.32 (-) [314.32]	24.78 (0.00) [0]
464	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA	8/2020	4/2021 (-) [4/2021]	272.98 (-) [272.98]	168.27 (0.00) [0]
465	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75	8/2020	4/2021 (-) [4/2021]	349.20 (-) [349.20]	316.84 (0.00) [0]
466	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF	3/2021	12/2024 (12/2024) [12/2024]	1,322.95 (1,442.47) [1,442.47]	498.17 (119.52) [0]
	<u>Urban Development</u>				
467	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D	4/2022	11/2024 (-) [11/2024]	512.34 (-) [512.34]	0.00 (0.00) [0]
	<u>JAMMU AND KASHMIR</u>				
	<u>Department Of Higher Education</u>				
468	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU	1/2018	4/2023	676.00	24.75

	(PHASE 1C)		(12/2023) [12/2023]	(1,085.04) [1,085.04]	(409.04) [8]
469	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (9/2023) [9/2023]	424.93 (-) [424.93]	363.19 (0.00) [14]
	<u>Health And Family Welfare</u>				
470	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [9/2025]	1,828.00 (-) [1,828.00]	740.13 (0.00) [0]
471	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [10/2023]	1,404.00 (-) [1,404.00]	95.63 (0.00) [1]
	<u>Power</u>				
472	KIRU HYDRO ELECTRIC PROJECT	3/2019	8/2024 (-) [3/2026]	4,287.59 (-) [4,287.59]	1,168.94 (0.00) [19]
473	KWAR HE PROJECT	5/2022	11/2026 (-) [11/2026]	4,526.12 (-) [4,526.12]	431.06 (0.00) [0]
474	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (7/2025) [9/2026]	8,112.12 (-) [8,112.12]	3,194.18 (0.00) [77]
475	RATLE HE PROJECT	2/2021	2/2026 (5/2026) [5/2026]	5,281.94 (5,281.94) [5,281.94]	333.41 (0.00) [3]
	<u>Railways</u>				
476	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (12/2023) [1/2024]	2,500.00 (37,012.26) [37,012.26]	36,017.83 (34,512.26) [254]
	<u>Road Transport And Highways</u>				
477	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL.	7/2021	8/2024 (8/2024) [8/2024]	614.48 (-) [614.48]	58.21 (0.00) [0]
478	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K	7/2021	2/2025 (2/2025) [2/2025]	1,912.17 (-) [1,912.17]	0.26 (0.00) [0]
479	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX	7/2021	6/2024 (6/2024) [6/2024]	1,401.87 (-) [1,401.87]	138.72 (0.00) [0]
480	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA	9/2021	12/2023 (1/2024) [1/2024]	811.19 (-) [811.19]	593.45 (0.00) [1]
481	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350	1/2020	1/2024 (1/2024) [1/2024]	336.01 (-) [336.01]	91.52 (0.00) [0]
482	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	2,199.36 (0.00) [0]
483	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI	7/2019	10/2020 (4/2023) [8/2023]	157.05 (-) [157.05]	109.95 (0.00) [34]
484	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY	3/2021	2/2024 (8/2024) [8/2024]	2,919.96 (-) [2,919.96]	1,659.64 (0.00) [6]
485	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	7/2021 (7/2023) [8/2023]	1,471.75 (1,471.75) [1,471.75]	1,439.30 (0.00) [25]
486	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM.	9/2021	10/2023 (10/2023) [10/2023]	442.14 (-) [442.14]	107.84 (0.00) [0]
487	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01	12/2019	12/2023 (-)	2,680.42 (-)	0.00 (0.00)

	SRINAGAR-SONA		[12/2023]	[2,680.42]	[0]
488	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH-	8/2022	6/2024 (-) [6/2024]	200.05 (200.05) [200.05]	5.75 (0.00) [0]
489	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5	10/2021	9/2024 (-) [9/2024]	3,044.02 (3,044.02) [3,044.02]	214.97 (0.00) [0]
490	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B	10/2021	9/2024 (-) [9/2024]	2,714.95 (2,714.95) [2,714.95]	276.91 (0.00) [0]
491	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4	9/2021	9/2024 (-) [9/2024]	1,821.72 (1,917.32) [1,917.32]	248.20 (95.60) [0]
492	DONIPAWA TO ASHAJIPORA BYPASS PKG-7	3/2021	12/2022 (-) [4/2023]	260.40 (-) [260.40]	152.09 (0.00) [0]
493	FOUR LANING OF JAMMU-AKHNOOR PKG-1	7/2022	1/2025 (-) [1/2025]	245.34 (-) [245.34]	3.94 (0.00) [0]
494	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (7/2023) [7/2023]	2,136.97 (2,288.97) [2,136.97]	2,362.99 (0.00) [55]
495	GOHA-KHELLANI PKG-3	2/2021	3/2023 (5/2023) [10/2023]	431.28 (-) [431.28]	173.60 (0.00) [7]
496	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B	7/2022	3/2025 (-) [3/2025]	198.28 (-) [198.28]	1.79 (0.00) [0]
497	KHELLANI-KHANABAL PKG-1	3/2021	9/2022 (6/2023) [10/2023]	486.45 (-) [486.45]	92.05 (0.00) [13]
498	KHELLANI-KHANABAL PKG-2	7/2021	2/2023 (-) [10/2024]	512.43 (-) [512.43]	38.94 (0.00) [20]
499	KHELLANI-KHANABAL PKG-3	3/2021	12/2022 (-) [11/2023]	398.51 (-) [398.51]	53.04 (0.00) [11]
500	KHELLANI-KHANABAL PKG-4	7/2021	8/2023 (-) [9/2024]	859.67 (-) [859.67]	66.85 (0.00) [13]
501	KHELLANI-KHANABAL PKG-5	7/2021	2/2023 (-) [1/2024]	497.09 (-) [497.09]	74.15 (0.00) [11]
502	KHELLANI-KHANABAL PKG-6	2/2021	9/2022 (-) [8/2023]	285.28 (-) [285.28]	218.89 (0.00) [11]
503	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (6/2023) [3/2024]	228.39 (-) [228.39]	36.59 (0.00) [23]
504	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (5/2023) [1/2024]	210.79 (-) [210.79]	46.44 (0.00) [21]
505	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2021 (3/2023) [8/2023]	253.44 (-) [253.44]	167.30 (0.00) [25]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
506	CHANDRAGUPT OCP	8/2020	3/2032 (-) [3/2032]	973.50 (-) [973.50]	5.95 (0.00) [0]
507	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-)	513.98 (-)	139.51 (0.01)

			[3/2024]	[513.99]	[0]
508	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2024]	163.51 (-) [163.51]	133.28 (0.00) [156]
509	EPR PUNDI OCP	11/2020	3/2024 (-) [3/2024]	713.35 (-) [713.35]	235.72 (0.00) [0]
510	EPR ROHINI KARKATA OCP	1/2021	3/2025 (-) [3/2025]	1,020.42 (-) [1,020.42]	79.34 (0.00) [0]
511	EPR TAPIN SOUTH OCP	11/2020	3/2025 (-) [3/2025]	230.41 (-) [230.41]	17.20 (0.00) [0]
512	EXPANSION OF ASHOK OCP	5/2021	3/2026 (-) [3/2026]	2,898.28 (-) [2,898.28]	173.90 (0.00) [0]
513	EXPANSION OF KARO OCP	1/2022	3/2026 (-) [3/2026]	908.47 (-) [908.47]	132.99 (0.00) [0]
514	EXPANSION OF KONAR OCP	1/2022	3/2032 (-) [3/2032]	799.34 (-) [799.34]	283.00 (0.00) [0]
515	EXPANSION PROJECT AMRAPALI OCP	8/2020	3/2028 (-) [3/2028]	5,136.15 (-) [5,136.15]	572.77 (0.00) [0]
516	HURA - C OC (3 MTY)	10/2015	3/2022 (3/2029) [3/2029]	359.69 (-) [859.41]	283.39 (499.72) [84]
517	JHARKHAND LAIYO OCP	8/2020	3/2031 (-) [3/2031]	764.57 (-) [764.57]	145.31 (0.00) [0]
518	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2024]	162.46 (-) [162.46]	94.69 (0.00) [120]
519	KOTRE BASANTPUR PACHMO OCP	8/2020	3/2032 (-) [3/2032]	861.06 (625.40) [861.06]	139.37 (0.00) [0]
520	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [11/2023]	289.45 (-) [302.00]	297.18 (12.55) [114]
521	MOONIDIH XV SEAM UG	8/2011	3/2019 (-) [4/2025]	1,230.27 (-) [1,230.27]	582.15 (0.00) [73]
522	MURAIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2025]	339.88 (-) [339.88]	151.04 (0.00) [138]
523	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2024]	555.52 (-) [555.52]	379.46 (0.00) [36]
524	PACHWARA SOUTH COAL BLOCK	7/2013	9/2028 (-) [9/2028]	1,795.01 (-) [1,795.01]	45.19 (0.00) [0]
525	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [3/2024]	243.00 (-) [334.27]	80.44 (91.27) [71]
526	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2025]	510.85 (-) [510.85]	487.68 (0.00) [108]
527	REVISED PROJECT REPORT MAGADH EXPANSION OCP	8/2020	3/2028 (-) [3/2028]	7,254.37 (-) [7,254.37]	902.16 (0.00) [0]
528	SIRKA OCP	5/2020	3/2025 (-)	222.82 (-)	139.31 (0.00)

			[3/2025]	[222.82]	[0]
529	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2025]	243.52 (-) [243.52]	41.66 (0.00) [24]
530	UCE OF EPR OF NORTH URIMARI OCP	7/2021	3/2026 (-) [3/2026]	778.80 (-) [778.80]	574.94 (0.00) [0]
	<u>Department Of Higher Education</u>				
531	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [0/2016]	171.86 (-) [171.86]	169.69 (0.00) [0]
	<u>Petroleum</u>				
532	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	12/2029 (3/2030) [3/2030]	613.00 (-) [613.00]	224.64 (0.00) [3]
533	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2023]	226.45 (-) [226.45]	217.29 (0.00) [12]
534	CITY GAS DISTRIBUTION NETWORK PROJECT AT CHATRA AND PALAMU	12/2019	3/2029 (-) [3/2029]	230.25 (-) [230.25]	42.85 (0.00) [0]
535	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [12/2023]	221.45 (-) [221.45]	152.54 (0.00) [14]
536	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1)	11/2019	1/2024 (-) [12/2024]	431.00 (-) [431.00]	76.44 (0.00) [11]
537	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2024) [3/2024]	823.27 (1,137.79) [1,137.79]	954.95 (314.52) [12]
538	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI	3/2023	2/2026 (-) [2/2026]	202.07 (-) [202.07]	0.23 (0.00) [0]
539	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (3/2023) [5/2023]	248.55 (-) [248.55]	217.31 (0.00) [0]
	<u>Power</u>				
540	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [6/2024]	14,366.58 (-) [17,007.00]	14,880.63 (2,640.42) [60]
541	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2025]	18,668.00 (-) [18,668.00]	11,484.39 (0.00) [24]
	<u>Railways</u>				
542	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [3/2024]	1,724.20 (3,029.04) [3,029.04]	1,693.74 (1,304.84) [36]
543	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2024]	459.91 (1,625.87) [1,625.87]	1,323.75 (1,165.96) [-]
544	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	4/2018	6/2022 (-) [3/2024]	428.65 (-) [472.50]	254.61 (43.85) [21]
545	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	4/2018	12/2021 (-) [8/2023]	390.39 (-) [513.92]	429.26 (123.53) [20]
	<u>Road Transport And Highways</u>				
546	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	3/2021 (6/2023) [6/2023]	1,005.08 (1,073.10) [1,073.10]	699.05 (68.02) [0]
547	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS]	9/2020	10/2023 (-)	748.99 (-)	675.22 (154.01)

			[10/2023]	[903.00]	[0]
548	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF	11/2021	7/2023 (-) [3/2024]	1,302.72 (-) [1,302.72]	521.32 (0.00) [8]
549	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH	8/2020	3/2024 (-) [3/2024]	1,034.00 (-) [1,589.00]	41.50 (555.00) [0]
550	BALANCE WORK OF RANCHI-MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG-	1/2019	12/2020 (-) [12/2023]	466.55 (518.00) [466.55]	0.00 (0.00) [36]
551	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM	2/2022	1/2025 (-) [1/2025]	534.73 (-) [534.73]	0.00 (0.00) [0]
552	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	11/2021 (-) [6/2023]	273.46 (-) [276.17]	219.58 (2.71) [0]
553	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98	9/2020	3/2024 (-) [3/2024]	755.26 (-) [1,039.00]	385.01 (283.74) [0]
554	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	11/2021 (-) [11/2023]	1,155.16 (-) [950.49]	564.62 (-204.67) [24]
555	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [3/2023]	196.00 (-) [196.00]	150.41 (0.00) [0]
	<u>Steel</u>				
556	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [9/2025]	1,034.01 (-) [1,034.01]	843.97 (0.00) [95]
557	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT	2/2022	6/2024 (-) [6/2024]	207.74 (-) [207.74]	104.27 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
558	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (3/2023) [3/2023]	246.31 (200.00) [195.00]	187.02 (-51.31) [0]
	<u>Department Of Higher Education</u>				
559	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL	8/2021	2/2024 (-) [2/2024]	316.25 (-) [316.25]	246.36 (0.00) [0]
560	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (10/2022) [3/2023]	851.00 (851.00) [851.00]	683.74 (0.00) [0]
	<u>Petroleum</u>				
561	CITY GAS DISTRIBUTION NETWORK PROJECT AT BALLARI AND GADAG	4/2019	9/2028 (-) [9/2028]	897.62 (-) [897.62]	179.90 (0.00) [0]
562	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (12/2023) [12/2023]	854.00 (854.00) [854.00]	384.42 (0.00) [12]
563	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (1/2024) [1/2024]	200.00 (304.00) [304.00]	162.85 (104.00) [7]
564	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE	1/2022	7/2025 (-) [7/2025]	463.00 (-) [463.00]	76.95 (0.00) [0]
	<u>Railways</u>				
565	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [3/2026]	986.30 (1,378.00) [1,649.31]	363.80 (663.01) [120]
566	GADAG-WADI NL	4/2013	12/2018	2,841.84	722.55

			(-) [3/2026]	(-) [2,841.84]	(0.00) [87]
567	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2024]	2,127.00 (-) [3,300.00]	3,204.74 (1,173.00) [12]
568	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [3/2030]	2,315.00 (-) [5,174.30]	159.49 (2,859.30) [-]
569	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2026]	644.78 (889.00) [826.18]	500.25 (181.40) [108]
570	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [5/2025]	279.54 (-) [279.54]	38.69 (0.00) [110]
571	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [12/2028]	832.47 (-) [832.47]	0.94 (0.00) [153]
572	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2026]	1,801.01 (-) [1,801.01]	126.80 (0.00) [-]
	Road Transport And Highways				
573	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (5/2025) [5/2025]	1,167.42 (-) [870.00]	408.72 (-297.42) [74]
574	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (6/2023) [7/2023]	1,655.01 (2,639.00) [2,639.00]	1,771.52 (983.99) [83]
575	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (12/2023) [12/2024]	701.40 (-) [701.40]	282.96 (0.00) [69]
576	4L OF ADDAHOLE TO BANTWAL CROSS SECTION	3/2021	10/2021 (9/2023) [9/2023]	317.90 (317.90) [317.90]	214.13 (0.00) [23]
577	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN	3/2021	11/2021 (4/2024) [4/2024]	1,100.88 (1,100.88) [1,100.88]	561.13 (0.00) [29]
578	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION	9/2020	1/2023 (-) [3/2025]	688.00 (-) [688.00]	399.88 (0.00) [26]
579	4L OF KM 0.00 TO KM 42.00 OF OFDOBBASPET TO DODDABALLAPURA BYPASS SECTION NH 648 OLD NH 207 BANGALO	1/2020	4/2021 (12/2023) [12/2023]	1,307.00 (-) [1,307.00]	701.00 (0.00) [32]
580	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE	3/2021	10/2024 (-) [10/2024]	1,409.68 (-) [1,409.68]	512.39 (0.00) [0]
581	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48	10/2022	4/2025 (4/2025) [4/2025]	1,479.30 (-) [1,479.30]	86.76 (0.00) [0]
582	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II)	1/2022	4/2025 (-) [4/2025]	1,388.70 (-) [1,388.70]	73.09 (0.00) [0]
583	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100	11/2022	5/2025 (-) [5/2025]	1,732.73 (-) [1,732.73]	214.41 (0.00) [0]
584	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000	12/2022	6/2025 (-) [6/2025]	2,718.46 (-) [2,718.46]	0.00 (0.00) [0]
585	AURAD - BIDAR KM 0.00 TO KM 45.878	9/2021	4/2023 (-) [9/2023]	912.37 (-) [912.37]	222.63 (0.00) [5]
586	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12	11/2022	5/2024 (5/2024) [5/2024]	226.76 (-) [226.76]	39.80 (0.00) [0]

587	BANGALORE/TN BORDER TO HOSKOTE	2/2023	2/2025 (-) [2/2025]	1,240.60 (-) [1,240.60]	403.45 (0.00) [0]
588	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4.	3/2018	12/2022 (12/2023) [2/2024]	440.16 (-) [440.16]	126.80 (0.00) [14]
589	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A	1/2021	1/2023 (12/2023) [6/2023]	1,167.52 (1,157.00) [1,167.52]	802.91 (0.00) [0]
590	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M	12/2020	9/2023 (-) [9/2023]	1,745.00 (-) [1,279.00]	822.13 (-466.00) [0]
591	CONSTRUCTION OF 4 LANE BANGALORE -CHENNAI EXPRESSWAY FROM KM 53.500 TO KM 71.000 SECTION OF NE-7 (BA	1/2021	1/2024 (-) [1/2024]	1,069.00 (-) [863.00]	508.94 (-206.00) [0]
592	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE-7(ALONG WITH 0.700	10/2020	9/2023 (-) [9/2023]	3,184.00 (-) [3,184.00]	799.94 (0.00) [0]
593	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	3/2019	12/2019 (11/2024) [11/2024]	423.15 (-) [423.15]	308.74 (0.00) [59]
594	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [11/2024]	157.32 (188.00) [187.61]	43.16 (30.29) [66]
595	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (10/2023) [10/2023]	171.60 (-) [171.60]	138.16 (0.00) [65]
596	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100	3/2021	3/2023 (12/2023) [12/2023]	1,065.06 (1,577.92) [1,577.92]	26.31 (512.86) [9]
597	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0	10/2021	10/2023 (10/2024) [10/2023]	1,331.77 (2,508.79) [2,508.79]	60.90 (1,177.02) [0]
598	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN	10/2019	10/2021 (1/2024) [1/2024]	1,225.24 (1,676.11) [1,676.11]	14.76 (450.87) [27]
599	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (8/2023) [8/2023]	946.00 (1,046.56) [1,046.56]	827.99 (100.56) [62]
600	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [8/2022]	325.86 (-) [386.41]	356.78 (60.55) [0]
601	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (7/2023) [12/2023]	175.50 (-) [241.60]	178.73 (66.10) [82]
602	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (12/2023) [12/2023]	159.97 (-) [242.61]	135.31 (82.64) [54]
603	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (6/2023) [9/2023]	165.67 (-) [165.67]	126.47 (0.00) [94]
604	TUMKUR - NELAMANGALA(6L)	8/2022	8/2025 (-) [8/2025]	2,032.15 (1,351.00) [2,032.15]	29.46 (0.00) [0]
605	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (5/2024) [5/2024]	950.69 (-) [1,108.00]	1,679.45 (157.31) [57]
606	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA	3/2022	3/2024 (3/2024) [3/2024]	294.62 (-) [294.62]	5.40 (0.00) [0]
607	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (7/2022) [7/2022]	396.96 (-) [396.96]	332.58 (0.00) [0]

608	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (7/2023) [7/2023]	314.90 (-) [314.90]	234.09 (0.00) [76]
609	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	1/2017	9/2017 (6/2023) [6/2023]	264.34 (-) [264.34]	193.05 (0.00) [0]
610	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (4/2022) [4/2022]	191.60 (-) [191.60]	112.05 (0.00) [0]
611	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (6/2022) [6/2022]	291.49 (-) [291.49]	238.77 (0.00) [0]
612	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (5/2023) [5/2023]	166.67 (-) [264.34]	193.04 (97.67) [0]
613	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (4/2022) [4/2022]	297.30 (-) [318.28]	279.03 (20.98) [0]
614	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION	1/2018	7/2018 (3/2022) [3/2022]	159.70 (-) [159.70]	155.15 (0.00) [0]
615	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (7/2023) [7/2023]	159.12 (-) [159.12]	128.18 (0.00) [90]
<u>Urban Development</u>					
616	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B	6/2021	6/2026 (-) [6/2026]	14,788.10 (-) [14,788.10]	2,424.04 (0.00) [0]
617	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2021 (-) [3/2025]	26,405.14 (-) [26,405.14]	20,936.29 (0.00) [49]
<u>KERALA</u>					
<u>Department Of Higher Education</u>					
618	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (3/2023) [3/2024]	753.63 (-) [753.63]	346.00 (0.00) [36]
619	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [10/2012]	165.23 (-) [165.23]	135.78 (0.00) [0]
<u>Health And Family Welfare</u>					
620	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	121.00 (0.00) [0]
<u>Petroleum</u>					
621	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (2/2024) [2/2025]	1,112.00 (1,507.24) [1,507.24]	1,094.66 (395.24) [68]
<u>Railways</u>					
622	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [3/2025]	1,431.90 (-) [1,431.90]	2,095.35 (0.00) [-]
623	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [3/2025]	1,000.00 (-) [1,339.00]	0.93 (339.00) [-]
<u>Road Transport And Highways</u>					
624	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (7/2023) [7/2023]	804.97 (571.45) [571.45]	648.26 (-233.52) [61]
625	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	5/2020 (11/2023) [11/2023]	1,124.11 (1,503.86) [1,503.86]	1,405.49 (379.75) [42]
626	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS)	2/2018	2/2023	1,424.77	465.92

	(I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH		(-) [9/2024]	(1,862.77) [1,862.77]	(438.00) [19]
627	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR	3/2020	6/2022 (1/2023) [12/2023]	210.37 (213.06) [213.06]	171.75 (2.69) [18]
628	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66	10/2020	4/2024 (5/2025) [5/2025]	3,219.47 (3,713.14) [3,713.14]	1,911.28 (493.67) [13]
629	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE	8/2022	1/2026 (-) [1/2026]	2,429.52 (-) [2,429.52]	0.00 (0.00) [0]
630	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX	6/2021	2/2025 (-) [2/2025]	3,606.00 (-) [3,923.82]	2,789.91 (317.82) [0]
631	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH –66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 (	11/2021	4/2025 (-) [4/2025]	3,565.82 (-) [3,064.11]	1,570.57 (-501.71) [0]
632	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH	2/2021	7/2024 (-) [7/2024]	3,375.31 (-) [3,790.17]	1,745.63 (414.86) [0]
633	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX.	6/2021	3/2025 (-) [3/2025]	2,595.00 (-) [3,994.60]	2,696.56 (1,399.60) [0]
634	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+	6/2020	4/2024 (10/2021) [4/2024]	1,746.45 (2,377.88) [1,746.45]	879.34 (0.00) [0]
635	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54	12/2021	1/2025 (1/2025) [1/2025]	3,635.64 (-) [3,635.64]	75.12 (0.00) [0]
636	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC	6/2021	10/2024 (10/2024) [10/2024]	2,842.14 (-) [2,842.14]	117.96 (0.00) [0]
637	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH	5/2020	5/2024 (11/2021) [5/2024]	1,981.07 (2,430.53) [1,981.07]	1,121.13 (0.00) [0]
638	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+	6/2020	4/2024 (10/2021) [4/2024]	3,041.65 (3,799.76) [3,041.65]	1,795.19 (0.00) [0]
639	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6	12/2021	2/2025 (2/2025) [2/2025]	3,273.61 (-) [3,273.61]	75.26 (0.00) [0]
640	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM	1/2021	7/2024 (-) [7/2024]	4,265.42 (-) [4,708.42]	2,751.50 (443.00) [0]
641	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66	6/2021	3/2025 (3/2025) [3/2025]	2,641.37 (-) [2,641.37]	138.53 (0.00) [0]
642	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH	8/2020	2/2024 (11/2021) [2/2024]	2,714.60 (3,319.41) [2,714.60]	1,414.01 (0.00) [0]
643	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O	9/2021	9/2024 (9/2024) [9/2024]	2,878.97 (-) [2,878.97]	154.45 (0.00) [0]
644	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK	2/2017	8/2017 (3/2022) [8/2023]	294.28 (296.53) [296.53]	274.50 (2.25) [72]
645	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49)	2/2017	9/2017 (1/2023) [6/2023]	380.76 (372.87) [372.87]	313.19 (-7.89) [0]
	<u>Urban Development</u>				
646	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (9/2020) [9/2020]	5,181.79 (-) [6,218.14]	6,059.17 (1,036.35) [0]

	<u>LADAKH</u>				
	<u>Civil Aviation</u>				
647	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (12/2023) [3/2024]	480.33 (-) [640.00]	245.19 (159.67) [30]
	<u>Road Transport And Highways</u>				
648	KARGIL-ZANSKR PACKAGE-1	3/2021	1/2023 (11/2023) [11/2023]	384.23 (-) [384.23]	48.09 (0.00) [10]
649	KARGIL-ZANSKR PACKAGE-2	3/2021	1/2023 (11/2023) [11/2023]	404.89 (-) [404.89]	40.59 (0.00) [10]
650	KARGIL-ZANSKR PACKAGE-3	8/2020	1/2023 (10/2023) [10/2023]	381.01 (-) [381.01]	83.24 (0.00) [9]
651	KARGIL-ZANSKR PACKAGE-5	8/2020	12/2023 (-) [12/2023]	169.79 (217.99) [169.79]	196.67 (0.00) [0]
652	KARGIL-ZANSKR PACKAGE-6	1/2021	5/2024 (-) [5/2024]	239.81 (265.41) [239.81]	171.38 (0.00) [0]
653	KARGIL-ZANSKR PACKAGE-7	1/2021	6/2024 (-) [6/2024]	308.86 (328.60) [308.86]	185.10 (0.00) [0]
654	KARGIL-ZANSKR PACKAGE-8	3/2021	1/2023 (8/2023) [8/2023]	398.37 (-) [398.37]	93.05 (0.00) [7]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
655	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01	10/2021	8/2023 (9/2023) [9/2023]	446.12 (-) [446.12]	271.14 (0.00) [1]
656	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (-) [9/2023]	412.24 (-) [412.24]	354.98 (0.00) [27]
	<u>Coal</u>				
657	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (3/2025) [3/2025]	869.44 (-) [869.44]	201.12 (0.00) [48]
658	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY)	9/2022	3/2027 (-) [3/2027]	497.01 (-) [497.01]	136.72 (0.00) [0]
659	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2027]	481.60 (-) [481.60]	1.08 (0.00) [48]
660	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2024]	231.92 (-) [231.92]	2.26 (0.00) [24]
661	BATURA WEST OC PROJECT (0.80 MTY)	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]
662	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2025]	998.71 (-) [998.71]	106.29 (0.00) [24]
663	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [8/2023]	1,255.17 (-) [1,255.17]	1,011.43 (0.00) [17]
664	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	24.41 (0.00) [0]
665	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-)	1,783.09 (-)	1,447.90 (0.00)

			[10/2023]	[1,783.09]	[31]
666	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	100.88 (0.00) [36]
667	NIGAHI EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	285.78 (0.00) [0]
668	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2024]	357.80 (-) [357.80]	86.99 (0.00) [36]
669	RAMPUR BATURA OC (4.0 MTY)	7/2019	3/2026 (-) [3/2026]	1,248.93 (-) [1,248.93]	408.00 (0.00) [0]
670	TAWA III UG MINE	12/2021	3/2027 (-) [3/2027]	324.25 (-) [324.25]	12.19 (0.00) [0]
671	VISHNUPURI UG TO OC	11/2022	3/2029 (-) [3/2029]	227.65 (-) [227.65]	7.02 (0.00) [0]
	<u>Petroleum</u>				
672	CGD PROJECT AT REWA DISTRICT	10/2018	2/2027 (9/2028) [9/2028]	177.00 (-) [177.00]	107.21 (0.00) [19]
673	CITY GAS DISTRIBUTION NETWORK PROJECT AT SATNA AND SHAHDOL	4/2019	9/2028 (-) [9/2028]	332.38 (-) [332.38]	86.74 (0.00) [0]
674	CITY GAS DISTRIBUTION NETWORK PROJECT AT SIDHI AND SANGRAULI	12/2019	3/2029 (-) [3/2029]	350.35 (-) [350.35]	66.39 (0.00) [0]
	<u>Power</u>				
675	OMKARESHWAR FLOATING SOLAR POWER PROJECT (90 MW)	11/2022	4/2024 (-) [4/2024]	646.17 (-) [646.17]	255.95 (0.00) [0]
676	SHAJAPUR 325MW SOLAR PV PROJECT	6/2022	3/2024 (3/2024) [2/2024]	1,530.49 (-) [1,530.49]	208.92 (0.00) [-1]
	<u>Railways</u>				
677	ANUPPUR-KATNI	4/2015	12/2021 (12/2023) [12/2024]	1,370.00 (-) [1,680.00]	1,171.79 (310.00) [36]
678	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (-) [10/2023]	700.00 (603.69) [603.69]	639.96 (-96.31) [40]
679	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2024]	1,763.93 (2,445.30) [2,445.30]	2,020.86 (681.37) [55]
680	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [9/2024]	582.13 (-) [1,247.64]	990.59 (665.51) [30]
681	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [6/2024]	2,478.23 (2,938.00) [2,938.00]	1,279.35 (459.77) [27]
682	NIMACH BADI SADRI NEW LINE PROJECT	4/2017	3/2022 (3/2026) [3/2026]	495.18 (495.18) [495.18]	0.83 (0.00) [48]
683	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (12/2025) [12/2025]	424.60 (2,909.99) [3,032.46]	2,080.00 (2,607.86) [57]
684	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2026) [3/2026]	3,503.69 (5,677.80) [6,021.00]	2,919.74 (2,517.31) [48]
	<u>Road Transport And Highways</u>				

685	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125	1/2021	10/2023 (-) [10/2023]	428.04 (-) [328.77]	291.27 (-99.27) [0]
686	2L PS OF UJJAIN - JHALAWAR (UPTO RJ BORDER) FROM KM. (-)0.650 TO KM. 132.955 OF NH-552G	10/2020	6/2023 (11/2023) [6/2023]	506.56 (498.00) [506.56]	345.36 (0.00) [0]
687	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (8/2021) [8/2023]	249.05 (-) [249.05]	221.19 (0.00) [61]
688	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	11/2019	7/2021 (11/2023) [7/2023]	716.00 (-) [716.00]	334.38 (0.00) [24]
689	4L MISSING LINK (OF REWA BYPASS) FROM JN. WITH NH 30 NEAR BELA TO JN. WITH MPRDC RING ROAD (NEAR SIL	2/2021	1/2023 (-) [12/2023]	197.87 (-) [197.87]	35.62 (0.00) [11]
690	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D	1/2020	6/2024 (-) [6/2024]	909.84 (-) [909.84]	130.08 (0.00) [0]
691	4L OF HARDA - BETUL (PKG-I) FROM KM.0 TO KM.30 [HARDA - TEMAGAON]	9/2021	9/2023 (-) [9/2023]	774.16 (-) [774.16]	336.63 (0.00) [0]
692	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI]	2/2023	2/2025 (-) [2/2025]	520.28 (-) [520.28]	75.46 (0.00) [0]
693	4L OF HARDA - BETUL (PKG-III) FROM KM. 81.00 TO KM.121.248 [CHICHOLI - BETUL]	9/2021	9/2023 (-) [9/2023]	814.04 (-) [814.04]	391.67 (0.00) [0]
694	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND	1/2021	4/2024 (-) [4/2024]	1,001.69 (-) [1,001.69]	29.75 (0.00) [0]
695	4L OF KHEDAKHAJURIYA TO SUHAGADI FROM KM. 41.400 TO KM. 89.200 OF NH-148NG (PKG-II)	1/2020	10/2024 (-) [6/2024]	876.37 (-) [876.37]	177.45 (0.00) [-4]
696	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69	2/2022	3/2024 (-) [3/2024]	417.51 (-) [417.51]	52.14 (0.00) [0]
697	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I)	3/2021	4/2024 (-) [4/2024]	790.78 (-) [790.78]	133.42 (0.00) [0]
698	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III)	1/2020	10/2024 (-) [6/2024]	823.05 (-) [823.05]	120.24 (0.00) [-4]
699	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D	10/2020	10/2024 (-) [10/2024]	1,352.56 (-) [1,352.56]	178.51 (0.00) [0]
700	4LBERKHEDI TO GODPEHRA NH-44	2/2022	11/2024 (-) [11/2024]	524.84 (-) [524.84]	1,600.30 (0.00) [0]
701	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N	8/2022	7/2024 (-) [7/2024]	207.77 (-) [207.77]	0.00 (0.00) [0]
702	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [1/2023]	359.00 (359.00) [359.00]	326.56 (0.00) [0]
703	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	2/2020 (-) [10/2023]	950.27 (-) [950.27]	521.56 (0.00) [44]
704	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (3/2022) [8/2023]	392.33 (470.72) [470.72]	431.91 (78.39) [65]
705	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF	8/2019	4/2023 (-) [11/2023]	323.51 (-) [323.51]	2.46 (0.00) [7]

706	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2021]	390.51 (-) [390.51]	306.63 (0.00) [0]
707	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	11/2022 (-) [8/2023]	656.98 (-) [840.00]	1,103.00 (183.02) [9]
708	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	12/2021 (11/2022) [8/2023]	743.88 (-) [743.89]	832.00 (0.01) [20]
709	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	2/2022 (11/2022) [8/2023]	1,094.97 (-) [1,094.97]	1,188.00 (0.00) [18]
710	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	12/2022 (-) [8/2023]	217.96 (-) [884.00]	2,298.00 (666.04) [8]
711	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (12/2021) [8/2023]	205.05 (-) [205.05]	140.29 (0.00) [77]
712	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2022) [3/2023]	264.50 (-) [264.50]	215.21 (0.00) [0]
713	DHANGAON - BORGAON SECTION (KM 81.000 TO KM 139.000) [INDORE - EDLABAD PKG IV]	11/2018	8/2023 (-) [12/2023]	831.00 (-) [831.00]	608.00 (0.00) [4]
714	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903]	1/2022	10/2024 (-) [10/2024]	1,011.29 (-) [1,011.29]	0.00 (0.00) [0]
715	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445]	10/2021	1/2024 (-) [1/2024]	1,146.22 (-) [1,146.22]	444.64 (0.00) [0]
716	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (6/2021) [4/2023]	628.45 (-) [628.45]	480.18 (0.00) [0]
717	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50	9/2019	9/2022 (-) [6/2023]	194.40 (-) [194.40]	134.69 (0.00) [0]
718	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [6/2023]	410.72 (-) [410.72]	392.45 (0.00) [0]
719	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2021 (9/2022) [8/2023]	990.97 (-) [990.97]	1,092.00 (0.00) [20]
720	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (3/2023) [8/2023]	1,047.00 (-) [1,047.00]	1,169.00 (0.00) [39]
721	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2022 (11/2022) [8/2023]	847.00 (-) [847.00]	920.50 (0.00) [17]
722	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2022 (11/2022) [8/2023]	996.27 (-) [996.27]	1,079.00 (0.00) [17]
723	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (12/2022) [12/2023]	169.63 (-) [169.63]	103.61 (0.00) [69]
724	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (12/2023) [12/2023]	511.83 (-) [511.83]	455.78 (0.00) [76]
725	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [6/2023]	233.04 (-) [233.04]	187.88 (0.00) [0]
726	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (11/2021) [5/2022]	279.44 (-) [279.44]	234.24 (0.00) [0]

727	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (8/2021) [4/2023]	166.21 (-) [174.90]	155.10 (8.69) [0]
728	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (9/2021) [4/2023]	184.62 (-) [184.62]	145.45 (0.00) [0]
729	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (12/2023) [12/2023]	214.69 (-) [214.69]	101.84 (0.00) [69]
730	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [4/2023]	162.56 (-) [162.56]	137.52 (0.00) [0]
	<u>Social Justice</u>				
731	CENTRE FOR DISABILITY SPORTS	2/2019	3/2024 (-) [3/2024]	170.99 (-) [170.99]	73.80 (0.00) [0]
	<u>Urban Development</u>				
732	BHOPAL METRO RAIL	11/2018	2/2023 (12/2026) [12/2026]	6,941.40 (-) [6,941.40]	1,271.31 (0.00) [46]
733	INDORE METRO RAIL	11/2018	2/2023 (12/2026) [12/2026]	7,500.80 (-) [7,500.80]	1,615.18 (0.00) [46]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
734	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [9/2023]	475.39 (-) [475.39]	391.54 (0.00) [29]
735	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM	6/2017	12/2020 (-) [9/2023]	255.68 (-) [255.68]	225.87 (0.00) [33]
	<u>Coal</u>				
736	DINESH (MAKARDHOKDA-III) OC (8.0 MTY)	2/2020	3/2027 (-) [3/2027]	1,184.33 (-) [1,184.33]	692.00 (0.00) [0]
737	ADASA UG TO OC (1.50 MTY)	11/2018	3/2024 (-) [3/2024]	333.43 (-) [333.43]	204.07 (0.00) [0]
738	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY)	9/2018	3/2024 (-) [3/2024]	313.34 (-) [313.34]	192.55 (0.00) [0]
739	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	505.75 (0.00) [0]
740	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (3/2024) [3/2024]	252.71 (-) [252.71]	121.58 (0.00) [36]
741	BHANEGAON OC (1.15MTY)	9/2022	3/2028 (-) [3/2028]	494.60 (-) [494.60]	97.51 (0.00) [0]
742	BHATADI EXPANSION OC	2/2020	3/2028 (-) [3/2028]	729.86 (-) [729.86]	158.48 (0.00) [0]
743	DHUPTALA OC(SASTI UG TO OC)	2/2019	3/2028 (-) [3/2028]	720.87 (-) [720.87]	171.31 (0.00) [0]
744	GHONSA EXPANSION DEEP OC	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	58.79 (0.00) [0]
745	GOKUL EXPANSION OC	4/2021	3/2026 (-) [3/2026]	456.95 (-) [456.95]	147.37 (0.00) [0]

746	MAKARDHOKDA I EXPANSION OC	6/2022	3/2026 (-) [3/2026]	497.06 (-) [497.06]	140.99 (0.00) [0]
747	MUNGOLI NIRGUDA EXTENSION (DEEP) OC	11/2020	3/2026 (-) [3/2026]	826.80 (-) [826.80]	340.53 (0.00) [0]
748	NEW MAJARI UG TO OC (3.0 MTY)	5/2019	3/2027 (-) [3/2027]	496.38 (-) [496.38]	105.47 (0.00) [0]
749	RPR PAUNI II EXPANSION OC	3/2023	3/2027 (-) [3/2027]	464.45 (-) [464.45]	177.30 (0.00) [0]
750	SAONER UG MINE I EXPANSION	1/2022	3/2028 (-) [3/2028]	253.51 (-) [253.51]	51.26 (0.00) [0]
751	SASTI EXPANSION OC	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	61.09 (0.00) [0]
752	SINGHORI DEEP OC	5/2022	3/2029 (-) [3/2029]	421.84 (-) [421.84]	110.40 (0.00) [0]
753	UKNI DEEP OC	11/2018	3/2021 (3/2025) [3/2025]	318.14 (-) [318.14]	249.15 (0.00) [48]
	<u>Department Of Higher Education</u>				
754	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2023) [9/2023]	223.37 (275.00) [230.00]	168.67 (6.63) [38]
	<u>Fertilisers</u>				
755	AN MELT PROJECT AT RCF TROMBAY	5/2022	9/2024 (-) [7/2024]	187.27 (187.27) [187.27]	18.53 (0.00) [-2]
756	INSTALLATION OF NEW NANO UREA FERTILIZER PLANT AT RCF TROMBAY	5/2023	3/2024 (-) [3/2024]	238.30 (-) [238.30]	0.30 (0.00) [0]
	<u>Petroleum</u>				
757	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA)	9/2022	8/2025 (-) [8/2025]	165.00 (-) [165.00]	0.24 (0.00) [0]
758	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS	3/2022	3/2030 (-) [3/2030]	865.00 (-) [865.00]	13.28 (0.00) [0]
759	CITY GAS DISTRIBUTION NETWORK PROJECT AT AHMEDNAGAR AND AURANGABAD	4/2019	9/2028 (-) [9/2028]	3,972.18 (-) [3,972.18]	1,233.81 (0.00) [0]
760	CITY GAS DISTRIBUTION NETWORK PROJECT AT SANGLI AND SATARA	4/2019	11/2028 (-) [11/2028]	2,337.98 (-) [2,337.98]	635.90 (0.00) [0]
761	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI	5/2022	3/2024 (-) [9/2024]	423.39 (-) [423.39]	63.90 (0.00) [6]
762	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK	6/2022	10/2025 (-) [10/2025]	4,144.41 (-) [4,144.41]	0.00 (0.00) [0]
763	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL	4/2021	6/2024 (-) [7/2025]	1,164.69 (-) [1,164.69]	169.72 (0.00) [13]
764	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY	9/2021	10/2023 (5/2024) [5/2024]	378.00 (-) [378.00]	66.49 (0.00) [7]
765	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (12/2023)	2,494.68 (-)	2,354.10 (0.00)

			[12/2023]	[2,494.68]	[21]
766	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (4/2023) [12/2023]	1,945.00 (2,251.00) [2,251.00]	2,005.03 (306.00) [22]
767	LEASE OF MBPT RECLAIMED LAND AT JAWAHAR DWEED	12/2022	12/2023 (-) [12/2023]	410.00 (-) [410.00]	40.71 (0.00) [0]
768	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (12/2023) [5/2026]	3,190.69 (3,375.90) [3,375.90]	2,897.83 (185.21) [97]
769	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (12/2023) [12/2023]	3,228.80 (3,976.67) [3,976.67]	3,793.93 (747.87) [21]
770	PIPELINE REPLACEMENT PROJECT - VII	1/2022	5/2024 (-) [5/2024]	3,183.58 (-) [3,183.58]	1,276.83 (0.00) [0]
771	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	1,753.85 (0.00) [0]
	<u>Power</u>				
772	BIKANER SOLAR POWER PROJECT	4/2022	5/2024 (-) [5/2024]	5,491.89 (532.00) [6,023.89]	2,211.03 (532.00) [0]
	<u>Railways</u>				
773	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (3/2025) [3/2026]	2,271.50 (-) [4,805.17]	3,491.85 (2,533.67) [60]
774	DAUND - MANMAD (236 KM)	2/2016	3/2023 (3/2025) [3/2026]	1,876.00 (-) [2,081.27]	1,335.69 (205.27) [36]
775	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (3/2025) [3/2024]	2,449.91 (-) [2,449.91]	928.90 (0.00) [12]
776	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2026]	792.89 (-) [792.89]	578.90 (0.00) [60]
777	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (3/2025) [3/2024]	1,035.16 (-) [1,035.16]	830.46 (0.00) [24]
778	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [3/2024]	265.88 (-) [311.36]	0.00 (45.48) [-]
779	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2014]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]
780	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (3/2025) [3/2024]	3,627.47 (3,627.00) [6,409.38]	2,826.85 (2,781.91) [0]
781	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2024]	1,908.51 (2,753.05) [3,544.25]	2,238.21 (1,635.74) [21]
782	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [3/2024]	217.38 (-) [393.62]	142.48 (176.24) [-]
783	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2025]	229.00 (-) [1,096.00]	230.25 (867.00) [48]
784	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [12/2024]	637.95 (-) [637.95]	513.52 (0.00) [21]
785	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (3/2025)	1,272.19 (-)	757.06 (112.53)

			[12/2024]	[1,384.72]	[33]
786	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2024]	3,168.29 (-) [3,445.48]	1,666.35 (277.19) [12]
787	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [12/2024]	540.02 (-) [540.02]	410.94 (0.00) [33]
<u>Road Transport And Highways</u>					
788	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (7/2022) [7/2024]	744.64 (-) [1,007.00]	257.01 (262.36) [52]
789	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [12/2023]	446.17 (-) [356.62]	318.13 (-89.55) [57]
790	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [2/2023]	1,142.62 (1,907.03) [1,142.62]	1,056.08 (0.00) [0]
791	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [12/2023]	1,101.58 (-) [1,101.58]	608.53 (0.00) [-]
792	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (7/2023) [7/2023]	400.25 (-) [304.07]	299.26 (-96.18) [52]
793	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	7/2021 (12/2023) [12/2023]	1,064.88 (-) [1,021.00]	800.70 (-43.88) [29]
794	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (5/2021) [6/2023]	1,059.73 (1,071.00) [1,071.00]	837.73 (11.27) [0]
795	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53	2/2021	11/2023 (-) [11/2023]	540.21 (-) [540.21]	164.19 (0.00) [0]
796	4L OF AHMEDNAGAR - MIRAJGAON - KARMALA - TEMBHURNI (PKG-I) [AHMEDNAGAR TO GHOGARGAON] FROM KM. 0.00	12/2021	12/2023 (-) [12/2023]	605.00 (605.00) [605.00]	415.21 (0.00) [0]
797	4L OF AHMEDNAGAR - MIRAJGAON - KARMALA - TEMBHURNI (PKG-II) [GHOGARGAON TO AHMEDNAGAR-SOLPAUR DISTR	1/2022	1/2024 (-) [1/2024]	629.00 (629.00) [629.00]	426.44 (0.00) [0]
798	4L OF AKOLA - MEDSHI FROM KM. 0.00 TO KM. 47.70 OF NH-161 INCLUDING BYPASSES AT PATUR AND MEDSHI	12/2019	11/2022 (9/2023) [9/2023]	1,393.95 (1,393.95) [576.00]	527.13 (-817.95) [10]
799	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361	3/2018	3/2021 (-) [6/2023]	1,169.04 (-) [1,693.95]	1,010.33 (524.91) [0]
800	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG)	9/2021	9/2023 (9/2023) [3/2024]	624.45 (627.79) [627.79]	309.89 (3.34) [6]
801	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S	5/2022	5/2024 (-) [5/2024]	519.93 (-) [519.93]	126.16 (0.00) [0]
802	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL – ALANDI S	1/2022	5/2024 (5/2024) [5/2024]	1,833.73 (-) [1,833.73]	126.16 (0.00) [0]
803	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG)	9/2021	9/2023 (9/2023) [3/2024]	667.66 (666.21) [666.21]	329.65 (-1.45) [6]
804	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J	2/2021	10/2023 (-) [4/2024]	1,166.96 (-) [1,251.00]	755.96 (84.04) [6]
805	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B	3/2022	10/2024 (10/2024) [10/2024]	1,013.33 (-) [1,111.33]	202.73 (98.00) [0]

806	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG-III)	5/2023	5/2025 (-) [5/2025]	986.00 (-) [986.00]	0.00 (0.00) [0]
807	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG – II)	5/2023	5/2025 (-) [5/2025]	839.00 (-) [839.00]	4.51 (0.00) [0]
808	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 (	11/2022	11/2024 (-) [11/2024]	930.00 (-) [930.00]	104.34 (0.00) [0]
809	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I)	1/2023	1/2025 (-) [1/2025]	1,025.20 (-) [1,025.20]	80.27 (0.00) [0]
810	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II)	12/2022	12/2024 (-) [12/2024]	1,749.86 (-) [1,749.86]	228.15 (0.00) [0]
811	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800	10/2021	1/2024 (-) [1/2024]	815.77 (-) [815.77]	227.75 (0.00) [0]
812	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [3/2023]	422.38 (-) [422.38]	256.59 (0.00) [0]
813	AHMEDNAGAR BYPASS	7/2021	7/2023 (-) [7/2023]	715.00 (715.00) [715.00]	398.42 (0.00) [0]
814	AKOLA TO AKOT	1/2017	6/2019 (-) [8/2023]	313.95 (-) [313.95]	270.26 (0.00) [50]
815	AKOT TO ANJANGAON	1/2017	6/2019 (-) [1/2023]	245.77 (246.00) [245.77]	221.84 (0.00) [0]
816	AMDHI TO SAONER	1/2017	6/2019 (-) [8/2023]	396.91 (397.00) [396.91]	289.79 (0.00) [50]
817	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [1/2023]	426.06 (426.00) [426.06]	271.40 (0.00) [0]
818	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [2/2023]	309.94 (310.00) [309.94]	207.17 (0.00) [0]
819	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [2/2023]	456.32 (-) [456.32]	342.78 (0.00) [0]
820	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794)	12/2019	9/2022 (-) [11/2023]	1,654.07 (-) [980.00]	724.63 (-674.07) [14]
821	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO	1/2023	12/2023 (-) [12/2023]	151.26 (-) [151.26]	15.85 (0.00) [0]
822	BALANCE WORK UNDER PHASE-I FOR 4L OF KHED SINNER SECTION COMPRISING OF THE STRETCHES (I) KHED BYPASS	10/2020	10/2022 (6/2023) [6/2023]	169.83 (-) [169.83]	201.04 (0.00) [0]
823	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG I) [AMRAVATI TO KURANKHED FROM KM. 166.00 TO KM. 220.00]	11/2019	7/2023 (-) [10/2023]	713.07 (-) [713.07]	281.00 (0.00) [3]
824	BALANCE WORKS OF 4L AMRAVATI - CHIKHLI (PKG II) [KURANKHED TO SHELAD FROM KM. 220.00 TO KM. 270.00]	11/2019	2/2023 (-) [9/2023]	633.70 (-) [633.70]	244.30 (0.00) [7]
825	BALANCE WORKS OF 4L AMRAVATI CHIKHLI (PKG IV) [NANDURA TO CHIKHLI FROM KM. 315.00 TO KM. 360.00]	11/2019	5/2023 (-) [8/2023]	583.61 (-) [583.61]	237.57 (0.00) [3]
826	BALANCE WORKS OF 4L PANVEL-INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 (	10/2022	5/2024 (-) [5/2024]	332.00 (-) [332.00]	0.00 (0.00) [0]

827	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [9/2023]	289.11 (290.00) [289.11]	232.56 (0.00) [60]
828	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [1/2023]	392.83 (393.00) [392.83]	274.75 (0.00) [0]
829	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2023]	743.21 (743.00) [743.21]	911.64 (0.00) [0]
830	BHOKAR TO SARSAM	2/2017	7/2019 (-) [11/2020]	295.09 (-) [295.99]	186.27 (0.90) [0]
831	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [11/2020]	178.26 (-) [178.26]	159.96 (0.00) [0]
832	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80	3/2018	3/2023 (-) [6/2023]	1,241.38 (-) [2,122.64]	1,577.64 (881.26) [0]
833	CHIKALI TO DHAD	3/2018	12/2019 (-) [3/2024]	189.46 (189.00) [189.46]	111.73 (0.00) [51]
834	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [1/2023]	393.10 (393.00) [393.10]	255.24 (0.00) [0]
835	CHIMUR TO WARORA	11/2016	3/2019 (-) [2/2023]	467.70 (-) [467.70]	323.36 (0.00) [0]
836	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	7/2021 (-) [9/2024]	1,162.92 (1,182.87) [1,182.87]	160.20 (19.95) [38]
837	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (11/2023) [11/2023]	649.50 (-) [649.50]	303.15 (0.00) [56]
838	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [6/2019]	168.30 (-) [168.30]	100.56 (0.00) [0]
839	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [6/2023]	247.02 (-) [157.49]	70.50 (-89.53) [0]
840	DAHEGAON TO KUHI	1/2017	6/2019 (-) [9/2023]	228.89 (229.00) [228.89]	154.82 (0.00) [51]
841	DEORI TO AMGAON	1/2017	5/2019 (-) [2/2023]	409.62 (410.00) [409.62]	290.44 (0.00) [0]
842	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2023]	336.21 (336.00) [336.21]	236.11 (0.00) [48]
843	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [8/2023]	217.14 (217.00) [217.14]	157.89 (0.00) [42]
844	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION	9/2021	9/2023 (-) [9/2023]	618.45 (-) [618.45]	353.77 (0.00) [0]
845	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [12/2023]	391.06 (391.00) [391.06]	263.11 (0.00) [54]
846	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [2/2023]	456.45 (-) [456.45]	427.43 (0.00) [0]
847	FOUR LANING OF AURANGABAD-PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA .	10/2022	7/2024 (-) [7/2024]	490.40 (-) [289.00]	13.29 (-201.40) [0]

848	GADCHIROLI TO MUL	12/2016	6/2019 (-) [1/2023]	484.15 (-) [484.15]	456.25 (0.00) [0]
849	HELWAK TO KARAD	2/2017	7/2019 (-) [1/2023]	416.99 (-) [416.99]	225.83 (0.00) [0]
850	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [9/2023]	294.87 (295.00) [294.87]	183.17 (0.00) [45]
851	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [2/2023]	355.17 (-) [355.17]	318.68 (0.00) [0]
852	INDAPUR TO VADPALE	1/2017	12/2019 (-) [6/2023]	1,202.52 (1,203.00) [1,202.52]	1,450.82 (0.00) [0]
853	INTEGRATED STRUCTURE WITH DEVELOPMENT OF OTHER ALLIED STRUCTURES ON BOTH SIDES OF CHANDNI CHOWK JUNC	2/2019	2/2022 (-) [8/2023]	397.60 (-) [397.60]	335.38 (0.00) [18]
854	JAHRABAD TO LATUR	1/2017	11/2019 (-) [2/2023]	461.96 (-) [461.96]	329.59 (0.00) [0]
855	JALGAON TO NANDURA	3/2018	12/2019 (-) [9/2023]	177.84 (177.00) [177.84]	110.20 (0.00) [45]
856	JALKOT TO TOGRI	7/2018	8/2020 (-) [12/2023]	299.92 (300.00) [299.92]	188.96 (0.00) [40]
857	JINTUR TO PARBHANI	1/2017	/ (-) [8/2023]	356.66 (-) [356.66]	209.48 (0.00) [-]
858	KALMATH TO ZARAP	9/2016	3/2020 (-) [1/2023]	1,338.13 (2,617.44) [1,338.13]	1,346.39 (0.00) [0]
859	KANTE TO WAKED	3/2016	11/2019 (-) [12/2023]	1,230.02 (1,230.00) [1,230.02]	791.80 (0.00) [49]
860	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2023]	407.19 (407.00) [407.19]	323.02 (0.00) [0]
861	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2023]	537.81 (538.00) [537.81]	245.41 (0.00) [0]
862	KARAD TO VITA	1/2018	12/2019 (-) [10/2023]	344.85 (245.00) [344.85]	281.41 (0.00) [46]
863	KARWANDI TO RAJURI	3/2018	12/2019 (-) [11/2023]	276.95 (277.00) [276.95]	160.17 (0.00) [47]
864	KATOL TO WARUD	1/2017	6/2019 (-) [3/2023]	463.62 (664.00) [463.62]	265.78 (0.00) [0]
865	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [1/2023]	249.29 (-) [249.29]	146.41 (0.00) [0]
866	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [9/2019]	203.21 (203.00) [203.21]	163.81 (0.00) [0]
867	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	1/2022 (5/2023) [8/2023]	594.75 (594.75) [613.75]	532.55 (19.00) [19]
868	KOLDE TO KHETIYA	1/2017	7/2019 (-) [3/2023]	509.18 (-) [509.18]	283.13 (0.00) [0]

869	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [12/2023]	281.78 (282.00) [281.78]	77.83 (0.00) [56]
870	KOTHARI TO DHANORA	9/2018	8/2020 (-) [9/2023]	301.38 (301.00) [301.38]	240.32 (0.00) [37]
871	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [12/2023]	406.51 (-) [406.51]	340.26 (0.00) [54]
872	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [9/2023]	307.63 (-) [307.63]	232.57 (0.00) [50]
873	LATUR TO PANGAON	3/2018	12/2019 (-) [8/2023]	336.47 (336.00) [336.47]	203.39 (0.00) [44]
874	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [12/2023]	237.40 (-) [237.40]	73.12 (0.00) [43]
875	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [8/2023]	256.15 (-) [256.15]	126.62 (0.00) [44]
876	MALEGAON TO RISOD	2/2018	12/2019 (-) [3/2023]	303.24 (303.00) [303.24]	199.08 (0.00) [0]
877	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [9/2023]	322.55 (-) [322.55]	242.09 (0.00) [51]
878	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [2/2023]	457.52 (-) [457.52]	426.61 (0.00) [0]
879	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [1/2023]	418.36 (-) [418.36]	263.13 (0.00) [0]
880	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [3/2023]	486.19 (-) [486.19]	315.19 (0.00) [0]
881	MEDSHI (KM 47.700) TO WASHIM (KM 92.200) OF NH-161 IN MAHARASHTRA	2/2018	10/2021 (5/2023) [5/2023]	1,061.29 (1,061.29) [683.10]	685.97 (-378.19) [0]
882	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [8/2023]	232.77 (-) [232.77]	151.60 (0.00) [49]
883	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [12/2023]	488.60 (-) [488.60]	279.42 (0.00) [53]
884	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	1/2022 (5/2023) [8/2023]	731.89 (731.99) [731.99]	626.45 (0.10) [19]
885	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2023]	341.16 (341.00) [341.16]	247.86 (0.00) [54]
886	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [2/2023]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
887	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [1/2023]	162.34 (-) [162.34]	107.56 (0.00) [0]
888	NAGAJ TO VAJJAPUR	1/2017	6/2019 (-) [1/2023]	376.72 (377.00) [376.72]	273.87 (0.00) [0]
889	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (7/2023) [12/2023]	546.00 (-) [546.00]	450.68 (0.00) [53]

890	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (3/2024) [3/2024]	591.66 (-) [591.66]	429.66 (0.00) [56]
891	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [1/2023]	244.04 (244.00) [244.04]	177.94 (0.00) [0]
892	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2023]	274.50 (275.00) [274.50]	143.39 (0.00) [48]
893	NANDED TO JALKOT	12/2017	9/2019 (-) [3/2023]	456.93 (457.00) [456.93]	278.22 (0.00) [0]
894	NANDGAON TO MORSHI	1/2017	6/2019 (-) [3/2023]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
895	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [12/2023]	406.54 (407.00) [406.54]	274.30 (0.00) [51]
896	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [6/2023]	420.63 (421.00) [420.63]	219.40 (0.00) [0]
897	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [12/2023]	344.25 (344.00) [344.25]	188.48 (0.00) [40]
898	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [3/2024]	341.80 (-) [341.80]	203.09 (0.00) [57]
899	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [9/2023]	227.19 (227.00) [227.19]	141.92 (0.00) [45]
900	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [12/2023]	381.08 (302.00) [381.08]	45.66 (0.00) [43]
901	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [9/2023]	218.38 (-) [218.38]	182.63 (0.00) [50]
902	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [8/2023]	238.19 (238.00) [238.19]	194.54 (0.00) [44]
903	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [8/2023]	205.72 (206.00) [205.72]	85.71 (0.00) [50]
904	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [6/2023]	983.14 (2,226.11) [983.14]	1,108.30 (0.00) [0]
905	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [2/2023]	420.57 (-) [420.57]	270.28 (0.00) [0]
906	PATAS-VASUNDE PHATA - BARAMATI BYPASS	9/2021	9/2023 (9/2023) [9/2023]	531.86 (532.41) [532.41]	489.85 (0.55) [0]
907	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [3/2023]	170.00 (-) [170.00]	125.80 (0.00) [0]
908	PEN TO KHOPOLI	3/2018	3/2018 (-) [1/2024]	301.39 (302.00) [301.39]	170.12 (0.00) [70]
909	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [1/2023]	595.77 (-) [595.77]	357.73 (0.00) [0]
910	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [8/2022]	223.46 (-) [223.46]	123.46 (0.00) [0]

911	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [8/2023]	228.31 (-) [228.31]	100.97 (0.00) [44]
912	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [8/2023]	210.81 (-) [210.81]	210.81 (0.00) [49]
913	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [6/2023]	225.81 (-) [225.81]	167.96 (0.00) [0]
914	REPANPALLI TO SIRONCHA	3/2022	6/2022 (-) [6/2024]	282.07 (-) [282.07]	34.65 (0.00) [24]
915	RISOD TO HINGOLI	2/2018	12/2019 (-) [1/2023]	355.99 (-) [355.99]	247.60 (0.00) [0]
916	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [9/2023]	362.96 (-) [362.96]	273.57 (0.00) [51]
917	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [1/2023]	415.25 (415.25) [415.25]	274.02 (0.00) [0]
918	SANGOLA TO JATH	1/2018	12/2019 (-) [2/2023]	257.38 (257.00) [257.38]	166.31 (0.00) [0]
919	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [2/2023]	250.46 (-) [250.46]	198.32 (0.00) [0]
920	SARSAM TO KOTHARI	2/2016	7/2019 (-) [9/2022]	545.64 (-) [545.64]	232.64 (0.00) [0]
921	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [6/2024]	388.44 (-) [388.44]	240.05 (0.00) [-]
922	SATARA TO MHASWAD	1/2017	7/2019 (-) [6/2023]	653.46 (-) [653.46]	369.62 (0.00) [0]
923	SELDOH TO PANVAR	7/2018	5/2020 (-) [3/2024]	404.33 (404.00) [404.33]	140.65 (0.00) [46]
924	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [3/2023]	150.79 (-) [150.79]	81.14 (0.00) [0]
925	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [1/2023]	373.10 (373.00) [373.10]	320.45 (0.00) [0]
926	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [8/2023]	211.34 (-) [211.34]	136.33 (0.00) [49]
927	SHIRUR TO KHARDA	2/2017	6/2019 (-) [3/2024]	381.77 (-) [381.77]	199.48 (0.00) [57]
928	SHIVUR TO YEOLA	3/2018	12/2019 (-) [3/2022]	181.08 (-) [181.08]	97.86 (0.00) [0]
929	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [10/2023]	337.46 (-) [337.46]	335.30 (0.00) [52]
930	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [2/2023]	264.41 (264.00) [264.41]	200.42 (0.00) [0]
931	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [2/2023]	422.02 (422.00) [422.02]	302.13 (0.00) [0]

932	TUNNEL AT KHAMBATKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0	2/2019	2/2022 (3/2023) [12/2023]	493.00 (-) [493.00]	374.15 (0.00) [22]
933	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH	11/2021	2/2022 (-) [12/2023]	223.35 (-) [223.35]	114.32 (0.00) [22]
934	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI)	5/2022	5/2024 (-) [5/2024]	1,260.00 (-) [1,260.00]	295.36 (0.00) [0]
935	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD)	3/2022	3/2024 (-) [3/2024]	1,549.02 (-) [1,549.02]	290.04 (0.00) [0]
936	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN)	2/2022	2/2024 (-) [2/2024]	2,747.00 (-) [2,747.00]	544.65 (0.00) [0]
937	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI)	11/2022	5/2024 (-) [5/2024]	1,124.00 (-) [1,124.00]	116.71 (0.00) [0]
938	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE)	11/2022	10/2024 (5/2024) [5/2024]	990.00 (-) [990.00]	153.78 (0.00) [-5]
939	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ)	11/2022	10/2024 (-) [10/2024]	1,450.00 (-) [1,450.00]	153.30 (0.00) [0]
940	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE)	9/2021	7/2025 (-) [7/2025]	2,208.68 (-) [2,208.68]	56.93 (0.00) [0]
941	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [2/2023]	1,598.47 (1,560.00) [1,598.47]	1,277.25 (0.00) [0]
942	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2023]	304.58 (305.00) [304.58]	150.26 (0.00) [48]
943	WADI TO ASOLA	1/2017	9/2019 (-) [8/2023]	363.82 (364.00) [363.82]	154.65 (0.00) [47]
944	WADIGODRI TO DHANGRIIMPRI	3/2018	2/2020 (-) [9/2023]	194.23 (194.00) [194.23]	136.55 (0.00) [43]
945	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [10/2023]	376.19 (-) [376.19]	113.66 (0.00) [53]
946	WAKED TO TALEGAON	2/2016	2/2019 (-) [2/2023]	1,244.75 (1,245.00) [1,244.75]	1,025.72 (0.00) [0]
947	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	1/2022 (6/2023) [6/2023]	362.46 (372.46) [372.46]	346.15 (10.00) [0]
948	WARDHA TO ARVI	2/2018	4/2020 (-) [8/2023]	313.58 (-) [313.58]	230.41 (0.00) [40]
949	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [8/2023]	216.90 (217.00) [216.90]	164.00 (0.00) [44]
Urban Development					
950	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	3/2020 (-) [12/2023]	23,136.00 (-) [37,276.00]	24,123.86 (14,140.00) [45]
951	NAGPUR METRO RAIL PROJECT PHASE II	12/2022	12/2027 (-) [12/2027]	6,708.00 (-) [6,708.00]	0.00 (0.00) [0]
952	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (12/2023)	11,420.00 (13,656.22)	10,829.00 (2,236.22)

			[12/2023]	[13,656.22]	[25]
	<u>Water Resources</u>				
953	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (9/2023) [12/2023]	233.57 (-) [233.57]	209.79 (0.00) [48]
	<u>MANIPUR</u>				
	<u>Civil Aviation</u>				
954	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX	11/2021	7/2024 (12/2024) [12/2024]	499.00 (-) [499.00]	83.88 (0.00) [5]
	<u>Railways</u>				
955	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (3/2025) [3/2025]	4,454.17 (12,264.15) [14,322.79]	13,763.33 (9,868.62) [168]
	<u>Road Transport And Highways</u>				
956	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [5/2023]	167.95 (-) [167.95]	84.16 (0.00) [0]
957	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [5/2023]	292.24 (-) [292.24]	127.86 (0.00) [0]
958	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [5/2023]	365.53 (-) [365.53]	142.51 (0.00) [0]
959	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [5/2023]	167.95 (204.12) [167.95]	77.72 (0.00) [0]
960	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [5/2023]	177.76 (-) [177.76]	70.23 (0.00) [0]
961	AKASH BRIDGE - JESSAMI SECTION PKG-2	3/2022	2/2025 (-) [2/2025]	152.11 (-) [152.11]	0.00 (0.00) [0]
962	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [8/2023]	673.27 (-) [673.27]	281.57 (0.00) [-2]
963	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM	9/2021	2/2024 (-) [2/2024]	310.76 (-) [310.76]	66.01 (0.00) [0]
964	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [11/2023]	195.14 (-) [195.14]	34.94 (0.00) [11]
965	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [9/2023]	467.00 (-) [467.00]	139.15 (0.00) [6]
966	IMPHAL - KHONGSANG PKG-4	8/2021	12/2023 (-) [12/2023]	579.63 (-) [579.63]	53.90 (0.00) [0]
967	IMPHAL - KHONGSANG PKG-5	12/2021	5/2024 (-) [5/2024]	410.68 (-) [410.68]	40.52 (0.00) [0]
968	IMPHAL - KHONGSANG PKG-6	12/2021	2/2025 (-) [2/2025]	504.76 (-) [504.76]	16.43 (0.00) [0]
969	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [5/2023]	277.99 (-) [277.99]	123.86 (0.00) [0]
970	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [8/2023]	259.31 (-) [259.31]	136.05 (0.00) [8]
971	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAPOKPI	8/2020	4/2022 (-)	268.98 (-)	22.08 (0.00)

	SECTIO		[4/2022]	[268.98]	[0]
972	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
973	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [8/2023]	379.39 (-) [379.39]	186.51 (0.00) [16]
974	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [3/2023]	471.00 (-) [471.00]	319.81 (0.00) [0]
975	MARAM - PEREN PKG-3	8/2021	5/2023 (-) [11/2023]	467.41 (-) [467.41]	126.80 (0.00) [6]
976	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [10/2023]	188.36 (-) [188.36]	81.38 (0.00) [10]
977	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	126.78 (0.00) [0]
978	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [10/2023]	226.32 (-) [226.32]	47.15 (0.00) [10]
979	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [8/2023]	232.26 (-) [232.26]	147.43 (0.00) [8]
980	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [5/2024]	211.70 (-) [211.70]	1.64 (0.00) [16]
981	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	52.65 (0.00) [0]
982	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	197.54 (0.00) [0]
983	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [4/2023]	234.08 (-) [234.08]	111.25 (0.00) [0]
984	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [4/2023]	198.77 (-) [198.77]	53.84 (0.00) [0]
985	TAMENGLONG - MAHUR PKG-5	8/2021	5/2023 (-) [5/2023]	477.86 (-) [477.86]	68.12 (0.00) [0]
986	TAMENGLONG - MAHUR PKG-6	9/2021	5/2023 (-) [5/2023]	311.18 (-) [311.18]	121.73 (0.00) [0]
	MEGHALAYA				
	Department Of Higher Education				
987	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (12/2023) [12/2023]	484.32 (429.70) [429.70]	262.25 (-54.62) [111]
	Doner				
988	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [9/2017]	151.33 (-) [151.33]	148.33 (0.00) [0]
	Railways				
989	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [8,324.28]	269.80 (7,417.82) [0]
	Road Transport And Highways				
990	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-	11/2020	12/2023 (-)	351.12 (-)	181.82 (0.00)

	LANING FROM (		[12/2023]	[351.12]	[0]
991	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	3/2022 (-) [10/2023]	306.28 (-) [306.28]	196.84 (0.00) [19]
992	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	45.46 (0.00) [0]
993	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [9/2023]	525.68 (-) [525.68]	357.03 (0.00) [-3]
994	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [7/2023]	445.51 (-) [445.51]	191.35 (0.00) [-5]
995	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2	11/2021	6/2024 (-) [6/2024]	283.50 (261.40) [283.50]	96.86 (0.00) [0]
996	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [11/2023]	260.21 (-) [260.21]	149.15 (0.00) [11]
997	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [1/2024]	157.86 (-) [157.86]	102.41 (0.00) [21]
998	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06	8/2020	2/2022 (1/2024) [1/2024]	302.88 (-) [302.88]	91.62 (0.00) [23]
999	REHABILITATION AND UP GRADATION OF NONGSTOIN- RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM	9/2021	5/2024 (-) [5/2024]	359.86 (-) [359.86]	169.42 (0.00) [0]
1000	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	9/2021 (9/2021) [7/2023]	553.51 (610.09) [553.51]	290.35 (0.00) [22]
	<u>MIZORAM</u>				
	<u>Railways</u>				
1001	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [2/2024]	2,393.47 (5,021.45) [9,362.06]	6,591.01 (6,968.59) [119]
	<u>Road Transport And Highways</u>				
1002	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (6/2023) [6/2023]	195.04 (434.65) [377.99]	415.11 (182.95) [0]
1003	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (6/2023) [6/2023]	186.96 (-) [322.24]	312.50 (135.28) [0]
1004	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2023) [6/2023]	193.69 (374.59) [327.92]	364.32 (134.23) [0]
1005	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (7/2023) [10/2023]	275.02 (-) [275.02]	166.23 (0.00) [12]
1006	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (8/2023) [12/2023]	206.88 (219.33) [278.98]	227.33 (72.10) [17]
1007	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (8/2023) [12/2023]	292.24 (331.17) [331.17]	235.26 (38.93) [17]
1008	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (7/2023) [10/2023]	281.78 (253.41) [253.41]	228.20 (-28.37) [15]
1009	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (11/2023) [11/2023]	374.39 (374.39) [374.39]	267.81 (0.00) [11]
1010	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022	233.25	153.10

			(7/2023) [1/2024]	(233.25) [233.25]	(0.00) [13]
1011	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (1/2024) [1/2024]	674.71 (674.71) [674.71]	521.28 (0.00) [7]
1012	KEIFANG - TUVAI PKG-1	9/2021	5/2023 (2/2024) [4/2024]	492.94 (492.94) [492.94]	230.26 (0.00) [11]
1013	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (10/2023) [12/2024]	698.44 (698.45) [698.45]	227.20 (0.01) [24]
1014	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (11/2023) [12/2024]	740.58 (740.58) [740.58]	104.66 (0.00) [23]
1015	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2023 (1/2024) [1/2024]	519.09 (775.47) [775.47]	532.37 (256.38) [9]
1016	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2023 (11/2023) [1/2024]	473.18 (667.06) [667.06]	465.49 (193.88) [9]
1017	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	7/2023 (2/2024) [2/2024]	640.07 (1,134.72) [640.07]	965.74 (0.00) [7]
1018	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	6/2023 (12/2023) [1/2024]	642.96 (1,139.85) [1,139.85]	528.71 (496.89) [7]
1019	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2023 (10/2023) [1/2024]	537.82 (820.42) [820.42]	619.87 (282.60) [9]
1020	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	4/2024 (7/2024) [7/2024]	404.29 (723.80) [723.80]	452.54 (319.51) [3]
1021	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2023 (5/2024) [5/2024]	428.11 (777.50) [777.50]	437.46 (349.39) [8]
1022	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	6/2023 (2/2024) [2/2024]	518.53 (902.20) [902.20]	623.42 (383.67) [8]
1023	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (6/2023) [6/2023]	624.41 (1,109.88) [992.67]	1,021.46 (368.26) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
1024	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2025]	836.42 (-) [836.42]	361.69 (0.00) [12]
1025	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (3/2025) [3/2025]	328.00 (-) [328.00]	310.44 (0.00) [48]
1026	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (3/2025) [3/2025]	319.76 (319.76) [319.76]	275.11 (0.00) [36]
	<u>Dpiit</u>				
1027	NATIONAL INDUSTRIAL CORRIDOR PROJECT	9/2011	3/2027 (3/2027) [3/2027]	20,084.00 (20,084.00) [20,084.00]	9,682.86 (0.00) [0]
	<u>Petroleum</u>				
1028	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (10/2023) [10/2023]	3,308.00 (3,992.00) [3,992.00]	3,537.30 (684.00) [22]
1029	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	12/2029 (3/2030)	169.00 (-)	64.99 (0.00)

			[3/2030]	[169.00]	[3]
1030	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	186.74 (0.00) [0]
1031	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (6/2024) [6/2024]	1,030.65 (-) [1,030.65]	625.20 (0.00) [19]
1032	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (11/2024) [11/2024]	2,915.00 (5,909.00) [5,909.00]	3,510.30 (2,994.00) [143]
1033	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (10/2024) [10/2024]	7,844.25 (-) [7,844.25]	4,595.80 (0.00) [17]
1034	NORTH EAST GAS GRID	11/2020	3/2024 (-) [3/2024]	9,265.00 (9,265.00) [9,265.00]	4,481.56 (0.00) [0]
1035	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (9/2024) [9/2024]	2,658.34 (-) [2,658.34]	1,553.40 (0.00) [26]
	<u>Power</u>				
1036	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION.	3/2022	3/2023 (-) [10/2023]	176.22 (-) [176.22]	39.82 (0.00) [7]
1037	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2024]	4,754.42 (-) [9,129.32]	5,600.77 (4,374.90) [72]
1038	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [8/2023]	235.53 (-) [243.74]	168.69 (8.21) [50]
1039	ER WR TRANSMISSION LIMITED	3/2023	3/2025 (-) [3/2025]	281.16 (-) [281.16]	0.00 (0.00) [0]
1040	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [9/2023]	197.40 (-) [197.40]	159.47 (0.00) [66]
1041	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [3/2024]	1,931.39 (-) [2,635.55]	1,952.75 (704.16) [49]
1042	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [1/2024]	5,111.33 (-) [6,700.00]	4,578.01 (1,588.67) [61]
1043	NORTH EASTERN REGION STRENGTHENING SCHEME - III	9/2015	12/2017 (-) [9/2023]	167.31 (-) [167.31]	129.77 (0.00) [69]
1044	NORTH EASTERN REGION STRENGTHENING SCHEME-XII	5/2021	3/2023 (-) [2/2024]	576.42 (-) [576.42]	366.29 (0.00) [11]
1045	POWERGRID NEEMUCH TRANSMISSION SYSTEM LIMITED	8/2022	2/2024 (-) [2/2024]	863.99 (-) [863.99]	118.49 (0.00) [0]
1046	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	11/2018	11/2021 (-) [9/2023]	241.38 (-) [241.38]	236.89 (0.00) [22]
1047	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION	11/2018	11/2021 (-) [6/2023]	173.94 (-) [173.94]	125.05 (0.00) [0]
1048	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION	10/2022	10/2025 (-) [10/2025]	307.87 (-) [307.87]	7.34 (0.00) [0]
1049	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B	7/2022	6/2023 (-) [6/2024]	4,546.26 (-) [4,546.26]	633.23 (0.00) [12]

1050	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C	7/2022	3/2025 (-) [3/2025]	186.19 (-) [186.19]	16.84 (0.00) [0]
1051	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B	3/2023	11/2024 (-) [11/2024]	3,546.94 (-) [3,546.94]	51.87 (0.00) [0]
1052	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM	3/2022	12/2024 (-) [12/2024]	288.71 (-) [288.71]	0.00 (0.00) [0]
1053	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	2/2022	9/2023 (-) [3/2024]	359.47 (-) [359.47]	54.26 (0.00) [6]
1054	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2022	11/2023 (-) [3/2024]	1,666.00 (-) [1,666.00]	511.39 (0.00) [4]
1055	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM	2/2022	4/2025 (-) [4/2025]	318.12 (-) [318.12]	102.00 (0.00) [0]
	<u>Railways</u>				
1056	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [8/2027]	1,08,000.00 (-) [1,08,000.00]	46,912.58 (0.00) [44]
1057	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [923.23]	2.46 (0.00) [0]
1058	CHANDIGARH-BADDI	4/2007	3/2023 (6/2025) [6/2025]	328.14 (1,540.14) [1,540.14]	482.67 (1,212.00) [27]
1059	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2024]	295.00 (-) [830.00]	853.32 (535.00) [61]
1060	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (12/2026) [12/2026]	1,347.26 (1,793.63) [1,793.63]	1,222.16 (446.37) [57]
1061	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2026) [12/2025]	1,640.04 (1,873.10) [1,873.10]	1,136.95 (233.06) [45]
1062	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [12/2022]	365.17 (-) [335.50]	794.67 (-29.67) [0]
1063	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [9/2023]	336.91 (-) [791.39]	572.99 (454.48) [-]
1064	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (5/2025) [12/2027]	2,030.50 (-) [746.83]	22.07 (-1,283.67) [-]
1065	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [51,219.00]	31,304.00 (39,630.00) [0]
1066	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	1,024.32 (932.64) [33]
1067	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [12/2024]	1,614.59 (-) [1,960.00]	1,887.40 (345.41) [69]
1068	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [1/2025]	2,063.03 (2,909.00) [2,909.00]	2,355.36 (845.97) [46]
1069	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2025]	1,856.95 (-) [1,952.68]	1,533.64 (95.73) [24]
1070	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-)	247.66 (-)	2,427.33 (8,000.84)

			[3/2025]	[8,248.50]	[202]
1071	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (12/2027) [12/2027]	120.70 (-) [2,053.39]	328.43 (1,932.69) [105]
1072	MONIGRAM- NIMTITA	4/2012	/ (-) [11/2023]	250.93 (-) [310.70]	753.91 (59.77) [-]
1073	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2000]	1,723.00 (1.00) [3,381.68]	2,532.11 (1,658.68) [0]
1074	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [10/2024]	414.84 (-) [1,187.49]	349.63 (772.65) [55]
1075	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [11/2024]	450.00 (-) [2,017.96]	845.23 (1,567.96) [148]
1076	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	3/2019	5/2023 (-) [2/2025]	1,866.31 (-) [1,866.31]	1,148.32 (0.00) [21]
1077	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [12/2024]	242.22 (-) [632.63]	172.50 (390.41) [57]
1078	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2023]	241.52 (-) [401.65]	343.30 (160.13) [0]
1079	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [1/2024]	1,798.00 (-) [2,647.51]	1,999.72 (849.51) [58]
1080	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [2/2024]	600.00 (-) [701.81]	585.21 (101.81) [47]
1081	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	980.46 (1,221.83) [36]
1082	RAYADURGA-TUMKUR NL	4/2007	/ (-) [12/2025]	2,062.30 (2,404.03) [2,404.03]	1,161.58 (341.73) [-]
1083	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	47,476.00 (34,509.00) [0]
	<u>Road Transport And Highways</u>				
1084	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000	11/2021	2/2025 (-) [2/2025]	2,155.95 (-) [2,155.95]	793.18 (0.00) [0]
1085	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O	4/2022	11/2024 (-) [11/2024]	796.65 (-) [796.65]	26.55 (0.00) [0]
1086	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [6/2024]	2,848.00 (-) [3,379.45]	3,656.21 (531.45) [123]
	<u>Shipping And Ports</u>				
1087	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [12/2026]	5,369.18 (4,633.10) [5,362.27]	2,498.52 (-6.91) [45]
	<u>Telecommunications</u>				
1088	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT	5/2023	8/2024 (-) [8/2024]	645.13 (-) [645.13]	0.00 (0.00) [0]
1089	NETWORK FOR SPECTRUM	3/2012	7/2015 (12/2022) [9/2023]	13,334.00 (-) [13,334.00]	21,913.00 (0.00) [98]
1090	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA	3/2020	6/2021	461.42	134.92

	CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART		(11/2021) [12/2023]	(461.42) [461.42]	(0.00) [30]
1091	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (PMPLS) NETWORK and	3/2023	3/2024 (-) [3/2024]	185.27 (-) [185.27]	0.00 (0.00) [0]
	<u>Urban Development</u>				
1092	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	16,368.35 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1093	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	2,556.74 (4,336.48) [132]
	<u>Road Transport And Highways</u>				
1094	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2022 (1/2023) [8/2023]	285.68 (-) [285.68]	155.93 (0.00) [11]
1095	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2020 (8/2022) [9/2023]	387.00 (-) [387.00]	384.58 (0.00) [36]
1096	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	11/2022 (6/2023) [12/2023]	500.09 (583.31) [500.09]	299.49 (0.00) [13]
1097	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (3/2023) [8/2023]	320.97 (-) [320.97]	168.47 (0.00) [14]
1098	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (2/2023) [12/2023]	355.79 (-) [355.79]	109.24 (0.00) [18]
1099	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (6/2023) [12/2023]	361.53 (-) [361.53]	112.55 (0.00) [18]
1100	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (3/2023) [3/2023]	330.78 (-) [330.78]	199.02 (0.00) [0]
1101	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (12/2022) [3/2024]	330.80 (-) [330.80]	83.11 (0.00) [27]
1102	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (10/2022) [6/2023]	278.95 (-) [278.95]	161.69 (0.00) [0]
1103	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (9/2022) [0/0]	206.53 (-) [206.53]	98.69 (0.00) [0]
1104	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J	3/2022	12/2024 (-) [12/2024]	605.36 (-) [605.36]	82.51 (0.00) [0]
1105	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (2/2023) [2/2023]	217.35 (-) [217.35]	197.79 (0.00) [0]
1106	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (2/2023) [7/2023]	257.15 (-) [257.15]	124.52 (0.00) [15]
1107	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [3/2024]	202.36 (-) [202.36]	62.66 (0.00) [23]
1108	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [7/2024]	277.44 (-) [277.44]	134.18 (0.00) [21]
1109	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM	3/2018	12/2021 (3/2023)	315.03 (-)	212.85 (0.00)

	79.040 TO		[3/2023]	[315.03]	[0]
1110	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	12/2021 (3/2023) [4/2023]	240.64 (255.58) [240.64]	172.36 (0.00) [0]
1111	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	12/2021 (8/2022) [12/2023]	215.79 (-) [215.79]	97.45 (0.00) [24]
1112	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	10/2022 (10/2022) [10/2023]	272.89 (-) [272.89]	145.48 (0.00) [12]
1113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (6/2023) [3/2024]	323.98 (-) [323.98]	70.01 (0.00) [66]
1114	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	9/2019 (9/2019) [9/2023]	373.07 (489.01) [387.00]	377.90 (13.93) [48]
1115	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2019 (8/2019) [9/2023]	396.52 (519.72) [396.52]	330.51 (0.00) [49]
1116	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2022 (8/2022) [1/2023]	429.52 (562.98) [429.52]	267.69 (0.00) [0]
1117	MERANGKONG-TAMLU-MON (MTM) PKG-5	7/2021	12/2023 (-) [3/2024]	161.73 (-) [161.73]	32.41 (0.00) [3]
1118	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [0/0]	207.33 (-) [207.33]	0.00 (0.00) [0]
1119	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (2/2023) [6/2023]	258.52 (-) [258.52]	57.58 (0.00) [0]
1120	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [8/2023]	315.63 (-) [315.63]	42.64 (0.00) [16]
1121	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I	6/2020	9/2024 (9/2024) [9/2024]	252.19 (-) [252.19]	0.28 (0.00) [0]
1122	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (5/2023) [5/2023]	237.51 (-) [237.51]	200.01 (0.00) [0]
1123	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N	3/2021	7/2024 (7/2024) [7/2024]	297.24 (-) [297.24]	44.41 (0.00) [0]
1124	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO	3/2021	2/2024 (2/2024) [2/2024]	226.44 (-) [226.44]	50.91 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1125	ANANTA OCP EXPANSION PH III	8/2008	3/2012 (3/2022) [3/2022]	228.08 (-) [398.14]	398.14 (170.06) [0]
1126	BALARAM EXPANSION OCP	8/2020	3/2029 (-) [3/2029]	3,504.21 (-) [3,504.21]	656.64 (0.00) [0]
1127	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2026]	479.15 (-) [479.15]	259.49 (0.00) [84]
1128	BHUBANESWARI EXPANSION OCP	8/2020	3/2031 (-) [3/2031]	3,145.45 (-) [3,145.45]	941.66 (0.00) [0]
1129	GARJANBAHAL OCP	11/2014	3/2021 (-)	1,375.38 (-)	779.83 (0.00)

			[3/2026]	[1,375.38]	[60]
1130	GOPALJI-KANIHA OCP	8/2020	3/2028 (-) [3/2028]	8,416.19 (-) [8,416.19]	1,399.84 (0.00) [0]
1131	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	1,438.58 (0.00) [0]
1132	KULDA EXPANSION OCP- 15 MTY	6/2014	3/2018 (-) [3/2026]	348.16 (-) [348.16]	186.02 (0.00) [96]
1133	NAINI COAL MINE	3/2020	3/2024 (-) [3/2025]	494.30 (-) [494.30]	397.67 (0.00) [12]
1134	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,432.59 (0.00) [0]
1135	RPR OF HINGULA -II EXPANSION PH-III	12/2022	3/2029 (-) [3/2029]	2,264.68 (-) [2,264.68]	934.65 (0.00) [0]
1136	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	3,339.10 (0.00) [0]
1137	SUBHADRA OCP	5/2021	3/2027 (3/2029) [3/2029]	1,693.81 (-) [1,693.81]	904.20 (0.00) [24]
1138	TALABIRA II AND III OCP	7/2017	1/2027 (-) [1/2027]	2,401.07 (-) [2,401.07]	1,051.59 (0.00) [0]
	<u>Department Of Higher Education</u>				
1139	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [3/2024]	790.79 (-) [790.79]	502.79 (0.00) [24]
	<u>Mines</u>				
1140	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [3/2025]	4,103.00 (5,055.00) [5,055.00]	2,259.22 (952.00) [47]
1141	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (9/2025) [9/2025]	355.00 (581.00) [581.00]	79.69 (226.00) [58]
1142	POTTANGI BAUXITE MINES	5/2018	12/2024 (3/2025) [5/2025]	1,437.00 (1,381.00) [1,381.00]	603.12 (-56.00) [5]
1143	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (5/2024) [5/2024]	483.00 (483.00) [483.00]	197.42 (0.00) [37]
1144	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (11/2023) [11/2023]	534.00 (667.23) [667.23]	605.95 (133.23) [46]
	<u>Petroleum</u>				
1145	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (7/2023) [4/2024]	462.30 (543.00) [543.00]	393.54 (80.70) [31]
1146	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [12/2023]	243.53 (-) [243.53]	223.48 (0.00) [17]
1147	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [12/2023]	182.20 (-) [182.20]	137.31 (0.00) [17]
1148	CITY GAS DISTRIBUTION NETWORK PROJECT AT ANGUL AND DHENKANAL	4/2019	3/2030 (-) [3/2030]	605.65 (-) [605.65]	158.42 (0.00) [0]
1149	CITY GAS DISTRIBUTION NETWORK PROJECT AT	4/2019	3/2030	599.19	157.48

	BARGARH, DEBGARH AND SAMBALPUR		(-) [3/2030]	(-) [599.19]	(0.00) [0]
1150	CITY GAS DISTRIBUTION NETWORK PROJECT AT JAGATSINGHPUR AND KENDRAPARA	4/2019	3/2030 (-) [3/2030]	485.91 (-) [485.91]	121.66 (0.00) [0]
1151	CITY GAS DISTRIBUTION NETWORK PROJECT AT JAJPUR AND KENDUJHAR	4/2019	3/2030 (-) [3/2030]	741.29 (-) [741.29]	209.95 (0.00) [0]
1152	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (3/2024) [3/2024]	3,361.00 (-) [3,361.00]	2,497.03 (0.00) [31]
1153	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [8/2023]	202.16 (-) [202.16]	135.57 (0.00) [13]
1154	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2024) [3/2024]	371.00 (427.10) [427.10]	204.58 (56.10) [18]
1155	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [7/2025]	13,805.00 (-) [13,805.00]	3,776.82 (0.00) [18]
1156	LPG BP PROJECT KHORDHA	12/2016	12/2019 (1/2023) [9/2023]	161.59 (161.59) [161.59]	135.83 (0.00) [45]
1157	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (4/2023) [7/2023]	1,297.50 (-) [1,297.50]	1,119.42 (0.00) [21]
1158	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha	8/2019	8/2022 (6/2023) [10/2024]	1,607.00 (-) [1,607.00]	867.50 (0.00) [26]
	<u>Power</u>				
1159	EASTERN REGION EXPANSION SCHEME XXIX	3/2023	11/2025 (-) [11/2025]	524.04 (-) [524.04]	15.25 (0.00) [0]
1160	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW)	8/2022	5/2027 (-) [5/2027]	11,844.00 (-) [11,844.00]	635.90 (0.00) [0]
	<u>Railways</u>				
1161	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (10/2023) [5/2023]	942.95 (-) [1,552.26]	1,772.12 (609.31) [0]
1162	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2024]	843.04 (1,284.39) [843.04]	723.04 (0.00) [41]
1163	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [2/2025]	1,172.92 (-) [1,172.92]	1,052.09 (0.00) [74]
1164	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [12/2025]	5,200.00 (-) [5,200.00]	0.00 (0.00) [69]
1165	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2024]	1,547.38 (-) [1,547.38]	790.93 (0.00) [24]
1166	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2025]	701.61 (-) [810.02]	179.43 (108.41) [76]
1167	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [7/2023]	133.41 (207.00) [433.00]	518.32 (299.59) [172]
1168	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [12/2026]	2,923.13 (3,791.66) [3,791.66]	2,904.31 (868.53) [213]
1169	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022	2,361.74	967.78

			(3/2026) [3/2026]	(2,361.74) [2,361.74]	(0.00) [48]
1170	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (2/2023) [2/2023]	1,111.99 (1,539.28) [1,539.28]	1,152.38 (427.29) [0]
1171	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2025]	810.78 (-) [1,928.07]	980.13 (1,117.29) [45]
1172	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	3,674.36 (992.05) [24]
	Road Transport And Highways				
1173	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD	12/2021	9/2024 (-) [9/2024]	714.00 (714.00) [714.00]	0.00 (0.00) [0]
1174	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8	12/2021	10/2024 (-) [10/2024]	1,592.00 (1,592.00) [1,592.00]	0.00 (0.00) [0]
1175	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE –	8/2021	6/2024 (-) [6/2024]	1,460.00 (1,460.00) [1,460.00]	0.00 (0.00) [0]
1176	6L GREENFIELD KALIAGURA – BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG	9/2021	5/2024 (-) [5/2024]	1,734.00 (1,734.00) [1,734.00]	6.94 (0.00) [0]
1177	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE – OD-3)	3/2021	4/2024 (-) [4/2024]	1,249.00 (-) [1,249.00]	0.00 (0.00) [0]
1178	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE – OD-1)	2/2021	3/2024 (-) [3/2024]	586.00 (-) [586.00]	0.00 (0.00) [0]
1179	6L OF HATIBENA - BADAKUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE – OD-2)	2/2021	3/2024 (-) [3/2024]	925.00 (-) [925.00]	0.00 (0.00) [0]
1180	6L OF KARKI – KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE – OD-4)	2/2021	3/2024 (-) [3/2024]	593.00 (-) [593.00]	0.00 (0.00) [0]
1181	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000	8/2020	3/2022 (-) [8/2023]	200.00 (154.73) [154.73]	137.04 (-45.27) [17]
1182	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [12/2023]	2,510.04 (-) [2,510.04]	783.15 (0.00) [52]
1183	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	11/2020 (6/2021) [5/2023]	476.56 (780.37) [780.37]	311.77 (303.81) [0]
1184	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	8/2022 (-) [3/2024]	633.68 (492.83) [633.68]	560.38 (0.00) [19]
1185	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	5/2020 (-) [5/2023]	953.09 (1,014.08) [1,014.08]	731.39 (60.99) [0]
1186	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	8/2021 (-) [10/2023]	614.48 (503.30) [757.12]	641.00 (142.64) [26]
1187	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	6/2021 (6/2022) [12/2023]	503.88 (609.03) [609.03]	221.76 (105.15) [30]
1188	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	7/2020 (-) [12/2023]	686.65 (565.00) [686.65]	461.14 (0.00) [41]
1189	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	9/2020 (-) [12/2023]	686.65 (504.09) [1,015.16]	355.84 (328.51) [39]

1190	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	9/2021 (-) [6/2023]	999.00 (1,152.70) [1,152.70]	339.23 (153.70) [0]
1191	SIX / FOUR LANING OF NH 5 (NEW NH 16) FROM PUINTOLA TO TANGI (KM. 284.000 TO KM. 355.000)	3/2018	12/2020 (-) [10/2023]	538.41 (478.32) [478.32]	415.11 (-60.09) [34]
1192	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (12/2023) [12/2023]	1,047.00 (-) [1,047.00]	1,855.00 (0.00) [114]
1193	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	4/2021 (9/2023) [9/2023]	806.11 (767.45) [767.45]	737.93 (-38.66) [29]
1194	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (10/2023) [10/2023]	287.70 (-) [287.70]	196.92 (0.00) [80]
1195	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (9/2023) [9/2023]	214.23 (-) [214.23]	179.48 (0.00) [61]
1196	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (10/2023) [10/2023]	223.50 (-) [223.50]	139.44 (0.00) [62]
1197	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (9/2023) [9/2023]	199.16 (-) [199.16]	101.34 (0.00) [61]
1198	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (9/2023) [9/2023]	295.67 (-) [295.67]	203.61 (0.00) [79]
1199	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (9/2023) [9/2023]	206.88 (-) [206.88]	123.50 (0.00) [65]
	<u>Steel</u>				
1200	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP	1/2022	5/2025 (-) [5/2025]	970.18 (-) [970.18]	168.95 (0.00) [0]
1201	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [2/2024]	377.18 (-) [377.18]	299.73 (0.00) [9]
	<u>PUDUCHERRY</u>				
	<u>Health And Family Welfare</u>				
1202	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020 (-) [9/2020]	195.00 (-) [195.00]	2.67 (0.00) [0]
	<u>PUNJAB</u>				
	<u>Department Of Higher Education</u>				
1203	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [3/2024]	348.24 (-) [348.24]	175.07 (0.00) [22]
1204	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [6/2023]	430.00 (-) [355.00]	357.89 (-75.00) [0]
	<u>Petroleum</u>				
1205	BHATINDA SANGRUR PIPELINE	11/2021	4/2024 (-) [4/2024]	367.00 (-) [367.00]	142.19 (0.00) [0]
1206	CGD PROJECT AT PATHANKOT DISTRICT	3/2022	3/2030 (-) [3/2030]	151.00 (-) [151.00]	6.36 (0.00) [0]
1207	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (12/2023) [12/2023]	1,421.46 (-) [1,421.46]	735.28 (0.00) [10]
	<u>Railways</u>				
1208	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL	6/2009	8/2016	404.00	190.00

	MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI		(-) [8/2025]	(-) [404.00]	(0.00) [108]
	Road Transport And Highways				
1209	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA)	7/2021	2/2025 (-) [2/2025]	1,501.02 (-) [1,501.02]	33.00 (0.00) [0]
1210	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6	11/2021	7/2024 (7/2024) [7/2024]	646.42 (646.42) [646.42]	158.90 (0.00) [0]
1211	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I	12/2020	6/2024 (-) [6/2024]	857.91 (-) [857.91]	73.50 (0.00) [0]
1212	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0	12/2020	6/2023 (8/2023) [8/2023]	366.85 (366.85) [366.85]	252.03 (0.00) [2]
1213	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N	3/2021	11/2024 (-) [11/2024]	1,229.38 (-) [1,229.38]	499.62 (0.00) [0]
1214	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD	3/2021	10/2024 (-) [10/2024]	1,525.31 (-) [1,525.31]	132.46 (0.00) [0]
1215	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV	12/2020	9/2023 (-) [9/2023]	524.88 (-) [524.88]	122.22 (0.00) [0]
1216	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM	1/2021	5/2024 (-) [5/2024]	1,741.86 (-) [1,741.86]	849.17 (0.00) [0]
1217	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA – RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR	5/2021	12/2024 (12/2024) [12/2024]	1,368.91 (1,368.91) [1,368.91]	63.88 (0.00) [0]
1218	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (8/2023) [8/2023]	754.54 (668.74) [668.74]	677.74 (-85.80) [41]
1219	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR	3/2021	10/2024 (-) [10/2024]	1,641.75 (-) [1,641.75]	69.48 (0.00) [0]
1220	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1	12/2020	1/2024 (5/2024) [5/2024]	733.00 (-) [733.00]	522.95 (0.00) [4]
1221	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH-	2/2021	4/2024 (11/2024) [11/2024]	1,269.96 (-) [1,269.96]	241.67 (0.00) [7]
1222	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR-	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]
1223	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO	12/2020	4/2024 (7/2024) [7/2024]	1,094.46 (-) [1,094.46]	357.25 (0.00) [3]
1224	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI	12/2020	1/2024 (3/2025) [3/2025]	989.66 (-) [989.66]	46.35 (0.00) [14]
1225	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO	12/2020	4/2024 (7/2024) [7/2024]	1,234.40 (-) [1,234.40]	344.12 (0.00) [3]
1226	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO	12/2020	4/2024 (7/2024) [7/2024]	881.00 (-) [881.00]	546.76 (0.00) [3]
1227	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K	3/2021	1/2025 (-) [1/2025]	1,754.84 (-) [1,754.84]	758.50 (0.00) [0]
1228	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI	2/2021	8/2024 (-) [8/2024]	1,474.77 (-) [1,474.77]	146.71 (0.00) [0]

1229	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V	1/2021	1/2024 (12/2023) [12/2023]	1,060.29 (-) [1,060.29]	745.17 (0.00) [-1]
1230	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE	5/2020	12/2024 (12/2024) [12/2024]	864.23 (864.23) [864.23]	342.25 (0.00) [0]
1231	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [12/2023]	1,069.59 (-) [1,069.59]	739.08 (0.00) [50]
1232	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [11/2023]	170.57 (192.48) [192.48]	94.84 (21.91) [36]
1233	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [3/2023]	293.64 (326.84) [293.64]	295.46 (0.00) [0]
1234	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [6/2023]	293.10 (341.84) [293.10]	302.40 (0.00) [0]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1235	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2023]	12,320.00 (17,079.00) [17,079.00]	16,576.00 (4,759.00) [84]
	<u>Civil Aviation</u>				
1236	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT	5/2022	11/2024 (-) [11/2024]	480.00 (-) [480.00]	0.19 (0.00) [0]
	<u>Coal</u>				
1237	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-) [9/2020]	2,112.60 (-) [2,112.60]	85.90 (0.00) [0]
1238	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	175.30 (0.00) [0]
1239	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020 (-) [9/2020]	2,196.30 (-) [2,196.30]	106.24 (0.00) [0]
1240	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Petroleum</u>				
1241	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGPUR DISTRICTS	3/2022	3/2030 (-) [3/2030]	575.00 (-) [575.00]	22.91 (0.00) [0]
1242	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE	12/2021	10/2024 (12/2024) [12/2024]	9,028.00 (-) [9,028.00]	4,088.75 (0.00) [2]
	<u>Power</u>				
1243	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART	3/2023	9/2024 (-) [9/2024]	1,433.28 (-) [1,433.28]	0.00 (0.00) [0]
1244	ANTA SOLAR 90 MW	1/2021	3/2022 (3/2024) [3/2024]	382.22 (-) [382.22]	65.29 (0.00) [24]
1245	BHADLA-II 500MW SOLAR PV PROJECT	6/2022	3/2024 (3/2024) [3/2024]	2,598.92 (-) [2,598.92]	1.75 (0.00) [0]
1246	BHENSARA 320 MW	1/2021	7/2022 (3/2024) [3/2024]	1,221.73 (-) [1,221.73]	153.13 (0.00) [20]
1247	CHHATTARGARH 150 MW	2/2021	7/2022 (3/2024)	599.99 (-)	262.95 (0.00)

			[3/2024]	[599.99]	[20]
1248	NOKH PLOT-1 SOLAR PV PROJECT 245MW	3/2022	8/2023 (9/2024) [9/2024]	1,352.71 (-) [1,352.71]	91.14 (0.00) [13]
1249	NOKH PLOT-2 SOLAR PV PROJECT 245MW	3/2022	8/2023 (9/2024) [9/2024]	1,409.52 (-) [1,409.52]	160.80 (0.00) [13]
1250	NOKH PLOT-3 SOLAR PV PROJECT 245MW	3/2022	8/2023 (9/2024) [9/2024]	1,426.94 (-) [1,426.94]	164.82 (0.00) [13]
1251	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (9/2024) [9/2024]	1,782.00 (-) [1,782.00]	1,267.99 (0.00) [36]
1252	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD	1/2020	1/2021 (-) [5/2023]	562.86 (545.88) [545.88]	394.19 (-16.98) [0]
1253	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2021	9/2022 (-) [12/2023]	1,184.88 (-) [1,184.88]	712.85 (0.00) [15]
1254	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	12/2022 (-) [7/2023]	1,340.81 (-) [1,340.81]	1,087.22 (0.00) [7]
1255	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [3/2024]	1,562.00 (-) [1,562.00]	805.08 (0.00) [15]
1256	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [3/2024]	1,006.00 (-) [1,006.00]	791.18 (0.00) [15]
1257	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [3/2024]	713.82 (-) [713.82]	433.26 (0.00) [15]
1258	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	12/2022 (-) [9/2023]	353.85 (-) [353.85]	239.56 (0.00) [9]
	<u>Railways</u>				
1259	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [9/2023]	410.08 (-) [970.00]	935.00 (559.92) [55]
	<u>Road Transport And Highways</u>				
1260	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK	9/2021	6/2024 (-) [6/2024]	672.35 (-) [672.35]	224.87 (0.00) [0]
1261	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR	12/2021	5/2024 (-) [5/2024]	411.40 (-) [411.40]	57.30 (0.00) [0]
1262	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG-	2/2021	1/2024 (-) [1/2024]	240.99 (-) [240.99]	110.30 (0.00) [0]
1263	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M	12/2021	8/2024 (-) [8/2024]	451.66 (-) [451.66]	186.59 (0.00) [0]
1264	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR	3/2022	11/2024 (-) [11/2024]	1,636.15 (-) [1,636.15]	281.01 (0.00) [0]
1265	4L OF KARWAR (KM. 281.980 OF NH-62 NAGAU ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II)	11/2021	8/2024 (-) [8/2024]	736.75 (-) [736.75]	61.63 (0.00) [0]
1266	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II	8/2020	12/2022 (-) [9/2023]	216.72 (-) [216.72]	151.46 (0.00) [9]
1267	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II.	12/2020	10/2023 (-)	339.65 (-)	170.39 (0.00)

			[6/2024]	[339.65]	[8]
1268	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I.	12/2020	10/2023 (-) [6/2024]	379.23 (-) [379.23]	143.30 (0.00) [8]
1269	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I.	7/2020	3/2024 (-) [7/2024]	319.09 (-) [319.09]	77.04 (0.00) [4]
1270	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	4/2021 (8/2023) [8/2023]	741.86 (649.00) [649.00]	634.53 (-92.86) [28]
1271	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M	11/2019	12/2022 (8/2023) [6/2023]	1,658.06 (-) [1,658.06]	153.69 (0.00) [0]
1272	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA	11/2019	10/2022 (9/2023) [7/2023]	1,272.97 (-) [1,272.97]	330.25 (0.00) [9]
1273	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL	11/2019	5/2023 (8/2023) [5/2023]	1,640.10 (-) [1,640.10]	1,099.00 (0.00) [0]
1274	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON	11/2019	3/2023 (11/2023) [8/2023]	1,425.02 (-) [1,425.02]	1,026.56 (0.00) [5]
1275	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S	11/2019	12/2023 (-) [12/2023]	1,341.36 (-) [1,341.36]	806.97 (0.00) [0]
1276	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N	11/2019	5/2023 (10/2023) [7/2023]	1,119.35 (-) [1,119.35]	1,108.34 (0.00) [2]
1277	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH	7/2020	1/2024 (9/2024) [1/2024]	1,788.69 (-) [1,788.69]	411.07 (0.00) [0]
1278	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-16) (CH. 427.300 TO CH.452.420) [MAJOR BRIDGE OVE	11/2019	1/2023 (10/2023) [6/2023]	952.57 (-) [952.57]	791.27 (0.00) [0]
1279	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-3)	2/2019	12/2022 (9/2023) [5/2023]	820.19 (-) [820.19]	7.37 (0.00) [0]
1280	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-4)	10/2019	11/2022 (9/2023) [5/2023]	598.01 (-) [598.01]	405.20 (0.00) [0]
1281	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-5)	10/2019	3/2023 (9/2023) [5/2023]	584.37 (-) [584.37]	429.13 (0.00) [0]
1282	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6)	10/2019	8/2023 (9/2023) [8/2023]	846.59 (-) [846.59]	37.29 (0.00) [0]
1283	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7)	10/2019	7/2023 (11/2023) [7/2023]	662.08 (-) [662.08]	32.02 (0.00) [0]
1284	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8)	10/2019	10/2023 (-) [10/2023]	839.63 (-) [839.63]	38.16 (0.00) [0]
1285	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	12/2020 (-) [2/2024]	1,308.73 (-) [1,308.73]	309.04 (0.00) [38]
1286	RASISAR (NEAR BIKANER)-DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-1)	2/2019	10/2022 (9/2023) [4/2023]	621.82 (-) [621.82]	479.50 (0.00) [0]
1287	RASISAR (NEAR BIKANER)-DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-2)	2/2019	1/2022 (9/2023) [4/2023]	676.19 (-) [676.19]	534.35 (0.00) [0]
1288	RASISAR (NEAR BIKANER)-DEOGARH (NEAR DHANDHANIYA) (PHASE-I) (AJ/RD-PACKAGE-3)	2/2019	1/2022 (9/2023)	732.84 (-)	558.75 (0.00)

			[4/2023]	[732.84]	[0]
1289	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF BEAWAR-ASIND SECTION (K)	8/2020	11/2022 (-) [9/2023]	196.23 (-) [196.00]	144.86 (-0.23) [10]
1290	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (AJ/SR-PACKAGE-9)	2/2019	6/2022 (9/2023) [6/2023]	656.57 (-) [656.57]	559.31 (0.00) [0]
1291	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-1)	2/2019	10/2023 (-) [10/2023]	738.90 (-) [738.90]	778.02 (0.00) [0]
1292	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-2)	2/2019	10/2023 (11/2023) [10/2023]	755.16 (-) [755.16]	723.96 (0.00) [0]
1293	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-3)	2/2019	10/2022 (9/2023) [5/2023]	672.72 (-) [672.72]	579.29 (0.00) [0]
1294	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-5)	2/2019	10/2022 (-) [8/2022]	515.45 (-) [515.45]	0.12 (0.00) [0]
1295	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-6)	2/2019	10/2022 (9/2023) [5/2023]	635.84 (-) [635.84]	445.96 (0.00) [0]
1296	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) SECTION OF NH-754K (PHASE-I) (AJ/SR-PACKAGE-7)	2/2019	5/2023 (9/2023) [6/2023]	520.63 (-) [520.63]	423.98 (0.00) [0]
1297	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (9/2023) [9/2023]	894.00 (-) [929.32]	880.00 (35.32) [41]
1298	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FROM	3/2020	10/2022 (-) [12/2023]	255.23 (-) [255.23]	179.27 (0.00) [14]
1299	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF BARMER GHAGARIYA SECTION FROM KM 0	3/2022	8/2024 (-) [8/2024]	304.87 (-) [304.87]	94.33 (0.00) [0]
1300	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	12/2019 (-) [8/2021]	370.30 (-) [370.30]	336.24 (0.00) [0]
1301	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH	12/2021	9/2024 (-) [9/2024]	150.11 (-) [150.11]	24.18 (0.00) [0]
1302	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE	1/2022	12/2024 (-) [12/2024]	194.88 (-) [194.88]	13.40 (0.00) [0]
1303	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	10/2019 (-) [4/2021]	187.82 (-) [187.82]	151.49 (0.00) [0]
	SIKKIM				
	Department Of Higher Education				
1304	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM	8/2020	1/2025 (-) [12/2024]	314.06 (-) [303.55]	15.70 (-10.51) [-1]
	Power				
1305	RANGIT IV HE PROJECT	3/2021	5/2024 (8/2024) [8/2024]	938.29 (938.29) [938.29]	658.71 (0.00) [3]
1306	TEESTA VI HE PROJECT	3/2019	3/2024 (8/2026) [8/2026]	5,748.04 (-) [5,748.04]	2,643.25 (0.00) [29]
	Railways				
1307	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [7,876.92]	3,290.96 (6,537.44) [96]

	Road Transport And Highways				
1308	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (9/2023) [9/2023]	230.45 (244.91) [244.91]	190.66 (14.46) [5]
1309	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [5/2024]	493.42 (478.79) [478.79]	230.22 (-14.63) [6]
1310	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [1/2024]	311.00 (273.78) [273.78]	200.01 (-37.22) [9]
1311	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [10/2023]	345.38 (395.59) [395.59]	300.58 (50.21) [6]
1312	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [4/2024]	183.31 (439.56) [439.56]	322.34 (256.25) [23]
1313	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [8/2024]	262.84 (414.20) [414.20]	185.56 (151.36) [15]
1314	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM)	10/2021	5/2024 (5/2024) [5/2024]	385.15 (-) [385.15]	81.83 (0.00) [0]
1315	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	4/2022 (5/2022) [12/2023]	375.80 (-) [375.80]	270.63 (0.00) [20]
1316	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	10/2020 (8/2023) [8/2023]	290.05 (-) [290.05]	218.36 (0.00) [34]
1317	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (9/2024) [9/2024]	816.79 (786.60) [786.60]	204.88 (-30.19) [9]
1318	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [1/2024]	402.94 (-) [402.94]	188.53 (0.00) [21]
1319	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (8/2023) [12/2023]	295.97 (-) [295.97]	190.56 (0.00) [8]
1320	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [12/2023]	242.97 (-) [242.97]	204.16 (0.00) [18]
1321	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (10/2023) [11/2024]	292.80 (-) [292.80]	94.56 (0.00) [30]
1322	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	117.90 (0.00) [0]
1323	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (2/2024) [2/2024]	410.60 (379.30) [379.30]	147.62 (-31.30) [0]
	TAMIL NADU				
	Atomic Energy				
1324	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6	6/2017	9/2027 (-) [9/2027]	49,621.00 (-) [49,621.00]	10,592.00 (0.00) [0]
1325	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	38,740.00 (0.00) [36]
1326	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (10/2022) [12/2024]	3,492.00 (6,840.00) [7,670.00]	6,569.75 (4,178.00) [171]
	Civil Aviation				
1327	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022	380.87	168.32

			(12/2023) [12/2023]	(-) [357.00]	(-23.87) [21]
1328	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [12/2025]	2,467.00 (-) [2,467.00]	1,335.88 (0.00) [46]
1329	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [12/2023]	951.28 (-) [951.28]	867.64 (0.00) [26]
	<u>Coal</u>				
1330	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [9/2027]	1,458.17 (-) [709.06]	541.79 (-749.11) [147]
1331	JAWAHAR KHANI OPENCAST (JK OC) MINE	12/2021	3/2025 (-) [3/2025]	297.88 (-) [297.88]	25.96 (0.00) [0]
1332	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (-) [8,990.00]	7,656.86 (3,082.89) [0]
	<u>Finance</u>				
1333	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (10/2022) [10/2022]	209.00 (-) [262.00]	249.00 (53.00) [0]
1334	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2022]	348.77 (-) [348.77]	296.23 (0.00) [0]
	<u>Mines</u>				
1335	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2023) [12/2023]	166.62 (163.17) [163.17]	135.00 (-3.45) [54]
	<u>Petroleum</u>				
1336	CBR 9 MMTPA PROJECT	1/2021	6/2025 (-) [0/0]	31,580.00 (31,580.00) [31,580.00]	906.79 (0.00) [0]
1337	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE	3/2022	11/2024 (-) [11/2024]	564.00 (-) [564.00]	96.53 (0.00) [0]
1338	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	288.06 (0.00) [0]
1339	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS	3/2022	3/2030 (-) [3/2030]	501.00 (-) [501.00]	41.04 (0.00) [0]
1340	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS	3/2022	3/2030 (-) [3/2030]	1,295.00 (-) [1,295.00]	39.23 (0.00) [0]
1341	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS	3/2022	3/2030 (-) [3/2030]	1,328.00 (-) [1,328.00]	41.85 (0.00) [0]
1342	CGD PROJECT AT SALEM DISTRICT	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	96.14 (0.00) [0]
1343	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [12/2024]	921.00 (-) [921.00]	315.45 (0.00) [15]
1344	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (11/2023) [3/2024]	4,497.00 (6,025.00) [6,025.00]	5,303.14 (1,528.00) [63]
1345	EXTENSION OF ASANUR-SANKARI SECTION OF CHENNAI-TRICHY-MADURAI PIPELINE UPTO COIMBATORE (IRUGUR)	1/2023	1/2025 (-) [1/2025]	346.70 (-) [346.70]	0.13 (0.00) [0]
1346	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021)	650.82 (-)	469.54 (0.00)

			[12/2024]	[650.82]	[69]
1347	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI	1/2022	7/2024 (-) [12/2024]	827.00 (-) [827.00]	222.66 (0.00) [5]
1348	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (1/2026) [1/2026]	678.00 (1,732.00) [1,732.00]	30.71 (1,054.00) [107]
1349	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI)	1/2022	7/2024 (-) [7/2024]	829.00 (-) [829.00]	102.68 (0.00) [0]
1350	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [2/2024]	1,398.00 (1,587.00) [1,587.00]	726.79 (189.00) [2]
	<u>Power</u>				
1351	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [8/2023]	186.17 (-) [219.66]	178.40 (33.49) [49]
	<u>Railways</u>				
1352	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [12/2023]	495.74 (-) [734.01]	576.39 (238.27) [126]
1353	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [8/2023]	760.00 (-) [1,536.00]	1,846.81 (776.00) [41]
1354	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [10/2023]	1,700.00 (-) [1,305.00]	1,556.55 (-395.00) [19]
1355	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [3,118.34]	1,877.71 (2,393.65) [73]
1356	TIDIVANAM-NAGARI (NL)	9/2006	/ (12/2025) [12/2025]	582.83 (-) [3,620.28]	758.81 (3,037.45) [-]
	<u>Road Transport And Highways</u>				
1357	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209	1/2019	1/2023 (2/2024) [2/2024]	1,051.69 (-) [1,051.69]	349.20 (0.00) [13]
1358	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83)	1/2019	12/2022 (-) [2/2024]	1,409.38 (-) [1,409.38]	520.63 (0.00) [14]
1359	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH-383	6/2018	3/2022 (-) [4/2024]	1,103.86 (-) [1,103.86]	295.97 (0.00) [25]
1360	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83)	1/2019	10/2022 (-) [12/2023]	1,518.53 (-) [1,518.53]	844.56 (0.00) [14]
1361	4-LANING OF VADIPPATTI - THAMARAI PATTI SECTION OF NH-744A (MADURAI RING ROAD)	12/2018	3/2022 (7/2024) [7/2024]	854.94 (-) [854.94]	169.70 (0.00) [28]
1362	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	8/2020 (6/2024) [6/2024]	1,227.87 (-) [1,227.87]	1,097.03 (0.00) [46]
1363	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT	2/2021	7/2024 (-) [7/2024]	2,948.31 (-) [3,392.00]	506.57 (443.69) [0]
1364	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH	11/2021	2/2023 (-) [5/2023]	463.44 (-) [464.00]	0.00 (0.56) [0]
1365	6L OF SRIPERUMBUDUR TO KARAI PETTAI FROM KM 37.000 TO KM 71.015 OF NH 48	1/2019	5/2021 (-) [2/2024]	654.26 (-) [821.00]	295.75 (166.74) [33]
1366	8L OF GUDUVANCHERY (KM 38.00) - MARAIMALAI	12/2020	2/2022	230.69	174.08

	NAGAR (KM 42.00) - SINGAPERUMAL KOIL (47.00) - CHETTIPIU		(-) [8/2023]	(-) [230.69]	(0.00) [18]
1367	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83)	10/2020	5/2023 (10/2023) [10/2023]	434.12 (-) [434.12]	161.17 (0.00) [5]
1368	BALANCE WORK OF 2L PS OF TINDIVANAM KRISHNAGIRI FROM KM 37.600 TO 219.782	5/2019	7/2021 (5/2023) [8/2023]	602.57 (621.38) [548.89]	313.44 (-53.68) [25]
1369	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS	1/2022	9/2024 (-) [9/2024]	467.99 (-) [468.00]	18.83 (0.01) [0]
1370	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2	12/2020	7/2024 (-) [7/2024]	843.48 (-) [966.00]	203.01 (122.52) [0]
1371	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K	11/2020	8/2024 (-) [8/2024]	1,155.49 (-) [1,155.49]	227.66 (0.00) [0]
1372	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1	10/2020	5/2024 (-) [5/2024]	1,023.91 (-) [1,285.00]	318.78 (261.09) [0]
1373	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6	2/2022	8/2022 (-) [10/2024]	191.33 (-) [191.33]	28.48 (0.00) [26]
1374	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 – 29/250 INCLUDING LA AND SHIFTING OF NH-234	1/2022	11/2024 (-) [11/2024]	221.03 (243.95) [243.95]	0.00 (22.92) [0]
1375	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460	2/2019	8/2023 (-) [8/2023]	1,291.37 (-) [1,291.37]	215.02 (0.00) [0]
1376	FOUR LANING OF MADURAI- CHETTikulAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	11/2020 (7/2023) [7/2023]	628.71 (-) [628.71]	583.02 (0.00) [32]
1377	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000	2/2019	5/2024 (-) [5/2024]	1,008.99 (-) [1,361.00]	12.42 (352.01) [0]
1378	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350	9/2021	10/2024 (-) [10/2024]	1,751.18 (-) [1,751.18]	308.26 (0.00) [0]
1379	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU	10/2022	11/2024 (-) [11/2024]	172.15 (-) [172.15]	0.00 (0.00) [0]
1380	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	3/2018	1/2022 (-) [1/2024]	2,120.40 (2,565.63) [2,565.63]	1,147.79 (445.23) [24]
1381	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	3/2018	10/2020 (-) [9/2024]	1,872.68 (2,661.51) [2,756.09]	848.82 (883.41) [47]
1382	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM	2/2019	12/2023 (-) [12/2023]	1,243.57 (-) [1,243.57]	171.63 (0.00) [0]
1383	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	3/2018	11/2021 (-) [11/2023]	998.70 (1,358.32) [1,358.32]	785.96 (359.62) [24]
1384	FOUR LANING OF CHETTikulAM TO NATHAM SECTION OF NH-785 FROM CHETTICULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	10/2022 (7/2023) [7/2023]	505.35 (-) [505.35]	354.35 (0.00) [9]
1385	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	9/2020 (6/2024) [6/2024]	1,176.37 (-) [1,176.37]	970.43 (0.00) [45]
1386	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (5/2024) [5/2024]	848.45 (-) [848.45]	296.66 (0.00) [50]
1387	FOUR LANING OF PUDUCHERRY (KM.29/000) TO	3/2018	11/2021	1,294.47	605.20

	POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER		(-) [11/2023]	(1,588.40) [1,588.40]	(293.93) [24]
1388	KARAIPTTAI TO WALAJAPET FROM KM 71.015 TO 107.091	10/2018	2/2021 (-) [12/2023]	707.90 (-) [717.00]	343.05 (9.10) [34]
1389	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS	2/2019	3/2021 (-) [9/2023]	166.90 (-) [166.90]	118.82 (0.00) [30]
1390	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM	7/2022	8/2023 (-) [8/2023]	186.50 (-) [201.00]	0.00 (14.50) [0]
1391	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	9/2023 (8/2023) [8/2023]	633.55 (736.33) [736.33]	194.97 (102.78) [-1]
1392	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	8/2020	2/2021 (-) [8/2023]	302.62 (306.14) [306.14]	293.37 (3.52) [30]
1393	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [9/2023]	297.55 (320.00) [320.00]	296.73 (22.45) [46]
1394	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR	2/2022	8/2022 (-) [8/2024]	184.15 (-) [184.15]	82.06 (0.00) [24]
	Urban Development				
1395	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (2/2021) [2/2021]	3,770.00 (-) [3,770.00]	2,527.73 (0.00) [0]
1396	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [12/2015]	14,600.00 (-) [18,380.00]	17,619.68 (3,780.00) [0]
	TELANGANA				
	Civil Aviation				
1397	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (6/2023) [6/2023]	353.61 (-) [353.61]	296.11 (0.00) [0]
	Coal				
1398	GODAVARIKHANI COAL MINE	7/2019	3/2023 (-) [3/2024]	438.98 (-) [438.98]	123.25 (0.00) [12]
1399	GOLETI OPENCAST MINE	7/2021	3/2026 (-) [3/2026]	345.60 (-) [345.60]	30.72 (0.00) [0]
1400	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2022 (-) [3/2024]	413.84 (-) [413.84]	409.48 (0.00) [24]
1401	RCE OF INDARAM OPENCAST PROJECT	8/2017	3/2021 (-) [3/2024]	349.28 (-) [424.81]	335.24 (75.53) [36]
1402	RCE OF KAKATHIYAKHANI OC - 2 PROJECT	8/2017	3/2020 (-) [3/2024]	442.42 (-) [442.42]	222.33 (0.00) [48]
1403	RCE OF KALYANIKHANI OPENCAST PROJECT	3/2016	3/2020 (-) [3/2024]	384.32 (-) [384.32]	180.58 (0.00) [48]
1404	RCE OF KISTARAM OPENCAST PROJECT	3/2017	3/2021 (-) [3/2024]	164.04 (-) [164.04]	143.08 (0.00) [36]
1405	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT	11/2015	3/2023 (-) [3/2024]	489.62 (-) [489.62]	392.20 (0.00) [12]
1406	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II	3/2019	3/2021 (-)	473.22 (-)	446.35 (0.00)

			[3/2023]	[473.22]	[0]
1407	SRP OC-II EXPANSION PROJECT	11/2016	3/2018 (-) [3/2024]	272.73 (-) [272.73]	153.75 (0.00) [72]
1408	VENKATESH KHANI COAL MINE	10/2020	3/2023 (-) [3/2025]	484.51 (-) [484.51]	64.04 (0.00) [24]
	<u>Health And Family Welfare</u>				
1409	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR	12/2018	7/2024 (-) [10/2024]	1,110.55 (-) [1,110.55]	269.09 (0.00) [3]
1410	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (244.97) [273.00]	240.58 (63.16) [0]
	<u>Petroleum</u>				
1411	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [10/2023]	611.00 (-) [611.00]	349.08 (0.00) [18]
	<u>Power</u>				
1412	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [8/2023]	10,598.98 (-) [10,998.00]	10,831.04 (399.02) [33]
	<u>Railways</u>				
1413	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (9/2023) [6/2023]	632.68 (-) [950.00]	973.99 (317.32) [0]
1414	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [242.28]	54.15 (122.55) [0]
1415	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2025]	1,160.48 (-) [3,014.00]	1,071.53 (1,853.52) [180]
	<u>Road Transport And Highways</u>				
1416	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29	1/2021	1/2024 (-) [1/2024]	1,307.95 (-) [1,307.95]	420.17 (0.00) [0]
1417	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (12/2022) [8/2023]	283.15 (-) [283.15]	250.50 (0.00) [39]
1418	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000,	3/2022	1/2025 (-) [1/2025]	955.49 (-) [955.49]	84.06 (0.00) [0]
1419	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20	1/2022	1/2025 (-) [1/2025]	1,227.57 (-) [1,227.57]	4.98 (0.00) [0]
1420	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM	2/2022	1/2025 (-) [1/2025]	972.06 (-) [972.06]	8.38 (0.00) [0]
1421	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44	12/2021	7/2024 (-) [7/2024]	521.53 (-) [521.53]	126.88 (0.00) [0]
1422	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (6/2024) [6/2024]	626.76 (-) [626.76]	255.13 (0.00) [47]
1423	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/2017]	153.21 (-) [153.21]	100.96 (0.00) [0]
1424	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	2/2023 (6/2023) [8/2023]	828.29 (1,140.50) [828.29]	448.81 (0.00) [6]
1425	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM	2/2022	9/2024 (-)	637.11 (-)	162.16 (0.00)

	VILLAGE TO CHINTAGUDEM V		[9/2024]	[637.11]	[0]
1426	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM	8/2022	10/2024 (-) [10/2024]	772.11 (-) [772.11]	234.08 (0.00) [0]
1427	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA	9/2022	2/2024 (-) [2/2024]	804.69 (-) [804.69]	257.86 (0.00) [0]
1428	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (6/2022) [7/2023]	192.67 (-) [192.67]	171.11 (0.00) [48]
1429	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (10/2019) [6/2021]	605.08 (-) [605.08]	412.60 (0.00) [0]
1430	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (9/2019) [9/2019]	270.00 (-) [270.00]	0.00 (0.00) [0]
1431	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (3/2022) [2/2023]	294.13 (-) [294.13]	193.20 (0.00) [0]
1432	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (6/2022) [4/2023]	322.81 (-) [322.81]	307.95 (0.00) [0]
1433	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (12/2022) [10/2023]	295.47 (-) [295.47]	221.36 (0.00) [80]
1434	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (4/2023) [4/2023]	248.83 (-) [248.83]	164.28 (0.00) [0]
1435	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (6/2022) [6/2023]	298.32 (-) [298.32]	171.24 (0.00) [0]
1436	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (11/2020) [11/2020]	230.03 (-) [230.03]	229.41 (0.00) [0]
1437	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (1/2021) [1/2021]	206.13 (-) [206.13]	187.55 (0.00) [0]
1438	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/	193.19 (249.72) [249.72]	219.90 (56.53) [0]
1439	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (10/2019) [10/2019]	196.52 (-) [196.52]	123.68 (0.00) [0]
1440	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (12/2019) [12/2019]	283.00 (-) [283.00]	253.40 (0.00) [0]
1441	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (8/2019) [8/2019]	244.54 (-) [244.54]	174.50 (0.00) [0]
1442	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (7/2021) [7/2021]	300.00 (-) [300.00]	224.70 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Petroleum</u>				
1443	CREATION OF GAS DEHYDRATION FACILITIES	3/2022	5/2024 (-) [5/2024]	209.33 (-) [209.33]	20.50 (0.00) [0]
1444	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT	6/2022	8/2025 (-) [8/2025]	656.00 (-) [656.00]	98.04 (0.00) [0]
	<u>Railways</u>				
1445	AGARTALA-AKHAURA NL	4/2012	3/2020	569.63	380.92

			(6/2022) [9/2022]	(-) [708.73]	(139.10) [0]
	<u>Road Transport And Highways</u>				
1446	2 LANING FROM MANU-SIMLUNG PKG-2	2/2022	1/2025 (-) [1/2025]	456.88 (-) [456.88]	11.22 (0.00) [0]
1447	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (6/2023) [12/2023]	201.99 (-) [201.99]	117.12 (0.00) [23]
1448	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (10/2022) [8/2023]	247.76 (251.89) [251.89]	137.58 (4.13) [19]
1449	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (4/2023) [7/2023]	347.36 (-) [347.36]	224.48 (0.00) [18]
1450	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (10/2022) [6/2023]	173.17 (-) [173.17]	64.05 (0.00) [0]
1451	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (3/2023) [4/2023]	165.54 (-) [210.54]	85.02 (45.00) [0]
1452	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (4/2023) [5/2023]	280.91 (296.48) [296.48]	202.06 (15.57) [0]
1453	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (6/2023) [10/2023]	159.13 (171.50) [171.50]	67.62 (12.37) [16]
1454	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (4/2023) [4/2023]	332.14 (-) [332.14]	148.07 (0.00) [0]
1455	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (6/2023) [11/2023]	354.79 (-) [354.79]	33.27 (0.00) [11]
1456	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (8/2023) [8/2023]	178.43 (-) [208.74]	77.89 (30.31) [13]
1457	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (3/2023) [7/2023]	154.51 (-) [154.51]	73.74 (0.00) [12]
1458	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (6/2023) [1/2024]	277.50 (302.02) [302.02]	201.23 (24.52) [24]
1459	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (5/2023) [5/2023]	197.67 (236.18) [236.18]	211.12 (38.51) [0]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1460	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [12/2024]	1,383.00 (-) [3,291.81]	769.80 (1,908.81) [39]
1461	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01	3/2021	12/2022 (9/2023) [9/2023]	242.14 (328.00) [328.00]	215.08 (85.86) [9]
	<u>Coal</u>				
1462	KHADIA EXPANSION OCP	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	8.49 (0.00) [0]
1463	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [12/2023]	17,237.00 (-) [19,406.12]	15,652.81 (2,169.12) [25]
	<u>Home Affairs</u>				
1464	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY	5/2019	1/2022	199.31	86.49

	QUARTERS AT GROUP CENTRE CRPF CHANDAULI		(3/2023) [3/2023]	(-) [199.31]	(0.00) [0]
	<u>Petroleum</u>				
1465	60 KTA POLYPROPYLENE PROJECT	3/2019	4/2024 (-) [4/2024]	910.56 (1,299.02) [1,299.02]	430.40 (388.46) [0]
1466	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (8/2029) [8/2029]	3,450.20 (-) [3,450.20]	1,340.47 (0.00) [5]
1467	CITY GAS DISTRIBUTION NETWORK PROJECT AT AMETHI, RAEBARELI AND PRATAPGARH	4/2019	9/2028 (-) [9/2028]	432.06 (-) [432.06]	122.52 (0.00) [0]
1468	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (11/2022) [8/2023]	255.40 (-) [255.40]	216.40 (0.00) [36]
1469	NEW LPG PLANT AT VARANASI	8/2017	5/2024 (-) [5/2024]	194.62 (-) [194.62]	154.12 (0.00) [0]
	<u>Power</u>				
1470	GUJRAI SOLAR POWER PROJECT	6/2022	8/2023 (-) [8/2023]	279.94 (-) [279.94]	194.48 (0.00) [0]
1471	GURHAH SOLAR POWER PROJECT	5/2022	8/2023 (-) [8/2023]	466.82 (-) [466.82]	411.95 (0.00) [0]
1472	KALPI SOLAR POWER PROJECT	7/2020	3/2022 (3/2024) [3/2024]	314.64 (350.46) [350.46]	242.14 (35.82) [24]
1473	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	7,902.37 (0.00) [11]
	<u>Railways</u>				
1474	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [5/2025]	602.50 (-) [800.00]	426.10 (197.50) [-]
1475	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [12/2023]	2,001.00 (2,001.00) [2,001.00]	1,118.80 (0.00) [33]
1476	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2026]	4,329.53 (-) [4,329.53]	60.37 (0.00) [36]
1477	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2023]	528.57 (-) [528.57]	616.92 (0.00) [0]
1478	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2024]	927.01 (-) [1,457.79]	1,491.77 (530.78) [60]
1479	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	4,306.50 (0.00) [0]
1480	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,587.43 (0.00) [21]
1481	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [12/2024]	150.00 (-) [341.66]	1.20 (191.66) [92]
1482	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	2,445.51 (0.00) [48]
1483	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [10/2023]	1,295.42 (-) [2,560.00]	2,121.53 (1,264.58) [19]

1484	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [3/2024]	1,177.96 (-) [1,500.95]	1,119.47 (322.99) [51]
1485	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2023]	943.60 (-) [1,500.00]	1,251.40 (556.40) [21]
Road Transport And Highways					
1486	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP	4/2020	3/2024 (-) [3/2024]	236.47 (-) [236.47]	46.55 (0.00) [0]
1487	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F	4/2020	7/2024 (-) [7/2024]	172.50 (-) [172.50]	46.73 (0.00) [0]
1488	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR	3/2021	4/2024 (-) [4/2024]	364.47 (-) [364.47]	28.87 (0.00) [0]
1489	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP	4/2020	7/2024 (-) [2/2024]	211.09 (-) [211.09]	31.61 (0.00) [-5]
1490	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV	9/2021	10/2023 (-) [10/2023]	300.79 (-) [300.79]	122.56 (0.00) [0]
1491	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR	8/2021	3/2024 (-) [3/2024]	1,147.26 (-) [1,147.26]	49.00 (0.00) [0]
1492	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74	2/2022	6/2024 (-) [6/2024]	570.98 (-) [570.98]	186.06 (0.00) [0]
1493	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH	10/2019	3/2023 (-) [8/2023]	1,936.68 (-) [2,458.03]	1,380.90 (521.35) [5]
1494	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00	3/2016	7/2020 (2/2024) [2/2024]	1,408.00 (1,659.12) [1,659.12]	1,115.46 (251.12) [43]
1495	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (12/2022) [7/2023]	1,587.49 (3,150.00) [3,063.99]	2,938.25 (1,476.50) [51]
1496	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	10/2019 (5/2023) [7/2023]	1,396.74 (4,041.80) [1,396.74]	3,738.01 (0.00) [45]
1497	4L BYPASSES FOR JAGATPUR, B4BUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA	12/2022	11/2024 (-) [11/2024]	1,699.00 (-) [1,699.00]	13.76 (0.00) [0]
1498	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C)	12/2021	1/2025 (-) [1/2025]	1,384.79 (-) [1,384.79]	398.01 (0.00) [0]
1499	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II	5/2019	11/2022 (-) [12/2023]	779.17 (-) [779.17]	0.00 (0.00) [13]
1500	4L OF SHAMLI TO MUZAFFARNAGAR SECTION OF NH-709AD, PKG-II	6/2020	10/2022 (-) [7/2023]	1,621.07 (-) [1,621.07]	977.49 (0.00) [9]
1501	4L PS OF MEERUT TO AFTER BRIDGE OVER RIVER YAMUNA, HARYANA VIA SHAMLI-FROM KM. 0.00 TO KM. 88.476 OF	9/2020	1/2023 (-) [6/2023]	798.96 (-) [798.96]	585.30 (0.00) [0]
1502	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT - SHAMLI - MUZAFFARNAGAR) AND NH-709A (KARN	8/2022	4/2024 (-) [4/2024]	326.79 (-) [329.79]	18.75 (3.00) [0]
1503	4L SPUR OF SHAMLI-MUZAFFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZAFFARNAGAR) AND NH-58 (MEERUT	1/2023	8/2024 (-) [8/2024]	391.26 (-) [391.26]	14.12 (0.00) [0]
1504	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III	11/2021	4/2024 (-)	923.15 (-)	455.61 (0.00)

			[4/2024]	[923.15]	[0]
1505	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K	1/2022	8/2024 (-) [8/2024]	1,159.96 (-) [1,159.96]	268.31 (0.00) [0]
1506	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL-LATIFPUR AT SAHARANPUR BYPASS FROM KM	3/2022	8/2024 (-) [8/2024]	1,428.19 (-) [1,428.19]	211.90 (0.00) [0]
1507	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM.	3/2022	8/2024 (-) [8/2024]	1,335.45 (-) [1,335.45]	173.11 (0.00) [0]
1508	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K	3/2022	8/2024 (-) [8/2024]	1,602.48 (-) [1,602.48]	162.20 (0.00) [0]
1509	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR – DEHRADUN SECTION FROM K	3/2021	10/2023 (10/2023) [10/2023]	836.24 (-) [836.24]	489.16 (0.00) [0]
1510	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744	12/2021	5/2025 (5/2025) [5/2025]	2,470.64 (-) [2,335.00]	139.84 (-135.64) [0]
1511	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR – DEHRADUN SECTION FROM	3/2021	10/2023 (10/2023) [10/2023]	990.28 (-) [990.28]	671.82 (0.00) [0]
1512	ALIGARH-KANPUR SECTION PACKAGEV FROM MITRASEN-KANPUR	10/2019	9/2023 (-) [10/2023]	2,325.28 (-) [2,325.28]	1,836.49 (0.00) [1]
1513	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00	4/2020	7/2024 (-) [7/2024]	294.84 (-) [294.84]	160.63 (0.00) [0]
1514	CONSTRUCTION OF 1 ROB CUM FLYOVER FROM KM 136.200 TO 137.800 AND 2 FLYOVERS	1/2022	4/2024 (-) [4/2024]	297.06 (-) [297.06]	184.94 (0.00) [0]
1515	CONSTRUCTION OF 4 LANE ELEVATED VIADUCT AT KM. 7.500 MUNSHI PULIA OF NH-24A	12/2021	9/2024 (-) [9/2024]	170.60 (-) [170.60]	40.08 (0.00) [0]
1516	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD	7/2018	2/2024 (-) [9/2024]	1,948.25 (-) [1,948.25]	640.55 (0.00) [7]
1517	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT	4/2021	9/2023 (-) [12/2024]	309.48 (-) [309.48]	63.83 (0.00) [15]
1518	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W	3/2021	9/2023 (-) [3/2024]	185.09 (-) [185.09]	92.62 (0.00) [6]
1519	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	12/2021 (12/2023) [12/2023]	1,117.84 (-) [1,117.84]	699.89 (0.00) [24]
1520	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	12/2019	4/2022 (-) [2/2024]	282.41 (-) [319.96]	248.23 (37.55) [22]
1521	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (7/2023) [6/2023]	667.00 (3,192.10) [3,006.53]	3,022.15 (2,339.53) [0]
1522	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (7/2023) [6/2023]	1,027.53 (2,950.04) [2,628.31]	2,615.85 (1,600.78) [0]
1523	FOUR LANNING OF JAGDISHPUR-FAIZABAD SECTION FROM KM 47.930 TO KM 107.680 OF NH-330A	3/2021	3/2023 (-) [7/2023]	1,980.00 (-) [1,980.00]	1,043.39 (0.00) [4]
1524	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (2/2024) [2/2024]	899.00 (1,381.45) [1,381.45]	939.15 (482.45) [58]
1525	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF	3/2022	2/2025 (-)	762.62 (-)	170.66 (0.00)

	KHUTAR B		[2/2025]	[762.62]	[0]
1526	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO	12/2021	7/2025 (-) [7/2025]	1,138.81 (-) [1,138.81]	122.05 (0.00) [0]
1527	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS	12/2021	10/2024 (-) [10/2024]	540.97 (-) [540.97]	50.31 (0.00) [0]
1528	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO	11/2021	5/2024 (-) [5/2024]	307.11 (-) [307.11]	21.55 (0.00) [0]
1529	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N	12/2021	7/2025 (7/2025) [7/2025]	1,972.10 (-) [1,936.00]	158.30 (-36.10) [0]
1530	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER	1/2018	2/2023 (8/2023) [8/2023]	1,916.38 (-) [2,078.00]	1,158.54 (161.62) [6]
1531	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00	3/2021	8/2023 (-) [11/2023]	264.86 (-) [264.86]	52.66 (0.00) [3]
1532	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP	4/2020	11/2024 (-) [11/2024]	325.24 (-) [325.24]	24.98 (0.00) [0]
1533	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	6/2021 (-) [9/2023]	306.59 (-) [306.59]	251.95 (0.00) [27]
1534	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM	4/2020	2/2024 (-) [2/2024]	199.39 (206.59) [199.39]	65.98 (0.00) [0]
1535	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U	10/2019	11/2023 (-) [11/2023]	1,779.83 (-) [2,200.00]	708.00 (420.17) [0]
1536	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75	6/2020	11/2023 (-) [11/2023]	2,002.79 (-) [2,002.79]	753.29 (0.00) [0]
1537	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	11/2017	7/2021 (4/2023) [5/2023]	2,159.00 (2,262.00) [2,262.00]	2,212.19 (103.00) [0]
1538	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	11/2021 (-) [3/2024]	2,140.93 (-) [2,140.93]	1,912.14 (0.00) [28]
1539	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN	1/2022	10/2024 (-) [10/2024]	953.79 (-) [953.79]	384.66 (0.00) [0]
1540	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [1/2024]	724.60 (-) [724.60]	464.18 (0.00) [10]
1541	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81	2/2019	2/2022 (-) [10/2023]	927.77 (-) [1,603.00]	1,104.18 (675.23) [20]
1542	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW	10/2021	4/2024 (-) [4/2024]	227.06 (-) [227.06]	42.18 (0.00) [0]
1543	WIDENING AND STRENGTHENING FROM KM.15.000 TO KM, 58.600 (BHADEWARA -DRAMANDGANJ SECTION) OF NATIONAL	12/2021	5/2024 (-) [5/2024]	257.97 (-) [257.97]	68.81 (0.00) [0]
1544	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF	3/2020	9/2024 (-) [9/2024]	262.37 (-) [343.77]	72.28 (81.40) [0]
1545	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR)	3/2021	5/2024 (-) [5/2024]	395.62 (-) [395.62]	62.63 (0.00) [0]
	<u>Urban Development</u>				

1546	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [12/2025]	8,379.62 (-) [8,379.62]	2,611.47 (0.00) [21]
1547	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [6/2026]	11,076.48 (-) [11,076.48]	5,323.53 (0.00) [27]
	<u>Water Resources</u>				
1548	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (2/2021) [4/2024]	213.62 (261.12) [261.12]	69.96 (47.50) [25]
1549	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [3/2023]	206.05 (-) [206.05]	137.58 (0.00) [0]
1550	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (1/2020) [6/2023]	231.79 (234.03) [234.03]	94.19 (2.24) [0]
1551	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [3/2024]	271.39 (-) [271.39]	59.32 (0.00) [31]
1552	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (5/2020) [4/2024]	298.12 (-) [213.91]	36.94 (-84.21) [33]
1553	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	276.97 (0.00) [0]
1554	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (6/2018) [12/2020]	460.45 (-) [460.45]	295.23 (0.00) [0]
1555	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [4/2024]	681.78 (-) [690.71]	0.00 (8.93) [22]
1556	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2023]	967.23 (708.70) [967.23]	220.73 (0.00) [24]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1557	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2023]	456.86 (-) [456.86]	446.26 (0.00) [36]
	<u>Power</u>				
1558	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [8/2017]	1,527.00 (-) [1,527.00]	149.93 (0.00) [0]
1559	NAITWAR MORI HEP	10/2017	12/2021 (-) [8/2023]	648.33 (-) [1,272.29]	1,172.12 (623.96) [20]
1560	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2024]	2,978.48 (5,867.38) [7,103.00]	5,911.37 (4,124.52) [141]
1561	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (6/2022) [6/2024]	1,657.00 (-) [4,825.60]	5,601.35 (3,168.60) [100]
1562	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [6/2026]	2,491.58 (3,860.35) [3,860.35]	3,163.57 (1,368.77) [156]
	<u>Railways</u>				
1563	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [24,659.00]	14,020.06 (8,443.00) [3]
	<u>Road Transport And Highways</u>				
1564	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER	3/2018	11/2020 (12/2022)	403.36 (-)	328.94 (0.00)

	CHARDHAM PARI		[4/2024]	[403.36]	[41]
1565	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	11/2020 (12/2022) [4/2024]	417.24 (-) [417.24]	337.20 (0.00) [41]
1566	4-LANING OF KASHIPUR-SITARGANJ SECTION	11/2012	8/2016 (-) [8/2016]	605.84 (-) [605.84]	0.00 (0.00) [0]
1567	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2)	3/2022	2/2025 (-) [2/2025]	1,092.90 (1,092.90) [1,092.90]	0.03 (0.00) [0]
1568	4L OF HARIDWAR NAGINA SECTION DESIGN CH. LME FROM KM 13.829 TO KM 17.110 AND KM 26.077 TO KM 27.508	6/2020	2/2024 (-) [2/2024]	183.92 (-) [183.92]	20.62 (0.00) [0]
1569	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR – DEHRADUN SECTION FROM KM.	3/2021	3/2024 (3/2024) [3/2024]	169.08 (-) [169.08]	60.65 (0.00) [0]
1570	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	11/2020 (12/2022) [12/2023]	274.31 (-) [274.31]	240.98 (0.00) [37]
1571	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2022 (7/2022) [5/2024]	1,383.78 (-) [1,383.78]	542.67 (0.00) [22]
1572	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (12/2023) [12/2023]	248.00 (-) [248.00]	111.85 (0.00) [43]
1573	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	10/2019 (3/2024) [3/2024]	720.00 (810.60) [810.60]	348.45 (90.60) [53]
1574	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	151.70 (0.00) [0]
1575	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	196.03 (0.00) [0]
1576	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	156.63 (0.00) [0]
1577	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	141.39 (0.00) [0]
1578	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (3/2023) [3/2023]	282.08 (-) [282.08]	206.46 (0.00) [0]
1579	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (3/2023) [3/2023]	418.88 (-) [418.88]	264.67 (0.00) [0]
1580	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	153.44 (0.00) [0]
1581	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2017]	234.88 (-) [234.88]	174.51 (0.00) [0]
1582	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (4/2023) [4/2023]	293.68 (-) [293.68]	201.20 (0.00) [0]
1583	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1584	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF	8/2021	10/2024 (10/2024) [10/2024]	1,377.79 (1,384.11) [1,377.79]	678.86 (0.00) [0]
1585	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM	12/2017	12/2019 (-)	248.22 (-)	146.17 (0.00)

	KM. 235.00		[12/2019]	[248.22]	[0]
	<u>Water Resources</u>				
1586	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (-) [2/2022]	158.00 (-) [158.00]	98.88 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1587	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [5/2023]	389.71 (-) [389.71]	391.78 (0.00) [0]
1588	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (6/2022) [8/2023]	458.00 (-) [458.00]	218.86 (0.00) [41]
	<u>Coal</u>				
1589	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [12/2023]	304.13 (341.22) [341.22]	207.24 (37.09) [81]
1590	BONJEMEHARI EXPANSION OCP	8/2021	3/2025 (-) [3/2025]	570.12 (-) [570.11]	14.55 (-0.01) [0]
1591	EXPANSION PR OF JHANJRA UG (5.00 MTY)	4/2020	3/2029 (-) [3/2029]	1,210.12 (-) [1,210.12]	259.91 (0.00) [0]
1592	MOHANPUR EXPANSION OC PHASE II	11/2020	3/2025 (-) [3/2025]	888.99 (-) [888.99]	27.06 (0.00) [0]
1593	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	42.62 (0.00) [0]
1594	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (389.10) [389.10]	4.47 (-437.32) [0]
1595	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	713.53 (2,484.75) [60]
1596	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	21.68 (0.00) [0]
1597	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	3.33 (0.00) [0]
1598	SONEPUR BAZARI EXPANSION OC	7/2021	3/2029 (-) [3/2029]	5,365.88 (5,366.00) [5,365.88]	316.12 (0.00) [0]
1599	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (749.08) [749.08]	9.72 (-167.54) [0]
	<u>Department Of Higher Education</u>				
1600	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [7/2023]	193.83 (-) [193.83]	150.97 (0.00) [37]
	<u>Home Affairs</u>				
1601	NSG AT KOLKATA	10/2014	4/2018 (-) [12/2024]	162.88 (210.83) [210.83]	177.77 (47.95) [80]
	<u>Mines</u>				
1602	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	4/2019	4/2022 (-) [10/2025]	255.37 (-) [255.37]	37.77 (0.00) [42]
	<u>Petroleum</u>				
1603	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18	3/2018	9/2022 (6/2023)	3,712.00 (3,696.00)	2,852.90 (-16.00)

	INCH HAL		[12/2023]	[3,696.00]	[15]
1604	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS	3/2022	3/2030 (-) [3/2030]	609.00 (-) [609.00]	6.56 (0.00) [0]
1605	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (8/2031) [8/2031]	5,830.20 (-) [5,830.20]	414.68 (0.00) [5]
1606	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (6/2024) [6/2024]	1,740.00 (2,433.15) [2,433.15]	1,547.50 (693.15) [42]
1607	HALDIA PANAGARH PIPELINE PROJECT	11/2022	11/2025 (-) [11/2025]	1,010.00 (-) [1,010.00]	5.55 (0.00) [0]
1608	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (11/2023) [11/2023]	1,019.00 (-) [1,019.00]	658.96 (0.00) [10]
	<u>Power</u>				
1609	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (3/2023) [11/2023]	529.68 (633.80) [679.00]	560.81 (149.32) [60]
1610	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [9/2026]	1,381.84 (-) [1,803.00]	909.90 (421.16) [84]
	<u>Railways</u>				
1611	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (12/2023) [12/2023]	4,874.58 (8,574.98) [10,442.41]	8,008.94 (5,567.83) [93]
1612	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	355.80 (435.44) [141]
1613	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [7/2025]	2,913.51 (-) [4,834.54]	3,020.54 (1,921.03) [112]
1614	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [3/2016]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1615	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2026]	3,951.98 (-) [8,964.35]	5,943.37 (5,012.37) [120]
1616	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	4/2018	6/2022 (-) [2/2024]	338.00 (-) [393.83]	67.88 (55.83) [20]
1617	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2024]	1,188.91 (-) [1,619.48]	1,141.34 (430.57) [60]
	<u>Road Transport And Highways</u>				
1618	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (8/2023) [8/2023]	1,083.00 (1,414.01) [1,414.01]	1,059.61 (331.01) [62]
1619	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [12/2023]	998.79 (-) [998.79]	2,170.28 (0.00) [124]
1620	BALANCE 4 LANING WORK OF RAIGANJ DALKHOLA SECTION OF NH34 FROM KM 398.000 TO KM 452.750 (PACKAGE V)	12/2018	9/2021 (-) [12/2023]	1,548.07 (-) [1,548.07]	1,086.32 (0.00) [27]
1621	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA	8/2018	12/2021 (-) [12/2024]	622.04 (-) [622.04]	295.81 (0.00) [36]
1622	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (12/2023) [12/2023]	271.17 (291.20) [291.20]	151.50 (20.03) [61]
1623	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU	3/2016	9/2023	160.27	70.95

	OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND)		(3/2024) [6/2024]	(213.97) [213.97]	(53.70) [9]
1624	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	9/2021 (2/2024) [2/2024]	236.78 (263.26) [263.26]	163.40 (26.48) [29]
1625	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO)	3/2018	10/2020 (3/2024) [3/2024]	254.30 (254.30) [254.30]	171.67 (0.00) [41]
1626	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5	3/2022	9/2025 (9/2025) [9/2025]	995.04 (995.04) [995.04]	18.84 (0.00) [0]
1627	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272	12/2018	2/2023 (8/2023) [8/2023]	2,375.87 (2,566.80) [2,566.80]	2,299.14 (190.93) [6]
1628	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE	8/2021	8/2023 (-) [12/2023]	557.55 (-) [557.55]	393.31 (0.00) [4]
1629	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU	3/2018	9/2022 (12/2022) [3/2024]	841.57 (1,619.48) [1,619.48]	1,368.06 (777.91) [18]
1630	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (3/2023) [3/2023]	396.86 (-) [396.86]	325.22 (0.00) [0]
1631	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700	3/2020	9/2024 (-) [9/2024]	2,193.23 (2,314.00) [2,314.00]	1,191.60 (120.77) [0]
1632	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA	3/2021	9/2024 (-) [9/2024]	2,200.93 (-) [2,200.93]	1,255.60 (0.00) [0]
1633	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	9/2016 (-) [12/2023]	1,665.00 (-) [2,360.65]	4,657.47 (695.65) [87]
1634	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (12/2023) [12/2023]	426.18 (426.18) [426.18]	339.05 (0.00) [39]
	Water Resources				
1635	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (1/2023) [6/2022]	274.76 (332.56) [274.76]	267.15 (0.00) [0]
1636	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [12/2024]	384.96 (-) [384.96]	0.00 (0.00) [32]
1637	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [12/2024]	234.31 (-) [234.31]	0.00 (0.00) [32]
1638	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [3/2024]	165.16 (-) [165.16]	0.00 (0.00) [21]
1639	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (9/2020) [6/2024]	160.00 (154.73) [154.73]	56.61 (-5.27) [28]
1640	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [12/2024]	287.53 (-) [287.53]	0.00 (0.00) [32]
1641	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (2/2021) [3/2024]	164.93 (-) [164.93]	45.45 (0.00) [27]
1642	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [3/2024]	198.43 (224.69) [224.69]	32.86 (26.26) [25]
1643	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [12/2026]	307.12 (-) [653.67]	0.00 (346.55) [51]

1644	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (2/2021) [9/2023]	172.10 (-) [172.10]	47.20 (0.00) [21]
1645	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (2/2021) [8/2023]	185.22 (-) [185.22]	49.99 (0.00) [20]
1646	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [4/2020]	272.32 (341.68) [272.32]	298.49 (0.00) [0]
	Total			23,92,837.89 (7,62,556.44) [28,58,394.39]	15,21,550.38 (4,65,556.50)

List of Projects having cost overrun with respect to Anticipated/Cumulative Expenditure

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
1	ATOMIC ENERGY	BHAVNI	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	3,492.00	7,670.00	6,569.75	4,178.00
2	ATOMIC ENERGY	NPCIL	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	11,459.00	19,220.00	20,460.00	9,001.00
3	ATOMIC ENERGY	NPCIL	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	12,320.00	17,079.00	16,576.00	4,759.00
4	CIVIL AVIATION	AAI	CCS INTERNATIONAL AIRPORT , LUCKNOW	1,383.00	3,291.81	769.80	1,909.00
5	CIVIL AVIATION	AAI	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	1,142.00	1,232.00	365.49	90.00
6	COAL	NLC	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	5,907.11	8,990.00	7,656.86	3,083.00
7	COAL	NLC	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	17,237.00	19,406.12	15,652.81	2,169.00
8	COAL	ECL	RANIGANJ MASTER PLAN	2,661.73	5,146.48	713.53	2,485.00
9	DEPARTMENT OF HIGHER EDUCATION	CPWD EDUCATION	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	676.00	1,085.04	24.75	409.00
10	DPIIT	IICC FOR DPIIT	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	4,773.00	5,401.00	4,071.81	628.00
11	HOME AFFAIRS	CPWD FOR MHA	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	1,219.21	1,900.00	1,583.95	681.00
12	MINES	NALCO	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	4,103.00	5,055.00	2,259.22	952.00
13	PETROLEUM	ONGC	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	3,190.69	3,375.90	2,897.83	185.00
14	PETROLEUM	BPCL	IRUGUR-DEVANGONTHI POL PIPELINE	678.00	1,732.00	30.71	1,054.00
15	PETROLEUM	HPCL	VISAKH REFINERY MODERNISATION PROJECT	20,928.00	26,264.00	23,860.04	5,336.00
16	PETROLEUM	NRL	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	12,366.00	18,968.00	6,125.60	6,602.00
17	PETROLEUM	IOCL	R and D CAMPUS II AT FARIDABAD	2,281.94	3,219.94	1,122.50	938.00
18	PETROLEUM	ONGC	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	3,228.80	3,976.67	3,793.93	748.00
19	PETROLEUM	GAIL	BARAUNI-GUWAHATI PIPELINE	3,308.00	3,992.00	3,537.30	684.00
20	PETROLEUM	BPCL	KOCHI SALEM LPG PIPELINE PROJECT	1,112.00	1,507.24	1,094.66	395.00
21	PETROLEUM	GAIL	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	2,915.00	5,909.00	3,510.30	2,994.00
22	PETROLEUM	GAIL	DURGAPUR-HALDIA PIPELINE PROJECT	1,740.00	2,433.15	1,547.50	693.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
23	PETROLEUM	IOCL	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	4,497.00	6,025.00	5,303.14	1,528.00
24	PETROLEUM	IOCL	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	1,945.00	2,251.00	2,005.03	306.00
25	PETROLEUM	GAIL	60 KTA POLYPROPYLENE PROJECT	910.56	1,299.02	430.40	388.00
26	PETROLEUM	IOCL	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	1,398.00	1,587.00	726.79	189.00
27	PETROLEUM	ONGC	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	823.27	1,137.79	954.95	315.00
28	POWER	NHPC	PARBATI HEP (4X200 MW) (NHPC) II	3,919.59	11,134.54	10,807.99	7,215.00
29	POWER	NHPC	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	6,285.33	21,247.54	18,903.19	14,962.00
30	POWER	NTPC	RAMMAM-III HEPP (3X40 MW)	1,381.84	1,803.00	909.90	421.00
31	POWER	NTPC	NORTH KARANPURA STPP (3X660 MW)	14,366.58	17,007.00	14,880.63	2,640.00
32	POWER	NTPC	TAPOVAN-VISHNUGAD HEP (4X130MW)	2,978.48	7,103.00	5,911.37	4,125.00
33	POWER	THDCIL	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	3,860.35	3,163.57	1,369.00
34	POWER	NTPC	BARH STPP(3X660MW) NTPC	8,692.97	21,312.11	21,304.21	12,619.00
35	POWER	SJVN	BIKANER SOLAR POWER PROJECT	5,491.89	6,023.89	2,211.03	532.00
36	POWER	PGCIL	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C	1,326.00	1,326.00	1,367.92	42.00
37	POWER	SJVN	NAITWAR MORI HEP	648.33	1,272.29	1,172.12	624.00
38	POWER	PGCIL	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	1,931.39	2,635.55	1,952.75	704.00
39	POWER	PGCIL	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	5,111.33	6,700.00	4,578.01	1,589.00
40	POWER	PGCIL	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	4,754.42	9,129.32	5,600.77	4,375.00
41	POWER	NTPC	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	10,598.98	10,998.00	10,831.04	399.00
42	POWER	THDCIL	TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	4,825.60	5,601.35	3,944.00
43	RAILWAYS	SCR	KOTLPALLI-NARASAPUR (NL) (SCR)	1,045.20	2,500.98	1,129.92	1,456.00
44	RAILWAYS	ER	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	1,188.91	1,619.48	1,141.34	431.00
45	RAILWAYS	WCR	RAMGANJMUNDI-BHOPAL (NL),WCR	424.60	3,032.46	2,080.00	2,608.00
46	RAILWAYS	ECOR	TALCHER-BIMALAGARH(NL)(ECOR)	810.78	1,928.07	980.13	1,117.00
47	RAILWAYS	SR	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	724.69	3,118.34	1,877.71	2,394.00
48	RAILWAYS	SR	TIDIVANAM-NAGARI (NL)	582.83	3,620.28	758.81	3,037.00
49	RAILWAYS	NFR	BHAIRABI SAIRONG, NL, NEFR	2,393.47	9,362.06	6,591.01	6,969.00
50	RAILWAYS	ECR	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	528.65	2,066.78	1,822.92	1,538.00
51	RAILWAYS	SCR	MANOHARABAD-KOTHPALL NEW LINE(SCR)	1,160.48	3,014.00	1,071.53	1,854.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
52	RAILWAYS	RVNL	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	2,913.51	4,834.54	3,020.54	1,921.00
53	RAILWAYS	WR	RATLAM-MHOW-KHANDWA-AKOLA (GC)	3,503.69	6,021.00	2,919.74	2,517.00
54	RAILWAYS	CR	WARDHA-NANDED MAHARASHTRA	3,168.29	3,445.48	1,666.35	277.00
55	RAILWAYS	SWR	BAGALKOT-KUDACHI NL	986.30	1,649.31	363.80	663.00
56	RAILWAYS	SCR	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	1,856.95	1,952.68	1,533.64	96.00
57	RAILWAYS	RVNL	BHANUPALI-BILASPUR BERI NL	2,966.99	6,753.42	3,955.01	3,786.00
58	RAILWAYS	NFR	MURKONGSELEK-PASIGHAT NL	414.84	1,187.49	349.63	773.00
59	RAILWAYS	NFR	NEW BG LINE FROM BYRNIHAT TO SHILLONG	906.46	8,324.28	269.80	7,418.00
60	RAILWAYS	NFR	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	1,798.00	2,647.51	1,999.72	850.00
61	RAILWAYS	ECR	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	372.14	1,700.00	2,044.95	1,673.00
62	RAILWAYS	NCR	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	2,912.96	3,845.60	1,024.32	933.00
63	RAILWAYS	WR	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	1,640.04	1,873.10	1,136.95	233.00
64	RAILWAYS	WR	CHOTTAUDEPUR-DHAR(NL)	1,347.26	1,793.63	1,222.16	446.00
65	RAILWAYS	M RTP	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	4,874.58	10,442.41	8,008.94	5,568.00
66	RAILWAYS	ECOR	SAMBALPUR-TALCHER DOUBLING	1,111.99	1,539.28	1,152.38	427.00
67	RAILWAYS	DFCC	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	11,589.00	51,219.00	31,304.00	39,630.00
68	RAILWAYS	ER	PIRPAINTI-JASIDIH	915.98	2,137.81	980.46	1,222.00
69	RAILWAYS	SR	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	120.70	2,053.39	328.43	1,933.00
70	RAILWAYS	SWR	RAYADURGA-TUMKUR NL	2,062.30	2,404.03	1,161.58	342.00
71	RAILWAYS	SCR	NADIKUDE-SRI KALAHASTI	2,288.70	3,122.35	1,267.65	834.00
72	RAILWAYS	RVNL	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	2,127.00	3,300.00	3,204.74	1,173.00
73	RAILWAYS	CR	AHMEDNAGAR-PARLI VAJNATH(NL) CR	2,271.50	4,805.17	3,491.85	2,534.00
74	RAILWAYS	WCR	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	247.66	8,248.50	2,427.33	8,001.00
75	RAILWAYS	ECR	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	324.73	1,110.00	1,165.40	841.00
76	RAILWAYS	ECOR	KHURDA ROAD-BOLANGIR(NL)ECOR	2,923.13	3,791.66	2,904.31	869.00
77	RAILWAYS	NFR	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4,454.17	14,322.79	13,763.33	9,869.00
78	RAILWAYS	DFCC	WESTERN DEDICATED FREIGHT CORRIDOR	16,592.00	51,101.00	47,476.00	34,509.00
79	RAILWAYS	RVNL	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	760.00	1,536.00	1,846.81	1,087.00
80	RAILWAYS	RVNL	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	943.60	1,500.00	1,251.40	556.00
81	RAILWAYS	SR	TURAVUR-AMBALAPUZHA DOUBLING	1,000.00	1,339.00	.93	339.00
82	RAILWAYS	SR	TRIVANDRUM-KANYAKUMARI DOUBLING	1,431.90	1,431.90	2,095.35	663.00
83	RAILWAYS	SER	BONDAMUNDA RANCHI DOUBLING	1,724.20	3,029.04	1,693.74	1,305.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
84	RAILWAYS	SCR	KAZIPET-BALHRSHA	2,063.03	2,909.00	2,355.36	846.00
85	RAILWAYS	NFR	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	2,232.32	4,059.65	2,898.81	1,827.00
86	RAILWAYS	RVNL	VIJAYAWADA-GUDUR	3,246.26	3,548.68	5,013.33	1,767.00
87	RAILWAYS	SCR	GUNTUR-GUNTAKAL	3,631.00	3,887.48	2,728.66	256.00
88	RAILWAYS	CR	DAUND - MANMAD (236 KM)	1,876.00	2,081.27	1,335.69	205.00
89	RAILWAYS	IRCON	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	3,055.00	3,438.39	2,976.72	383.00
90	RAILWAYS	SECR	ANUPPUR-KATNI	1,370.00	1,680.00	1,171.79	310.00
91	RAILWAYS	SECR	JHARSUGUDA-BILASPUR 4TH LINE	1,973.00	2,135.34	1,488.70	162.00
92	RAILWAYS	SECR	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	229.00	1,096.00	230.25	867.00
93	RAILWAYS	ECR	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	329.39	1,510.00	2,102.69	1,773.00
94	RAILWAYS	ECR	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	731.64	1,185.73	965.84	454.00
95	RAILWAYS	ECR	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	744.04	1,215.54	950.34	472.00
96	RAILWAYS	NER	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	1,177.96	1,500.95	1,119.47	323.00
97	RAILWAYS	NR	CHANDIGARH-BADDI	328.14	1,540.14	482.67	1,212.00
98	RAILWAYS	RVNL	MATHURA-JHANSI-3RD LINE (273.80 KM)	3,677.76	3,677.76	4,306.50	629.00
99	RAILWAYS	SECR	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	1,908.51	3,544.25	2,238.21	1,636.00
100	RAILWAYS	ECR	RAMNA - SINGRAULI DOUBLING	2,436.21	2,436.21	2,445.51	9.00
101	RAILWAYS	WCR	KATNI GRADE SEPARATOR/BYE PASS	582.13	1,247.64	990.59	666.00
102	RAILWAYS	WCR	KATNI-BINA 3RD LINE (263 KM)	2,478.23	2,938.00	1,279.35	460.00
103	RAILWAYS	RVNL	BANASPANI- JAKHPURA - DOUBLING	942.95	1,552.26	1,772.12	829.00
104	RAILWAYS	RVNL	VIZIANAGARAM -SAMABALPUR 3RD LINE	2,335.67	3,327.72	3,674.36	1,339.00
105	RAILWAYS	RVNL	RISHIKESH - KARNAPRAYAG NEW LINE	16,216.00	24,659.00	14,020.06	8,443.00
106	RAILWAYS	RVNL	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	927.01	1,457.79	1,491.77	565.00
107	RAILWAYS	CR	PUNE-MIRAJ-LONDA (467 KM)	3,627.47	6,409.38	2,826.85	2,782.00
108	RAILWAYS	CR	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	1,272.19	1,384.72	757.06	113.00
109	RAILWAYS	WCR	KATNI - SINGRAULI DOUBLING PROJECT	1,763.93	2,445.30	2,020.86	681.00
110	RAILWAYS	ECR	KIUL - GAYA DOUBLING PROJECT	1,200.20	1,200.20	1,346.62	146.00
111	RAILWAYS	NER	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	1,295.42	2,560.00	2,121.53	1,265.00
112	RAILWAYS	ECR	KODERMA-TILAIYA (NL), ECR	459.91	1,625.87	1,323.75	1,166.00
113	RAILWAYS	SWR	HOTGI-KUDGI-GADAG	1,614.59	1,960.00	1,887.40	345.00
114	RAILWAYS	ECOR	KIRANDUL - JAGDALPUR DOUBLING	1,160.00	1,440.00	1,058.66	280.00
115	RAILWAYS	NFR	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	385.20	1,304.62	1,104.78	919.00
116	RAILWAYS	NFR	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	532.87	2,650.00	1,761.52	2,117.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
117	RAILWAYS	NFR	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	2,326.52	6,663.00	2,556.74	4,336.00
118	RAILWAYS	NFR	SEVOK RANGPO, NEFR	1,339.48	7,876.92	3,290.96	6,537.00
119	RAILWAYS	NR	NANGALDAM-TALWARA(NL),NR	450.00	2,017.96	845.23	1,568.00
120	RAILWAYS	NR	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	2,500.00	37,012.26	36,017.83	34,512.00
121	RAILWAYS	RVNL	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	3,951.98	8,964.35	5,943.37	5,012.00
122	RAILWAYS	RVNL	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	2,298.42	2,733.86	355.80	435.00
123	RAILWAYS	SCR	MUNEERABAD-MAHABOBNAGAR(NL),SCR	1,723.00	3,381.68	2,532.11	1,659.00
124	RAILWAYS	SWR	HUBLI-ANKOLA(NL),SWR	2,315.00	5,174.30	159.49	2,859.00
125	RAILWAYS	WR	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	318.24	1,095.12	201.24	777.00
126	ROAD TRANSPORT AND HIGHWAYS	NHAI	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	946.00	1,046.56	827.99	101.00
127	ROAD TRANSPORT AND HIGHWAYS	NHAI	VARANASI-AURANGABAD KM.786 TO KM.978.40	2,848.00	3,379.45	3,656.21	808.00
128	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	1,047.00	1,047.00	1,855.00	808.00
129	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	1,655.01	2,639.00	1,771.52	984.00
130	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	2,136.97	2,136.97	2,362.99	226.00
131	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	998.70	1,358.32	785.96	360.00
132	ROAD TRANSPORT AND HIGHWAYS	NHAI	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	1,226.88	1,569.68	1,054.39	343.00
133	ROAD TRANSPORT AND HIGHWAYS	NHAI	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	1,047.00	1,047.00	1,169.00	122.00
134	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	1,094.97	1,094.97	1,188.00	93.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
135	ROAD TRANSPORT AND HIGHWAYS	MoRTH	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	1,979.00	2,036.90	1,253.04	58.00
136	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	2,159.00	2,262.00	2,212.19	103.00
137	ROAD TRANSPORT AND HIGHWAYS	MoRTH	KALMATH TO ZARAP	1,338.13	1,338.13	1,346.39	8.00
138	ROAD TRANSPORT AND HIGHWAYS	MoRTH	INDAPUR TO VADPALE	1,202.52	1,202.52	1,450.82	248.00
139	ROAD TRANSPORT AND HIGHWAYS	NHIDCL	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	642.96	1,139.85	528.71	497.00
140	ROAD TRANSPORT AND HIGHWAYS	NHAI	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT	2,948.31	3,392.00	506.57	444.00
141	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN	1,225.24	1,676.11	14.76	451.00
142	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0	1,331.77	2,508.79	60.90	1,177.00
143	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100	1,065.06	1,577.92	26.31	513.00
144	ROAD TRANSPORT AND HIGHWAYS	NHAI	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66	3,219.47	3,713.14	1,911.28	494.00
145	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH	3,375.31	3,790.17	1,745.63	415.00
146	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM	4,265.42	4,708.42	2,751.50	443.00
147	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX.	2,595.00	3,994.60	2,696.56	1,400.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
148	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH – 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX	3,606.00	3,923.82	2,789.91	318.00
149	ROAD TRANSPORT AND HIGHWAYS	NHAI	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF	1,322.95	1,442.47	498.17	120.00
150	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHAKUR LOHA SECTION OF NH-361 FROM KM 114.600 TO KM 187.80	1,241.38	2,122.64	1,577.64	881.00
151	ROAD TRANSPORT AND HIGHWAYS	NHAI	4L OF AUSA-CHAKUR SECTION FROM KM 55.835 TO KM 114.345 OF NH-361	1,169.04	1,693.95	1,010.33	525.00
152	ROAD TRANSPORT AND HIGHWAYS	NHAI	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J	1,166.96	1,251.00	755.96	84.00
153	ROAD TRANSPORT AND HIGHWAYS	NHAI	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B	1,013.33	1,111.33	202.73	98.00
154	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA	1,710.30	1,927.00	265.19	217.00
155	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU	2,271.86	3,916.00	426.80	1,644.00
156	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU	1,259.00	1,910.00	60.25	651.00
157	ROAD TRANSPORT AND HIGHWAYS	NHAI	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O	2,067.67	2,160.00	1,496.49	92.00
158	ROAD TRANSPORT AND HIGHWAYS	NHAI	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1)	922.50	1,128.68	435.46	206.00
159	ROAD TRANSPORT AND HIGHWAYS	NHAI	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81	927.77	1,603.00	1,104.18	675.00
160	ROAD TRANSPORT AND HIGHWAYS	NHAI	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP	1,863.09	2,238.00	894.15	375.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
161	ROAD TRANSPORT AND HIGHWAYS	NHAI	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE	1,075.27	1,307.00	384.53	232.00
162	ROAD TRANSPORT AND HIGHWAYS	NHAI	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP	1,137.74	1,289.00	321.70	151.00
163	ROAD TRANSPORT AND HIGHWAYS	NHAI	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I)	1,484.83	1,768.00	383.07	283.00
164	ROAD TRANSPORT AND HIGHWAYS	NHAI	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III)	1,102.63	1,303.00	212.43	200.00
165	ROAD TRANSPORT AND HIGHWAYS	NHAI	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV)	818.73	1,105.00	73.20	286.00
166	ROAD TRANSPORT AND HIGHWAYS	NHAI	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154)	1,002.11	1,358.00	28.69	356.00
167	ROAD TRANSPORT AND HIGHWAYS	NHAI	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21)	2,507.00	3,030.73	1,155.70	524.00
168	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH	1,936.68	2,458.03	1,380.90	521.00
169	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272	2,375.87	2,566.80	2,299.14	191.00
170	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700	2,193.23	2,314.00	1,191.60	121.00
171	ROAD TRANSPORT AND HIGHWAYS	NHAI	LUCKNOW RING ROAD PKG-1 (SULTANPUR ROAD TO BEHTA ROAD) [BYPASS CONNECTING NH-56 AT KM. 17.40 AND TER	1,916.38	2,078.00	1,158.54	162.00
172	ROAD TRANSPORT AND HIGHWAYS	NHAI	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U	1,779.83	2,200.00	708.00	420.00
173	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000	1,008.99	1,361.00	12.42	352.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
174	ROAD TRANSPORT AND HIGHWAYS	NHAI	BANGALORE CHENNAI EXPRESSWAY PHASE-III – PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1	1,023.91	1,285.00	318.78	261.00
175	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANE OF BILASPUR TO URGU PROJECT (KM 0.00 TO KM 70.2) OF NH-130A	1,855.59	1,869.85	187.36	14.00
176	ROAD TRANSPORT AND HIGHWAYS	NHAI	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH	1,034.00	1,589.00	41.50	555.00
177	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98	755.26	1,039.00	385.01	284.00
178	ROAD TRANSPORT AND HIGHWAYS	NHAI	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4	1,821.72	1,917.32	248.20	96.00
179	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP	1,690.23	2,010.17	1,067.66	320.00
180	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	1,872.68	2,756.09	848.82	883.00
181	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	2,120.40	2,565.63	1,147.79	445.00
182	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER	1,294.47	1,588.40	605.20	294.00
183	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	1,005.08	1,073.10	699.05	68.00
184	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	478.74	1,136.83	1,016.30	658.00
185	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	1,162.92	1,182.87	160.20	20.00
186	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	1,484.30	2,182.41	1,219.02	698.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
187	ROAD TRANSPORT AND HIGHWAYS	NHAI	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	1,161.39	1,404.00	396.76	243.00
188	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1,251.11	1,361.00	563.93	110.00
189	ROAD TRANSPORT AND HIGHWAYS	NHAI	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	950.69	1,108.00	1,679.45	729.00
190	ROAD TRANSPORT AND HIGHWAYS	MoRTH	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1,408.85	2,138.16	1,560.46	729.00
191	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00	1,408.00	1,659.12	1,115.46	251.00
192	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	899.00	1,381.45	939.15	482.00
193	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	1,587.49	3,063.99	2,938.25	1,477.00
194	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	1,396.74	1,396.74	3,738.01	2,341.00
195	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX-LANING OF BARWA ADDA-PANAGARH	1,665.00	2,360.65	4,657.47	2,992.00
196	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	1,167.45	1,182.94	589.65	15.00
197	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	667.00	3,006.53	3,022.15	2,355.00
198	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1,027.53	2,628.31	2,615.85	1,601.00
199	ROAD TRANSPORT AND HIGHWAYS	NHAI	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU	841.57	1,619.48	1,368.06	778.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
200	ROAD TRANSPORT AND HIGHWAYS	NHAI	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	1,424.77	1,862.77	465.92	438.00
201	ROAD TRANSPORT AND HIGHWAYS	NHAI	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	999.00	1,152.70	339.23	154.00
202	ROAD TRANSPORT AND HIGHWAYS	NHAI	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	686.65	1,015.16	355.84	329.00
203	ROAD TRANSPORT AND HIGHWAYS	NHAI	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	953.09	1,014.08	731.39	61.00
204	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF THALSERRY -MAHE BYPASS	1,124.11	1,503.86	1,405.49	380.00
205	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	950.64	1,168.33	729.78	218.00
206	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	1,059.73	1,071.00	837.73	11.00
207	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	744.64	1,007.00	257.01	262.00
208	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	1,083.00	1,414.01	1,059.61	331.00
209	STEEL	NMDC	NMDC INTEGRATED STEEL PLANT	15,525.00	23,840.00	23,131.35	8,315.00
210	STEEL	NMDC	SCREENING PLANT-III AT KIRANDUL	2,092.97	2,221.86	704.51	129.00
211	TELECOMMUNICATIONS	DOT	NETWORK FOR SPECTRUM	13,334.00	13,334.00	21,913.00	8,579.00
212	URBAN DEVELOPMENT	KMRCL	KOCHI METRO RAIL PROJECT	5,181.79	6,218.14	6,059.17	1,036.00
213	URBAN DEVELOPMENT	MEGA	AHMEDABAD METRO RAIL PROJECT PHASE 1	10,773.00	12,925.22	11,786.54	2,152.00
214	URBAN DEVELOPMENT	PATNA METRO RAI	PATNA METRO RAIL CORPORATION LIMITED	13,365.77	13,925.50	1,353.32	560.00
215	URBAN DEVELOPMENT	MMRC	PUNE METRO RAIL PROJECT (PHASE 1)	11,420.00	13,656.22	10,829.00	2,236.00
216	URBAN DEVELOPMENT	CMRL	CHENNAI METRO RAIL LTD (PHASE 1)	14,600.00	18,380.00	17,619.68	3,780.00
217	URBAN DEVELOPMENT	DMRC	DELHI MRTS PHASE-III	38,585.00	40,180.91	40,217.45	1,632.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
218	URBAN DEVELOPMENT	MMRCL	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	23,136.00	37,276.00	24,123.86	14,140.00
219	WATER RESOURCES	PPA	POLAVARAM IRRIGATION PROJECT	10,151.04	55,548.87	21,727.98	45,398.00
			TOTAL	6,57,217.05	11,19,232.13	8,04,256.00	4,84,514.00
