



Government of India
Ministry of Statistics and
Programme Implementation



OCMS
Ministry of Statistics & Programme Implementation

471st — Flash Report on Central Sector Infrastructure Projects —



(Rs. 150 crore & above)

January 2025

CONTENTS

Synopsis	1-2
List of Tables	3-235
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-6
Table:-3. Project List: Completed during January 2025.....	7-9
Table:-4. Project List: Added during January 2025.....	10-12
Table:-5. Project List: Frozen/Deleted during January 2025.....	13-13
Table:-6. Project List: Ongoing Projects of North-East Region.....	14-37
Table:-7. Project List: Ongoing Projects as of 31st January 2025.....	38-235

SYNOPSIS

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects
(1719, ₹25,94,280.08 crore)

Mega*
(601 projects,
₹ 20,93,998.28
crore)

Major*
(1118 projects,
₹ 5,00,281.8
crore)

**Completed[@]
projects
during January
2025**
(20 projects,
₹ 24658.82
crore)


**Newly Added/
elevated\$
Projects during
January 2025**
(17 projects,
₹ 60646.63
crore)

Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
other Indicated legends are in format (Project count, Original Cost)


* Mega Project if having original cost >= 1000 crore

* Major Project if original cost < 1000 crore

\$ reported Anticipated cost more than 150 crore

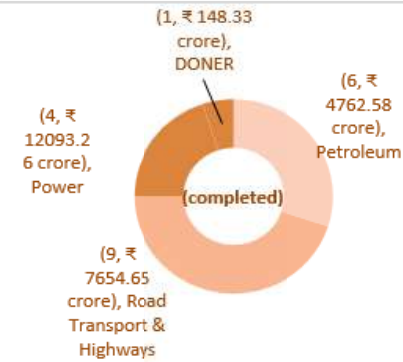

Note: all indicated legends are in format (Project count, Cumulative expenditure)

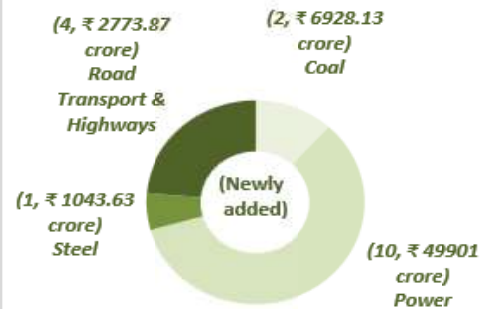


Note: all indicated legends are in format (Project count, Original Cost)

Total North East Region Ongoing Projects
(210, ₹ 176,103.72 crore)


Mega*
(22 projects,
Rs. 99,317.61
crore)

Major*
(188 projects,
Rs. 76,786.11
crore)


Cost and Expenditure Details
(Amount in ₹ Crore)

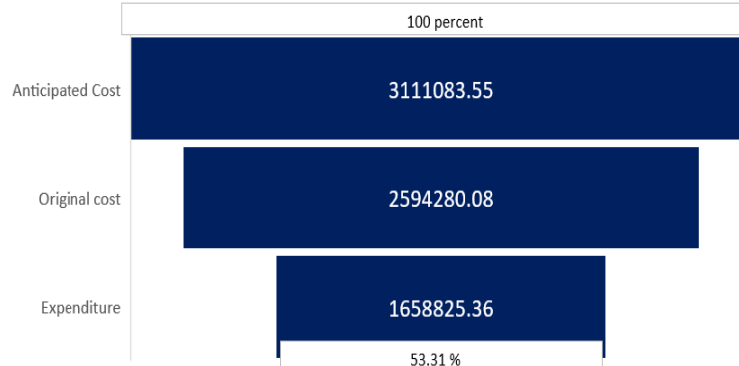


Project Volume (nos.)

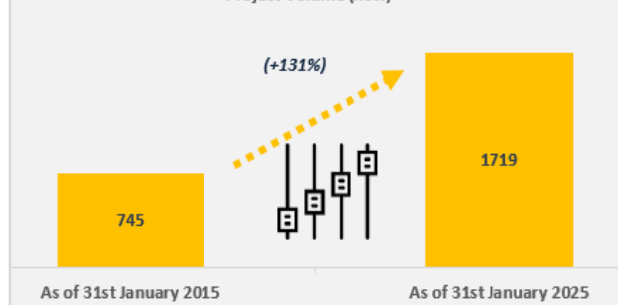


Total Project Value (in crore)

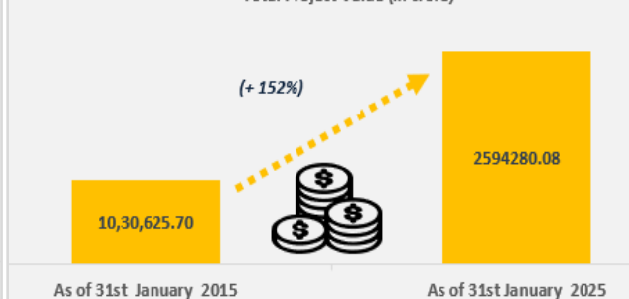

Cumulative Expenditure (in crore)

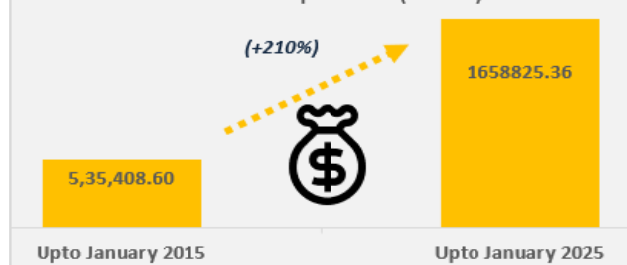


State Comparison : Major States (as per count)
 [Outer Ring:Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

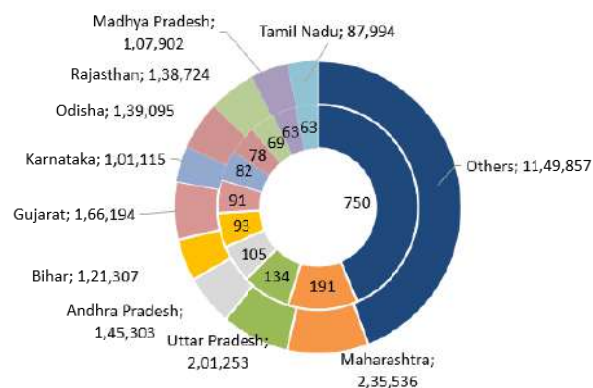


*Others include Jharkhand, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Assam, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N

Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

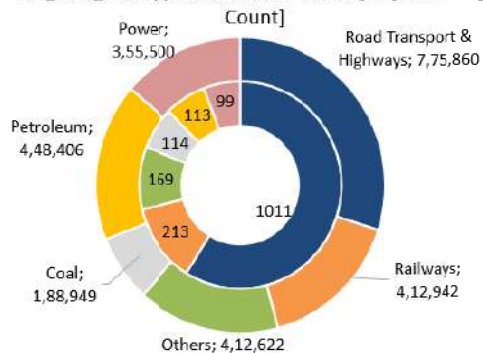

*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

Sectoral Distribution of total 637 projects with reported Physical Progress between 80-100%

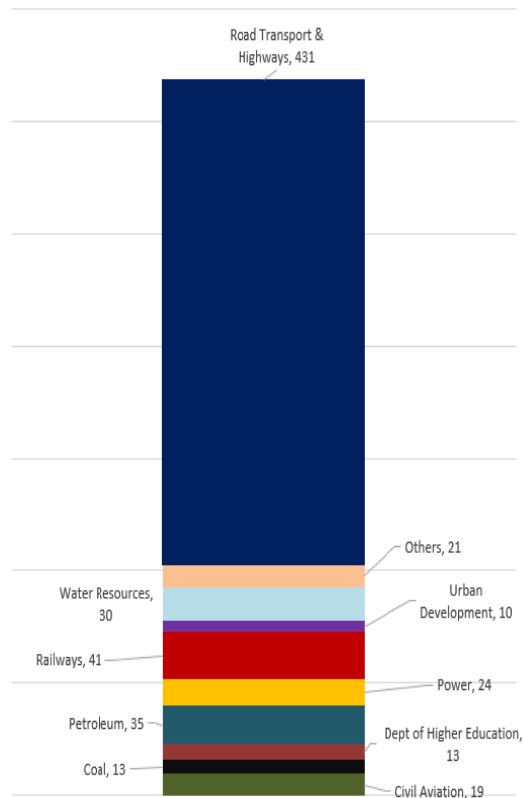

Note: This report is as of January 2025, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th February 2025.

A decorative frame with scrollwork at the top-left and bottom-left corners, enclosing the title.

LIST OF TABLES

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	41	28,039.58 (28,969.70) {32,092.62}	17,418.50
2	COAL	114	188,949.00 (193,493.04) {199,313.43}	71,034.65
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,076.78) {10,127.07}	7,558.10
4	DPIIT	2	24,857.00 (24,857.00) {25,485.00}	16,112.62
5	FINANCE	2	577.27 (577.27) {569.04}	399.67
6	HEALTH AND FAMILY WELFARE	8	7,301.27 (7,358.40) {7,356.19}	4,763.37
7	HOME AFFAIRS	5	2,025.73 (2,949.25) {2,949.25}	2,442.30
8	MINES	8	7,559.78 (9,356.73) {9,833.57}	5,602.74
9	PETROLEUM	113	448,405.74 (506,031.62) {516,773.47}	2,58,546.15
10	POWER	99	355,500.36 (373,176.19) {433,145.67}	2,12,248.25
11	RAILWAYS	213	412,942.26 (532,137.68) {650,651.33}	4,30,027.36
12	ROAD TRANSPORT AND HIGHWAYS	1011	775,860.29 (809,656.64) {819,224.22}	3,99,010.93
13	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,258.79
14	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80
15	STEEL	13	12,381.62 (16,313.15) {16,313.15}	6,580.14
16	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	7,425.01
17	URBAN DEVELOPMENT	27	265,881.46 (272,720.33) {286,578.30}	1,86,971.98

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
18	WATER RESOURCES	35	21,815.94 (21,770.16) {68,489.21}	29,351.00
	Total	1719	2,594,280.08 (2,841,625.97) {3,111,083.55}	16,58,825.36

***Either Revised or Original Cost**

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	10	2,956.02 (3,029.18) {3,010.04}	1,799.41
2	ANDHRA PRADESH	105	145,302.56 (155,482.89) {208,744.60}	1,23,519.92
3	ARUNACHAL PRADESH	19	46,132.10 (46,195.63) {66,045.78}	31,582.32
4	ASSAM	61	64,150.38 (64,272.17) {73,813.13}	45,376.16
5	BIHAR	93	121,307.33 (138,999.85) {149,855.33}	95,011.45
6	CHHATTISGARH	53	82,054.75 (86,111.52) {88,733.15}	37,723.69
7	DELHI	25	92,085.93 (97,627.29) {96,356.97}	75,486.48
8	GOA	4	1,526.58 (1,526.58) {1,613.08}	766.80
9	GUJARAT	91	166,194.29 (173,061.38) {175,601.48}	80,753.84
10	HARYANA	28	66,918.90 (76,247.06) {76,298.65}	36,491.35
11	HIMACHAL PRADESH	29	27,974.61 (29,004.29) {45,336.39}	30,160.25
12	JAMMU AND KASHMIR	54	75,963.99 (111,538.56) {118,249.03}	76,545.85
13	JHARKHAND	62	103,211.49 (108,413.39) {111,861.34}	62,553.97
14	KARNATAKA	82	101,114.55 (103,541.49) {105,198.47}	47,973.97
15	KERALA	32	63,946.16 (69,477.13) {70,321.90}	32,952.05
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	1,201.32
17	MADHYA PRADESH	63	107,901.94 (113,434.23) {123,039.48}	40,304.47
18	MAHARASHTRA	191	235,536.06 (240,039.88) {271,237.40}	1,33,724.51

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
19	MANIPUR	31	15,322.05 (23,178.11) {30,385.58}	18,942.82
20	MEGHALAYA	14	5,877.44 (5,868.46) {5,822.82}	3,322.63
21	MIZORAM	20	11,677.77 (16,810.85) {20,243.12}	16,259.30
22	MULTI STATE	53	284,355.68 (330,230.20) {348,888.78}	2,36,409.28
23	NAGALAND	31	11,425.91 (17,111.27) {16,810.24}	8,311.68
24	ODISHA	78	139,095.04 (142,243.81) {150,821.07}	62,733.79
25	PUNJAB	39	37,885.48 (38,173.84) {38,262.08}	14,746.53
26	RAJASTHAN	69	138,723.59 (166,903.54) {167,944.46}	86,127.98
27	SIKKIM	21	14,334.80 (25,524.43) {26,384.72}	17,305.76
28	TAMIL NADU	63	87,994.38 (96,955.60) {102,734.23}	26,781.18
29	TELANGANA	52	28,645.95 (29,039.83) {30,970.34}	14,924.98
30	TRIPURA	13	7,183.27 (7,220.16) {7,305.64}	1,045.52
31	UTTAR PRADESH	134	201,253.25 (208,040.88) {222,829.56}	1,08,321.50
32	UTTARAKHAND	33	36,921.91 (42,146.02) {64,262.80}	44,502.95
33	WEST BENGAL	60	66,830.95 (71,701.48) {89,467.25}	45,161.65
	Total	1719	2,594,280.08 (2,841,625.97) {3,111,083.55}	16,58,825.36

***Either Revised or Original Cost**

Table:-3. Project List: Completed during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
DONER					
	1	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103) (MEGHALAYA)	151.33	09/2017	148.33
PETROLEUM					
	2	Fuel Quality Upgradation Project at Paradip Refinery (IOCL) (N16000362) (ODISHA)	3,361.00	08/2021	2,727.60
	3	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY (IOCL) (N16000368) (ODISHA)	427.10	09/2022	312.13
	4	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAU DISTRICTS (IOCL) (N16000489) (RAJASTHAN)	575.00	03/2030	124.37
	5	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS (IOCL) (N16000490) (TAMIL NADU)	1,328.00	03/2030	149.21
	6	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS (IOCL) (N16000492) (TAMIL NADU)	1,295.00	03/2030	145.61
	7	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI (IOCL) (N16000405) (TAMIL NADU)	1,398.00	12/2023	1,303.66
POWER					
	8	ANTA SOLAR 90 MW (NTPC) (N18000292) (RAJASTHAN)	382.22	03/2022	497.17

Table:-3. Project List: Completed during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	CHHATTARGARH 150 MW (NTPC) (N18000294) (RAJASTHAN)	599.99	07/2022	599.99
	10	DURGAPUR PP-III (2X20 MW) - NSPCL (NTPC) (N18000277) (WEST BENGAL)	529.68	11/2018	558.39
	11	TELANGANA SUPER THERMAL POWER PROJECT PHASE I (NTPC) (N18000212) (TELANGANA)	10,598.98	11/2020	10,437.71
ROAD TRANSPORT AND HIGHWAYS					
	12	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P (NHAI) (N24000835) (HARYANA)	1,484.30	12/2020	1,376.15
	13	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N (MoRTH) (N24000887) (WEST BENGAL)	236.78	09/2021	232.54
	14	2L+PS OF THIKRI ANJAD SECTION OF NH-347B (MoRTH) (N24000892) (MADHYA PRADESH)	249.05	07/2018	221.19
	15	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH ? 14 (NHAI) (N24001185) (UTTAR PRADESH)	2,159.00	07/2021	3,110.50
	16	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352) (MANIPUR)	259.31	12/2022	144.94
	17	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 (MoRTH) (N24001463) (UTTAR PRADESH)	294.84	07/2024	303.27

Table:-3. Project List: Completed during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	18	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) (NHAI) (N24001780) (HARYANA)	2,228.00	11/2020	1,628.60
	19	MULAKALACHERUVU TO MADANAPALLE SECTION OF NH42 FROM KM 202.050 TO KM 245.640 EXCLUDING RETAINED STRE (MoRTH) (N24001933) (ANDHRA PRADESH)	480.10	12/2024	443.87
	20	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248) (ASSAM)	208.84	04/2022	193.59
		Total	28,246.52		24,658.82

Table:-4. Project List: Added during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
COAL	1	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285) (ODISHA)	11-2022	1,561.85 (N.A.) {1,561.85}	3/2029 (N.A.) {3/2029}
	2	BHUBANESWARI EXPANSION OCP (MCL) (N06000286) (ODISHA)	3-2024	5,366.28 (N.A.) {5,366.28}	3/2031 (N.A.) {3/2031}
POWER	3	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396) (RAJASTHAN)	8-2024	369.00 (N.A.) {369.00}	2/2026 (N.A.) {2/2026}
	4	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397) (RAJASTHAN)	8-2024	1,382.00 (N.A.) {1,382.00}	8/2026 (N.A.) {8/2026}
	5	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398) (GUJARAT)	10-2024	329.00 (N.A.) {329.00}	7/2026 (N.A.) {7/2026}
	6	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399) (MADHYA PRADESH)	10-2024	3,674.00 (N.A.) {3,674.00}	10/2026 (N.A.) {10/2026}
	7	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400) (GUJARAT)	10-2024	4,766.00 (N.A.) {4,766.00}	10/2026 (N.A.) {10/2026}
	8	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401) (RAJASTHAN)	11-2024	2,735.00 (N.A.) {2,735.00}	11/2026 (N.A.) {11/2026}

Table:-4. Project List: Added during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	9	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402) (GUJARAT)	11-2024	501.00 (N.A.) {501.00}	11/2026 (N.A.) {11/2026}
	10	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX] (PGCIL) (N18000403) (RAJASTHAN)	11-2024	5,969.00 (N.A.) {5,969.00}	11/2026 (N.A.) {11/2026}
	11	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE] (PGCIL) (N18000404) (RAJASTHAN)	11-2024	5,357.00 (N.A.) {5,357.00}	11/2026 (N.A.) {11/2026}
	12	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405) (GUJARAT)	11-2024	24,819.00 (N.A.) {24,819.00}	5/2029 (N.A.) {5/2029}
ROAD TRANSPORT AND HIGHWAYS	13	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA- CHOWKIBAL-TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210) (JAMMU AND KASHMIR)	3-2024	1,404.94 (N.A.) {1,404.94}	5/2027 (N.A.) {5/2027}
	14	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211) (UTTAR PRADESH)	1-2022	296.02 (N.A.) {296.02}	1/2027 (N.A.) {1/2027}
	15	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212) (UTTAR PRADESH)	3-2023	371.89 (N.A.) {371.89}	7/2026 (N.A.) {7/2026}
	16	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213) (UTTAR PRADESH)	3-2023	701.02 (N.A.) {701.02}	7/2026 (N.A.) {7/2026}

Table:-4. Project List: Added during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>STEEL</u>	17	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136) (KARNATAKA)	9-2023	1,043.63 (N.A.) {1,043.63}	8/2026 (N.A.) {8/2026}
<u>Grand Total</u>				60,646.63 (-) {60,646.63}	

Table:-5. Project List: Frozen/Deleted during January 2025

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
COAL						
	1	BHUBANESWARI EXPANSION OCP (MCL) (N06000227) (ODISHA)	6,321.73	03/2031	1,354.15	18.2
	2	RPR OF HINGULA -II EXPANSION PH-III (MCL) (N06000261) (ODISHA)	2,264.68	03/2029	1,054.83	39.2
		Total	8,586.41		2,408.98	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (Mar-25) {3/2025}	645.63 (N.A.) {712.15}	681.02	99.15
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	23,186.47	94.69
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,855.56	13.99
	ROAD TRANSPORT AND HIGHWAYS	4	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	161.60	71.47
		5	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3-2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		6	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3-2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100
		7	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3-2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100
		8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.26
		9	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		11	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (Feb-24) {3/2025}	184.88 (N.A.) {184.88}	97.69	95.84
		12	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2-2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	496.88	100
		13	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6-2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	365.93	100
		14	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	158.92	37.33
		15	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (Mar-24) {3/2025}	180.57 (244.10) {180.57}	160.43	96.59
		16	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2-2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	145.20	100
		17	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (Jun-25) {6/2025}	1,718.59 (1,718.59) {1,718.59}	693.18	69.95

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		18	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (Aug-24) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		19	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
ASSAM	CIVIL AVIATION	20	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (N.A.) {7/2025}	1,142.00 (N.A.) {2,333.00}	1,604.18	76.92
	HEALTH AND FAMILY WELFARE	21	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	769.30	99.26
	PETROLEUM	22	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	19.50	6.4
		23	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	17.70	20
		24	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	53.91	16.6
		25	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	166.36	41.6
		26	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	228.16	42.7

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		27	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	87
		28	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (Dec-24) {6/2025}	543.91 (N.A.) {670.90}	491.56	93.89
		29	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	14,668.34	69.31
		30	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,711.78	81.9
		31	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (Feb-25) {5/2026}	412.00 (509.84) {509.84}	365.71	80.4
		32	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (Mar-24) {6/2025}	430.76 (N.A.) {430.76}	279.38	75.35
		33	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	163.98	59.1
		34	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (Apr-25) {4/2025}	860.00 (N.A.) {860.00}	467.22	92.4
		35	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	64.39	24.6

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	36	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,549.96	92.25
	ROAD TRANSPORT AND HIGHWAYS	37	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {2/2025}	437.39 (N.A.) {437.39}	408.81	62.57
		38	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	427.05	21.94
		39	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (Jun-19) {6/2025}	520.01 (N.A.) {520.01}	305.01	91.89
		40	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (Jul-21) {3/2025}	289.99 (N.A.) {289.99}	232.95	87.62
		41	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {2/2025}	294.17 (N.A.) {294.17}	344.58	78.5
		42	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	193.59	54.53
		43	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	192.50	30.65

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		44	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12-2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100
		45	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	307.60	60.22
		46	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {2/2025}	625.64 (N.A.) {625.64}	518.79	95
		47	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	151.24	100
		48	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,235.15	56.59
		49	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.73	100
		50	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	109.23	53.98
		51	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (Jan-25) {5/2025}	216.49 (241.52) {216.49}	104.36	80.43
		52	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (May-25) {5/2025}	261.13 (N.A.) {261.13}	64.96	57.26
		53	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (Apr-25) {4/2025}	217.50 (N.A.) {217.50}	84.36	68.03

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		54	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	216.83	97.76
		55	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {2/2025}	204.10 (N.A.) {204.10}	136.11	91.06
		56	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {3/2025}	909.02 (N.A.) {909.02}	472.45	92.08
		57	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCHES (NHAI) (N24001545)	8-2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	200.80	100
		58	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	480.84	61.02
		59	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {2/2025}	457.72 (N.A.) {457.72}	355.87	99.02
		60	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	18.59	5.1
		61	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	168.68	48.89
		62	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	9.62	15

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		63	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	432.39	23.03
		64	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	852.05	45.18
		65	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	221.01	36.99
		66	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	327.35	44.92
		67	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	168.22	19.24
		68	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	75.08	3.21
		69	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.06	100
		70	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	417.30	32.18
		71	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	243.57	17.73

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		72	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	374.62	17.38
		73	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	208.51	64.98
		74	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	117.89	11.23
		75	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	67.40	8.89
		76	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	366.82	54.95
		77	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	335.61	48.7
		78	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	395.47	46.7
		79	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	263.91	82.14

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		80	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	237.82	81.64
MANIPUR	CIVIL AVIATION	81	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (Mar-26) {3/2026}	499.00 (N.A.) {499.00}	133.55	38.12
	RAILWAYS	82	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	3/2011 (Mar-28) {12/2028}	4,454.17 (12,274.06) {19,517.70}	15,068.36	81.25
	ROAD TRANSPORT AND HIGHWAYS	83	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (Sep-25) {9/2025}	315.56 (N.A.) {315.56}	93.08	63.74
		84	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (Dec-25) {12/2025}	760.16 (N.A.) {760.16}	89.50	38.82
		85	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (Mar-26) {3/2026}	578.98 (N.A.) {578.98}	94.21	40.9
		86	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (Mar-25) {3/2025}	310.76 (N.A.) {310.76}	129.15	84.05
		87	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (Feb-25) {10/2025}	410.68 (N.A.) {410.68}	118.03	59.04
		88	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (Sep-25) {9/2025}	504.76 (N.A.) {504.76}	133.28	59.15

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		89	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3-2022	2/2025 (Feb-25) {2/2025}	152.11 (N.A.) {152.11}	62.86	89.65
		90	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (Mar-25) {3/2025}	226.32 (N.A.) {226.32}	96.41	71.2
		91	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (Oct-24) {2/2025}	188.36 (N.A.) {188.36}	126.71	98.5
		92	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (Mar-25) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		93	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (Jan-25) {6/2025}	234.08 (N.A.) {234.08}	139.45	90.34
		94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (Jan-25) {5/2025}	292.24 (N.A.) {292.24}	127.86	85.33
		95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (Jan-25) {5/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		96	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (Jan-25) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		97	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (Feb-25) {2/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		98	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (May-25) {6/2025}	379.39 (N.A.) {379.39}	193.87	53.3

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		99	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8-2020	4/2022 (N.A.) {3/2025}	228.97 (N.A.) {228.97}	0.00	0
		100	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (May-25) {5/2025}	211.70 (N.A.) {211.70}	58.43	52.64
		101	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (Mar-25) {3/2025}	467.00 (N.A.) {467.00}	188.84	76.34
		102	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (Jan-25) {1/2025}	185.80 (N.A.) {185.80}	114.69	100
		103	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (Aug-24) {6/2025}	483.87 (N.A.) {483.87}	278.89	91.72
		104	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (Feb-25) {3/2025}	198.77 (N.A.) {198.77}	113.05	89.98
		105	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (Mar-25) {3/2025}	673.27 (N.A.) {673.27}	367.93	74.4
		106	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (Jul-25) {7/2025}	579.63 (N.A.) {579.63}	149.36	59.58
		107	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (Apr-25) {6/2025}	477.86 (N.A.) {477.86}	239.80	82.21
		108	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (Nov-24) {6/2025}	311.18 (N.A.) {311.18}	171.57	76.45

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		109	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (Oct-24) {2/2025}	467.41 (N.A.) {467.41}	258.10	98.41
		110	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	0.00	0
		111	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	0.00	3.8
	DEPARTMENT OF HIGHER EDUCATION	112	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	289.55	75.8
	ROAD TRANSPORT AND HIGHWAYS	113	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (Feb-25) {2/2025}	302.88 (N.A.) {302.88}	221.73	94.96
		114	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (Mar-25) {3/2025}	553.51 (610.09) {553.51}	366.39	74.24
		115	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (Jun-24) {2/2025}	157.86 (146.92) {157.86}	149.39	98.62
		116	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	273.37	12.63
		117	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (Jun-24) {2/2025}	260.21 (N.A.) {260.21}	224.90	98.39

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		118	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	196.37	12.5
		119	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	58.34	8.6
		120	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11-2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	259.62	42
		121	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	398.05	17
		122	RANIKOR- MAHESHKHOLA- BAGHMARA PKG- 2 (NHIDCL) (N24001541)	11-2021	6/2024 (Dec-24) {3/2025}	283.50 (N.A.) {283.50}	224.23	83.3
		123	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (Dec-24) {12/2025}	359.86 (N.A.) {359.86}	220.74	83.5
		124	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	184.85	15.91
		125	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	255.10	10.09
MIZORAM	RAILWAYS	126	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,721.26	94

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	127	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	148.96	41.52
		128	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	263.25	49.8
		129	DULTE - KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3-2021	12/2022 (Mar-24) {3/2024}	374.39 (N.A.) {318.92}	292.37	100
		130	DULTE - KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (Apr-24) {4/2024}	233.25 (N.A.) {233.25}	178.37	100
		131	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	400.71	43
		132	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	293.89	42
		133	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL- TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (Mar-24) {3/2024}	275.02 (247.25) {247.25}	231.19	99.73
		134	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (Jun-24) {6/2024}	206.88 (219.33) {219.33}	206.58	97.01
		135	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (Oct-24) {10/2024}	292.24 (331.17) {331.17}	293.90	91.64

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		136	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (Nov-24) {1/2025}	519.09 (785.65) {785.65}	657.51	90.12
		137	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (May-24) {5/2024}	640.07 (990.88) {1,286.35}	1,217.65	99
		138	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.84	99.5
		139	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (Nov-24) {2/2025}	473.18 (688.25) {688.25}	521.23	85.1
		140	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (Jul-24) {2/2025}	537.82 (789.05) {789.05}	752.90	91.6
		141	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (Oct-24) {3/2025}	518.53 (906.76) {906.76}	804.57	90.15
		142	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (Nov-24) {3/2025}	404.29 (750.32) {750.32}	599.84	85.6
		143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (Nov-24) {3/2025}	428.11 (746.39) {746.39}	588.02	87.7

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
NAGALAND		144	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (May-24) {5/2024}	492.94 (492.94) {492.94}	357.26	84.7
		145	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	0.00	0
	PETROLEUM	146	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	2.76	13.9
	RAILWAYS	147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	4,072.86	65
	ROAD TRANSPORT AND HIGHWAYS	148	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (Nov-22) {2/2025}	373.07 (534.41) {534.41}	382.50	99.81
		149	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	311.07	87.21
		150	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (Feb-23) {3/2025}	387.00 (688.12) {688.12}	387.55	99.46
		151	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (Aug-24) {3/2025}	500.09 (698.81) {698.81}	373.62	96.93
		152	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3-2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	193.90	99.9

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		153	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	118.72	49.47
		154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	99.61	37.47
		155	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	60.74
		156	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		157	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	130.84	73.01
		158	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	63.64	11.01
		159	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (Sep-24) {6/2026}	277.44 (N.A.) {277.44}	166.31	64.48
		160	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	84.96	20.04
		161	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	72.03	27.58

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		162	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		163	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	78.00	70.33
		164	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	51.05	40.04
		165	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		166	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	50.74	34.57
		167	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	15.4
		168	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	109.02	46.17
		169	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	92.58	79.74
		170	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	33.10	45.54

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		171	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	261.48	100
		172	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	0
		173	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	121.54	71.63
		174	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (Feb-25) {2/2025}	226.44 (N.A.) {226.44}	129.94	91.65
		175	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		176	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
SIKKIM	CIVIL AVIATION	177	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	17.83	8
	DEPARTMENT OF HIGHER EDUCATION	178	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	179	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,989.92	64.97
		180	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,331.27	83.64
	RAILWAYS	181	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	12/2015 (Dec-27) {12/2027}	1,339.48 (12,132.95) {12,132.95}	7,893.89	70
		182	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	239.34	74.78
	ROAD TRANSPORT AND HIGHWAYS	183	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (Nov-24) {3/2025}	295.97 (N.A.) {295.97}	245.00	94.19
		184	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	0
		185	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {348.92}	149.38	41.04
		186	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	205.76	64.1
		187	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	195.37	54.16

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		188	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	254.48	94.53
		189	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (Aug-24) {3/2025}	345.38 (395.59) {395.59}	356.67	90.19
		190	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.80	46.98
		191	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17
		192	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	204.72	80.18
		193	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	277.14	44.83
		194	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	292.56	48.05
		195	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.54	96.55

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
TRIPURA		196	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		197	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (Jan-26) {1/2026}	385.15 (N.A.) {385.15}	170.32	78
	PETROLEUM	198	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	371.70	72.1
	ROAD TRANSPORT AND HIGHWAYS	199	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	10.60	5.2
		200	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {11/2024}	201.99 (N.A.) {287.47}	144.07	0
		201	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (Feb-24) {12/2024}	277.50 (302.02) {302.02}	256.89	99.94
		202	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (Oct-23) {11/2024}	159.13 (171.50) {171.50}	84.33	100
		203	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2
		204	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	0.52	1.31

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		205	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	7.67	14.16
		206	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	0
		207	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
		208	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {9/2025}	195.95 (N.A.) {195.95}	21.95	27.34
		209	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH- 8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	4.25
		210	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (N.A.) {5/2025}	456.88 (N.A.) {456.88}	105.40	43.68
			Total			176,103.72 (58,391.73) {246,811.03}	1,42,146.19	

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10-2013	9/2018 (May-23) {6/2023}	417.23 (707.73) {707.73}	698.80	100.00
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH- JHL SECTION (NR) (N22000584)	3-2019	3/2025 (N.A.) {3/2025}	235.72 (N.A.) {235.72}	46.56	50.00
	ROAD TRANSPORT AND HIGHWAYS	3	MAJOR BRIDGE OVER MIDDLE STRAIT CREEK (NHIDCL) (N24002207)	12-2024	2/2026 (N.A.) {2/2026}	371.80 (207.99) {207.99}	0.00	1.30
		4	PACKAGE-3A (NHIDCL) (N24002208)	2-2018	9/2025 (Mar-24) {9/2025}	207.54 (154.01) {154.01}	16.21	22.43
		5	PACKAGE-3B (NHIDCL) (N24002209)	2-2018	11/2025 (N.A.) {11/2025}	183.47 (N.A.) {183.47}	0.00	-
		6	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3-2017	12/2019 (Mar-23) {9/2024}	409.85 (N.A.) {409.85}	214.23	94.59
		7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3-2018	9/2020 (Nov-22) {12/2024}	234.27 (N.A.) {234.27}	126.50	80.26
		8	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11-2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	98.23
		9	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11-2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2-2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97.00
ANDHRA PRADESH	CIVIL AVIATION	11	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3-2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	31.78	19.00
		12	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4-2020	3/2023 (N.A.) {6/2025}	611.80 (N.A.) {611.80}	396.34	66.00
		13	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8-2017	2/2020 (Dec-21) {1/2024}	177.10 (N.A.) {177.10}	143.08	100.00
		14	RAJAHMUNDY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12-2022	8/2025 (N.A.) {8/2025}	347.15 (N.A.) {347.15}	58.79	35.00
	DEPARTMENT OF HIGHER EDUCATION	15	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2-2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95.00
		16	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC (CPWD EDUCATION) (N42000007)	9-2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	666.18	100.00
	PETROLEUM	17	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235)	7-2016	7/2020 (Feb-25) {2/2025}	20,928.00 (30,609.00) {30,609.00}	27,738.00	98.70
		18	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3-2016	6/2020 (Mar-25) {3/2025}	34,012.00 (N.A.) {34,012.00}	32,076.43	96.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		19	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4-2018	4/2022 (Mar-25) {3/2025}	355.00 (N.A.) {355.00}	247.36	79.30
		20	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378)	9-2019	7/2020 (N.A.) {3/2025}	196.26 (196.26) {196.26}	171.66	87.50
		21	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9-2021	6/2024 (Mar-26) {3/2026}	160.00 (220.00) {220.00}	19.73	47.00
		22	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3-2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	131.98	5.10
		23	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9-2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.62	73.50
		24	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7-2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.23	14.00
		25	CONSTRUCTION OF AVIATION FUEL FARM FACILITIES AT BHOGAPURAM AIRPORT (HPCL) (N16000538)	8-2024	3/2026 (N.A.) {3/2026}	240.00 (N.A.) {240.00}	0.94	8.80
		26	VISAKHA RAIPUR PIPELINE PROJECT (HPCL) (N16000539)	9-2024	9/2027 (N.A.) {9/2027}	2,212.00 (N.A.) {2,212.00}	0.00	1.03
	POWER	27	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9-2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	226.81	46.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		28	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5-2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	5.00	9.00
	RAILWAYS	29	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12-2001	3/2009 (N.A.) {3/2027}	1,045.20 (N.A.) {2,500.98}	1,150.74	18.00
		30	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4-2011	3/2021 (N.A.) {5/2027}	2,288.70 (N.A.) {3,122.35}	1,842.58	-
		31	GUNTUR-GUNTAKAL (SCR) (N22000368)	4-2016	3/2022 (N.A.) {12/2025}	3,631.00 (N.A.) {3,887.48}	3,294.00	-
		32	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4-2015	12/2023 (N.A.) {12/2024}	3,246.26 (N.A.) {6,238.67}	5,883.89	-
		33	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4-2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,837.78	69.00
		34	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4-2019	3/2026 (N.A.) {6/2025}	294.67 (307.66) {307.66}	163.41	41.00
		35	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9-2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	39.46	12.00
		36	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3-2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	-
		37	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4-2016	12/2025 (N.A.) {12/2025}	226.72 (N.A.) {226.72}	200.17	55.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		38	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4-2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	182.35	50.00
	ROAD TRANSPORT AND HIGHWAYS	39	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3-2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	319.02	57.00
		40	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8-2020	10/2024 (N.A.) {3/2025}	311.22 (N.A.) {311.22}	129.54	60.50
		41	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3-2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	181.63	52.00
		42	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8-2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	216.41	79.00
		43	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8-2020	7/2024 (N.A.) {3/2025}	349.29 (N.A.) {349.29}	177.64	67.00
		44	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8-2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	40.06
		45	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10-2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	307.08	70.25

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		46	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7-2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	9.97
		47	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3-2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	331.55	98.28
		48	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10-2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	270.83	42.35
		49	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3-2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	174.53	44.20
		50	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3-2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,513.36	50.30
		51	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10-2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	278.89	76.10
		52	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6-2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	121.47	76.20
		53	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2-2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	453.03	50.01

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		54	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7-2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	20.01
		55	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9-2022	1/2025 (N.A.) {1/2025}	166.52 (N.A.) {166.52}	44.07	75.16
		56	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2-2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	35.63	10.29
		57	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2-2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	89.89	7.10
		58	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2-2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	73.63	10.50
		59	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2-2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	161.92	26.52
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2-2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	54.54	2.34
		61	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3-2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	330.88	47.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		62	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4-2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	220.10	47.00
		63	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6-2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	193.87	85.00
		64	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8-2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	34.23	15.00
		65	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8-2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	76.08	35.00
		66	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8-2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	337.03	54.00
		67	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11-2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	60.76	64.00
		68	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH-167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11-2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	9.00	-
		69	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE- 2) (MoRTH) (N24002147)	12-2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	68.23	40.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		70	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3-2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	22.77	-
		71	DAVUALAPALLY TO MALLAPALEM SECTION (DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1-2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	41.66	-
		72	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2-2019	3/2023 (Oct-24) {10/2024}	757.45 (N.A.) {757.45}	593.27	95.02
		73	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2-2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	529.33	22.10
		74	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3-2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	1,029.44	86.70
		75	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2-2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,346.84	78.78
		76	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11-2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	966.72	90.08
		77	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12-2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	840.36	69.45

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		78	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1-2022	1/2025 (Jan-23) {1/2025}	1,852.12 (N.A.) {1,787.00}	687.20	76.90
		79	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3-2020	1/2024 (Dec-24) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	97.06
		80	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2-2021	10/2024 (N.A.) {12/2025}	824.29 (N.A.) {924.00}	391.85	64.90
		81	6L JAKKUVA ? KORLAM SECTION OF NH- 130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2-2021	3/2024 (Jul-24) {3/2025}	663.60 (N.A.) {768.00}	342.92	97.74
		82	6L ALURU - JAKKUVA SECTION OF NH- 130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2-2021	3/2024 (N.A.) {4/2025}	922.50 (N.A.) {1,128.68}	421.63	75.02
		83	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12-2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	179.07	37.21
		84	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12-2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	122.50	31.24
		85	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12-2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	128.64	26.12

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		86	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12-2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	210.57	31.30
		87	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2-2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	113.40	7.20
		88	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2-2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.89	3.20
		89	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1-2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	136.50	26.90
		90	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK (NHAI) (N24001848)	2-2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	64.45	7.85
		91	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5-2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	387.30	59.94
		92	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5-2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	164.04	38.33
		93	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3-2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	393.81	98.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		94	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3-2022	9/2024 (N.A.) {3/2025}	401.72 (N.A.) {401.72}	173.24	71.00
		95	NH440 RAYACHOTY TO VEMPALLI 2LPS (MoRTH) (N24001934)	12-2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	193.63	27.00
		96	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3-2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	410.30	93.84
		97	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3-2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	312.17	52.00
		98	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3-2021	7/2024 (N.A.) {3/2025}	423.67 (N.A.) {423.67}	228.15	70.00
		99	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12-2021	3/2024 (N.A.) {1/2025}	277.30 (N.A.) {277.30}	195.88	98.00
		100	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3-2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	279.80	93.17
		101	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1-2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	282.58	95.32

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		102	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3-2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	171.73	86.74
		103	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12-2021	9/2024 (N.A.) {3/2025}	388.71 (N.A.) {388.71}	199.43	75.00
		104	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3-2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	334.73	86.00
		105	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9-2021	9/2022 (Sep-24) {5/2025}	517.05 (N.A.) {655.06}	460.10	75.93
		106	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9-2021	9/2022 (Sep-24) {6/2025}	622.00 (N.A.) {817.91}	466.77	58.32
		107	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11-2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,278.03	81.50
		108	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT (MoRTH) (N24001386)	8-2020	3/2021 (N.A.) {10/2024}	222.61 (N.A.) {222.61}	152.53	93.15
		109	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3-2015	10/2015 (May-21) {5/2021}	271.45 (N.A.) {271.45}	238.23	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		110	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3-2018	12/2020 (Dec-22) {12/2024}	314.43 (N.A.) {348.72}	85.61	65.81
		111	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11-2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90.00
		112	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3-2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	254.19	98.50
		113	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8-2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	457.55	98.00
		114	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1-2017	9/2017 (N.A.) {3/2025}	263.45 (N.A.) {263.45}	257.85	89.56
	<u>WATER RESOURCES</u>	115	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2-2009	3/2020 (N.A.) {3/2026}	10,151.04 (N.A.) {55,548.87}	21,670.32	77.00
<u>ARUNACHAL PRADESH</u>	<u>CIVIL AVIATION</u>	116	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2-2019	8/2022 (Mar-25) {3/2025}	645.63 (N.A.) {712.15}	681.02	99.15
	<u>POWER</u>	117	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9-2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {26,075.54}	23,186.47	94.69
		118	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2-2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,855.56	13.99

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	119	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8-2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	161.60	71.47
		120	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3-2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100.00
		121	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3-2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100.00
		122	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3-2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100.00
		123	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3-2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	389.68	95.26
		124	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2-2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	496.88	100.00
		125	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6-2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	365.93	100.00
		126	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6-2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	158.92	37.33

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		127	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8-2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		128	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8-2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	147.13	100.00
		129	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8-2020	4/2022 (Feb-24) {3/2025}	184.88 (N.A.) {184.88}	97.69	95.84
		130	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2-2017	11/2023 (Mar-24) {3/2025}	180.57 (244.10) {180.57}	160.43	96.59
		131	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2-2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	145.20	100.00
		132	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3-2017	3/2022 (Jun-25) {6/2025}	1,718.59 (1,718.59) {1,718.59}	693.18	69.95
		133	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9-2016	12/2019 (Aug-24) {9/2024}	568.92 (568.92) {568.92}	508.65	100.00
		134	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1-2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ASSAM	CIVIL AVIATION	135	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12-2016	3/2021 (N.A.) {7/2025}	1,142.00 (N.A.) {2,333.00}	1,604.18	76.92
	HEALTH AND FAMILY WELFARE	136	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5-2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	769.30	99.26
	PETROLEUM	137	DCU REVAMP PROJECT (NRL) (N16000511)	8-2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	228.16	42.70
		138	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3-2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	87.00
		139	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1-2018	2/2020 (Dec-24) {6/2025}	543.91 (N.A.) {670.90}	491.56	93.89
		140	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1-2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	14,668.34	69.31
		141	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1-2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,711.78	81.90
		142	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5-2021	10/2023 (Feb-25) {5/2026}	412.00 (509.84) {509.84}	365.71	80.40
		143	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12-2020	7/2024 (Mar-24) {6/2025}	430.76 (N.A.) {430.76}	279.38	75.35

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		144	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3-2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	163.98	59.10
		145	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6-2021	12/2024 (Apr-25) {4/2025}	860.00 (N.A.) {860.00}	467.22	92.40
		146	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6-2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	64.39	24.60
		147	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3-2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	17.70	20.00
		148	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3-2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	53.91	16.60
		149	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1-2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	166.36	41.60
		150	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9-2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	19.50	6.40
	RAILWAYS	151	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4-2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,549.96	92.25
	ROAD TRANSPORT AND HIGHWAYS	152	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH- 137) I (NHIDCL) (N24001969)	3-2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	366.82	54.95

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {(MM/YYYY)}	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		153	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3-2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	335.61	48.70
		154	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3-2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	395.47	46.70
		155	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3-2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	263.91	82.14
		156	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3-2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	237.82	81.64
		157	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3-2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	417.30	32.18
		158	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3-2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	243.57	17.73
		159	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3-2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	374.62	17.38
		160	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1-2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	208.51	64.98
		161	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1-2023	12/2025 (N.A.) {12/2026}	356.65 (N.A.) {356.65}	117.89	11.23

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		162	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3-2023	12/2025 (N.A.) {12/2026}	643.42 (N.A.) {643.42}	67.40	8.89
		163	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2-2020	3/2022 (N.A.) {9/2024}	592.06 (N.A.) {592.06}	308.06	100.00
		164	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2-2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	432.39	23.03
		165	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3-2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	852.05	45.18
		166	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2-2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	221.01	36.99
		167	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12-2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	327.35	44.92
		168	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3-2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	168.22	19.24
		169	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3-2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	75.08	3.21
		170	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3-2022	2/2025 (N.A.) {11/2026}	613.89 (N.A.) {613.89}	18.59	5.10

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		171	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1-2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	168.68	48.89
		172	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3-2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	9.62	15.00
		173	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11-2021	7/2024 (N.A.) {2/2025}	204.10 (N.A.) {204.10}	136.11	91.06
		174	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3-2022	1/2025 (N.A.) {3/2025}	909.02 (N.A.) {909.02}	472.45	92.08
		175	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8-2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	200.80	100.00
		176	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3-2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	480.84	61.02
		177	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3-2022	6/2024 (N.A.) {2/2025}	457.72 (N.A.) {457.72}	355.87	99.02
		178	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3-2020	12/2022 (N.A.) {6/2024}	220.20 (N.A.) {220.20}	216.83	97.76
		179	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3-2020	3/2022 (Jan-25) {5/2025}	216.49 (241.52) {216.49}	104.36	80.43

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		180	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11-2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,235.15	56.59
		181	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3-2020	6/2022 (May-25) {5/2025}	261.13 (N.A.) {261.13}	64.96	57.26
		182	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3-2020	6/2022 (Apr-25) {4/2025}	217.50 (N.A.) {217.50}	84.36	68.03
		183	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3-2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	247.73	100.00
		184	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3-2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	109.23	53.98
		185	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2-2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	192.50	30.65
		186	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12-2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100.00
		187	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8-2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	307.60	60.22
		188	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9-2021	7/2024 (N.A.) {2/2025}	625.64 (N.A.) {625.64}	518.79	95.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		189	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3-2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	151.24	100.00
		190	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6-2015	8/2023 (N.A.) {2/2025}	437.39 (N.A.) {437.39}	408.81	62.57
		191	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6-2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	427.05	21.94
		192	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1-1991	6/2019 (Jun-19) {6/2025}	520.01 (N.A.) {520.01}	305.01	91.89
		193	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12-2015	12/2018 (Jul-21) {3/2025}	289.99 (N.A.) {289.99}	232.95	87.62
		194	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1-2016	1/2016 (N.A.) {2/2025}	294.17 (N.A.) {294.17}	344.58	78.50
		195	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1-2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	193.59	54.53
BIHAR	CIVIL AVIATION	196	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7-2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	27.05	7.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		197	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5-2018	10/2022 (Jun-25) {6/2025}	1,216.90 (N.A.) {1,216.90}	881.96	82.10
	DEPARTMENT OF HIGHER EDUCATION	198	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE- II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2-2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	436.15	100.00
		199	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9-2018	9/2020 (N.A.) {3/2025}	375.00 (N.A.) {375.00}	333.45	99.60
	PETROLEUM	200	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1-2020	4/2023 (Dec-24) {8/2026}	14,810.00 (N.A.) {14,810.00}	10,319.56	82.90
		201	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6-2019	12/2029 (Mar-30) {3/2030}	163.00 (N.A.) {163.00}	89.94	27.80
		202	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1-2022	4/2025 (N.A.) {8/2026}	389.00 (N.A.) {389.00}	32.31	23.90
		203	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12-2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	229.20	12.70
		204	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12-2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	259.93	14.70
	POWER	205	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2-2005	10/2011 (Jul-23) {3/2025}	8,692.97 (21,312.11) {21,312.11}	22,571.28	94.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		206	BUXAR THERMAL POWER PLANT (1320 MW) (<i>SJVN</i>) (<i>N18000194</i>)	3-2019	1/2024 (N.A.) {6/2025}	10,439.09 (N.A.) {12,999.36}	10,892.17	85.21
	RAILWAYS	207	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (<i>ECR</i>) (<i>220100257</i>)	4-1997	(N.A.) {12/2026}	162.87 (614.45) {614.45}	460.73	50.00
		208	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (<i>ECR</i>) (<i>220100303</i>)	4-2003	(N.A.) {12/2024}	528.65 (2,087.36) {2,087.36}	2,152.18	48.00
		209	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (<i>NFR</i>) (<i>N22000087</i>)	9-2006	3/2019 (N.A.) {9/2025}	532.87 (2,132.03) {4,412.25}	3,267.44	82.00
		210	SAKRI-HASANPUR ROAD (NL) (<i>ECR</i>) (<i>N22000171</i>)	4-1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	589.42	78.00
		211	ARARIA-SUPAUL (NL) (<i>ECR</i>) (<i>N22000177</i>)	4-2008	(N.A.) {1/2025}	1,605.17 (1,605.17) {1,605.17}	1,510.86	31.00
		212	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC (<i>ECR</i>) (<i>N22000181</i>)	4-2009	3/2020 (N.A.) {3/2026}	548.00 (548.00) {783.83}	544.31	78.00
		213	SAMASTIPUR-DARBANGHA (<i>ECR</i>) (<i>N22000329</i>)	5-2015	(N.A.) {3/2025}	380.00 (519.33) {519.33}	603.70	64.00
		214	KIUL - GAYA DOUBLING PROJECT (<i>ECR</i>) (<i>N22000349</i>)	12-2015	3/2020 (N.A.) {11/2024}	1,200.20 (1,200.20) {1,771.07}	1,790.93	96.00
		215	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (<i>ECR</i>) (<i>N22000350</i>)	12-2015	3/2020 (N.A.) {5/2025}	1,491.47 (1,491.47) {1,600.00}	1,680.42	77.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		216	SAGALI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4-2016	3/2021 (N.A.) {12/2024}	744.04 (1,215.54) {1,215.54}	1,472.94	85.00
		217	MUZAFFARPUR SAGALI DOUBLING 100.60 KM (ECR) (N22000473)	4-2016	3/2021 (N.A.) {12/2024}	731.64 (1,185.73) {1,300.00}	1,441.14	80.00
		218	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, (ECR) (N22000476)	4-1991	(N.A.) {12/2024}	329.39 (803.09) {2,722.16}	2,687.01	90.00
		219	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6-2019	6/2025 (N.A.) {9/2024}	983.62 (253.23) {415.00}	409.41	80.00
		220	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7-2022	7/2027 (N.A.) {6/2025}	486.00 (N.A.) {486.00}	117.09	30.00
		221	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2-2019	6/2028 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	2.53	-
		222	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10-2022	10/2027 (N.A.) {6/2025}	234.00 (223.69) {223.69}	22.57	-
		223	KATIHAR-KUMEDPUR & KATIHAR- MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8-2022	8/2027 (N.A.) {8/2027}	745.00 (N.A.) {745.00}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	224	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3-2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	44.34	3.64

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		225	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12-2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	100.28	68.58
		226	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12-2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	77.78	28.66
		227	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2-2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	12.23
		228	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG- I) (NHAI) (N24002066)	2-2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		229	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3-2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	86.54	81.15
		230	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2-2022	11/2024 (N.A.) {11/2025}	624.43 (N.A.) {624.43}	246.60	78.00
		231	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3-2021	1/2025 (N.A.) {3/2025}	477.54 (N.A.) {477.54}	278.93	71.79
		232	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3-2021	3/2024 (N.A.) {9/2025}	566.15 (N.A.) {566.15}	208.58	43.03
		233	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7-2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	288.28	30.42

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		234	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2-2022	12/2024 (N.A.) {4/2025}	427.29 (N.A.) {427.29}	166.86	64.40
		235	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3-2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	53.51	40.25
		236	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH- 119D (PKG-III) (NHAI) (N24001697)	2-2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	183.47	13.51
		237	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8-2022	8/2024 (N.A.) {8/2024}	1,198.02 (N.A.) {1,198.02}	2.27	-
		238	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3-2022	12/2024 (N.A.) {7/2025}	312.58 (N.A.) {312.58}	166.41	69.14
		239	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12-2021	3/2024 (Dec-24) {12/2024}	552.55 (553.00) {553.00}	414.79	54.95
		240	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4-2022	4/2024 (Sep-25) {9/2025}	1,769.50 (N.A.) {1,769.50}	0.00	-
		241	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12-2021	9/2024 (N.A.) {9/2024}	184.90 (185.00) {185.00}	163.01	93.40

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		242	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2-2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	-
		243	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3-2021	3/2024 (Dec-24) {12/2024}	1,020.84 (N.A.) {1,020.84}	89.52	-
		244	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3-2022	3/2024 (Jun-25) {6/2025}	1,485.66 (N.A.) {1,485.66}	0.00	-
		245	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9-2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	98.23
		246	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9-2020	4/2023 (Dec-24) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		247	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9-2020	3/2023 (Dec-24) {12/2024}	939.43 (N.A.) {939.43}	370.62	100.00
		248	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8-2020	7/2023 (Dec-24) {12/2024}	690.00 (N.A.) {690.00}	770.73	98.80
		249	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12-2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100.00
		250	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2-2019	9/2024 (N.A.) {2/2026}	2,926.42 (N.A.) {2,926.42}	1,208.79	50.58

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		251	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10-2013	12/2020 (Dec-24) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.30
		252	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10-2013	11/2020 (Dec-24) {12/2024}	446.97 (598.48) {740.50}	638.80	96.30
		253	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10-2013	11/2020 (Dec-24) {12/2024}	464.09 (605.53) {765.12}	698.25	97.30
		254	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10-2019	8/2023 (Dec-24) {12/2024}	1,101.99 (N.A.) {1,101.99}	817.40	71.23
		255	CONSTRUCTION OF 4 LANE ROB AND ITS APPROACHES AT THE LEVEL OF CROSSING (L C NO. 29-B) OF KM 29 (EKAN (MoRTH) (N24002193)	3-2023	7/2026 (N.A.) {7/2026}	201.08 (N.A.) {201.08}	10.34	10.00
		256	CONSTRUCTION OF 6-LANE ELEVATED / EXTRA DOSE CABLE BRIDGE ON RIVER GANGA PARALLEL TO AND WESTERN SID (MoRTH) (N24002194)	1-2024	11/2027 (N.A.) {11/2027}	3,064.45 (N.A.) {3,064.45}	58.37	0.50
		257	ESTIMATE FOR IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM RAMNAGAR TO ROSEDA FROM (KM 3.500 TO 4 (MoRTH) (N24002195)	1-2022	4/2026 (N.A.) {4/2026}	495.16 (N.A.) {495.16}	94.41	6.50
		258	CONSTRUCTION OF BHABHUA BYPASS FROM CH. 10+800(DESIGN CH. 10+800) TO CH. 19+860 (DESIGN CH. 18+150) (MoRTH) (N24002196)	2-2022	3/2026 (N.A.) {3/2026}	179.86 (N.A.) {179.86}	21.75	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		259	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDER FROM JUNCTION OF NH-22 NEAR HAJIPUR TO JUNCTION OF NH-12 (MoRTH) (N24002197)	2-2024	2/2026 (N.A.) {2/2026}	226.15 (N.A.) {226.15}	6.52	8.00
		260	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF BH/WBBORDER- AMDABAD-MANIHARI SECTION FROM DESIGN KM (MoRTH) (N24002198)	1-2022	3/2026 (N.A.) {3/2026}	353.27 (N.A.) {353.27}	24.44	-
		261	PATNA-MUZZAFFARPUR (NHAI) (N24000165)	8-2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.78
		262	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1-2011	7/2013 (Jun-25) {6/2025}	575.00 (N.A.) {575.00}	557.43	86.92
		263	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1-2014	10/2019 (Apr-25) {4/2025}	675.00 (N.A.) {780.77}	702.20	92.70
		264	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12-2015	4/2019 (Mar-25) {3/2025}	1,041.10 (567.00) {639.58}	553.73	97.55
		265	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12-2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	96.00
		266	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2-2016	11/2018 (Mar-25) {3/2025}	319.68 (N.A.) {503.28}	440.98	99.00
		267	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2-2016	5/2016 (Mar-25) {3/2025}	178.85 (N.A.) {278.54}	232.61	98.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		268	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2-2016	5/2016 (Mar-25) {3/2025}	553.30 (N.A.) {706.39}	614.38	98.00
		269	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1-2014	10/2016 (Jun-25) {6/2025}	1,408.85 (N.A.) {2,138.16}	1,715.96	96.65
		270	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3-2017	3/2020 (Mar-25) {3/2025}	672.89 (736.01) {830.31}	616.15	81.85
		271	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8-2017	2/2022 (Oct-24) {3/2025}	950.64 (1,161.00) {1,168.33}	1,069.28	92.10
		272	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12-2017	10/2024 (Apr-25) {12/2026}	2,598.00 (N.A.) {1,978.01}	1,284.48	71.80
		273	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1-2018	12/2021 (Dec-24) {6/2025}	573.70 (644.50) {726.99}	476.99	81.22
		274	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3-2018	11/2021 (Dec-24) {12/2024}	496.20 (470.18) {537.17}	398.41	96.44
		275	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9-2018	6/2024 (May-26) {5/2026}	1,478.40 (N.A.) {1,478.40}	854.53	63.55

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	URBAN DEVELOPMENT	276	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAIL) (N28000148)	2-2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	2,849.65	42.00
	WATER RESOURCES	277	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3-2018	7/2021 (Dec-19) {12/2024}	230.06 (N.A.) {230.06}	237.44	96.00
		278	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10-2017	9/2020 (Nov-20) {2/2025}	254.13 (413.29) {413.29}	120.95	85.00
		279	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028)	11-2018	12/2020 (N.A.) {2/2024}	236.15 (N.A.) {236.15}	150.75	100.00
		280	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3-2018	8/2021 (Mar-18) {6/2025}	305.19 (N.A.) {305.19}	323.73	92.00
		281	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3-2018	10/2021 (Mar-18) {6/2024}	294.02 (350.79) {522.85}	414.52	100.00
		282	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037)	12-2014	3/2020 (N.A.) {6/2022}	225.77 (N.A.) {398.90}	363.79	100.00
		283	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4-2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	490.14	100.00
		284	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040)	5-2017	4/2021 (May-17) {2/2023}	356.37 (364.00) {356.37}	312.30	100.00
		285	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043)	5-2017	11/2020 (May-17) {5/2022}	191.62 (N.A.) {191.62}	123.56	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
CHHATTISGARH		286	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3-2017	5/2021 (Mar-17) {2/2023}	277.42 (253.98) {277.42}	355.31	100.00
		287	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8-2017	6/2022 (N.A.) {12/2025}	578.89 (453.83) {578.89}	158.41	48.00
		288	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8-2017	6/2022 (N.A.) {12/2025}	824.00 (734.09) {824.00}	377.18	50.00
	COAL	289	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6-2010	3/2023 (N.A.) {3/2025}	11,816.40 (N.A.) {11,816.40}	6,254.79	77.00
		290	PELMA OCP(15.00MTY) (SECL) (N06000045)	11-2014	3/2023 (N.A.) {3/2033}	1,624.59 (N.A.) {1,624.59}	14.91	17.00
		291	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY (SECL) (N06000008)	8-2013	3/2023 (N.A.) {3/2030}	7,612.33 (N.A.) {8,547.98}	4,647.14	81.00
		292	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12-2013	3/2022 (Mar-25) {3/2025}	610.63 (N.A.) {610.63}	572.04	85.00
		293	AMERA OC RCE (SECL) (N06000123)	2-2015	3/2018 (Mar-26) {3/2026}	335.97 (N.A.) {335.97}	86.89	42.00
		294	AMGAON OPENCAST PROJECT RCE (SECL) (N06000135)	7-2015	3/2020 (Mar-26) {3/2026}	316.10 (N.A.) {316.10}	188.32	65.00
		295	MAHAMAYA OPENCAST PROJECT (SECL) (N06000164)	5-2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	179.93	38.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		296	JHIRIA WEST OPENCASE PROJECT (SECL) (N06000166)	11-2018	3/2026 (N.A.) {3/2026}	366.94 (N.A.) {366.94}	32.59	36.00
		297	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8-2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	868.56	39.00
		298	JAMPALI OCP RCE (SECL) (N06000198)	5-2020	3/2024 (Mar-25) {3/2025}	278.64 (N.A.) {278.64}	207.96	73.00
		299	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12-2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	45.48	10.00
		300	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12-2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,734.37	37.00
		301	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7-2016	3/2020 (Mar-05) {3/2025}	459.49 (N.A.) {459.49}	262.19	92.00
		302	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1-2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	60.34	2.00
	DEPARTMENT OF HIGHER EDUCATION	303	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3-2020	7/2022 (Feb-24) {3/2024}	808.62 (879.22) {808.62}	879.22	100.00
	PETROLEUM	304	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3-2021	3/2024 (Mar-25) {3/2025}	456.00 (N.A.) {456.00}	370.55	95.60
	POWER	305	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (NTPC) (N18000381)	8-2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	1,179.38	5.50

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		306	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2-2023	11/2023 (N.A.) {3/2025}	385.84 (N.A.) {385.84}	206.71	78.00
		307	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3-2023	9/2024 (N.A.) {2/2025}	271.69 (N.A.) {271.69}	173.03	87.00
		308	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX (PGCIL) (N18000355)	3-2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	172.79	98.00
	RAILWAYS	309	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12-2012	3/2020 (N.A.) {3/2024}	1,160.00 (N.A.) {1,440.00}	1,482.58	92.00
		310	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4-2015	3/2021 (Dec-23) {12/2025}	1,973.00 (2,135.34) {2,135.34}	2,140.33	88.00
		311	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4-2013	9/2018 (N.A.) {12/2025}	3,055.00 (N.A.) {3,438.39}	3,070.00	92.60
		312	Gauge conversion of Raipur(Kendri)-Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7-2011	10/2024 (N.A.) {6/2025}	1,171.30 (N.A.) {1,171.30}	560.45	80.00
		313	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9-2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.12	-
		314	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12-2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	0.21	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		315	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.17	-
		316	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9-2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	2.05	-
		317	4TH LINE - RAJNANDGAON-DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9-2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	8.03	5.00
		318	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9-2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	-
		319	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6-2022	6/2030 (N.A.) {3/2027}	1,376.20 (1,242.94) {1,242.94}	100.06	10.00
		320	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3-2008	6/2025 (N.A.) {6/2025}	631.78 (N.A.) {1,627.56}	1,349.09	-
		321	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10-2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	-
		322	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3-2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	146.46	20.46
		323	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6-2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	390.95	23.32
	ROAD TRANSPORT AND HIGHWAYS							

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		324	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6-2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	616.56	27.59
		325	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3-2020	5/2024 (N.A.) {2/2025}	278.97 (N.A.) {278.97}	190.57	81.65
		326	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (MoRTH) (N24001919)	12-2020	9/2023 (Feb-25) {2/2025}	193.16 (N.A.) {193.16}	89.63	79.70
		327	UPGRADATION OF NH 130A MUNGELI TO PONDII FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3-2021	9/2024 (N.A.) {2/2025}	218.57 (N.A.) {218.57}	115.05	77.12
		328	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12-2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	582.37	67.31
		329	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11-2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	806.32	92.10
		330	4 LANE OF BILASPUR TO URGHA PROJECT (KM 0.00 TO KM 70.2) OF NH- 130A (NHAI) (N24001611)	4-2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	569.22	80.90
		331	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1-2016	8/2016 (N.A.) {3/2025}	497.14 (572.66) {572.66}	376.54	60.41

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		332	REHABILITATION AND UPGADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1-2016	10/2016 (N.A.) {2/2025}	624.98 (N.A.) {731.50}	620.52	99.00
		333	REHABILITATION AND UPGADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3-2016	7/2016 (N.A.) {3/2025}	452.94 (N.A.) {435.61}	307.02	66.30
		334	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3-2018	1/2019 (N.A.) {3/2025}	349.03 (N.A.) {349.03}	316.52	97.90
		335	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH- 130A (MoRTH) (N24001228)	11-2017	5/2019 (N.A.) {2/2025}	188.80 (N.A.) {188.80}	136.81	97.00
	STEEL	336	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7-2021	11/2024 (N.A.) {12/2025}	282.44 (349.75) {349.75}	174.59	63.56
		337	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11-2015	6/2023 (Jul-24) {12/2025}	2,907.00 (5,427.06) {5,427.06}	2,468.23	67.40
		338	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3-2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,376.15	68.02
		339	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10-2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	42.06	5.73

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
DELHI		340	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11-2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	289.97	57.73
	URBAN DEVELOPMENT	341	CONSTRUCTION 729 QUARTERS (TYPE II- 180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5-2019	9/2020 (Oct-24) {10/2024}	299.97 (299.97) {299.97}	256.87	86.00
	CIVIL AVIATION	342	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11-2016	4/2020 (Apr-24) {4/2024}	303.80 (374.98) {351.21}	340.52	100.00
	DPIIT	343	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11-2017	12/2019 (Feb-25) {11/2024}	4,773.00 (N.A.) {5,401.00}	4,895.41	99.50
	FINANCE	344	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7-2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85.00
	HOME AFFAIRS	345	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10-2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,945.21	100.00
		346	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6-2019	7/2022 (N.A.) {9/2025}	277.35 (N.A.) {277.35}	97.05	58.00
	RAILWAYS	347	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4-2012	(N.A.) {}	295.68 (N.A.) {419.00}	133.78	-
	ROAD TRANSPORT AND HIGHWAYS	348	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6-2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		349	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAITPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5-2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	1,113.16	82.43
		350	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7-2020	10/2023 (N.A.) {6/2025}	2,171.80 (N.A.) {2,171.80}	958.13	99.75
		351	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778)	7-2020	10/2023 (N.A.) {12/2024}	801.46 (N.A.) {801.46}	382.03	99.33
		352	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK- RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3-2018	9/2022 (N.A.) {6/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	86.75
		353	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1-2018	10/2021 (N.A.) {3/2025}	2,067.67 (N.A.) {2,160.00}	1,496.49	98.50
		354	DEVELOPMENT OF 6L UER II (PACKAGE - II) (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7-2020	10/2023 (N.A.) {6/2025}	1,894.96 (N.A.) {1,894.96}	741.88	88.10
	TELECOMMUNICATIONS	355	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10-2014	3/2018 (N.A.) {3/2025}	248.20 (N.A.) {248.20}	232.04	98.00
	URBAN DEVELOPMENT	356	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7-2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	14,291.87	60.52

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		357	DELHI MRTS PHASE-III (DMRC) (N28000056)	9-2011	3/2016 (Aug-21) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,545.86	99.99
		358	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7-2016	(N.A.) {10/2024}	2,694.00 (N.A.) {2,694.00}	2,402.68	98.00
		359	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10-2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2.00
		360	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10-2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	610.30	55.00
		361	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1-2022	11/2024 (May-25) {5/2025}	646.52 (N.A.) {646.52}	380.65	82.00
		362	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10-2016	3/2024 (Mar-25) {3/2025}	1,536.72 (N.A.) {1,536.72}	412.06	83.01
	WATER RESOURCES	363	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3-2017	12/2022 (N.A.) {12/2024}	665.78 (N.A.) {665.78}	782.51	96.00
		364	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015)	5-2016	12/2021 (N.A.) {2/2024}	211.79 (223.70) {211.79}	208.71	100.00
		365	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016)	5-2016	2/2022 (Sep-23) {7/2023}	239.11 (314.71) {239.11}	268.13	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		366	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (<i>DJB</i>) (<i>N30000017</i>)	12-2018	1/2021 (N.A.) {3/2022}	515.07 (N.A.) {515.07}	388.08	100.00
GOA	CIVIL AVIATION	367	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (<i>AAI</i>) (<i>N04000095</i>)	11-2017	9/2021 (N.A.) {3/2025}	255.69 (N.A.) {255.69}	101.36	75.00
	DEPARTMENT OF HIGHER EDUCATION	368	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (<i>CPWD EDUCATION</i>) (<i>N42000002</i>)	5-2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	364.00	93.00
	PETROLEUM	369	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (<i>ONGC</i>) (<i>N16000502</i>)	3-2023	6/2024 (N.A.) {2/2025}	325.53 (N.A.) {325.53}	301.44	99.80
	ROAD TRANSPORT AND HIGHWAYS	370	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (<i>MoRTH</i>) (<i>N24002181</i>)	4-2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	0.00	-
GUJARAT	CIVIL AVIATION	371	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (<i>AAI</i>) (<i>N04000093</i>)	8-2018	2/2021 (N.A.) {2/2025}	353.25 (N.A.) {353.25}	346.57	98.75
		372	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (<i>AAI</i>) (<i>N04000088</i>)	1-2018	8/2022 (May-24) {12/2024}	1,405.00 (N.A.) {1,405.00}	1,302.23	100.00
		373	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (<i>AAI</i>) (<i>N04000099</i>)	6-2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	312.11	42.00
	PETROLEUM	374	REDEVELOPMENT OF SANTHAL FIELD (<i>ONGC</i>) (<i>N16000279</i>)	2-2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,145.82	92.60

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		375	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11-2019	5/2023 (Mar-24) {3/2025}	5,251.00 (5,894.00) {5,894.00}	4,559.99	99.10
		376	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9-2020	8/2024 (Dec-25) {12/2025}	18,936.00 (N.A.) {18,936.00}	10,077.63	78.60
		377	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10-2020	8/2023 (Jun-25) {6/2025}	1,614.00 (N.A.) {1,614.00}	1,069.57	93.44
		378	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4-2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	308.13	63.00
		379	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8-2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	482.50	56.90
		380	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1-2022	11/2024 (N.A.) {11/2025}	621.40 (N.A.) {621.40}	123.10	21.40
		381	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1-2022	9/2024 (N.A.) {8/2025}	328.00 (N.A.) {328.00}	40.15	32.80
		382	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5-2022	2/2025 (N.A.) {9/2025}	249.43 (N.A.) {249.43}	177.24	88.20
		383	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8-2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	859.39	56.80

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		384	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7-2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	134.01	81.60
		385	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11-2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	117.38	32.90
	POWER	386	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7-2023	7/2025 (N.A.) {7/2025}	334.00 (N.A.) {334.00}	0.00	4.00
		387	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12-2023	12/2025 (N.A.) {12/2025}	3,752.00 (N.A.) {3,752.00}	357.02	5.00
		388	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5-2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	0.00	4.00
		389	AUGMENTATION OF TRANSFORMATION CAPACITY AT JAM KHAMBHALIYA PS [GIS] [SPV NAME POWERGRID JAM KHAMBHAL (PGCIL) (N18000398)	10-2024	7/2026 (N.A.) {7/2026}	329.00 (N.A.) {329.00}	0.00	-
		390	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000400)	10-2024	10/2026 (N.A.) {10/2026}	4,766.00 (N.A.) {4,766.00}	65.00	1.00
		391	PROVISION OF DYNAMIC REACTIVE COMPENSATION AT KHAVDA POOLING STATION 1 [KPS1] AND KHAVDA POOLING STA (PGCIL) (N18000402)	11-2024	11/2026 (N.A.) {11/2026}	501.00 (N.A.) {501.00}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		392	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF G (PGCIL) (N18000405)	11-2024	5/2029 (N.A.) {5/2029}	24,819.00 (N.A.) {24,819.00}	0.00	-
		393	Bagodara Solar Power Project (SJVN) (N18000297)	5-2021	10/2022 (N.A.) {6/2025}	339.35 (N.A.) {339.35}	315.95	51.00
		394	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5-2021	9/2022 (N.A.) {3/2025}	674.92 (N.A.) {674.92}	543.02	91.00
		395	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11-2021	5/2023 (N.A.) {3/2025}	937.80 (N.A.) {937.80}	776.65	98.00
		396	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1-2021	7/2022 (N.A.) {3/2025}	842.27 (N.A.) {842.27}	668.91	30.00
		397	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11-2022	3/2024 (N.A.) {3/2026}	1,442.60 (N.A.) {1,442.60}	787.54	2.00
		398	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7-2022	3/2025 (N.A.) {1/2026}	1,316.02 (N.A.) {1,316.02}	296.21	23.00
		399	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9-2022	9/2024 (N.A.) {1/2026}	7,179.54 (N.A.) {7,179.54}	2,991.10	61.00
		400	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3-2023	12/2024 (N.A.) {3/2025}	922.30 (N.A.) {922.30}	465.67	74.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		401	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3-2023	3/2025 (N.A.) {3/2025}	815.12 (N.A.) {815.12}	9.99	59.00
		402	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3-2023	12/2024 (N.A.) {3/2025}	966.79 (N.A.) {966.79}	362.22	74.00
		403	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3-2023	3/2025 (N.A.) {4/2025}	1,167.55 (N.A.) {1,167.55}	622.14	47.00
		404	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3-2023	3/2025 (N.A.) {4/2025}	2,820.99 (N.A.) {2,820.99}	2,063.46	52.00
		405	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6-2023	12/2024 (N.A.) {1/2026}	6,283.81 (N.A.) {6,283.81}	1,441.89	16.00
		406	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5-2023	1/2025 (N.A.) {5/2025}	1,095.01 (N.A.) {1,095.01}	325.61	-
	RAILWAYS	407	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4-2011	(Oct-26) {10/2026}	844.10 (844.10) {844.10}	588.47	41.00
		408	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4-2017	3/2020 (Feb-25) {2/2025}	692.25 (692.26) {692.26}	648.67	97.00
		409	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4-2018	3/2024 (Oct-24) {10/2024}	537.31 (537.31) {671.91}	844.55	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		410	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2-2023	3/2027 (Feb-27) {2/2027}	961.67 (961.67) {961.67}	73.59	2.50
		411	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2-2023	12/2025 (Oct-25) {10/2025}	152.44 (152.44) {152.44}	55.61	20.00
		412	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10-2021	10/2026 (Mar-26) {12/2025}	1,011.72 (1,080.58) {1,080.58}	1,281.42	55.00
		413	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6-2022	2/2030 (Jun-25) {6/2025}	354.99 (482.42) {482.42}	758.59	70.00
		414	PETLAD-BHADLAN (22.5 KM) (WR) (N22000538)	5-2022	5/2030 (Dec-25) {12/2025}	202.50 (307.12) {307.12}	61.66	7.00
		415	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5-2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	72.93	7.00
		416	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2-2023	3/2030 (Jul-26) {7/2026}	401.48 (670.17) {670.17}	75.62	12.00
		417	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5-2022	3/2030 (Dec-25) {12/2025}	216.72 (349.93) {349.93}	79.09	25.00
		418	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2-2023	1/2028 (Sep-26) {9/2026}	410.46 (410.46) {410.46}	33.59	2.00
		419	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5-2022	3/2030 (Jun-25) {6/2025}	309.81 (415.38) {415.38}	513.59	75.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		420	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5-2022	5/2030 (N.A.) {5/2030}	296.54 (N.A.) {296.54}	0.00	-
		421	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD (16.51 KM) (PB#29/NR/202 (WR) (N22000551)	10-2022	10/2027 (N.A.) {10/2027}	437.21 (N.A.) {437.21}	0.00	-
		422	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6-2022	12/2026 (N.A.) {12/2026}	492.83 (N.A.) {492.83}	0.00	-
		423	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7-2022	7/2030 (N.A.) {12/2026}	1,695.82 (N.A.) {2,798.16}	888.53	8.50
		424	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9-2012	3/2027 (Mar-26) {3/2026}	261.68 (261.68) {261.68}	631.22	45.00
	ROAD TRANSPORT AND HIGHWAYS	425	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9-2022	12/2023 (Dec-25) {12/2025}	237.28 (N.A.) {237.28}	0.59	-
		426	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12-2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	435.97	62.50
		427	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9-2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	262.60	20.77
		428	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10-2022	2/2024 (Feb-26) {2/2026}	246.60 (291.00) {291.00}	29.33	15.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		429	UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12-2022	2/2024 (Aug-25) {8/2025}	173.06 (N.A.) {219.00}	0.15	-
		430	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3-2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	532.24	66.82
		431	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3-2021	3/2024 (N.A.) {9/2025}	1,259.00 (2,652.24) {1,910.00}	195.15	26.68
		432	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7-2020	12/2023 (N.A.) {2/2025}	2,271.86 (3,372.97) {3,916.00}	1,053.53	97.40
		433	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7-2020	8/2023 (N.A.) {3/2025}	1,710.30 (2,665.08) {1,927.00}	650.04	85.73
		434	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS- PACKAGE-3) (NHAI) (N24001790)	2-2020	8/2023 (Dec-24) {12/2024}	752.30 (N.A.) {766.20}	451.11	98.14
		435	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS- PACKAGE-1) (NHAI) (N24001791)	2-2020	6/2023 (Mar-24) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
		436	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3-2021	9/2022 (N.A.) {1/2025}	536.03 (N.A.) {536.03}	465.77	99.48

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		437	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3-2021	9/2022 (N.A.) {4/2025}	485.75 (N.A.) {485.75}	385.38	97.30
		438	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2-2020	3/2023 (Dec-24) {12/2024}	778.15 (N.A.) {785.67}	547.22	99.70
		439	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE) (NHAI) (N24001827)	3-2022	3/2023 (N.A.) {2/2025}	162.73 (N.A.) {162.73}	131.79	95.30
		440	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9-2020	2/2024 (N.A.) {6/2025}	1,542.02 (N.A.) {1,542.02}	922.09	67.00
		441	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9-2020	2/2024 (Aug-24) {8/2024}	1,185.69 (N.A.) {1,185.69}	913.91	90.01
		442	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11-2019	9/2023 (N.A.) {3/2025}	1,669.56 (N.A.) {1,669.56}	1,013.36	93.50
		443	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9-2020	11/2023 (N.A.) {9/2024}	1,198.55 (N.A.) {1,198.55}	869.60	94.54
		444	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11-2019	5/2024 (N.A.) {3/2025}	1,604.06 (N.A.) {1,604.06}	1,229.92	95.73

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		445	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6-2020	4/2023 (Sep-24) {9/2024}	166.21 (N.A.) {166.21}	98.65	93.00
		446	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5-2020	3/2024 (Nov-24) {1/2025}	690.30 (929.95) {929.95}	1,193.08	86.40
		447	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5-2020	1/2024 (Nov-24) {1/2025}	882.00 (N.A.) {882.00}	1,256.69	93.05
		448	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5-2020	7/2023 (Nov-24) {1/2025}	691.52 (903.85) {903.85}	909.80	93.05
		449	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5-2020	12/2023 (Nov-24) {1/2025}	894.00 (1,210.06) {1,210.06}	1,025.93	88.84
		450	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDORFROM KM 38/660 TO KM 42/690 (ISCON JUNCTION (MoRTH) (N24002182)	3-2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	0.00	-
		451	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3-2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	0.00	-
		452	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5-2016	8/2019 (N.A.) {6/2024}	998.18 (N.A.) {998.18}	802.34	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		453	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5-2016	9/2019 (May-24) {2/2025}	723.64 (N.A.) {723.64}	559.77	96.00
		454	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5-2016	8/2019 (N.A.) {2/2025}	763.08 (N.A.) {763.08}	514.25	96.00
		455	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7-2016	7/2020 (N.A.) {2/2025}	829.97 (N.A.) {829.97}	472.83	93.10
		456	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1-2017	12/2020 (Jun-25) {6/2025}	1,251.11 (1,527.75) {1,527.75}	684.13	83.84
		457	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3-2018	10/2021 (Apr-25) {4/2025}	1,161.39 (1,738.03) {1,404.00}	510.21	68.06
		458	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10-2018	11/2020 (Sep-24) {9/2024}	400.76 (394.44) {394.44}	287.39	87.00
	URBAN DEVELOPMENT	459	AHMEDABAD METRO RAIL PROJECT PHASE 1 (AMR) (N28000122)	11-2014	12/2018 (N.A.) {5/2025}	10,773.00 (N.A.) {12,924.55}	12,408.71	99.85
		460	AHMEDABAD METRO RAIL PROJECT PHASE II (AMR) (N28000137)	3-2019	3/2024 (N.A.) {6/2025}	5,384.17 (N.A.) {5,384.17}	3,748.56	79.74
		461	SURAT METRO RAIL PROJECT (AMR) (N28000138)	3-2019	3/2024 (N.A.) {10/2025}	12,020.32 (N.A.) {12,020.32}	5,982.53	57.96

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
HARYANA	<u>HEALTH AND FAMILY WELFARE</u>	462	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3-2019	3/2023 (Mar-26) {3/2026}	1,294.34 (1,294.34) {1,294.34}	161.44	8.55
	<u>HOME AFFAIRS</u>	463	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1-2020	10/2023 (Mar-25) {3/2025}	166.98 (170.23) {170.23}	123.85	90.00
	<u>PETROLEUM</u>	464	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6-2019	12/2022 (Jul-25) {7/2025}	2,281.94 (3,219.94) {3,219.94}	1,638.21	62.00
		465	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2-2021	9/2024 (Dec-25) {12/2025}	34,627.00 (38,231.00) {38,231.00}	17,325.96	80.60
		466	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3-2022	3/2025 (N.A.) {6/2026}	1,459.00 (2,102.79) {2,102.79}	739.39	54.00
	<u>RAILWAYS</u>	467	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2-2023	2/2028 (N.A.) {12/2025}	471.06 (N.A.) {471.06}	62.38	39.00
		468	DOUBLING BETWEEN REWARI- KATHUWAS (27.73 KM) (NWR) (N22000606)	2-2023	6/2027 (N.A.) {12/2025}	352.41 (N.A.) {352.41}	104.24	29.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	469	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA- KO (NHAI) (N24002037)	1-2023	12/2025 (N.A.) {3/2026}	609.32 (609.00) {609.00}	136.57	34.05
		470	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11-2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	591.02	42.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		471	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2-2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	356.69	39.00
		472	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4-2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	447.15	43.50
		473	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4-2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	657.76	42.50
		474	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11-2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	271.91	67.10
		475	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3-2022	6/2025 (N.A.) {6/2025}	927.22 (N.A.) {927.22}	423.72	65.35
		476	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6-2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	170.00	74.00
		477	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7-2022	6/2025 (N.A.) {6/2025}	2,414.67 (2,898.00) {2,898.00}	1,108.26	38.00
		478	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH- 352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12-2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,092.84	61.25

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		479	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH- 11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2-2020	1/2023 (Dec-24) {12/2024}	808.31 (N.A.) {958.00}	850.55	99.79
		480	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11-2018	9/2021 (N.A.) {2/2025}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95
		481	CONSTRUCTION OF 4-LANE NH-344P- PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11-2021	11/2023 (Jan-24) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100.00
		482	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11-2020	12/2023 (N.A.) {2/2025}	1,690.23 (N.A.) {2,010.17}	1,368.23	98.00
		483	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12-2020	1/2024 (Apr-24) {2/2025}	1,334.04 (N.A.) {1,334.00}	995.68	98.50
		484	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7-2020	7/2022 (May-24) {3/2025}	899.00 (1,882.46) {1,882.46}	1,123.98	93.58
		485	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7-2020	7/2022 (N.A.) {2/2025}	817.00 (1,605.00) {1,605.00}	1,025.56	99.61
		486	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12-2020	12/2023 (Feb-24) {2/2025}	1,430.88 (1,549.23) {1,549.23}	1,120.50	99.60

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		487	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1-2021	12/2023 (Mar-24) {2/2025}	1,306.95 (1,453.34) {1,453.34}	942.57	98.50
		488	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3-2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	218.00	49.00
		489	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3-2020	3/2023 (Nov-24) {3/2025}	510.97 (N.A.) {510.97}	529.00	93.00
<u>HIMACHAL PRADESH</u>	<u>DEPARTMENT OF HIGHER EDUCATION</u>	490	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3-2021	11/2024 (Jul-25) {7/2025}	512.37 (300.45) {300.45}	113.35	63.00
		491	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9-2018	6/2022 (Dec-24) {6/2025}	392.51 (N.A.) {446.43}	312.13	90.60
	<u>POWER</u>	492	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9-2002	9/2009 (N.A.) {3/2025}	3,919.59 (N.A.) {12,475.00}	12,115.38	98.71
		493	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11-2020	1/2026 (N.A.) {12/2028}	1,810.56 (N.A.) {3,060.71}	1,659.55	51.02
		494	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10-2020	11/2025 (N.A.) {3/2027}	687.97 (N.A.) {1,426.00}	787.53	63.90
		495	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1-2023	4/2028 (N.A.) {12/2028}	2,614.51 (N.A.) {3,605.30}	880.05	27.61

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	496	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4-2008	12/2026 (N.A.) {3/2025}	2,966.99 (N.A.) {6,753.42}	5,369.57	-
	ROAD TRANSPORT AND HIGHWAYS	497	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3-2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.50
		498	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2-2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	346.91	44.18
		499	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7-2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	307.60	64.41
		500	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2-2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	895.20	58.68
		501	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3-2021	12/2024 (Dec-24) {12/2024}	1,322.95 (1,442.47) {1,442.47}	886.42	91.48
		502	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5-2022	3/2024 (Dec-24) {12/2024}	469.95 (N.A.) {280.00}	299.33	95.68
		503	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2-2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		504	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4-2021	6/2024 (N.A.) {3/2025}	583.93 (770.00) {704.30}	171.22	98.21
		505	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3-2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.79}	189.65	43.39
		506	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7-2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.60
		507	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3-2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	20.16	20.00
		508	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3-2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	76.05	43.73
		509	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN- MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8-2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	80.06	-
		510	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8-2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	140.69	98.00
		511	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8-2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	91.93	86.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		512	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8-2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100.00
		513	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2-2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	152.01	84.00
		514	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8-2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	194.31	13.00
		515	REHABILITATION AND UP-GRADATION TO 4L CONFIGURATION AND STRENGTHENING OF THANPURI TO PAROR SECTION F (NHAI) (N24002192)	6-2022	12/2025 (N.A.) {12/2025}	815.69 (815.69) {815.69}	347.25	17.62
		516	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9-2016	7/2020 (N.A.) {3/2025}	1,273.71 (N.A.) {1,478.61}	1,437.37	94.02
		517	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3-2018	5/2021 (Dec-24) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83.00
	URBAN DEVELOPMENT	518	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4-2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	-
JAMMU AND KASHMIR	CIVIL AVIATION	519	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7-2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	108.48	21.50

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	520	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1-2018	4/2023 (Feb-25) {2/2025}	676.00 (1,148.68) {1,144.68}	64.75	100.00
		521	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3-2019	7/2022 (Jan-25) {1/2025}	424.93 (N.A.) {500.91}	473.74	96.00
	<u>HEALTH AND FAMILY WELFARE</u>	522	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3-2019	9/2023 (Jan-25) {1/2025}	1,404.00 (1,642.00) {1,642.00}	1,449.66	100.00
		523	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3-2019	9/2025 (Jan-25) {11/2025}	1,828.00 (1,577.00) {1,577.00}	1,201.19	61.50
	<u>PETROLEUM</u>	524	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4-2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	439.05	63.00
		525	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3-2022	3/2032 (Sep-34) {9/2034}	538.00 (N.A.) {538.00}	3.10	0.40
	<u>POWER</u>	526	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10-2014	4/2020 (Jul-25) {9/2026}	8,112.12 (N.A.) {8,112.12}	5,678.44	64.00
		527	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3-2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {4,287.59}	2,191.03	51.80
		528	RATLE HE PROJECT (NHPC) (N18000324)	2-2021	2/2026 (N.A.) {11/2028}	5,281.94 (N.A.) {5,281.94}	871.65	19.01
		529	KWAR HE PROJECT (CVPPPL) (N18000363)	5-2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	844.94	18.50

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	530	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (NR) (220100133)	3-1995	11/2002 (Dec-24) {12/2024}	2,500.00 (37,012.26) {42,930.00}	41,877.51	100.00
	ROAD TRANSPORT AND HIGHWAYS	531	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6-2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	362.09	46.00
		532	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9-2022	6/2026 (Jun-26) {12/2026}	1,183.60 (N.A.) {1,183.60}	153.78	9.87
		533	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3-2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {975.38}	189.40	24.00
		534	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8-2022	6/2025 (N.A.) {8/2025}	2,474.47 (N.A.) {2,894.74}	809.19	24.80
		535	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10-2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	99.06	25.00
		536	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7-2022	3/2025 (N.A.) {8/2025}	198.28 (N.A.) {198.28}	77.00	64.22
		537	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3-2021	7/2024 (Mar-25) {3/2024}	642.24 (N.A.) {642.24}	498.80	95.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		538	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7-2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	180.48	87.00
		539	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2-2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	211.75	64.00
		540	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3-2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	468.35	79.00
		541	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3-2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	103.81	78.00
		542	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3-2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	320.82	49.96
		543	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9-2021	12/2023 (Jun-24) {6/2024}	811.19 (N.A.) {811.19}	824.22	99.00
		544	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3-2021	2/2024 (Apr-25) {10/2025}	2,919.96 (N.A.) {2,919.96}	2,257.33	64.80
		545	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7-2022	1/2025 (N.A.) {4/2025}	245.34 (N.A.) {245.34}	56.86	38.13

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		546	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9-2021	9/2024 (Sep-25) {9/2025}	1,821.72 (1,917.32) {1,917.32}	810.73	67.80
		547	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10-2021	9/2024 (Jul-25) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,469.64	60.40
		548	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10-2021	9/2024 (Sep-25) {9/2025}	2,714.95 (2,714.95) {2,714.95}	1,625.93	74.00
		549	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8-2022	6/2024 (Jun-25) {6/2025}	200.05 (200.05) {208.92}	119.56	47.30
		550	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SKIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9-2021	10/2023 (May-25) {5/2025}	442.14 (N.A.) {442.14}	292.03	19.88
		551	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7-2021	8/2024 (Jun-25) {6/2025}	614.48 (N.A.) {614.48}	176.24	7.00
		552	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7-2021	6/2024 (Jun-25) {6/2025}	1,401.87 (N.A.) {1,401.87}	641.41	-
		553	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1-2020	1/2024 (Feb-25) {2/2025}	336.01 (N.A.) {336.01}	213.50	34.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		554	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7-2019	10/2020 (Apr-23) {9/2024}	157.05 (N.A.) {157.05}	139.54	100.00
		555	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7-2021	2/2025 (May-26) {5/2026}	1,912.17 (N.A.) {1,912.17}	72.85	-
		556	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8-2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		557	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA- KHEL (NHIDCL) (N24001264)	7-2020	4/2022 (Oct-24) {10/2025}	228.39 (N.A.) {228.39}	67.60	87.03
		558	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7-2020	4/2022 (Nov-23) {4/2025}	210.79 (N.A.) {210.79}	69.67	89.54
		559	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3-2021	9/2022 (Oct-24) {3/2025}	486.45 (N.A.) {486.45}	120.08	96.58
		560	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3-2021	12/2022 (Oct-24) {3/2025}	398.51 (N.A.) {398.51}	76.47	92.40
		561	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342)	3-2021	12/2022 (N.A.) {7/2024}	260.40 (N.A.) {260.40}	191.88	93.80
		562	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7-2021	2/2023 (Jun-25) {3/2026}	512.43 (N.A.) {512.43}	65.31	49.32

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		563	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7-2021	8/2023 (Dec-25) {6/2026}	859.67 (N.A.) {859.67}	187.65	43.22
		564	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7-2021	2/2023 (Mar-25) {6/2025}	497.09 (N.A.) {497.09}	156.00	77.19
		565	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2-2021	3/2023 (Oct-24) {3/2025}	431.28 (N.A.) {431.28}	339.76	94.37
		566	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3-2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	300.02	8.00
		567	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9-2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8.00
		568	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3-2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	338.33	-
		569	WIDENING AND STRENGTHENING OF RAFIABAD-KUPWARA-CHOWKIBAL- TANGDHAR-CHAMKOT (NH-701) ROAD FROM DESIGN (BRO) (N24002210)	3-2024	5/2027 (N.A.) {5/2027}	1,404.94 (N.A.) {1,404.94}	0.00	-
		570	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12-2015	12/2018 (Mar-25) {3/2025}	2,136.97 (2,644.00) {2,644.00}	2,386.12	99.50
		571	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12-2017	7/2021 (Feb-25) {2/2025}	1,471.75 (1,471.75) {1,903.98}	1,651.32	98.18

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		572	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3-2018	7/2021 (Aug-23) {6/2025}	253.44 (N.A.) {253.44}	184.29	80.26
JHARKHAND	COAL	573	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12-2009	3/2016 (N.A.) {3/2025}	510.85 (N.A.) {510.85}	488.31	74.50
		574	MURAIIDIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2-2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	190.48	70.00
		575	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8-2011	3/2019 (N.A.) {2/2026}	1,230.27 (N.A.) {1,230.27}	596.63	80.20
		576	MADHUBAND NLW WASHERY (BCCL) (N06000126)	5-2010	5/2014 (N.A.) {11/2023}	289.45 (N.A.) {302.00}	300.01	100.00
		577	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8-2018	3/2024 (Mar-26) {3/2026}	513.98 (N.A.) {513.98}	219.21	51.00
		578	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11-2019	3/2023 (N.A.) {3/2025}	243.52 (N.A.) {243.52}	44.39	46.60
		579	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7-2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	378.34	44.00
		580	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10-2015	4/2018 (N.A.) {6/2025}	334.27 (N.A.) {334.27}	127.62	43.84
		581	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7-2021	3/2026 (N.A.) {3/2026}	778.80 (N.A.) {778.80}	683.42	75.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		582	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8-2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,318.42	19.00
		583	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8-2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	770.67	19.00
		584	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8-2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	411.40	60.00
		585	CHANDRAGUPT OCP (CCL) (N06000238)	8-2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	7.95	12.40
		586	SIRKA OCP (CCL) (N06000239)	5-2020	3/2025 (N.A.) {3/2025}	222.82 (N.A.) {222.82}	139.31	60.00
		587	JHARKHAND LAIYO OCP (CCL) (N06000240)	8-2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	20.00
		588	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11-2020	3/2025 (N.A.) {3/2025}	230.41 (N.A.) {230.41}	18.14	18.30
		589	EPR PUNDI OCP (CCL) (N06000242)	11-2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	39.00
		590	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1-2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	82.92	11.70
		591	EXPANSION OF KONAR OCP (CCL) (N06000245)	1-2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	390.37	32.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		592	EXPANSION OF KARO OCP (CCL) (N06000246)	1-2022	3/2026 (N.A.) {3/2026}	908.47 (N.A.) {908.47}	145.93	17.20
		593	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5-2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	175.01	12.10
		594	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1-2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	389.65	24.69
		595	HURA C OC (ECL) (N06000275)	8-2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	438.86	62.00
		596	CHUPERBHITA- SIMLONG OCP (ECL) (N06000280)	12-2023	3/2033 (Mar-37) {3/2037}	979.08 (N.A.) {979.08}	0.00	-
	DEPARTMENT OF HIGHER EDUCATION	597	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9-2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	176.02	-
	PETROLEUM	598	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6-2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	192.76	19.00
		599	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239)	12-2015	3/2023 (Mar-24) {3/2025}	823.27 (1,137.79) {1,137.79}	1,060.31	83.30
		600	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11-2019	1/2024 (Mar-25) {3/2025}	431.00 (N.A.) {431.00}	173.22	56.90
		601	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3-2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	47.10	37.48

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	602	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2-2014	6/2019 (Oct-22) {3/2025}	16,242.90 (N.A.) {17,007.00}	16,605.62	97.00
		603	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11-2017	3/2023 (N.A.) {11/2025}	17,112.00 (N.A.) {17,112.00}	15,460.45	79.00
		604	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2-2019	10/2024 (N.A.) {6/2025}	501.79 (784.00) {501.79}	274.96	59.79
		605	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9-2015	11/2019 (Jan-24) {1/2024}	1,553.00 (N.A.) {2,804.00}	1,914.00	56.00
	RAILWAYS	606	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4-2002	(N.A.) {3/2025}	459.91 (1,625.87) {1,700.00}	1,851.89	70.00
		607	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3-2016	3/2021 (N.A.) {6/2026}	1,724.20 (3,029.04) {3,029.04}	2,258.49	82.00
		608	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4-2018	6/2022 (N.A.) {6/2026}	428.65 (N.A.) {472.50}	275.36	2.00
		609	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11-2022	11/2027 (N.A.) {11/2027}	202.00 (349.22) {349.22}	31.70	-
		610	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12-2015	3/2025 (N.A.) {3/2025}	1,116.00 (N.A.) {3,270.07}	2,899.45	-
		611	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11-2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		612	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3-2017	3/2024 (N.A.) {3/2025}	262.71 (N.A.) {262.71}	201.76	73.00
		613	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1-2018	12/2025 (N.A.) {12/2025}	487.73 (N.A.) {487.73}	344.09	16.00
	ROAD TRANSPORT AND HIGHWAYS	614	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4-2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	606.60	64.00
		615	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH- 75 PKG SEC-III (NHAI) (N24002054)	10-2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	296.46	60.03
		616	FOUR LANING OF BASUKINATH- DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3-2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	-
		617	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6-2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	373.92	40.03
		618	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12-2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	-
		619	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6-2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,324.95}	702.00	56.00
		620	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2-2020	8/2023 (N.A.) {12/2024}	153.01 (N.A.) {153.01}	83.63	96.23

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		621	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1-2022	7/2024 (N.A.) {12/2024}	315.21 (N.A.) {315.21}	105.63	80.00
		622	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3-2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	10.49	6.10
		623	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3-2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	-
		624	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9-2020	3/2024 (Dec-24) {4/2025}	755.26 (N.A.) {1,039.00}	552.69	83.60
		625	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9-2020	10/2023 (Dec-24) {1/2025}	748.99 (N.A.) {903.00}	817.44	100.00
		626	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2-2022	1/2025 (Mar-25) {3/2025}	534.73 (N.A.) {534.73}	125.31	82.00
		627	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8-2020	3/2024 (Jun-25) {6/2025}	1,034.00 (1,879.55) {1,879.55}	41.50	94.21
		628	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11-2021	7/2023 (Jun-25) {6/2025}	1,302.72 (1,504.80) {1,504.80}	842.02	69.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)	
		629	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12-2016	9/2021 (N.A.) {12/2024}	196.00 (N.A.) {196.00}	164.21	90.10	
		630	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1-2018	11/2021 (Jun-25) {6/2025}	1,155.16 (N.A.) {950.49}	629.74	69.00	
	STEEL	631	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3-2015	10/2017 (Nov-26) {11/2026}	1,034.01 (1,752.30) {1,752.30}	872.03	51.75	
	632	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9-2023	7/2025 (N.A.) {7/2025}	513.82 (N.A.) {513.82}	90.72	57.00		
	633	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11-2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	67.50	31.00		
	634	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3-2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	0.00	5.00		
	KARNATAKA	CIVIL AVIATION	635	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6-2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	63.36	28.00
			636	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6-2023	2/2026 (N.A.) {1/2026}	320.47 (N.A.) {320.47}	31.25	21.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	637	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7-2019	3/2022 (N.A.) {3/2023}	851.00 (851.00) {851.00}	888.66	-
		638	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8-2021	2/2024 (Nov-24) {11/2024}	316.25 (N.A.) {316.25}	333.42	94.00
	<u>PETROLEUM</u>	639	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12-2018	12/2022 (Mar-25) {3/2025}	854.00 (854.00) {854.00}	654.47	93.60
		640	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1-2022	7/2025 (Dec-25) {12/2025}	463.00 (500.62) {500.62}	206.94	64.50
		641	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10-2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	70.94	37.58
		642	DEMO PLANT FOR PRODUCTION OF BIO- ATF (MANGALORE REFIN) (N16000536)	3-2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	8.26	1.20
	<u>POWER</u>	643	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12-2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	250.00	13.00
		644	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2-2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	318.00	28.00
	<u>RAILWAYS</u>	645	HOSPET-HUBLI-LONDA-VASCODAGAMA DL (RVNL) (N22000297)	4-2010	3/2023 (N.A.) {12/2026}	2,127.00 (N.A.) {3,692.60}	3,505.49	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		646	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4-2011	(N.A.) {12/2027}	1,801.01 (N.A.) {1,801.01}	488.95	12.00
		647	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4-2010	3/2016 (N.A.) {3/2027}	986.30 (1,378.00) {1,378.00}	593.54	34.00
		648	GADAG-WADI NL (SWR) (N22000299)	4-2013	12/2018 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,226.74	28.00
		649	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4-2012	3/2016 (N.A.) {12/2027}	279.54 (296.72) {296.72}	112.64	14.00
		650	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3-1996	3/2017 (N.A.) {3/2026}	644.78 (825.31) {825.31}	629.21	66.00
		651	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4-2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	-
		652	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4-2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	-
		653	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019- 20/NR) (SWR) (N22000557)	9-2020	3/2026 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.56	-
		654	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000558)	6-2019	4/2028 (N.A.) {3/2028}	663.03 (748.85) {748.85}	0.34	1.00
		655	SHIMOGA-SHIKARIPURA-RANEENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9-2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	67.29	7.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		656	BANGALORE-WHITEFIELD-BANGALORE CITY-KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3-2018	3/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	189.26	46.00
	ROAD TRANSPORT AND HIGHWAYS	657	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3-2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	521.50	61.19
		658	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12-2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	483.76	53.30
		659	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5-2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	274.76	53.21
		660	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12-2021	6/2024 (Dec-24) {12/2024}	516.96 (N.A.) {516.96}	19.93	70.00
		661	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3-2023	3/2025 (Mar-25) {3/2025}	718.52 (N.A.) {718.52}	24.81	23.00
		662	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA- SANKESWAR SE (MoRTH) (N24002013)	3-2021	2/2022 (Oct-24) {10/2024}	766.64 (N.A.) {766.64}	13.55	75.00
		663	BALANCE WORK OF CONTRSUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3-2021	3/2023 (Jul-24) {7/2024}	344.79 (N.A.) {344.79}	10.00	90.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		664	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2-2023	2/2024 (Feb-25) {2/2025}	398.48 (N.A.) {398.48}	5.00	50.00
		665	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6-2021	6/2024 (Jun-25) {6/2025}	298.00 (N.A.) {298.00}	10.70	52.00
		666	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1-2023	1/2026 (Sep-25) {9/2025}	166.58 (N.A.) {166.58}	3.54	-
		667	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1-2023	1/2025 (Jan-25) {1/2025}	350.69 (N.A.) {350.69}	10.00	56.00
		668	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9-2022	3/2024 (Jan-25) {1/2025}	172.98 (N.A.) {172.98}	6.48	65.00
		669	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANGES KM 112.750 TO (MoRTH) (N24001944)	1-2023	6/2024 (Jul-24) {7/2024}	255.88 (N.A.) {255.88}	60.99	78.00
		670	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8-2022	2/2024 (Dec-24) {12/2024}	170.34 (N.A.) {170.34}	4.25	72.00
		671	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11-2022	11/2024 (Nov-24) {11/2024}	218.93 (N.A.) {218.93}	10.00	95.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		672	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2-2023	2/2025 (Feb-25) {2/2025}	177.94 (N.A.) {177.94}	6.66	47.00
		673	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10-2022	10/2024 (Dec-24) {12/2024}	355.72 (N.A.) {355.72}	11.32	60.00
		674	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1-2022	4/2025 (Apr-25) {4/2025}	1,388.70 (1,388.70) {1,388.70}	367.36	57.40
		675	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3-2018	12/2022 (Dec-25) {12/2025}	440.16 (N.A.) {440.16}	311.29	64.51
		676	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2-2023	2/2025 (N.A.) {2/2025}	1,240.60 (N.A.) {1,240.60}	771.46	76.06
		677	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11-2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	540.35	96.75
		678	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12-2022	6/2025 (Mar-26) {6/2025}	2,718.46 (N.A.) {2,718.46}	312.90	41.30
		679	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11-2022	5/2024 (May-24) {5/2024}	226.76 (226.76) {226.76}	77.32	64.25

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		680	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10-2022	4/2025 (Apr-25) {4/2025}	1,479.30 (1,479.30) {1,479.30}	515.99	70.15
		681	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3-2021	10/2024 (Dec-25) {12/2025}	1,409.68 (1,808.12) {1,808.12}	928.03	50.50
		682	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8-2022	8/2025 (Aug-25) {3/2027}	2,032.15 (2,032.15) {2,032.15}	175.86	43.80
		683	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	3-2022	3/2024 (May-26) {5/2026}	294.62 (309.90) {309.90}	49.92	13.61
		684	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9-2021	4/2023 (Dec-24) {12/2024}	912.37 (N.A.) {424.16}	330.84	99.10
		685	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9-2020	1/2023 (Sep-20) {5/2025}	688.00 (602.09) {688.00}	488.15	77.33
		686	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3-2021	3/2023 (Apr-25) {4/2025}	1,065.06 (1,444.50) {1,444.50}	170.68	92.16
		687	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10-2021	10/2023 (Aug-25) {8/2025}	1,331.77 (2,082.98) {2,082.98}	358.32	70.70

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		688	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10-2019	10/2021 (Jan-25) {1/2025}	1,225.24 (1,505.85) {1,505.85}	80.99	93.99
		689	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1-2017	9/2017 (May-23) {5/2023}	166.67 (N.A.) {264.34}	192.08	100.00
		690	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8-2016	2/2017 (Jul-24) {7/2024}	175.50 (N.A.) {241.60}	189.72	90.10
		691	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3-2018	6/2019 (Dec-23) {12/2023}	159.97 (N.A.) {242.61}	113.15	100.00
		692	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1-2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100.00
		693	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9-2017	10/2018 (Apr-22) {4/2022}	191.60 (N.A.) {191.60}	112.03	100.00
		694	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12-2017	1/2019 (Apr-22) {4/2022}	297.30 (N.A.) {318.28}	280.25	100.00
		695	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3-2018	10/2018 (Nov-22) {11/2022}	325.86 (N.A.) {386.41}	356.78	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		696	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10-2016	3/2017 (Jul-22) {7/2022}	396.96 (N.A.) {396.96}	329.58	100.00
		697	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11-2016	3/2017 (Oct-21) {10/2021}	314.90 (N.A.) {314.90}	233.95	100.00
		698	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3-2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98.06
		699	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5-2018	5/2018 (Dec-23) {12/2023}	171.60 (N.A.) {171.60}	134.81	100.00
		700	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1-2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100.00
		701	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2-2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	62.31	60.00
		702	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1-2017	9/2017 (May-23) {5/2023}	264.34 (N.A.) {264.34}	201.07	100.00
		703	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3-2019	12/2019 (Nov-24) {11/2024}	423.15 (N.A.) {423.15}	284.58	82.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		704	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3-2021	11/2021 (Aug-25) {8/2025}	1,100.88 (1,687.31) {1,687.31}	1,009.48	71.50
		705	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3-2021	10/2021 (Mar-25) {3/2025}	317.90 (572.01) {572.01}	351.22	95.60
		706	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3-2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	-
		707	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C (MoRTH) (N24002187)	2-2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	-
		708	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3-2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	-
		709	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9-2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	-
		710	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3-2015	11/2015 (Aug-24) {8/2024}	165.67 (N.A.) {165.67}	126.47	99.00
		711	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	5-2014	8/2016 (Jan-20) {3/2025}	1,655.01 (1,990.99) {1,990.99}	1,810.43	97.80
		712	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552)	3-2016	3/2019 (Dec-23) {6/2025}	701.40 (591.86) {701.40}	497.23	85.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		713	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8-2016	3/2019 (May-25) {5/2025}	1,167.42 (N.A.) {1,224.01}	915.13	84.25
	<u>STEEL</u>	714	SCREENING PLANT-II, DONIMALAI (NMDC) (N12000136)	9-2023	8/2026 (N.A.) {8/2026}	1,043.63 (N.A.) {1,043.63}	143.37	6.63
	<u>URBAN DEVELOPMENT</u>	715	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCL) (N28000058)	2-2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89.00
		716	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCL) (N28000151)	6-2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30.00
<u>KERALA</u>	<u>CIVIL AVIATION</u>	717	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6-2023	9/2025 (N.A.) {9/2025}	323.98 (N.A.) {323.98}	12.14	5.00
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	718	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7-2019	3/2021 (N.A.) {11/2025}	753.63 (N.A.) {753.63}	412.37	66.00
	<u>HEALTH AND FAMILY WELFARE</u>	719	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9-2017	3/2020 (May-24) {11/2024}	150.29 (N.A.) {162.00}	150.47	99.95
	<u>PETROLEUM</u>	720	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3-2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	138.62	73.20
		721	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12-2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	91.15	6.90

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	722	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2-2015	(N.A.) {12/2027}	1,431.90 (N.A.) {3,785.45}	3,184.42	-
		723	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12-2010	3/2028 (N.A.) {12/2026}	600.82 (N.A.) {595.39}	270.57	-
		724	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12-2011	8/2023 (N.A.) {12/2026}	812.85 (N.A.) {802.80}	258.69	-
	ROAD TRANSPORT AND HIGHWAYS	725	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074)	8-2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	209.15	25.20
		726	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8-2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	828.51	47.79
		727	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12-2021	2/2025 (Feb-25) {2/2025}	3,273.61 (N.A.) {3,273.61}	567.30	52.04
		728	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12-2021	1/2025 (Aug-25) {8/2025}	3,635.64 (N.A.) {3,635.64}	280.92	37.25
		729	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9-2021	9/2024 (Mar-26) {9/2024}	2,878.97 (N.A.) {2,878.97}	364.74	31.62

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		730	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3-2020	6/2022 (Feb-24) {6/2024}	210.37 (216.94) {216.94}	198.10	100.00
		731	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH- 17) FROM DESIGN CHAINAGE 397+750 () (NHAI) (N24001653)	11-2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,911.43	51.80
		732	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6-2021	3/2025 (Feb-25) {2/2025}	2,641.37 (N.A.) {2,641.37}	523.26	67.98
		733	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6-2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,034.04	61.04
		734	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6-2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	2,917.31	54.64
		735	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6-2021	10/2024 (Dec-25) {12/2025}	2,842.14 (N.A.) {2,842.14}	477.69	61.41
		736	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1-2021	7/2024 (Mar-25) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,371.31	92.28
		737	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD- SECTION OF NH-66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2-2021	7/2024 (Mar-25) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,246.61	91.40

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		738	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8-2020	2/2024 (Nov-21) {12/2025}	2,714.60 (3,557.65) {2,714.60}	1,780.62	66.26
		739	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10-2020	4/2024 (May-25) {12/2025}	3,219.47 (3,898.46) {3,896.46}	2,091.28	57.16
		740	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5-2020	5/2024 (Nov-21) {3/2025}	1,981.07 (2,627.66) {1,981.07}	1,406.57	84.38
		741	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6-2020	4/2024 (Oct-21) {12/2025}	3,041.65 (3,799.76) {3,041.65}	2,156.43	70.14
		742	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6-2020	4/2024 (Oct-21) {11/2025}	1,746.45 (2,377.88) {1,746.45}	1,125.92	69.00
		743	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2-2017	8/2017 (Mar-22) {8/2024}	294.28 (296.53) {296.53}	286.80	98.00
		744	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2-2017	9/2017 (Jan-23) {8/2024}	380.76 (372.87) {372.87}	347.04	100.00
		745	4-LANNING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704)	9-2017	5/2020 (Nov-23) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,524.07	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		746	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2-2018	2/2023 (Dec-24) {4/2025}	1,424.77 (2,065.95) {2,065.95}	780.07	84.20
	URBAN DEVELOPMENT	747	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPUNITHURA (KMRCL) (N28000159)	6-2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	-
		748	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7-2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	2.81	-
LADAKH	CIVIL AVIATION	749	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7-2018	9/2021 (Oct-24) {10/2025}	480.33 (N.A.) {640.00}	402.66	62.47
	ROAD TRANSPORT AND HIGHWAYS	750	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11-2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	76.75	37.00
		751	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3-2021	1/2023 (Dec-24) {11/2025}	384.23 (N.A.) {384.23}	115.95	58.53
		752	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3-2021	1/2023 (Feb-25) {11/2025}	404.89 (N.A.) {404.89}	190.72	64.36
		753	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8-2020	1/2023 (Aug-25) {8/2025}	381.01 (N.A.) {381.01}	205.56	73.97
		754	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3-2021	1/2023 (Aug-25) {8/2025}	398.37 (N.A.) {398.37}	209.68	82.11

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MADHYA PRADESH	CIVIL AVIATION	755	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6-2016	6/2021 (N.A.) {7/2024}	412.24 (N.A.) {412.24}	401.38	100.00
		756	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10-2021	8/2023 (Jun-24) {8/2024}	446.12 (N.A.) {446.12}	432.58	100.00
	COAL	757	KANCHAN OC EXPANSION (SECL) (N06000125)	12-2014	3/2021 (Mar-26) {3/2026}	371.04 (N.A.) {371.04}	135.31	47.00
		758	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3-2016	3/2021 (Mar-27) {3/2027}	869.44 (N.A.) {869.44}	258.63	64.00
		759	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162)	11-2017	3/2022 (N.A.) {8/2024}	1,255.17 (N.A.) {1,398.56}	1,254.21	100.00
		760	GANDHIGRAM UG MINE (WCL) (N06000183)	8-2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	11.75	28.00
		761	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7-2019	3/2023 (N.A.) {3/2025}	998.71 (N.A.) {998.71}	402.44	28.08
		762	NIGAHI EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11-2020	3/2025 (N.A.) {3/2025}	1,729.68 (N.A.) {1,729.68}	718.18	42.40
		763	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7-2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	480.27	44.00
		764	TAWA III UG MINE (WCL) (N06000250)	12-2021	3/2027 (N.A.) {3/2027}	314.09 (N.A.) {324.25}	0.56	9.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		765	URDHAN OC (WCL) (N06000265)	1-2023	3/2031 (N.A.) {3/2031}	206.88 (N.A.) {228.42}	22.12	9.00
		766	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9-2022	3/2027 (N.A.) {3/2027}	399.20 (N.A.) {497.01}	64.13	42.00
		767	VISHNUPURI UG TO OC (WCL) (N06000260)	11-2022	3/2029 (N.A.) {3/2029}	220.62 (N.A.) {227.65}	0.00	7.00
		768	SHARDA UG (WCL) (N06000266)	9-2023	3/2028 (N.A.) {3/2028}	166.25 (N.A.) {200.16}	1.69	11.00
	PETROLEUM	769	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5-2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	1,133.10	8.90
	POWER	770	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART- C (PGCIL) (N18000392)	8-2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	27.00	6.00
		771	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-2 5.5GW] [JAISALMER/BARME (PGCIL) (N18000399)	10-2024	10/2026 (N.A.) {10/2026}	3,674.00 (N.A.) {3,674.00}	54.00	1.00
		772	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6-2022	3/2024 (N.A.) {3/2025}	1,530.49 (N.A.) {1,530.49}	1,164.70	70.00
	RAILWAYS	773	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4-2001	3/2021 (Dec-25) {3/2026}	424.60 (3,032.46) {5,125.16}	3,187.96	68.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		774	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4-2008	3/2022 (Feb-27) {2/2027}	3,503.69 (5,677.80) {6,203.51}	4,132.14	80.00
		775	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12-2015	3/2020 (Dec-27) {12/2027}	1,763.93 (2,445.30) {4,353.50}	3,016.61	86.00
		776	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8-2016	3/2022 (N.A.) {9/2024}	582.13 (N.A.) {1,247.64}	1,276.23	-
		777	ANUPPUR-KATNI (SECR) (N22000485)	4-2015	12/2021 (Dec-23) {3/2025}	1,370.00 (1,680.00) {2,311.02}	1,760.05	76.00
		778	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4-2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	230.46	17.00
		779	SATNA - REWA (50 KM) (WCR) (N22000554)	11-2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80.00
		780	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10-2021	10/2027 (Jun-25) {6/2025}	910.00 (1,095.88) {1,095.88}	912.02	71.00
		781	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9-2018	9/2030 (N.A.) {9/2030}	4,340.00 (N.A.) {7,393.75}	1,004.86	-
		782	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3-2022	12/2024 (N.A.) {2/2025}	179.19 (N.A.) {179.19}	75.91	95.00
		783	UPGRADATION OF NASRULLAGANI- REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12-2021	10/2024 (N.A.) {3/2025}	305.12 (N.A.) {305.12}	96.88	34.46
	ROAD TRANSPORT AND HIGHWAYS							

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		784	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3-2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	161.96	64.00
		785	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3-2022	2/2025 (N.A.) {3/2025}	386.49 (N.A.) {386.49}	119.76	48.77
		786	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI- SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12-2020	4/2023 (May-23) {6/2025}	529.44 (N.A.) {529.44}	191.24	58.43
		787	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL- KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11-2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	68.23	28.00
		788	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER- MP-RJ B (MoRTH) (N24002018)	1-2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	172.70	98.00
		789	UPGRADATION OF DINDORI- SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1-2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	145.04	50.12
		790	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3-2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	40.05	25.00
		791	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1-2021	7/2023 (N.A.) {12/2024}	178.18 (N.A.) {178.18}	161.64	84.39

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		792	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH- 30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12-2022	3/2025 (N.A.) {3/2025}	652.33 (N.A.) {652.33}	307.86	57.04
		793	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7-2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	139.27	100.00
		794	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1-2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	479.20	74.50
		795	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9-2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	187.67	32.28
		796	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756)	10-2020	10/2024 (N.A.) {3/2025}	1,352.56 (N.A.) {1,480.94}	838.62	99.90
		797	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH- 752D (PKG-III) (NHAI) (N24001758)	1-2020	10/2024 (N.A.) {2/2025}	823.05 (N.A.) {823.05}	402.78	100.00
		798	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH- 752D (NHAI) (N24001759)	1-2020	6/2024 (Mar-25) {3/2025}	909.84 (N.A.) {909.84}	462.58	91.40
		799	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761)	2-2023	2/2025 (Feb-25) {2/2025}	520.28 (N.A.) {520.28}	392.85	100.00
		800	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10-2021	1/2024 (Dec-24) {12/2024}	1,146.22 (N.A.) {1,146.22}	569.40	90.30

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		801	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765)	8-2022	7/2024 (N.A.) {5/2025}	207.77 (N.A.) {207.77}	52.83	39.75
		802	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1-2022	10/2024 (N.A.) {5/2025}	1,011.29 (N.A.) {1,011.29}	171.00	47.48
		803	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1-2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	502.69	79.50
		804	BALANCE WORK OF 4L OF INDORE- GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8-2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	51.96	100.00
		805	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2-2022	3/2024 (Dec-24) {12/2024}	417.51 (N.A.) {417.51}	252.29	80.98
		806	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 9OF EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8-2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	169.81	32.94
		807	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2-2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,217.65	35.00
		808	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3-2021	4/2024 (May-24) {8/2024}	790.78 (N.A.) {790.78}	1,715.94	62.50
		809	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1-2021	10/2023 (N.A.) {2/2025}	428.04 (N.A.) {428.04}	351.27	98.92

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		810	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9-2019	9/2022 (N.A.) {1/2025}	194.40 (235.00) {235.00}	197.87	95.38
		811	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3-2024	3/2026 (Mar-26) {3/2026}	799.20 (N.A.) {799.20}	200.56	20.09
		812	BALANCE WORKS OF 4 LANE DIVIDED CARRIAGEWAY OF MISSING LINK SECTION OF NH-39 (REWA BYPASS) FROM JUNC (NHAI) (N24002200)	4-2024	4/2026 (N.A.) {4/2026}	355.36 (N.A.) {355.36}	11.67	9.71
		813	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3-2015	8/2017 (Dec-23) {6/2025}	511.83 (N.A.) {511.83}	485.18	93.06
		814	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12-2017	2/2020 (Dec-24) {12/2024}	950.27 (N.A.) {786.43}	634.27	99.50
	<u>SOCIAL JUSTICE</u>	815	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2-2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74.00
	<u>URBAN DEVELOPMENT</u>	816	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11-2018	2/2023 (Jun-28) {6/2028}	6,941.40 (N.A.) {6,941.40}	2,692.56	38.25
		817	INDORE METRO RAIL (MPMRCL) (N28000125)	11-2018	2/2023 (Dec-28) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,425.69	49.85
<u>MAHARASHTRA</u>	<u>CIVIL AVIATION</u>	818	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3-2017	4/2021 (N.A.) {12/2023}	475.39 (N.A.) {520.00}	508.14	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		819	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6-2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	267.86	100.00
	COAL	820	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8-2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	530.02	86.00
		821	UKNI DEEP OC (WCL) (N06000179)	1-2019	3/2021 (Mar-25) {3/2025}	237.06 (N.A.) {318.14}	163.86	91.00
		822	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3-2021	3/2028 (N.A.) {3/2029}	184.71 (N.A.) {241.72}	9.25	6.00
		823	SASTI EXPANSION OC (WCL) (N06000206)	8-2020	3/2026 (N.A.) {3/2026}	319.04 (N.A.) {371.59}	68.64	24.00
		824	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	10-2021	3/2028 (N.A.) {3/2028}	711.00 (N.A.) {720.87}	159.15	33.00
		825	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11-2018	3/2024 (Mar-25) {3/2025}	316.00 (N.A.) {333.43}	208.20	78.00
		826	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2-2020	3/2027 (N.A.) {3/2027}	822.88 (N.A.) {1,184.33}	578.89	48.00
		827	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9-2018	3/2024 (Mar-25) {3/2025}	235.90 (N.A.) {313.34}	116.46	87.00
		828	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (WCL) (N06000231)	11-2020	3/2026 (N.A.) {3/2026}	826.80 (N.A.) {826.80}	518.85	52.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		829	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1-2022	3/2028 (N.A.) {3/2028}	228.64 (N.A.) {253.51}	118.34	27.00
		830	SINGHORI DEEP OC (WCL) (N06000252)	5-2022	3/2029 (N.A.) {3/2029}	335.75 (N.A.) {421.84}	22.01	16.00
		831	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6-2022	3/2026 (N.A.) {3/2026}	361.87 (N.A.) {497.06}	33.90	12.00
		832	BHATADI EXPANSION OC (WCL) (N06000254)	5-2022	3/2028 (N.A.) {3/2028}	580.60 (N.A.) {729.86}	61.33	17.00
		833	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	9-2022	3/2027 (N.A.) {3/2027}	402.27 (N.A.) {496.38}	47.99	27.00
		834	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9-2022	3/2028 (N.A.) {3/2028}	405.20 (N.A.) {494.60}	10.21	7.00
		835	GOKUL EXPANSION OC (WCL) (N06000264)	4-2021	3/2026 (N.A.) {3/2026}	309.58 (N.A.) {456.95}	3.65	7.00
		836	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	9-2023	3/2027 (N.A.) {3/2027}	198.71 (N.A.) {206.19}	0.55	5.00
		837	GAURI CENTRAL OCM (WCL) (N06000278)	6-2024	3/2030 (N.A.) {3/2030}	973.07 (N.A.) {1,015.07}	0.00	-
		838	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3-2024	3/2030 (N.A.) {3/2030}	1,225.21 (N.A.) {1,428.25}	52.83	17.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		839	BALLARPUR NORTHWEST OC MINE (WCL) (N06000282)	12-2022	3/2029 (N.A.) {3/2029}	360.18 (N.A.) {360.18}	0.00	-
		840	NORTHERN EXTENSION OF MUNGOLI NIRGUDA DEEP OC (WCL) (N06000283)	6-2024	3/2029 (N.A.) {3/2029}	1,024.91 (N.A.) {1,184.44}	0.00	-
		841	AMALGAMATED GONDEGAON - GHATROHAN EXPANSION OCM (WCL) (N06000284)	9-2024	3/2029 (N.A.) {3/2029}	668.54 (N.A.) {871.59}	0.00	-
	DEPARTMENT OF HIGHER EDUCATION	842	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1-2018	7/2020 (Nov-23) {2/2024}	223.37 (275.00) {230.00}	141.16	100.00
	HEALTH AND FAMILY WELFARE	843	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7-2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	99.08	-
	PETROLEUM	844	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4-2022	10/2024 (Aug-26) {8/2026}	341.43 (436.14) {436.14}	222.23	37.70
		845	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5-2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	299.83	45.80
		846	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3-2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	138.75	61.50
		847	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12-2015	4/2018 (Dec-23) {6/2025}	3,190.69 (3,375.90) {3,375.90}	2,967.37	87.80

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		848	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4-2019	3/2022 (Jun-24) {2/2025}	3,228.80 (3,976.67) {3,976.67}	3,957.65	99.50
		849	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5-2019	4/2025 (Oct-25) {10/2025}	8,797.00 (11,256.00) {11,256.00}	5,775.34	79.30
		850	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436)	1-2022	5/2024 (Jan-25) {3/2025}	3,183.58 (N.A.) {3,645.23}	3,417.00	99.50
		851	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4-2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	707.46	66.40
		852	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9-2021	10/2023 (May-24) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08
		853	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3-2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	49.13	1.90
		854	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5-2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	211.00	71.00
		855	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9-2022	8/2025 (N.A.) {3/2026}	165.00 (N.A.) {165.00}	63.09	57.62
		856	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6-2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	1,431.67	23.70

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		857	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11-2022	5/2024 (Dec-24) {3/2025}	1,219.48 (N.A.) {1,145.10}	477.49	65.40
		858	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6-2017	5/2025 (Jun-26) {6/2026}	281.35 (389.67) {389.67}	207.95	44.60
		859	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2-2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	272.30	23.40
		860	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6-2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	221.91	20.70
		861	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6-2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	16.15	17.20
		862	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5-2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	3.60
	POWER	863	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4-2022	5/2024 (N.A.) {9/2025}	5,491.89 (532.00) {5,491.89}	3,123.44	65.49
		864	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11-2023	7/2025 (N.A.) {7/2025}	224.00 (N.A.) {224.00}	0.00	3.00
	RAILWAYS	865	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2-1997	3/2021 (N.A.) {12/2025}	2,271.50 (N.A.) {4,909.82}	4,606.38	91.00
		866	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4-2008	3/2014 (N.A.) {3/2014}	5,300.00 (N.A.) {918.53}	7,135.77	77.30

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		867	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4-2012	3/2022 (N.A.) {5/2025}	540.02 (N.A.) {540.02}	674.26	72.00
		868	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4-2011	3/2021 (N.A.) {12/2025}	792.89 (N.A.) {1,432.61}	819.32	50.00
		869	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4-2008	3/2023 (N.A.) {12/2026}	3,168.29 (N.A.) {3,445.34}	2,928.87	47.00
		870	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2-2016	3/2023 (N.A.) {5/2025}	637.95 (N.A.) {637.95}	871.04	70.00
		871	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2-2015	3/2022 (N.A.) {8/2025}	1,272.19 (N.A.) {1,384.72}	1,341.25	67.00
		872	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2-2015	3/2023 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,554.61	48.00
		873	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2-2015	3/2024 (N.A.) {3/2025}	3,627.47 (3,627.00) {6,463.49}	4,309.66	84.00
		874	DAUND - MANMAD (236 KM) (CR) (N22000360)	2-2016	3/2023 (N.A.) {9/2025}	1,876.00 (N.A.) {2,081.27}	2,493.96	87.00
		875	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2-2016	3/2022 (N.A.) {3/2025}	1,035.16 (N.A.) {1,552.24}	1,506.48	75.00
		876	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9-2016	3/2023 (N.A.) {12/2025}	1,908.51 (N.A.) {3,544.25}	2,943.44	90.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		877	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3-2010	(N.A.) {3/2024}	265.88 (N.A.) {311.36}	0.00	-
		878	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6-2018	12/2021 (N.A.) {12/2026}	229.00 (N.A.) {1,886.05}	624.50	22.00
		879	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2-2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	9.19	-
		880	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8-2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,093.82}	60.69	-
		881	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1-2019	3/2028 (N.A.) {10/2027}	904.92 (N.A.) {3,295.74}	1,067.98	5.00
		882	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1-2019	3/2026 (N.A.) {9/2027}	492.76 (N.A.) {1,170.04}	176.04	5.00
		883	BARAMATI - LONAND (CR) (N22000615)	2-1999	3/2027 (N.A.) {2/2026}	736.44 (N.A.) {1,843.90}	629.53	50.00
		884	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4-2019	3/2025 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	846.83	-
		885	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10-2019	6/2024 (Mar-25) {3/2025}	1,400.00 (N.A.) {1,400.00}	0.00	78.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	886	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3-2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	229.31	31.27
		887	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7-2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	20.08	2.00
		888	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2-2024	3/2025 (N.A.) {3/2025}	175.00 (N.A.) {175.00}	144.18	76.00
		889	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA (NHAI) (N24001795)	10-2022	7/2024 (N.A.) {12/2024}	490.40 (N.A.) {289.00}	275.78	88.00
		890	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3-2022	10/2024 (Apr-25) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		891	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10-2021	1/2024 (N.A.) {3/2025}	815.77 (N.A.) {815.77}	671.66	94.83
		892	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2-2021	11/2023 (N.A.) {2/2025}	540.21 (N.A.) {540.21}	433.66	98.98
		893	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2-2021	10/2023 (N.A.) {3/2025}	1,166.96 (N.A.) {1,251.00}	1,064.43	80.33

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		894	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12-2019	9/2022 (Jun-24) {6/2024}	1,654.07 (N.A.) {980.00}	835.19	95.18
		895	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5-2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	433.13	45.75
		896	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5-2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	387.44	44.10
		897	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3-2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	27.35
		898	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3-2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8.00
		899	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3-2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65.00
		900	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3-2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		901	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2-2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		902	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10-2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78
		903	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8-2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	78.44
		904	UP-GRADATION OF TIROGA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIROGA) TO KM 191+ (MoRTH) (N24001888)	8-2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31
		905	2 LANE + PS PIMPLNER TO SATANA - [DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9-2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	90.00
		906	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2-2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46.00
		907	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7-2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66
		908	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2-2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.50
		909	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9-2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		910	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11-2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99.00
		911	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11-2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
		912	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12-2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34.00
		913	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8-2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	-
		914	KOPARGAON TO SAVALI VIHAR SECTION (MoRTH) (N24001904)	9-2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		915	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10-2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.80
		916	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8-2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48.00
		917	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6-2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		918	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12-2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		919	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL) (MoRTH) (N24001909)	11-2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
		920	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7) (MoRTH) (N24001910)	9-2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		921	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3-2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		922	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3-2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	-
		923	TUNNEL AT KHAMBATKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2-2019	2/2022 (Dec-24) {10/2025}	493.00 (N.A.) {493.00}	385.16	75.07
		924	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9-2021	9/2023 (Dec-24) {3/2025}	618.45 (N.A.) {618.45}	606.34	92.30
		925	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12-2022	12/2024 (N.A.) {12/2024}	1,749.86 (N.A.) {1,749.86}	1,807.94	62.54
		926	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 ((NHAI) (N24001495)	11-2022	11/2024 (N.A.) {11/2024}	930.00 (N.A.) {930.00}	579.71	70.45

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		927	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501)	9-2021	9/2023 (Jul-23) {7/2023}	531.86 (532.41) {532.41}	520.71	0.50
		928	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9-2021	9/2023 (May-25) {5/2025}	624.45 (580.15) {580.15}	405.31	2.00
		929	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9-2021	9/2023 (Jan-25) {3/2025}	667.66 (666.21) {666.21}	598.65	3.00
		930	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5-2022	5/2024 (Jan-25) {1/2025}	1,260.00 (N.A.) {1,260.00}	608.72	93.20
		931	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3-2022	3/2024 (May-25) {5/2025}	1,549.02 (N.A.) {1,549.02}	537.10	61.00
		932	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2-2022	2/2024 (Jun-25) {6/2025}	2,747.00 (N.A.) {2,747.00}	929.38	69.11
		933	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11-2022	5/2024 (Jun-25) {6/2025}	1,124.00 (N.A.) {1,124.00}	360.76	53.35
		934	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11-2022	10/2024 (Jun-25) {6/2025}	1,450.00 (N.A.) {1,450.00}	638.66	75.13

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		935	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11-2022	10/2024 (Apr-25) {4/2025}	990.00 (N.A.) {990.00}	352.70	60.02
		936	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1-2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	428.49	41.85
		937	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH- 17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10-2022	5/2024 (Dec-25) {12/2025}	332.00 (N.A.) {332.00}	237.61	59.64
		938	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9-2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	488.60	64.67
		939	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH- 66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1-2023	12/2023 (Mar-25) {3/2025}	151.26 (N.A.) {151.26}	141.21	75.51
		940	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1-2022	5/2024 (Mar-25) {3/2025}	1,833.73 (N.A.) {1,833.73}	481.89	89.41
		941	SHAHNUR PATGAON SECTION I (MoRTH) (N24001027)	1-2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	71.00
		942	JINTUR TO PARBHANI (MoRTH) (N24001039)	1-2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	80.00
		943	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1-2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.50

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		944	VITA TO NAGAJ (MoRTH) (N24001050)	3-2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		945	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2-2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	89.97
		946	KARWANDI TO RAJURI (MoRTH) (N24001058)	3-2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		947	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3-2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95.00
		948	NANDED TO JALKOT (MoRTH) (N24001069)	12-2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	-
		949	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3-2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	94.00
		950	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12-2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25
		951	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3-2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98.00
		952	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3-2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	89.99
		953	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3-2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		954	KOLDE TO KHETIYA (MoRTH) (N24001090)	1-2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	95.00
		955	SATARA TO MHASWAD (MoRTH) (N24001092)	1-2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	76.76
		956	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1-2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	88.00
		957	SELDOH TO PANVAR (MoRTH) (N24001097)	7-2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	-
		958	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1-2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.50
		959	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1-2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.00
		960	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7-2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		961	PEN TO KHOPOLI (MoRTH) (N24001106)	3-2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		962	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7-2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	-
		963	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4-2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		964	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7-2016	9/2019 (N.A.) {3/2024}	406.54 (407.00) {406.54}	274.30	80.70
		965	INDAPUR TO VADPALE (MoRTH) (N24001114)	1-2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		966	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3-2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.60
		967	SHIRUR TO KHARDA (MoRTH) (N24001123)	2-2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		968	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2-2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		969	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2-2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		970	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2-2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	87.84
		971	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9-2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		972	KANTE TO WAKED (MoRTH) (N24001134)	3-2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	-
		973	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2-2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		974	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377)	2-2019	1/2022 (Aug-23) {8/2023}	731.89 (731.99) {731.99}	692.21	0.20
		975	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378)	2-2019	1/2022 (Jun-23) {6/2023}	362.46 (372.46) {372.46}	352.01	0.70
		976	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379)	2-2019	1/2022 (Aug-23) {8/2023}	594.75 (594.75) {613.75}	585.20	0.50
		977	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11-2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88
		978	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3-2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	0.00	-
		979	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3-2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	0.00	-
		980	REHABILITATION & UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START F (MoRTH) (N24002171)	2-2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	0.00	-
		981	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172)	2-2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		982	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2-2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	0.00	-
		983	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHI (MoRTH) (N24002174)	2-2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	0.00	-
		984	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2-2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	0.00	-
		985	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STANDA (MoRTH) (N24002176)	3-2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	0.00	-
		986	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILOD TOWN WITH D (MoRTH) (N24002177)	3-2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	0.00	-
		987	REHABILITATION, UPGRADATION & WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHOUL (MoRTH) (N24002178)	2-2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	0.00	-
		988	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1-2015	(N.A.) {}	225.81 (N.A.) {225.81}	167.96	96.00
		989	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12-2015	3/2019 (Nov-23) {3/2025}	649.50 (N.A.) {649.50}	601.19	90.34

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		990	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3-2016	7/2019 (Mar-24) {2/2025}	591.66 (N.A.) {591.66}	617.70	95.15
		991	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3-2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		992	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3-2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	-
		993	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655)	3-2017	3/2020 (Nov-24) {11/2024}	247.02 (N.A.) {157.49}	92.22	100.00
		994	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3-2017	3/2020 (Jul-22) {3/2025}	744.64 (N.A.) {1,007.00}	467.65	92.01
		995	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3-2017	3/2017 (May-21) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	82.04
		996	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3-2018	7/2021 (N.A.) {6/2025}	1,162.92 (1,182.87) {1,182.87}	371.48	55.80
		997	SARSAM TO KOTHARI (MoRTH) (N24001002)	2-2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		998	AKOLA TO AKOT (MoRTH) (N24001003)	1-2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		999	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1-2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
		1000	DAHEGAON TO KUHI (MoRTH) (N24001017)	1-2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99.00
		1001	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1-2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100.00
		1002	AMDIT TO SAONER (MoRTH) (N24001021)	1-2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69
		1003	WADI TO ASOLA (MoRTH) (N24001022)	1-2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
	URBAN DEVELOPMENT	1004	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) (MMRCL) (N28000086)	7-2013	3/2020 (N.A.) {12/2023}	23,136.00 (N.A.) {37,276.00}	23,687.33	87.20
		1005	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12-2016	11/2021 (Sep-24) {9/2024}	11,420.00 (13,656.22) {13,656.22}	12,908.85	100.00
		1006	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12-2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	548.89	17.13
		1007	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10-2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	40.54	9.10
		1008	PUNE METRO PHASE-1 EXTENSION FROM SWARGATE TO KATRAJ (MMRC) (N28000160)	9-2024	3/2029 (N.A.) {3/2029}	2,954.53 (N.A.) {2,954.53}	1.90	1.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MANIPUR	CIVIL AVIATION	1009	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11-2021	7/2024 (Mar-26) {3/2026}	499.00 (N.A.) {499.00}	133.55	38.12
	RAILWAYS	1010	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4-2003	3/2011 (Mar-28) {12/2028}	4,454.17 (12,274.06) {19,517.70}	15,068.36	81.25
	ROAD TRANSPORT AND HIGHWAYS	1011	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9-2021	1/2025 (Sep-25) {9/2025}	315.56 (N.A.) {315.56}	93.08	63.74
		1012	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1-2023	12/2025 (Dec-25) {12/2025}	760.16 (N.A.) {760.16}	89.50	38.82
		1013	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3-2023	2/2026 (Mar-26) {3/2026}	578.98 (N.A.) {578.98}	94.21	40.90
		1014	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9-2021	2/2024 (Mar-25) {3/2025}	310.76 (N.A.) {310.76}	129.15	84.05
		1015	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12-2021	5/2024 (Feb-25) {10/2025}	410.68 (N.A.) {410.68}	118.03	59.04
		1016	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12-2021	2/2025 (Sep-25) {9/2025}	504.76 (N.A.) {504.76}	133.28	59.15
		1017	AKASH BRIDGE - JESSAMI SECTION PKG- 2 (NHIDCL) (N24001540)	3-2022	2/2025 (Feb-25) {2/2025}	152.11 (N.A.) {152.11}	62.86	89.65

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {MM/YYYY}	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1018	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3-2020	6/2022 (Jan-25) {5/2025}	292.24 (N.A.) {292.24}	127.86	85.33
		1019	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6-2020	8/2022 (Jan-25) {5/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		1020	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3-2020	6/2022 (Jan-25) {5/2025}	167.95 (204.12) {167.95}	88.05	69.89
		1021	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7-2020	8/2022 (Feb-25) {2/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		1022	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8-2020	4/2022 (May-25) {6/2025}	379.39 (N.A.) {379.39}	193.87	53.30
		1023	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8-2020	4/2022 (N.A.) {3/2025}	228.97 (N.A.) {228.97}	0.00	-
		1024	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2-2021	12/2022 (Mar-25) {3/2025}	226.32 (N.A.) {226.32}	96.41	71.20
		1025	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2-2021	12/2022 (Oct-24) {2/2025}	188.36 (N.A.) {188.36}	126.71	98.50
		1026	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3-2021	12/2022 (Mar-25) {3/2026}	195.14 (N.A.) {195.14}	61.81	50.79
		1027	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3-2021	12/2022 (Jan-25) {6/2025}	234.08 (N.A.) {234.08}	139.45	90.34

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {MM/YYYY}	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1028	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3-2021	1/2023 (May-25) {5/2025}	211.70 (N.A.) {211.70}	58.43	52.64
		1029	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7-2021	3/2023 (Mar-25) {3/2025}	467.00 (N.A.) {467.00}	188.84	76.34
		1030	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7-2021	3/2023 (Jan-25) {1/2025}	185.80 (N.A.) {185.80}	114.69	100.00
		1031	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7-2021	3/2023 (Aug-24) {6/2025}	483.87 (N.A.) {483.87}	278.89	91.72
		1032	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7-2021	3/2023 (Feb-25) {3/2025}	198.77 (N.A.) {198.77}	113.05	89.98
		1033	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7-2021	10/2023 (Mar-25) {3/2025}	673.27 (N.A.) {673.27}	367.93	74.40
		1034	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8-2021	5/2023 (Apr-25) {6/2025}	477.86 (N.A.) {477.86}	239.80	82.21
		1035	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9-2021	5/2023 (Nov-24) {6/2025}	311.18 (N.A.) {311.18}	171.57	76.45
		1036	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8-2021	5/2023 (Oct-24) {2/2025}	467.41 (N.A.) {467.41}	258.10	98.41
		1037	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8-2021	12/2023 (Jul-25) {7/2025}	579.63 (N.A.) {579.63}	149.36	59.58

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		1038	MARREM KHULLEN TO JESSAMI SECTION IMPHAL- UKHRUL - JESSAMI PKG-6 (DESIGN CHAINAGE KM 95.700 TO KM 14 (NHIDCL) (N24002202)	3-2023	12/2026 (N.A.) {12/2026}	554.66 (N.A.) {554.66}	0.00	-
		1039	IMPHAL-KOHIMA ROAD PKG-4B (NHIDCL) (N24002203)	9-2020	6/2026 (N.A.) {6/2026}	268.98 (N.A.) {268.98}	0.00	3.80
	DEPARTMENT OF HIGHER EDUCATION	1040	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9-2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	289.55	75.80
	ROAD TRANSPORT AND HIGHWAYS	1041	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH- 06 NEAR LADUM (NHIDCL) (N24002156)	3-2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	184.85	15.91
		1042	SHILLONG WESTERN BYPASS PACKAGE- 2 (NHIDCL) (N24002157)	3-2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	255.10	10.09
		1043	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9-2021	5/2024 (Dec-24) {12/2025}	359.86 (N.A.) {359.86}	220.74	83.50
		1044	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11-2021	6/2024 (Dec-24) {3/2025}	283.50 (N.A.) {283.50}	224.23	83.30
		1045	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11-2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	259.62	42.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1046	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11-2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	398.05	17.00
		1047	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11-2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	196.37	12.50
		1048	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11-2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	58.34	8.60
		1049	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10-2020	4/2022 (Jun-24) {2/2025}	157.86 (146.92) {157.86}	149.39	98.62
		1050	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3-2021	12/2022 (Jun-24) {2/2025}	260.21 (N.A.) {260.21}	224.90	98.39
		1051	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8-2020	2/2022 (Feb-25) {2/2025}	302.88 (N.A.) {302.88}	221.73	94.96
		1052	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH- 06 NEAR LADU (NHIDCL) (N24002158)	3-2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	273.37	12.63
		1053	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4-2017	9/2021 (Mar-25) {3/2025}	553.51 (610.09) {553.51}	366.39	74.24

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MIZORAM	RAILWAYS	1054	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4-2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,721.26	94.00
	ROAD TRANSPORT AND HIGHWAYS	1055	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9-2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	263.25	49.80
		1056	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12-2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	148.96	41.52
		1057	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL - TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9-2020	10/2022 (Mar-24) {3/2024}	275.02 (247.25) {247.25}	231.19	99.73
		1058	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3-2020	7/2022 (Jun-24) {6/2024}	206.88 (219.33) {219.33}	206.58	97.01
		1059	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3-2020	7/2022 (Oct-24) {10/2024}	292.24 (331.17) {331.17}	293.90	91.64
		1060	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3-2021	12/2022 (Mar-24) {3/2024}	374.39 (N.A.) {318.92}	292.37	100.00
		1061	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3-2021	12/2022 (Apr-24) {4/2024}	233.25 (N.A.) {233.25}	178.37	100.00
		1062	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3-2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	400.71	43.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1063	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3-2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	293.89	42.00
		1064	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9-2021	5/2023 (May-24) {5/2024}	492.94 (492.94) {492.94}	357.26	84.70
		1065	ZORINPUI- HMAWNGBU-LONGMASU (NH-502A) (NHIDCL) (N24002204)	2-2023	12/2026 (N.A.) {12/2026}	781.85 (N.A.) {781.85}	0.00	-
		1066	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4-2017	4/2023 (Nov-24) {1/2025}	519.09 (785.65) {785.65}	657.51	90.12
		1067	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4-2017	7/2023 (May-24) {5/2024}	640.07 (990.88) {1,286.35}	1,217.65	99.00
		1068	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4-2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.84	99.50
		1069	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4-2017	4/2023 (Nov-24) {2/2025}	473.18 (688.25) {688.25}	521.23	85.10
		1070	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4-2017	4/2023 (Jul-24) {2/2025}	537.82 (789.05) {789.05}	752.90	91.60
		1071	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4-2017	6/2023 (Oct-24) {3/2025}	518.53 (906.76) {906.76}	804.57	90.15

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1072	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4-2017	4/2024 (Nov-24) {3/2025}	404.29 (750.32) {750.32}	599.84	85.60
		1073	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4-2017	9/2023 (Nov-24) {3/2025}	428.11 (746.39) {746.39}	588.02	87.70
MULTI STATE	COAL	1074	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8-2016	3/2022 (Mar-25) {3/2025}	319.76 (319.76) {319.76}	183.67	98.00
		1075	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8-2020	3/2024 (N.A.) {3/2025}	836.42 (N.A.) {836.42}	714.34	56.74
	DPIIT	1076	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9-2011	3/2027 (Mar-27) {3/2027}	20,084.00 (20,084.00) {20,084.00}	11,217.21	50.99
	PETROLEUM	1077	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6-2009	12/2012 (Feb-25) {3/2025}	2,915.00 (5,909.00) {5,909.00}	4,153.30	93.30
		1078	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9-2019	7/2022 (Jun-25) {6/2025}	2,658.34 (N.A.) {2,658.34}	2,037.90	93.30
		1079	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3-2020	11/2022 (Jul-25) {12/2025}	1,030.65 (N.A.) {1,030.65}	810.40	85.40
		1080	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6-2020	5/2023 (Jun-25) {6/2025}	7,844.25 (N.A.) {7,844.25}	5,927.50	91.90
		1081	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6-2019	12/2029 (Mar-30) {3/2030}	169.00 (N.A.) {169.00}	74.75	18.10

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1082	NORTH EAST GAS GRID (IGGL) (N16000439)	11-2020	3/2024 (Jul-25) {3/2027}	9,265.00 (9,265.00) {9,265.00}	5,746.93	83.98
		1083	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7-2023	7/2026 (Jul-26) {7/2026}	521.92 (521.92) {521.92}	82.10	23.90
	POWER	1084	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12-2014	12/2018 (Mar-25) {3/2025}	4,754.42 (9,129.32) {9,129.32}	6,938.35	77.90
		1085	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12-2014	12/2018 (Mar-25) {3/2025}	5,111.33 (6,700.00) {6,700.00}	5,026.36	95.50
		1086	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264)	8-2017	2/2020 (Apr-23) {9/2025}	1,931.39 (2,635.55) {2,635.55}	1,972.44	99.00
		1087	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5-2022	11/2023 (N.A.) {3/2025}	1,666.00 (N.A.) {1,666.00}	1,428.62	83.00
		1088	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7-2022	6/2023 (N.A.) {5/2025}	4,546.26 (N.A.) {4,546.26}	2,550.35	84.00
		1089	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2-2022	4/2025 (N.A.) {4/2025}	318.12 (N.A.) {318.12}	154.75	90.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1090	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3-2022	12/2024 (N.A.) {9/2025}	288.71 (N.A.) {288.71}	133.79	47.00
		1091	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2-2022	9/2023 (N.A.) {3/2025}	359.47 (N.A.) {359.47}	271.16	79.00
		1092	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7-2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	69.53	90.00
		1093	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10-2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	135.31	68.00
		1094	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3-2023	11/2024 (N.A.) {5/2025}	3,546.94 (N.A.) {3,546.94}	1,940.14	80.00
		1095	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3-2023	3/2025 (N.A.) {3/2025}	281.16 (N.A.) {281.16}	89.14	63.00
	RAILWAYS	1096	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3-1981	7/2012 (Jan-27) {1/2027}	450.00 (N.A.) {2,017.96}	1,487.70	70.00
		1097	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9-1998	5/2008 (N.A.) {3/2025}	247.66 (63.57) {8,248.50}	2,520.04	43.00
		1098	CHHAPRA-BALLIA UP (NER) (N22000134)	3-2013	1/2019 (N.A.) {4/2025}	295.00 (954.00) {1,025.00}	999.02	95.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1099	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4-2007	3/2022 (Dec-27) {12/2027}	1,347.26 (1,793.63) {1,793.63}	1,581.16	58.00
		1100	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4-2007	3/2022 (Feb-27) {2/2027}	1,640.04 (1,873.10) {2,873.11}	2,570.16	58.00
		1101	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4-2011	3/2022 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	-
		1102	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI- TANTPUR AND TAMPUR-BANSI PAHARPUR (NCR) (N22000158)	4-2010	(Dec-26) {12/2026}	2,030.50 (746.83) {746.83}	121.79	30.00
		1103	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4-2007	(N.A.) {}	336.91 (N.A.) {791.39}	572.99	-
		1104	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4-2013	3/2019 (N.A.) {10/2024}	1,798.00 (N.A.) {2,832.35}	3,456.93	99.50
		1105	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4-2010	3/2020 (N.A.) {3/2027}	242.22 (N.A.) {1,206.60}	390.69	5.00
		1106	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4-2010	(Dec-26) {12/2026}	241.52 (485.96) {485.96}	365.06	86.21
		1107	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4-2011	3/2020 (N.A.) {11/2025}	414.84 (N.A.) {1,252.49}	664.78	41.00
		1108	PIRPAINTI-JASIDIH (ER) (N22000219)	4-2013	3/2022 (Mar-28) {3/2028}	915.98 (N.A.) {2,610.84}	856.63	45.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1109	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4-2012	3/2023 (N.A.) {3/2025}	1,856.95 (N.A.) {1,952.68}	1,538.88	-
		1110	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4-2007	(N.A.) {2/2028}	2,062.30 (2,495.59) {2,495.59}	1,582.66	60.00
		1111	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12-2015	12/2023 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	70,051.00	49.00
		1112	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3-2015	3/2019 (N.A.) {2/2026}	1,614.59 (1,877.81) {2,458.87}	2,470.09	89.00
		1113	KAZIPET-BALHRSHA (SCR) (N22000367)	4-2015	3/2021 (N.A.) {1/2025}	2,063.03 (N.A.) {2,909.00}	2,711.95	-
		1114	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11-2007	3/2020 (N.A.) {3/2020}	16,592.00 (51,101.00) {51,101.00}	47,476.00	83.00
		1115	CHANDIGARH-BADDI (NR) (N22000467)	4-2007	3/2023 (Apr-26) {7/2026}	328.14 (1,540.14) {1,540.14}	898.24	14.00
		1116	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3-2019	5/2023 (N.A.) {6/2026}	1,866.31 (N.A.) {1,866.31}	1,770.76	57.00
	ROAD TRANSPORT AND HIGHWAYS	1117	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11-2021	2/2025 (N.A.) {2/2025}	2,155.95 (N.A.) {2,155.95}	1,195.52	54.76
		1118	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4-2022	11/2024 (Mar-25) {3/2025}	796.65 (N.A.) {796.65}	353.25	75.53

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1119	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9-2011	3/2014 (N.A.) {9/2024}	2,848.00 (N.A.) {3,241.56}	3,901.66	87.67
	SHIPPING AND PORTS	1120	JAL MARG VIKAS PROJECT (IWAI) (N25000072)	1-2018	3/2023 (Dec-25) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,258.79	64.91
	TELECOMMUNI CATIONS	1121	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3-2023	3/2024 (Jul-24) {2/2025}	239.60 (N.A.) {239.60}	174.09	100.00
		1122	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB- P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3-2020	6/2021 (Nov-21) {3/2025}	461.42 (461.42) {461.42}	165.04	81.00
		1123	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5-2023	8/2024 (Nov-24) {3/2025}	645.13 (N.A.) {645.13}	330.40	85.63
		1124	PLANNIN ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGRATION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6-2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	6,098.44	78.16
		1125	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2-2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	425.00	80.32
	URBAN DEVELOPMENT	1126	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTE) (N28000134)	3-2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	23,738.20	82.50
NAGALAND	PETROLEUM	1127	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8-2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	2.76	13.90

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	RAILWAYS	1128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4-2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	4,072.86	65.00
	ROAD TRANSPORT AND HIGHWAYS	1129	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12-2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	50.74	34.57
		1130	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12-2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	15.40
		1131	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12-2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	109.02	46.17
		1132	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2-2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	92.58	79.74
		1133	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2-2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	33.10	45.54
		1134	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6-2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	-
		1135	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3-2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	121.54	71.63

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1136	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3-2021	2/2024 (Feb-25) {2/2025}	226.44 (N.A.) {226.44}	129.94	91.65
		1137	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3-2022	12/2024 (N.A.) {1/2025}	605.36 (N.A.) {605.36}	261.48	100.00
		1138	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3-2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100.00
		1139	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3-2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100.00
		1140	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9-2020	10/2022 (Sep-24) {6/2026}	277.44 (N.A.) {277.44}	166.31	64.48
		1141	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8-2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	84.96	20.04
		1142	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8-2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	72.03	27.58
		1143	UPGRADATION OF EXISTING ROAD TO 2- LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9-2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1144	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3-2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	60.74
		1145	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3-2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100.00
		1146	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4-2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	130.84	73.01
		1147	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8-2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	63.64	11.01
		1148	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3-2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.40
		1149	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7-2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	78.00	70.33
		1150	MERANGKONG-TAMLU-MON (MTM) PKG- 5 (NHIDCL) (N24001438)	7-2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	51.05	40.04
		1151	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3-2016	9/2019 (Nov-22) {2/2025}	373.07 (534.41) {534.41}	382.50	99.81
		1152	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3-2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	311.07	87.21

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1153	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2-2017	9/2020 (Feb-23) {3/2025}	387.00 (688.12) {688.12}	387.55	99.46
		1154	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3-2018	11/2022 (Aug-24) {3/2025}	500.09 (698.81) {698.81}	373.62	96.93
		1155	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3-2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	193.90	99.90
		1156	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3-2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	118.72	49.47
		1157	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3-2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	99.61	37.47
ODISHA	COAL	1158	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5-2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	267.05	62.00
		1159	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2-2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,430.37	42.80
		1160	GARJANBAHAL OCP (MCL) (N06000117)	11-2014	3/2021 (N.A.) {3/2026}	1,375.38 (N.A.) {1,375.38}	849.48	58.10
		1161	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP (MCL) (N06000167)	5-2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,866.35	55.10

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1162	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11-2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,734.45	44.60
		1163	TALABIRA II AND III OCP (NLC) (N06000189)	7-2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,477.16	57.00
		1164	NAINI COAL MINE (SCCL) (N06000203)	3-2020	3/2024 (N.A.) {3/2026}	494.30 (N.A.) {494.30}	491.33	35.00
		1165	GOPALJI-KANIHA OCP (MCL) (N06000229)	4-2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,648.02	16.70
		1166	BALARAM EXPANSION OCP (MCL) (N06000230)	8-2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	983.88	49.90
		1167	KULDA EXPANSION OCP- 15 MTY (MCL) (N06000248)	6-2014	3/2018 (N.A.) {3/2026}	348.16 (N.A.) {348.16}	207.75	60.00
		1168	SUBHADRA OCP (MCL) (N06000249)	5-2021	3/2029 (Mar-29) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,171.56	39.10
		1169	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1-2024	5/2029 (Mar-30) {3/2030}	27,213.00 (N.A.) {27,213.00}	1,433.30	1.55
		1170	RPR OF HINGULA EXPANSION OCP (MCL) (N06000285)	11-2022	3/2029 (N.A.) {3/2029}	1,561.85 (N.A.) {1,561.85}	0.00	-
		1171	BHUBANESWARI EXPANSION OCP (MCL) (N06000286)	3-2024	3/2031 (N.A.) {3/2031}	5,366.28 (N.A.) {5,366.28}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	DEPARTMENT OF HIGHER EDUCATION	1172	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1-2019	3/2022 (N.A.) {4/2025}	790.79 (N.A.) {790.79}	685.11	95.00
	MINES	1173	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12-2014	4/2021 (Sep-25) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,479.10	70.53
		1174	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5-2016	1/2020 (Nov-23) {3/2024}	534.00 (N.A.) {1,021.97}	770.80	83.50
		1175	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11-2017	4/2021 (May-25) {5/2025}	483.00 (483.00) {483.00}	367.40	87.62
		1176	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12-2015	11/2020 (Sep-25) {11/2026}	355.00 (581.00) {581.00}	130.79	12.60
		1177	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9-2019	3/2023 (May-24) {5/2024}	225.79 (N.A.) {270.66}	5.00	100.00
		1178	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5-2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	649.96	50.60
	PETROLEUM	1179	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11-2018	9/2021 (Dec-24) {3/2025}	462.30 (552.44) {552.44}	481.20	96.90
		1180	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7-2020	1/2024 (Apr-25) {4/2025}	13,805.00 (N.A.) {13,805.00}	7,116.57	87.50

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1181	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3-2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	324.97	75.00
		1182	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8-2022	5/2027 (N.A.) {5/2027}	11,844.00 (N.A.) {12,539.00}	2,638.09	19.70
	RAILWAYS	1183	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4-2005	6/2021 (N.A.) {3/2026}	810.78 (N.A.) {1,928.07}	1,552.14	40.00
		1184	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4-1994	3/2009 (Dec-26) {12/2026}	2,923.13 (3,791.66) {5,089.37}	4,396.72	82.00
		1185	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4-2015	3/2022 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,234.44	91.00
		1186	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3-2013	10/2020 (Oct-25) {10/2025}	843.04 (1,284.39) {1,284.39}	1,175.97	75.00
		1187	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4-2015	11/2018 (N.A.) {8/2026}	701.61 (N.A.) {810.02}	548.52	-
		1188	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4-2015	12/2018 (Sep-25) {9/2025}	1,172.92 (N.A.) {2,022.75}	1,800.38	75.00
		1189	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1-1991	12/2024 (N.A.) {12/2026}	2,335.67 (N.A.) {4,803.16}	4,691.52	-
		1190	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4-2015	3/2022 (Mar-26) {3/2026}	2,361.74 (2,361.74) {2,361.74}	1,673.98	74.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1191	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4-2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	0.00	17.40
		1192	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2-2018	7/2033 (N.A.) {7/2033}	642.69 (N.A.) {642.69}	200.33	0.10
		1193	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7-2017	7/2028 (N.A.) {7/2028}	499.99 (N.A.) {747.91}	0.00	-
		1194	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7-2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	-
		1195	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9-2022	9/2027 (N.A.) {9/2027}	189.93 (N.A.) {189.93}	5.14	-
		1196	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12-2009	12/2026 (N.A.) {12/2026}	48.44 (N.A.) {297.00}	293.90	10.00
		1197	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8-2019	8/2027 (Aug-27) {8/2027}	183.00 (257.97) {257.97}	0.60	-
		1198	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8-2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	-
		1199	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9-2022	9/2026 (N.A.) {3/2026}	209.75 (N.A.) {244.99}	55.28	10.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	1200	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12-2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	111.78	32.10
		1201	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12-2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	149.56	35.65
		1202	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12-2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	161.57	37.09
		1203	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8-2022	1/2025 (N.A.) {7/2025}	153.61 (N.A.) {153.61}	14.22	33.14
		1204	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3-2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	41.10	12.00
		1205	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3-2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	216.63	16.66
		1206	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6-2020	12/2023 (May-25) {3/2025}	414.24 (N.A.) {414.24}	287.48	60.00
		1207	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR- BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3-2022	6/2025 (N.A.) {6/2025}	499.79 (N.A.) {499.79}	262.85	20.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1208	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3-2021	3/2024 (N.A.) {5/2025}	196.94 (N.A.) {196.94}	66.09	15.00
		1209	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITION (MoRTH) (N24001860)	1-2022	4/2025 (N.A.) {5/2025}	300.33 (N.A.) {300.33}	188.27	50.00
		1210	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LAND IN THE STATE (MoRTH) (N24001861)	2-2022	11/2024 (May-25) {5/2025}	157.49 (N.A.) {157.49}	63.33	31.74
		1211	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESIGN KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2-2022	10/2025 (Nov-25) {11/2025}	238.78 (N.A.) {238.78}	28.40	12.00
		1212	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3-2021	6/2024 (N.A.) {6/2025}	154.05 (N.A.) {154.05}	47.47	25.00
		1213	CONSTRUCTION OF FOUR LANE ROAD AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11-2021	6/2025 (N.A.) {6/2025}	154.49 (N.A.) {154.49}	56.36	17.00
		1214	CONSTRUCTION OF 4 LANE ROAD WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT) (MoRTH) (N24001865)	12-2021	5/2025 (N.A.) {5/2025}	324.09 (N.A.) {324.09}	84.25	20.00
		1215	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8-2020	3/2022 (N.A.) {3/2025}	200.00 (154.73) {154.73}	137.04	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1216	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12-2021	10/2024 (N.A.) {10/2025}	1,592.00 (1,592.00) {1,592.00}	1,005.88	72.05
		1217	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE- OD (NHAI) (N24001666)	12-2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	511.04	82.68
		1218	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9-2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	1,117.58	78.02
		1219	6L OF BADAKUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH- 130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3-2021	4/2024 (N.A.) {3/2025}	1,249.00 (N.A.) {1,249.00}	462.56	78.61
		1220	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH- 130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2-2021	3/2024 (N.A.) {6/2025}	586.00 (N.A.) {586.00}	213.49	71.80
		1221	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH- 130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2-2021	3/2024 (N.A.) {3/2025}	593.00 (N.A.) {593.00}	280.69	90.10
		1222	6L OF HATIBENA - BADAKUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2-2021	3/2024 (N.A.) {3/2025}	925.00 (N.A.) {925.00}	445.07	94.91
		1223	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8-2021	6/2024 (N.A.) {8/2025}	1,460.00 (1,460.00) {1,460.00}	883.90	82.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1224	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9-2016	8/2019 (N.A.) {3/2025}	2,510.04 (N.A.) {2,510.04}	1,104.98	99.00
		1225	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12-2017	7/2020 (N.A.) {3/2025}	686.65 (565.00) {686.65}	574.26	93.75
		1226	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHAI) (N24000733)	1-2018	8/2022 (N.A.) {6/2025}	633.68 (492.83) {633.68}	560.38	82.72
		1227	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1-2018	8/2021 (N.A.) {3/2025}	614.48 (503.30) {757.12}	664.48	99.00
		1228	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1-2018	9/2020 (N.A.) {3/2025}	686.65 (504.09) {1,015.16}	435.85	90.20
		1229	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (NHAI) (N24000738)	1-2018	9/2021 (N.A.) {3/2025}	999.00 (1,152.70) {1,152.70}	498.82	79.49
		1230	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHAI) (N24000739)	1-2018	6/2021 (Mar-25) {3/2025}	503.88 (609.03) {609.03}	536.89	96.69
		1231	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8-2016	2/2017 (N.A.) {3/2025}	287.70 (N.A.) {293.66}	274.44	98.66

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1232	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12-2016	8/2018 (N.A.) {3/2025}	223.50 (N.A.) {223.50}	220.50	92.00
		1233	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3-2018	8/2018 (N.A.) {3/2025}	199.16 (N.A.) {199.16}	155.44	98.00
	STEEL	1234	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1-2022	5/2025 (N.A.) {5/2025}	970.18 (N.A.) {970.18}	571.77	75.02
		1235	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11-2020	5/2023 (N.A.) {3/2025}	377.18 (N.A.) {377.18}	421.26	94.68
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1236	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10-2019	5/2022 (N.A.) {6/2025}	348.24 (N.A.) {348.24}	279.64	89.00
	PETROLEUM	1237	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5-2020	2/2023 (Sep-24) {3/2025}	1,421.46 (N.A.) {1,421.46}	1,111.28	95.40
		1238	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3-2022	3/2030 (Sep-33) {9/2033}	151.00 (N.A.) {151.00}	7.78	1.50
		1239	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11-2021	5/2024 (Feb-25) {2/2025}	367.00 (397.00) {397.00}	307.68	87.20
	RAILWAYS	1240	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6-2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1241	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9-2020	3/2025 (N.A.) {3/2025}	82.99 (N.A.) {235.00}	0.00	-
		1242	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4-2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {299.74}	0.00	-
	ROAD TRANSPORT AND HIGHWAYS	1243	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR- MUKTS (MoRTH) (N24001960)	3-2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	94.08	42.00
		1244	WORK OF WIDENING/UPGRADATION OF 2-LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3-2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	81.25	69.00
		1245	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12-2020	8/2025 (Aug-25) {8/2025}	757.13 (757.00) {757.00}	246.51	94.00
		1246	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADAUR ROAD NEAR DYALPURA BHA (NHAI) (N24002076)	3-2021	10/2025 (Jun-26) {6/2026}	2,029.17 (2,029.00) {2,029.00}	84.23	36.00
		1247	6L ACCESS CONTROLLED LUDHIANA- BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6-2021	9/2025 (May-26) {5/2026}	906.51 (906.51) {906.51}	184.35	37.00
		1248	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3-2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	892.68	26.60

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1249	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3-2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	116.00	37.00
		1250	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10-2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	248.53	65.01
		1251	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8-2021	6/2025 (Dec-25) {12/2025}	809.51 (N.A.) {809.51}	164.99	41.90
		1252	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1-2020	4/2026 (N.A.) {4/2027}	2,165.23 (N.A.) {2,165.23}	141.72	16.50
		1253	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7-2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	333.00	75.00
		1254	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3-2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	323.00	75.00
		1255	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1-2021	5/2024 (Apr-25) {4/2025}	1,741.86 (2,086.91) {2,086.91}	1,203.40	92.66
		1256	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5-2021	12/2024 (Oct-26) {10/2026}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1257	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3-2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	1,082.62	31.49
		1258	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11-2021	7/2024 (Apr-25) {4/2025}	646.42 (646.42) {646.42}	481.67	94.00
		1259	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5-2020	12/2024 (Aug-25) {8/2025}	864.23 (864.23) {864.23}	434.88	50.00
		1260	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3-2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	729.77	36.41
		1261	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3-2021	10/2024 (Dec-25) {12/2025}	1,641.75 (N.A.) {1,641.75}	179.85	24.60
		1262	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2-2021	8/2024 (Dec-25) {12/2025}	1,474.77 (N.A.) {1,474.77}	411.34	68.70
		1263	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12-2020	6/2024 (Jun-25) {6/2025}	857.91 (N.A.) {857.91}	127.71	38.50
		1264	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12-2020	9/2023 (Sep-25) {9/2025}	524.88 (416.58) {416.58}	157.14	69.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1265	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA- BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12-2020	4/2024 (Jul-24) {7/2024}	881.00 (N.A.) {881.00}	882.83	89.33
		1266	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA- MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12-2020	1/2024 (Mar-25) {3/2025}	989.66 (N.A.) {989.66}	324.77	31.08
		1267	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12-2020	4/2024 (Sep-25) {9/2025}	1,234.40 (N.A.) {1,234.40}	792.35	57.84
		1268	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12-2020	4/2024 (Sep-25) {9/2025}	1,094.46 (N.A.) {1,094.46}	802.93	61.96
		1269	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2-2021	4/2024 (Nov-24) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1270	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- (NHAI) (N24001420)	2-2021	4/2024 (Dec-25) {12/2025}	853.66 (N.A.) {853.66}	132.99	15.33
		1271	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3-2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100.00
		1272	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10-2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	62.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
RAJASTHAN		1273	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0.000) (MoRTH) (N24000910)	3-2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	104.98	79.00
		1274	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES) (MoRTH) (N24000941)	3-2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100.00
	CIVIL AVIATION	1275	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5-2022	11/2024 (N.A.) {6/2025}	480.00 (N.A.) {480.00}	180.53	62.00
		1276	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6-2023	3/2026 (Sep-26) {9/2026}	887.00 (N.A.) {887.00}	201.53	47.17
	COAL	1277	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3-2023	9/2024 (N.A.) {3/2025}	1,813.00 (N.A.) {1,813.00}	451.16	58.00
	PETROLEUM	1278	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12-2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	213.16	17.10
		1279	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10-2017	10/2022 (Mar-25) {3/2025}	43,129.00 (72,937.00) {72,937.00}	52,868.75	84.50
		1280	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12-2021	10/2024 (Dec-25) {12/2025}	9,028.00 (N.A.) {9,028.00}	6,252.17	74.03
		1281	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAUJI (HPCL) (N16000496)	3-2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	205.12	21.90

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1282	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12-2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	48.24	30.80
	POWER	1283	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12-2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	356.98	26.00
		1284	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12-2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	426.00	30.00
		1285	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSI (PGCIL) (N18000389)	2-2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	482.00	32.00
		1286	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8-2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	34.00	4.00
		1287	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8-2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	0.00	6.00
		1288	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8-2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	62.00	6.00
		1289	ADDITIONAL TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM BHADLA-III PS AS PART OF RAJASTHAN REZ P (PGCIL) (N18000396)	8-2024	2/2026 (N.A.) {2/2026}	369.00 (N.A.) {369.00}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1290	TRANSMISSION SYSTEM STRENGTHENING FOR INTERCONNECTIONS OF BHADLA-III AND BIKANER III COMPLEX [SPV NA (PGCIL) (N18000397)	8-2024	8/2026 (N.A.) {8/2026}	1,382.00 (N.A.) {1,382.00}	0.00	-
		1291	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BAR (PGCIL) (N18000401)	11-2024	11/2026 (N.A.) {11/2026}	2,735.00 (N.A.) {2,735.00}	0.00	-
		1292	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6GW)] [BIKANER COMPLEX (PGCIL) (N18000403)	11-2024	11/2026 (N.A.) {11/2026}	5,969.00 (N.A.) {5,969.00}	0.00	-
		1293	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3 (6 GW)] [BIKANER COMPLE (PGCIL) (N18000404)	11-2024	11/2026 (N.A.) {11/2026}	5,357.00 (N.A.) {5,357.00}	0.00	-
		1294	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3-2020	9/2021 (N.A.) {3/2025}	1,782.00 (12.00) {1,782.00}	1,350.50	95.00
		1295	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3-2022	8/2023 (N.A.) {3/2025}	1,352.71 (N.A.) {1,352.71}	969.36	45.00
		1296	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3-2022	8/2023 (N.A.) {3/2025}	1,409.52 (N.A.) {1,409.52}	1,345.14	95.00
		1297	BHENSARA 320 MW (NTPC) (N18000293)	1-2021	7/2022 (N.A.) {3/2025}	1,221.73 (1,521.00) {1,221.73}	1,015.31	-
		1298	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3-2022	8/2023 (N.A.) {3/2025}	1,426.94 (N.A.) {1,426.94}	1,017.04	80.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1299	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6-2022	3/2024 (N.A.) {3/2025}	2,598.92 (N.A.) {2,598.92}	1,390.10	12.00
		1300	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3-2023	9/2024 (N.A.) {3/2025}	1,433.28 (N.A.) {1,433.28}	801.47	80.00
		1301	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5-2022	11/2023 (N.A.) {8/2025}	1,677.12 (N.A.) {1,677.12}	742.96	72.00
		1302	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372)	6-2023	1/2025 (Feb-25) {2/2025}	202.39 (N.A.) {202.39}	20.04	100.00
		1303	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8-2023	2/2025 (N.A.) {3/2025}	688.74 (N.A.) {688.74}	264.00	72.00
		1304	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10-2023	4/2025 (N.A.) {4/2025}	2,211.00 (N.A.) {2,211.00}	720.63	43.00
		1305	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10-2023	4/2025 (N.A.) {10/2025}	1,796.00 (N.A.) {1,796.00}	736.48	45.00
		1306	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9-2023	4/2025 (N.A.) {4/2025}	2,191.00 (N.A.) {2,191.00}	843.26	53.00
		1307	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12-2022	3/2025 (N.A.) {8/2025}	331.00 (N.A.) {331.00}	8.66	26.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1308	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11-2023	6/2025 (N.A.) {6/2025}	428.00 (N.A.) {428.00}	0.00	6.00
	RAILWAYS	1309	AGRA FORT-BANDIKUI (NCR) (N22000553)	6-2022	6/2027 (May-26) {5/2026}	1,389.81 (N.A.) {987.83}	28.86	12.00
		1310	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4-2019	3/2025 (N.A.) {3/2025}	528.48 (N.A.) {500.85}	338.85	73.00
		1311	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11-2021	11/2026 (N.A.) {12/2025}	466.42 (N.A.) {466.22}	647.62	73.00
		1312	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2-2023	2/2028 (N.A.) {12/2025}	422.60 (N.A.) {422.60}	161.53	70.00
		1313	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (NWR) (N22000607)	12-2022	6/2026 (N.A.) {12/2025}	304.00 (239.54) {239.54}	90.97	20.00
		1314	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1-2023	6/2028 (N.A.) {12/2026}	968.92 (N.A.) {968.92}	281.56	26.00
	ROAD TRANSPORT AND HIGHWAYS	1315	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8-2022	6/2024 (Mar-25) {3/2025}	409.64 (N.A.) {409.64}	211.81	71.83
		1316	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3-2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	78.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1317	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3-2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	104.08	80.00
		1318	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3-2022	8/2025 (N.A.) {6/2025}	187.65 (N.A.) {187.65}	66.57	72.00
		1319	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12-2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	92.69	83.00
		1320	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2-2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	245.87	64.00
		1321	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3-2022	4/2025 (N.A.) {4/2025}	317.74 (N.A.) {317.74}	136.23	10.00
		1322	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12-2021	5/2024 (Apr-25) {4/2025}	411.40 (N.A.) {411.40}	163.61	60.00
		1323	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1-2022	12/2024 (Mar-25) {3/2024}	194.88 (N.A.) {194.88}	104.69	75.00
		1324	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12-2021	8/2024 (Mar-25) {3/2024}	451.66 (N.A.) {451.66}	401.78	97.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1325	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12-2021	9/2024 (N.A.) {3/2025}	150.11 (N.A.) {150.11}	57.83	75.00
		1326	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3-2022	11/2024 (Feb-25) {2/2025}	1,636.15 (N.A.) {1,636.15}	725.68	85.00
		1327	4L OF KARWAR (KM. 281.980 OF NH-62 NAGAU ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11-2021	8/2024 (Mar-25) {3/2025}	736.75 (N.A.) {736.75}	234.95	84.10
		1328	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE - 0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9-2021	6/2024 (Feb-25) {2/2025}	672.35 (N.A.) {672.35}	392.56	98.50
		1329	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561)	10-2019	10/2023 (Jan-25) {1/2025}	839.63 (N.A.) {839.63}	227.66	100.00
		1330	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10-2019	8/2023 (Feb-25) {2/2025}	846.59 (N.A.) {846.59}	155.11	97.80
		1331	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10-2019	7/2023 (Feb-25) {2/2025}	662.08 (N.A.) {662.08}	120.77	96.50
		1332	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566)	11-2019	5/2023 (Jan-25) {1/2025}	1,640.10 (N.A.) {1,640.10}	1,159.50	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1333	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11-2019	10/2022 (Mar-25) {3/2025}	1,272.97 (N.A.) {1,272.97}	618.95	84.83
		1334	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11-2019	5/2023 (Jan-25) {1/2025}	1,119.35 (N.A.) {1,119.35}	1,438.04	99.80
		1335	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569)	11-2019	3/2023 (May-24) {5/2024}	1,425.02 (N.A.) {1,425.02}	1,386.89	100.00
		1336	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571)	11-2019	12/2023 (Jan-25) {1/2025}	1,341.36 (N.A.) {1,341.36}	1,089.73	99.65
		1337	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11-2019	12/2022 (Jan-25) {1/2025}	1,658.06 (N.A.) {1,658.06}	180.45	99.90
		1338	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7-2020	1/2024 (Sep-25) {9/2025}	1,788.69 (N.A.) {1,788.69}	887.71	72.67
		1339	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241)	3-2020	10/2022 (Jun-25) {6/2024}	255.23 (N.A.) {255.23}	256.00	97.00
		1340	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG- I. (MoRTH) (N24001411)	12-2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	233.62	96.10

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1341	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3-2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	28.00	15.00
		1342	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3-2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	36.00	6.00
		1343	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA (NHAI) (N24000795)	2-2018	4/2021 (Mar-25) {3/2025}	741.86 (649.00) {649.00}	672.53	96.00
SIKKIM	CIVIL AVIATION	1344	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11-2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	17.83	8.00
	DEPARTMENT OF HIGHER EDUCATION	1345	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8-2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	-
	POWER	1346	TEESTA VI HE PROJECT (NHPC) (N18000325)	3-2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,989.92	64.97
		1347	RANGIT IV HE PROJECT (NHPC) (N18000326)	3-2021	5/2024 (N.A.) {12/2025}	938.29 (N.A.) {1,828.11}	1,331.27	83.64
	RAILWAYS	1348	SEVOK RANGPO, NEFR (NFR) (N22000102)	4-2008	12/2015 (Dec-27) {12/2027}	1,339.48 (12,132.95) {12,132.95}	7,893.89	70.00
	ROAD TRANSPORT AND HIGHWAYS	1349	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3-2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	239.34	74.78

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1350	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8-2020	4/2023 (Nov-24) {3/2025}	295.97 (N.A.) {295.97}	245.00	94.19
		1351	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3-2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	-
		1352	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8-2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	254.48	94.53
		1353	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7-2020	4/2023 (Aug-24) {3/2025}	345.38 (395.59) {395.59}	356.67	90.19
		1354	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9-2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.80	46.98
		1355	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9-2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17
		1356	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8-2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	195.37	54.16
		1357	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM 27.200 (END OF RO (NHIDCL) (N24001336)	8-2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	204.72	80.18

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1358	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10-2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	277.14	44.83
		1359	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10-2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	292.56	48.05
		1360	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1-2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {348.92}	149.38	41.04
		1361	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12-2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	205.76	64.10
		1362	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10-2021	5/2024 (Jan-26) {1/2026}	385.15 (N.A.) {385.15}	170.32	78.00
		1363	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3-2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.54	96.55
		1364	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11-2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	100.00
TAMIL NADU	CIVIL AVIATION	1365	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6-2018	2/2022 (Mar-26) {3/2026}	2,467.00 (N.A.) {2,467.00}	1,534.29	69.00
		1366	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8-2018	10/2021 (N.A.) {12/2023}	951.28 (N.A.) {1,112.49}	1,112.49	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1367	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6-2019	3/2022 (Mar-25) {3/2025}	380.87 (N.A.) {455.99}	341.91	98.00
	COAL	1368	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12-2021	3/2025 (N.A.) {3/2025}	297.88 (N.A.) {297.88}	45.15	20.00
		1369	50 MW SOLAR POWER PROJECT - NEYVELI MINED OUT AREA (NLC) (N06000279)	5-2023	6/2025 (N.A.) {4/2025}	218.03 (N.A.) {218.03}	108.84	26.00
	FINANCE	1370	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11-2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100.00
	MINES	1371	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9-2017	6/2019 (Mar-24) {12/2024}	166.62 (163.17) {163.17}	135.63	65.00
	PETROLEUM	1372	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3-2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	99.83	4.90
		1373	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12-2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	152.00	7.20
		1374	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11-2012	2/2017 (Oct-25) {10/2025}	678.00 (1,732.00) {1,732.00}	532.09	48.10
		1375	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1-2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,303.96	10.20
		1376	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1-2022	7/2024 (Jun-25) {6/2025}	827.00 (887.71) {887.71}	536.10	80.10

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1377	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1-2022	7/2024 (May-26) {5/2026}	829.00 (N.A.) {829.00}	226.53	56.53
	RAILWAYS	1378	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTPT) (N22000028)	4-2006	6/2013 (May-25) {5/2025}	495.74 (N.A.) {734.01}	632.33	98.00
		1379	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9-2006	(Mar-28) {3/2028}	582.83 (3,631.34) {3,631.34}	825.64	12.00
		1380	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (SR) (N22000568)	3-2022	3/2026 (Feb-25) {3/2025}	359.60 (274.20) {274.20}	241.58	85.00
		1381	MORAPPUR-DHARMAPURI (SR) (N22000618)	2-2019	3/2028 (Mar-27) {3/2027}	358.95 (N.A.) {358.95}	38.37	1.00
		1382	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1-2019	3/2026 (Mar-25) {3/2025}	304.22 (N.A.) {373.42}	254.70	80.00
		1383	NAGAPATTINAM THIRUTURAI PUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7-2008	3/2026 (Mar-27) {3/2027}	677.12 (N.A.) {788.05}	140.73	19.00
	ROAD TRANSPORT AND HIGHWAYS	1384	CONSTRUCTION OF STRR (WEST SIDE)- NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4-2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	487.46	44.95

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1385	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3-2022	2/2025 (N.A.) {3/2025}	1,076.97 (N.A.) {1,076.97}	475.89	76.50
		1386	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3-2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	-
		1387	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3-2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	-
		1388	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3-2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	-
		1389	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3-2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	-
		1390	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2-2019	12/2025 (Dec-25) {12/2025}	825.94 (1,116.13) {1,116.13}	223.99	30.31
		1391	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3-2023	7/2024 (N.A.) {3/2025}	200.30 (N.A.) {200.30}	72.69	71.04
		1392	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3-2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	337.04	30.45

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1393	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2-2022	4/2025 (N.A.) {4/2025}	1,097.59 (N.A.) {1,317.06}	655.62	91.44
		1394	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3-2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	158.92	56.00
		1395	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3-2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	206.02	86.00
		1396	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3-2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	72.62	47.00
		1397	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12-2020	7/2024 (N.A.) {7/2025}	843.48 (1,068.60) {1,068.60}	389.23	90.00
		1398	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2-2021	7/2024 (N.A.) {9/2025}	2,948.31 (3,605.73) {3,605.73}	728.20	69.95
		1399	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10-2020	5/2024 (N.A.) {6/2025}	1,023.91 (1,438.62) {1,438.62}	574.44	78.01
		1400	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2-2019	5/2024 (Aug-25) {3/2026}	1,008.99 (1,360.53) {1,360.53}	169.75	41.20

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1401	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11-2021	2/2023 (N.A.) {2/2025}	463.44 (463.07) {463.44}	331.22	98.50
		1402	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10-2018	2/2021 (N.A.) {4/2025}	707.90 (766.51) {766.51}	475.43	85.45
		1403	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1-2019	5/2021 (N.A.) {1/2025}	819.89 (1,314.82) {922.85}	394.75	57.32
		1404	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1-2022	11/2024 (N.A.) {3/2025}	221.03 (243.95) {243.95}	149.75	80.00
		1405	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10-2022	11/2024 (N.A.) {3/2025}	172.15 (N.A.) {172.15}	124.30	95.00
		1406	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10-2020	5/2023 (Mar-25) {3/2025}	434.12 (N.A.) {434.12}	258.89	99.30
		1407	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1-2019	1/2023 (Jun-25) {6/2025}	1,051.69 (N.A.) {1,051.69}	573.98	79.72
		1408	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH- 83) (NHAI) (N24001602)	1-2019	12/2022 (Nov-25) {11/2025}	1,409.38 (N.A.) {1,409.38}	652.18	90.08

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1409	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603)	1-2019	10/2022 (Feb-25) {2/2025}	1,518.53 (N.A.) {1,607.54}	915.40	100.00
		1410	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS (NHAI) (N24001604)	2-2019	3/2021 (N.A.) {2/2025}	166.90 (N.A.) {166.90}	121.94	100.00
		1411	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH-383 (NHAI) (N24001605)	6-2018	3/2022 (N.A.) {5/2025}	1,103.86 (N.A.) {1,103.86}	461.32	71.40
		1412	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHAI) (N24001606)	12-2018	3/2022 (Jul-25) {7/2025}	854.94 (N.A.) {854.94}	369.07	68.25
		1413	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1-2022	9/2024 (Feb-25) {6/2025}	467.99 (N.A.) {468.00}	22.34	62.15
		1414	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9-2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	-
		1415	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2-2019	12/2023 (Dec-24) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	-
		1416	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG- III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2-2019	8/2023 (Dec-24) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1417	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7-2022	8/2023 (Dec-24) {12/2024}	186.50 (242.40) {242.40}	16.70	95.00
		1418	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11-2020	8/2024 (N.A.) {12/2025}	1,155.49 (1,525.10) {1,525.10}	485.62	52.75
		1419	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428)	3-2018	11/2021 (Dec-24) {12/2024}	998.70 (1,358.32) {1,358.32}	917.97	97.67
		1420	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3-2018	11/2021 (Dec-24) {12/2024}	1,294.47 (1,588.40) {1,588.40}	854.96	98.50
		1421	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3-2018	1/2022 (Dec-24) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,579.19	99.80
		1422	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3-2018	10/2020 (Aug-25) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,283.62	54.20
		1423	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2-2022	8/2022 (N.A.) {3/2025}	191.33 (N.A.) {191.33}	185.78	94.00
		1424	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3-2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {260.07}	56.53	13.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1425	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8-2017	9/2020 (N.A.) {2/2025}	1,176.37 (N.A.) {1,176.37}	1,325.06	99.50
		1426	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9-2017	8/2020 (Mar-25) {3/2025}	1,227.87 (N.A.) {1,227.87}	1,374.80	93.90
		1427	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3-2018	10/2022 (Feb-25) {2/2025}	505.35 (N.A.) {837.69}	376.61	99.75
TELANGANA	CIVIL AVIATION	1428	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5-2020	5/2022 (Jun-23) {6/2023}	353.61 (N.A.) {353.61}	303.22	100.00
	COAL	1429	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 (SCCL) (N06000161)	3-2017	3/2022 (N.A.) {3/2025}	413.84 (N.A.) {413.84}	382.88	60.00
		1430	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7-2019	3/2023 (N.A.) {3/2025}	438.98 (N.A.) {438.98}	167.99	68.00
		1431	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10-2020	3/2023 (N.A.) {3/2026}	484.51 (N.A.) {484.51}	281.16	30.00
		1432	RCE OF RAMAGUNDAM OPENCASE II EXTENSION PROJECT (SCCL) (N06000210)	11-2015	3/2023 (N.A.) {3/2025}	489.62 (N.A.) {489.62}	405.54	70.00
		1433	RCE OF INDARAM OPENCASE PROJECT (SCCL) (N06000211)	8-2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	402.64	80.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1434	RCE OF KALYANIKHANI OPENCASE PROJECT (SCCL) (N06000213)	3-2016	3/2020 (N.A.) {3/2025}	384.32 (N.A.) {384.32}	247.36	75.00
		1435	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8-2017	3/2020 (N.A.) {3/2025}	442.42 (N.A.) {442.42}	201.29	63.00
		1436	GOLETI OPENCASE MINE (SCCL) (N06000258)	7-2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	56.00	18.00
	HEALTH AND FAMILY WELFARE	1437	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12-2018	7/2024 (N.A.) {3/2025}	1,110.55 (N.A.) {1,110.55}	679.84	80.00
		1438	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10-2016	3/2020 (Jan-25) {1/2025}	209.84 (281.05) {281.05}	252.39	97.50
	RAILWAYS	1439	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4-2006	3/2010 (N.A.) {3/2025}	1,160.48 (N.A.) {3,014.00}	1,439.12	-
	ROAD TRANSPORT AND HIGHWAYS	1440	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3-2021	7/2024 (N.A.) {8/2024}	317.19 (N.A.) {317.19}	164.72	67.00
		1441	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1-2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	291.30	65.63
		1442	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1-2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	209.98	68.96

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1443	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1-2022	12/2024 (N.A.) {3/2025}	549.28 (N.A.) {549.28}	196.96	64.28
		1444	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3-2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	305.02	73.08
		1445	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3-2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	258.65	76.25
		1446	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10-2017	6/2023 (N.A.) {12/2024}	186.71 (N.A.) {186.71}	184.20	88.11
		1447	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3-2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	168.83	49.71
		1448	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET- ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1-2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	196.36	78.35
		1449	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1-2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	276.18	58.62
		1450	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3-2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	58.81	21.87

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1451	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2-2022	9/2024 (N.A.) {1/2026}	541.58 (N.A.) {541.58}	20.82	-
		1452	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3-2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,414.46}	915.90	60.30
		1453	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8-2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	465.96	69.30
		1454	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2-2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	333.95	73.01
		1455	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9-2022	2/2024 (Dec-24) {12/2024}	804.69 (N.A.) {804.69}	464.41	74.70
		1456	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1-2021	1/2024 (Dec-24) {12/2024}	1,307.95 (N.A.) {1,307.95}	638.32	98.06
		1457	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3-2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	204.38	35.12
		1458	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12-2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	229.74	45.88

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1459	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1-2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	40.90
		1460	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2-2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	408.48	52.75
		1461	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM-VIJAYAWADA) (NHAI) (N24002190)	3-2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	0.00	5.10
		1462	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1-2014	3/2016 (Sep-19) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15
		1463	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10-2014	2/2017 (Dec-22) {3/2025}	295.47 (N.A.) {295.47}	224.42	98.51
		1464	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3-2015	1/2017 (N.A.) {12/2023}	153.21 (N.A.) {153.21}	101.15	93.11
		1465	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10-2016	2/2019 (Jun-22) {8/2024}	298.32 (N.A.) {298.32}	178.47	98.00
		1466	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10-2016	3/2019 (Apr-23) {8/2024}	248.83 (N.A.) {248.83}	173.82	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1467	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1-2017	5/2019 (Aug-19) {8/2019}	244.54 (N.A.) {244.54}	176.32	99.90
		1468	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1-2017	10/2019 (Oct-19) {2/2024}	196.52 (N.A.) {196.52}	125.53	95.70
		1469	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1-2017	12/2019 (Dec-19) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.30
		1470	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1-2017	5/2019 (Jul-21) {1/2024}	300.00 (N.A.) {300.00}	243.36	96.05
		1471	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1-2018	5/2020 (Dec-22) {8/2024}	283.15 (N.A.) {283.15}	279.54	92.59
		1472	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1-2018	12/2019 (Nov-20) {11/2020}	230.03 (N.A.) {230.03}	232.00	99.90
		1473	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2-2018	6/2020 (Jan-21) {1/2021}	206.13 (N.A.) {206.13}	192.73	98.36
		1474	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2-2018	11/2019 (Mar-22) {1/2024}	294.13 (N.A.) {294.13}	203.07	87.44

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1475	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3-2018	9/2020 (Jun-22) {6/2023}	322.81 (N.A.) {322.81}	325.47	98.09
		1476	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3-2018	7/2020 (Jun-24) {2/2026}	626.76 (N.A.) {626.76}	282.78	44.30
		1477	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1-2017	10/2019 (Oct-19) {6/2021}	605.08 (N.A.) {605.08}	416.45	99.84
		1478	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3-2018	7/2019 (Jun-22) {8/2024}	192.67 (N.A.) {192.67}	178.95	92.00
		1479	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1-2019	(Jan-23) {8/2024}	193.19 (249.72) {249.72}	230.79	95.00
TRIPURA	PETROLEUM	1480	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6-2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	371.70	72.10
	ROAD TRANSPORT AND HIGHWAYS	1481	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3-2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	4.25
		1482	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5-2023	11/2024 (N.A.) {9/2025}	195.95 (N.A.) {195.95}	21.95	27.34

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1483	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2-2022	1/2025 (N.A.) {5/2025}	456.88 (N.A.) {456.88}	105.40	43.68
		1484	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6-2020	1/2022 (Feb-24) {12/2024}	277.50 (302.02) {302.02}	256.89	99.94
		1485	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11-2020	6/2022 (Oct-23) {11/2024}	159.13 (171.50) {171.50}	84.33	100.00
		1486	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6-2020	1/2022 (N.A.) {11/2024}	201.99 (N.A.) {287.47}	144.07	-
		1487	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3-2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.20
		1488	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2-2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	0.52	1.31
		1489	IMPROVEMENT AND WIDENING TO 2- LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1-2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	7.67	14.16
		1490	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1-2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	-
		1491	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1-2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1492	CHAMPAK NAGAR TO KHAYERPUR SECTION (DESIGN KM 242+500 TO KM 261+610) (NHIDCL) (N24002205)	12-2023	9/2026 (N.A.) {9/2026}	920.66 (N.A.) {920.66}	10.60	5.20
UTTAR PRADESH	CIVIL AVIATION	1493	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6-2018	9/2021 (Oct-26) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,601.36	79.03
		1494	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6-2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	17.35	6.00
		1495	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3-2021	12/2022 (Mar-25) {3/2025}	242.14 (328.00) {358.00}	339.44	99.90
		1496	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5-2023	11/2024 (Jun-25) {6/2025}	185.75 (274.38) {274.38}	165.59	83.00
		1497	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7-2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	45.40	6.00
		1498	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7-2016	11/2021 (Jun-25) {6/2025}	17,237.00 (21,780.94) {21,780.94}	19,230.70	88.50
	COAL	1499	KHADIA EXPANSION OCP (NCL) (N06000208)	6-2021	3/2025 (N.A.) {3/2025}	491.67 (N.A.) {491.67}	80.87	7.38
	HOME AFFAIRS	1500	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI (CPWD FOR MHA) (N45000003)	5-2019	1/2022 (Mar-23) {3/2023}	199.31 (N.A.) {199.31}	86.49	85.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1501	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4-2022	4/2025 (Dec-26) {12/2026}	260.12 (N.A.) {260.12}	1.03	22.80
		1502	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3-2019	4/2024 (Apr-24) {3/2025}	910.56 (1,299.02) {1,299.02}	921.40	93.70
		1503	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9-2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	146.18	40.30
		1504	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12-2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	349.85	6.40
	POWER	1505	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (NTPC) (N18000382)	3-2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	1,114.00	0.50
		1506	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3-2019	9/2023 (N.A.) {4/2025}	11,089.42 (N.A.) {13,276.16}	11,885.35	94.00
	RAILWAYS	1507	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (RVNL) (N22000401)	4-2015	3/2022 (N.A.) {12/2024}	943.60 (N.A.) {2,018.23}	1,780.22	-
		1508	RAMNA - SINGRAULI DOUBLING (ECR) (N22000417)	8-2015	3/2020 (N.A.) {9/2024}	2,436.21 (2,880.40) {2,880.40}	3,034.23	90.00
		1509	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419)	8-2015	3/2019 (N.A.) {8/2024}	528.57 (762.97) {762.97}	799.97	90.00
		1510	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4-2016	(N.A.) {9/2025}	602.50 (N.A.) {1,069.29}	984.35	49.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1511	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4-2016	12/2019 (N.A.) {3/2025}	1,177.96 (N.A.) {2,025.00}	2,010.02	80.00
		1512	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3-2018	3/2023 (N.A.) {3/2027}	4,329.53 (N.A.) {4,329.53}	1,607.42	32.00
		1513	JHANSI BINA DOUBLING (NCR) (N22000496)	9-2016	3/2021 (Mar-27) {3/2027}	2,001.00 (N.A.) {2,001.00}	1,685.23	85.00
		1514	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6-2016	12/2023 (N.A.) {12/2024}	3,677.76 (N.A.) {5,190.26}	5,046.07	-
		1515	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10-2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	-
		1516	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4-2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	42.61	42.00
		1517	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4-2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	2.25	8.00
		1518	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3-2017	12/2024 (Jun-25) {6/2025}	260.00 (356.00) {356.00}	170.50	52.00
		1519	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8-2019	12/2026 (N.A.) {12/2026}	2,390.00 (N.A.) {2,390.00}	83.10	55.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1520	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4-2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	10.14	8.00
		1521	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4-2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	72.74	32.00
		1522	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8-2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	540.05	2.00
		1523	BAHRAICH - NANPARA - NEPALGANJ (56.15 KM) (NER) (N22000566)	7-2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	228.71	18.00
		1524	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10-2018	10/2030 (N.A.) {3/2027}	1,600.00 (N.A.) {4,939.78}	1,022.17	5.50
		1525	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11-2017	3/2025 (N.A.) {3/2025}	701.98 (N.A.) {1,100.00}	0.00	-
		1526	BARABANKI MALHAUR 3RD AND 4TH LINE (32.84 KM) (NR) (N22000590)	1-2019	3/2025 (N.A.) {3/2025}	323.85 (N.A.) {323.85}	0.00	-
		1527	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3-2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.00	-
		1528	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11-2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	-
		1529	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5-2018	3/2024 (N.A.) {2/2025}	1,177.96 (N.A.) {2,529.46}	1,636.33	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1530	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8-2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	-
		1531	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11-2016	6/2024 (N.A.) {5/2025}	186.85 (N.A.) {470.47}	452.36	85.00
	ROAD TRANSPORT AND HIGHWAYS	1532	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH- 87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8-2022	2/2024 (Mar-25) {3/2025}	199.31 (199.38) {199.38}	130.59	73.46
		1533	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH- 731B ON (MoRTH) (N24001996)	3-2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	408.12	56.00
		1534	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10-2022	5/2025 (N.A.) {5/2025}	189.31 (N.A.) {189.31}	50.73	15.00
		1535	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11-2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	113.15	45.00
		1536	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH- 31 TO NH-330 (MoRTH) (N24002016)	10-2022	6/2025 (N.A.) {6/2025}	225.17 (N.A.) {225.17}	94.39	47.00
		1537	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3-2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	525.37	34.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1538	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12-2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	434.00	24.00
		1539	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1-2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	286.10	40.00
		1540	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4-2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	814.70	41.00
		1541	GARHMUKTESHWAR (KM. 83.200 OF NH- 24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10-2019	10/2023 (N.A.) {6/2024}	2,068.99 (2,171.00) {2,171.00}	209.60	53.08
		1542	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11-2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	98.50
		1543	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10-2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	719.13	53.50
		1544	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10-2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	93.30	40.90
		1545	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10-2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	492.86	38.17

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1546	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10-2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	106.20	53.59
		1547	CONSTRUCTION OF FOUR-LANE WESTERN SIDE SPUR OF RAMPUR- RUDRAPUR SECTION CONNECTING NH- 24 TO NH-87 BY (NHAI) (N24002090)	3-2021	11/2024 (Apr-25) {4/2025}	646.27 (N.A.) {646.27}	45.26	30.40
		1548	IMPROVEMENT , UP-GRADATION OF NH- 734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: PACKAGE- I: MORA (NHAI) (N24002093)	10-2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	331.68	40.60
		1549	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9-2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	296.56	20.25
		1550	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12-2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	864.10	43.45
		1551	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2-2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	652.14	30.25
		1552	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 () (NHAI) (N24002097)	2-2023	9/2025 (N.A.) {3/2025}	526.45 (N.A.) {526.45}	157.94	68.85
		1553	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH- 321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1-2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	55.81	19.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1554	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1-2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	266.58	22.00
		1555	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8-2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	122.48	19.65
		1556	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8-2023	3/2025 (N.A.) {3/2025}	993.77 (N.A.) {349.48}	338.90	84.50
		1557	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 ((MoRTH) (N24002120)	2-2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	110.35	80.00
		1558	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1-2022	9/2025 (N.A.) {9/2025}	509.65 (N.A.) {509.65}	144.69	12.00
		1559	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3-2023	8/2025 (N.A.) {8/2025}	438.24 (362.39) {438.24}	175.39	20.00
		1560	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH- 730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3-2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	190.86	12.00
		1561	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH- 731A (I/C Y (MoRTH) (N24002138)	3-2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	297.62	23.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1562	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12-2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	140.62	13.00
		1563	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT- SHAMLI-MUZZAFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1-2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	79.50
		1564	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3-2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	460.82	78.56
		1565	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12-2021	7/2025 (N.A.) {7/2025}	1,138.81 (N.A.) {1,138.81}	440.25	98.50
		1566	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZZAFARNAGAR) AND NH- 709A (KARN (NHAI) (N24001729)	8-2022	4/2024 (N.A.) {3/2025}	326.79 (N.A.) {329.79}	105.11	86.00
		1567	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12-2021	1/2025 (N.A.) {3/2025}	1,384.79 (N.A.) {1,384.79}	657.94	97.98
		1568	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12-2021	5/2025 (May-25) {5/2025}	2,470.64 (N.A.) {2,335.00}	613.44	75.50
		1569	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12-2021	10/2024 (N.A.) {4/2025}	540.97 (N.A.) {540.97}	241.50	74.58

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1570	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3-2022	8/2024 (N.A.) {4/2025}	1,602.48 (N.A.) {1,602.48}	372.73	82.00
		1571	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3-2022	8/2024 (N.A.) {4/2025}	1,335.45 (N.A.) {1,335.45}	382.09	74.00
		1572	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KHYAWARI TO VILL.-LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3-2022	8/2024 (N.A.) {4/2025}	1,428.19 (N.A.) {1,428.19}	462.53	80.00
		1573	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KARAUNDA MAHAJAN TO VILL.-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1-2022	8/2024 (N.A.) {4/2025}	1,159.96 (N.A.) {1,159.96}	510.48	98.00
		1574	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11-2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	97.73
		1575	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9-2021	10/2023 (Dec-24) {12/2024}	300.79 (N.A.) {300.79}	122.56	64.36
		1576	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10-2019	11/2023 (Dec-24) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,066.00	99.80
		1577	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5-2019	11/2022 (N.A.) {3/2025}	779.17 (N.A.) {779.17}	54.69	96.45

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1578	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12-2021	7/2025 (Jul-25) {7/2025}	1,972.10 (N.A.) {1,936.00}	431.50	57.25
		1579	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3-2021	4/2024 (Mar-25) {3/2025}	364.47 (N.A.) {364.47}	164.40	82.44
		1580	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2-2022	6/2024 (Feb-25) {2/2025}	570.98 (578.02) {578.02}	371.14	90.10
		1581	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1-2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	48.55
		1582	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10-2019	3/2023 (Dec-24) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	98.80
		1583	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8-2021	3/2024 (Dec-24) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	48.00
		1584	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12-2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	97.60
		1585	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2-2019	2/2022 (Dec-24) {12/2024}	927.77 (N.A.) {1,603.00}	1,202.77	79.45

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1586	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6-2020	11/2023 (Dec-24) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99.00
		1587	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1-2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	742.13	65.00
		1588	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10-2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	832.80	86.00
		1589	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10-2021	9/2024 (Mar-25) {3/2025}	772.05 (N.A.) {772.05}	593.39	67.50
		1590	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1-2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	281.64	73.00
		1591	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4-2020	2/2024 (N.A.) {1/2025}	199.39 (212.96) {199.39}	182.29	100.00
		1592	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH- 730C F (MoRTH) (N24001457)	4-2020	7/2024 (N.A.) {3/2025}	172.50 (169.56) {172.50}	95.75	65.00
		1593	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4-2020	3/2024 (N.A.) {4/2025}	236.47 (N.A.) {236.47}	129.55	84.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1594	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4-2020	7/2024 (N.A.) {3/2025}	211.09 (N.A.) {211.09}	136.60	93.00
		1595	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3-2021	8/2023 (N.A.) {3/2025}	264.86 (N.A.) {264.86}	112.75	78.00
		1596	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11-2021	5/2024 (N.A.) {3/2025}	307.11 (N.A.) {307.11}	181.16	86.00
		1597	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4-2020	11/2024 (N.A.) {4/2025}	325.24 (340.16) {325.24}	236.73	91.00
		1598	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3-2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	257.02	66.00
		1599	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10-2021	4/2024 (N.A.) {2/2025}	227.06 (N.A.) {227.06}	135.14	99.00
		1600	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3-2021	10/2023 (Feb-25) {2/2025}	836.24 (N.A.) {836.24}	782.45	98.85
		1601	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3-2021	10/2023 (Feb-25) {2/2025}	990.28 (N.A.) {990.28}	997.52	98.78

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1602	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3-2020	9/2024 (N.A.) {3/2025}	262.37 (343.77) {343.77}	261.19	77.00
		1603	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10-2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	95.10
		1604	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7-2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	1,055.99	72.00
		1605	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3-2021	9/2023 (N.A.) {1/2025}	185.09 (269.81) {269.81}	262.09	100.00
		1606	WIDENING TO 4L RIGID PAVEMENT CONFIGURATION FROM KM 90.00 TO KM 100.800 OF NH-96 (KM 42.0 TO KM 53.3 (MoRTH) (N24002199)	12-2022	11/2026 (N.A.) {11/2026}	309.63 (N.A.) {309.63}	3.62	-
		1607	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER/FOUR LANE CONFIGURATION FROM EXISTING K (MoRTH) (N24002201)	1-2022	5/2027 (N.A.) {5/2027}	974.19 (N.A.) {974.19}	556.54	-
		1608	REHABILITATION AND UPGRADATION TO FOUR LANE ROAD FROM KM 70.500 TO KM 78.600 OF NH-92 UNDER EPC MODE (MoRTH) (N24002211)	1-2022	1/2027 (N.A.) {1/2027}	296.02 (N.A.) {296.02}	24.72	-
		1609	WIDENING AND STRENGTHENING FROM DESIGN KM. 67.280 TO KM. 88.622 OF NH-727A (SALEMPUR-MAIRWA ROAD) TO (MoRTH) (N24002212)	3-2023	7/2026 (N.A.) {7/2026}	371.89 (N.A.) {371.89}	101.82	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1610	REHABILITATION and UP-GRADATION TO 2L+PS FROM KM. 0.0 TO KM. 7.80 AND KM. 35.400 TO KM. 52.345 (DESI (MoRTH) (N24002213)	3-2023	7/2026 (N.A.) {7/2026}	701.02 (N.A.) {701.02}	233.36	-
		1611	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12-2019	4/2022 (N.A.) {4/2025}	282.41 (N.A.) {319.96}	271.17	88.00
		1612	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 (NHAI) (N24000556)	3-2016	4/2019 (Mar-25) {3/2025}	899.00 (1,633.98) {1,633.98}	1,143.19	95.12
		1613	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3-2016	7/2020 (Mar-25) {3/2025}	1,408.00 (1,659.12) {1,659.12}	1,254.46	83.46
		1614	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3-2018	12/2021 (Dec-23) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,198.22	99.76
		1615	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3-2018	11/2021 (N.A.) {6/2025}	2,140.93 (N.A.) {2,140.93}	2,065.46	98.40
	URBAN DEVELOPMENT	1616	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5-2019	3/2024 (N.A.) {12/2026}	8,379.62 (N.A.) {8,379.62}	4,412.78	50.50
		1617	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5-2019	3/2024 (N.A.) {12/2026}	11,076.48 (N.A.) {11,076.48}	8,224.03	70.50

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>WATER RESOURCES</u>	1618	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UPJalNigam) (N30000006)	5-2017	9/2021 (N.A.) {6/2023}	767.59 (N.A.) {767.59}	276.97	100.00
		1619	FARRUKHABAD I AND D AND STP WORKS HAM (UPJalNigam) (N30000008)	10-2017	3/2022 (Feb-21) {11/2024}	213.62 (261.12) {261.12}	177.62	100.00
		1620	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UPJalNigam) (N30000010)	3-2018	9/2021 (N.A.) {7/2023}	967.23 (708.70) {967.23}	254.98	100.00
		1621	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UPJalNigam) (N30000013)	3-2019	8/2021 (N.A.) {7/2024}	271.39 (N.A.) {271.39}	182.26	100.00
		1622	MATHURA SEWERAGE SCHEME (UPJalNigam) (N30000019)	12-2017	12/2020 (Jun-18) {6/2022}	460.45 (N.A.) {460.45}	315.30	100.00
		1623	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1-2019	12/2021 (Jan-20) {12/2024}	231.79 (234.03) {234.03}	141.79	96.00
		1624	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UPJalNigam) (N30000022)	1-2019	10/2021 (N.A.) {7/2023}	206.05 (N.A.) {206.05}	140.22	100.00
		1625	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2-2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	-
		1626	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UPJalNigam) (N30000025)	3-2019	7/2021 (May-20) {9/2024}	298.12 (N.A.) {240.93}	103.24	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
UTTARAKHAN D	CIVIL AVIATION	1627	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7-2018	9/2020 (N.A.) {9/2024}	456.86 (N.A.) {500.00}	483.76	100.00
	POWER	1628	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11-2006	3/2013 (N.A.) {4/2029}	2,978.48 (N.A.) {10,907.00}	6,679.38	75.00
		1629	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7-2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	-
		1630	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7-2006	2/2016 (Jun-22) {6/2025}	1,657.00 (4,825.60) {8,182.82}	7,533.55	97.90
		1631	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8-2008	6/2013 (N.A.) {12/2026}	2,491.58 (3,860.35) {6,303.00}	4,404.36	69.00
	RAILWAYS	1632	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4-2011	12/2024 (N.A.) {3/2025}	16,216.00 (N.A.) {24,659.00}	18,820.04	-
	ROAD TRANSPORT AND HIGHWAYS	1633	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG- 1) (NHAI) (N24001990)	6-2022	5/2025 (May-25) {5/2025}	524.54 (683.26) {683.26}	75.94	70.80
		1634	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5-2022	9/2024 (May-25) {5/2025}	314.31 (N.A.) {314.31}	167.62	63.58
		1635	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3-2021	3/2024 (Feb-25) {2/2025}	169.08 (N.A.) {169.08}	95.67	99.99

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1636	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8-2021	10/2024 (Aug-25) {8/2025}	1,377.79 (1,384.11) {1,377.79}	679.10	46.81
		1637	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3-2022	2/2025 (Feb-25) {2/2025}	1,092.90 (1,092.90) {1,092.90}	462.92	73.60
		1638	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8-2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100.00
		1639	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND- TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12-2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	15.09	31.06
		1640	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND- TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12-2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	18.41	37.00
		1641	CONSTRUCTION FOR MITIGATION MEASURES PKG-2 (NHIDCL) (N24002206)	12-2023	6/2026 (N.A.) {6/2026}	259.64 (N.A.) {259.64}	0.00	-
		1642	4-LANING OF KASHIPUR-SITARGANJ SECTION (AMR) (N24000465)	11-2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	-
		1643	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHAI) (N24000559)	3-2016	10/2019 (Feb-25) {2/2025}	720.00 (1,150.00) {1,150.00}	665.47	97.12

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1644	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3-2018	11/2020 (N.A.) {3/2024}	274.31 (N.A.) {274.31}	251.61	-
		1645	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3-2018	11/2020 (Dec-22) {3/2024}	403.36 (N.A.) {403.36}	337.72	98.93
		1646	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3-2018	11/2020 (N.A.) {3/2024}	417.24 (N.A.) {417.24}	344.20	-
		1647	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12-2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100.00
		1648	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12-2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100.00
		1649	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12-2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100.00
		1650	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6-2017	6/2019 (Mar-23) {3/2023}	282.08 (N.A.) {282.08}	234.97	100.00
		1651	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11-2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1652	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2-LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11-2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100.00
		1653	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11-2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100.00
		1654	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2-2018	2/2020 (Mar-23) {3/2023}	418.88 (N.A.) {418.88}	339.71	94.00
		1655	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2-2018	(Apr-23) {4/2023}	293.68 (N.A.) {293.68}	244.25	100.00
		1656	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5-2018	5/2020 (Dec-23) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56
		1657	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3-2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	-
		1658	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3-2018	7/2022 (N.A.) {1/2026}	1,383.78 (N.A.) {1,383.78}	605.80	62.62
	WATER RESOURCES	1659	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UKJalNigam) (N30000004)	3-2017	11/2019 (N.A.) {2/2022}	158.00 (N.A.) {158.00}	107.86	100.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
WEST BENGAL	CIVIL AVIATION	1660	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA (AAI) (N04000080)	1-2016	3/2020 (Jun-22) {12/2023}	458.00 (N.A.) {458.00}	246.68	100.00
		1661	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1-2019	11/2021 (N.A.) {5/2023}	389.71 (N.A.) {397.00}	396.57	100.00
		1662	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8-2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	70.32	3.45
		1663	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4-2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	73.04	35.00
	COAL	1664	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5-2018	3/2026 (N.A.) {3/2027}	535.18 (N.A.) {535.17}	4.20	14.00
		1665	RANIGANJ MASTER PLAN (ECL) (N06000163)	8-2009	8/2019 (N.A.) {8/2024}	2,661.73 (N.A.) {5,146.48}	773.95	42.00
		1666	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8-2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	65.80	25.00
		1667	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4-2020	3/2025 (Mar-26) {3/2026}	483.65 (N.A.) {483.65}	51.11	12.00
		1668	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12-2015	9/2020 (N.A.) {2/2025}	341.22 (341.22) {341.22}	340.47	96.58

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1669	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7-2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	524.60	17.00
		1670	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4-2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	463.11	38.00
		1671	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11-2020	3/2025 (Mar-26) {3/2026}	888.99 (N.A.) {888.99}	61.45	30.00
		1672	BONJEMEHARI EXPANSION OCP (ECL) (N06000244)	8-2021	3/2025 (Mar-26) {3/2026}	570.12 (N.A.) {570.11}	80.09	16.00
		1673	ITAPARA OC (ECL) (N06000272)	12-2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	59.55	7.00
		1674	UCE OF TILABONI UG (ECL) (N06000276)	1-2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	51.13	10.00
		1675	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1-2023	3/2029 (Mar-28) {3/2028}	389.10 (N.A.) {389.10}	130.56	16.00
		1676	PARASCOLE JAMBAD OCP (ECL) (N06000281)	11-2024	3/2037 (N.A.) {3/2037}	1,193.55 (N.A.) {1,193.55}	0.00	-
	DEPARTMENT OF HIGHER EDUCATION	1677	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3-2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	185.75	-
	HOME AFFAIRS	1678	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10-2014	4/2018 (N.A.) {8/2025}	162.88 (210.83) {210.83}	189.70	90.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>MINES</u>	1679	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR- V, SA (CPWD) (N10000015)	4-2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	64.06	30.00
	<u>PETROLEUM</u>	1680	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3-2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	57.97	1.50
		1681	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12-2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	122.45	22.90
		1682	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3-2017	12/2020 (Jul-25) {12/2025}	1,740.00 (2,433.15) {2,433.15}	2,117.50	88.00
		1683	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3-2019	3/2031 (Mar-29) {3/2029}	5,830.20 (N.A.) {5,830.20}	828.43	27.00
		1684	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6-2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	177.63	19.90
		1685	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11-2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	344.83	66.59
	<u>POWER</u>	1686	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9-2014	9/2019 (N.A.) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,119.24	45.10
	<u>RAILWAYS</u>	1687	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4-2000	3/2019 (Feb-26) {2/2026}	1,188.91 (N.A.) {2,582.49}	1,146.80	75.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1688	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA- BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4-2010	3/2016 (N.A.) {3/2016}	2,397.72 (N.A.) {2,397.72}	197.20	17.00
		1689	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4-2010	3/2014 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	-
		1690	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4-2010	3/2016 (N.A.) {3/2026}	3,951.98 (N.A.) {8,964.35}	7,387.40	-
		1691	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4-2010	3/2016 (N.A.) {12/2026}	2,913.51 (N.A.) {4,834.54}	3,918.86	-
		1692	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4-2018	6/2022 (N.A.) {2/2025}	338.00 (N.A.) {393.83}	268.43	80.00
		1693	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10-2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	158.25	100.00
		1694	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7-2015	3/2025 (Mar-26) {3/2026}	283.54 (N.A.) {283.54}	162.52	44.00
		1695	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2-2009	9/2016 (N.A.) {6/2024}	4,874.58 (8,575.00) {10,442.41}	0.00	-
		1696	KALIPAHARI - BAKHTARNAGAR 5TH LINE (17.61 KM) (ER) (N22000630)	4-2024	6/2027 (N.A.) {6/2027}	350.46 (N.A.) {350.46}	0.00	-

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1697	SITARAMPUR BYE - PASS LINE (6.59 KM) (ER) (N22000631)	2-2023	3/2027 (N.A.) {3/2027}	461.64 (N.A.) {461.64}	0.34	-
	ROAD TRANSPORT AND HIGHWAYS	1698	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3-2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	2,048.00	88.78
		1699	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3-2021	9/2024 (N.A.) {6/2025}	2,200.93 (N.A.) {2,614.86}	2,614.86	95.34
		1700	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8-2021	8/2023 (N.A.) {3/2025}	557.55 (N.A.) {557.55}	472.82	91.41
		1701	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8-2018	12/2021 (N.A.) {7/2025}	622.04 (N.A.) {622.04}	521.47	83.60
		1702	DEVELOPMENT TO 4/6-LANNING OF NH- 31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3-2022	9/2025 (Sep-25) {9/2025}	995.04 (995.04) {995.04}	336.05	39.07
		1703	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3-2023	3/2026 (Mar-26) {3/2026}	410.83 (N.A.) {410.83}	117.72	17.00
		1704	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF LEVEL CROSSING NO 10 B T AT KM 307 050 OF NH 60 B (MoRTH) (N24002191)	3-2016	8/2025 (N.A.) {8/2025}	155.87 (N.A.) {155.87}	15.43	6.90

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1705	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12-2015	6/2018 (May-24) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100.00
		1706	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4-2014	9/2016 (N.A.) {3/2025}	1,665.00 (N.A.) {4,944.44}	4,944.44	94.25
		1707	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3-2018	9/2022 (Dec-22) {12/2025}	841.57 (708.30) {708.30}	9,091.34	94.20
		1708	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3-2016	11/2018 (Dec-23) {3/2025}	271.17 (291.20) {291.20}	193.14	79.44
		1709	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2-2018	9/2020 (Jan-24) {2/2025}	426.18 (426.18) {426.18}	364.92	100.00
		1710	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND (MoRTH) (N24000885)	3-2016	9/2023 (N.A.) {2/2025}	160.27 (N.A.) {213.97}	174.36	100.00
	<u>STEEL</u>	1711	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11-2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	62.49	4.30
	<u>WATER RESOURCES</u>	1712	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5-2018	2/2022 (N.A.) {3/2025}	198.43 (224.69) {286.97}	75.85	88.00

Table:-7. Project List: Ongoing Projects as of 31st January 2025

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1713	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8-2017	9/2022 (Jan-23) {12/2026}	307.12 (N.A.) {653.67}	0.00	-
		1714	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH (KMDA) (N30000042)	5-2018	2/2022 (Sep-20) {3/2025}	160.00 (154.73) {154.73}	87.35	89.00
		1715	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045)	8-2017	12/2021 (Feb-21) {2/2024}	185.22 (N.A.) {185.22}	49.99	100.00
		1716	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046)	2-2014	12/2019 (N.A.) {6/2022}	274.76 (N.A.) {332.56}	278.02	100.00
		1717	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047)	12-2014	4/2020 (N.A.) {6/2022}	272.32 (341.68) {272.32}	307.73	100.00
		1718	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048)	1-2018	12/2021 (Feb-21) {2/2024}	172.10 (N.A.) {172.10}	47.20	100.00
		1719	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049)	10-2017	12/2021 (Feb-21) {2/2024}	164.93 (N.A.) {164.93}	45.45	100.00
			Total			2,594,280.08 (916,322.52) {3,111,083.55}	16,58,825.36	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	rites
rites OF HIGHER EDUCATION	rites OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
