



Government of India
Ministry of Statistics and
Programme Implementation



OCMS

Ministry of Statistics & Programme Implementation



465th

Flash Report on Central Sector Infrastructure Projects

(Rs. 150 crore & above)

July 2024

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above


Total Ongoing Projects
(1793, Rs. 27,54,025.80 crore)

Mega*
(622 projects,
Rs. 22,31,330.08
crore)

Major*
(1171 projects,
Rs. 5,22,695.72
crore)

Completed@
projects during
July 2024
(21 projects,
Rs. 7570.75
crore)

**Newly Added/
elevated\$**
Projects during
July 2024
(4 projects,
Rs. 3263.92
crore)

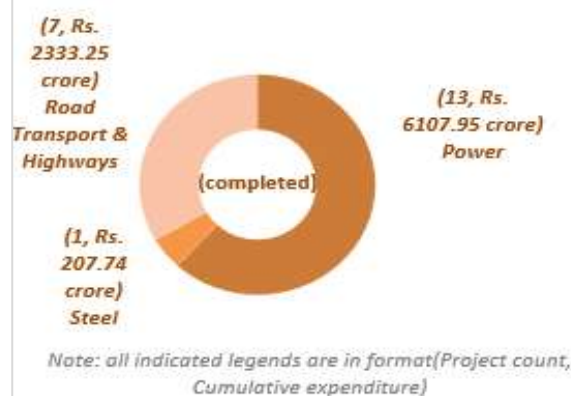


Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
other Indicated legends are in format (Project count, Original Cost)

* Mega Project if having original cost $\geq$ Rs. 1000 crore

* Major Project if original cost $<$ Rs. 1000 crore

\$ reported Anticipated cost more than Rs. 150 crore




reported Anticipated cost less than Rs. 150 crore

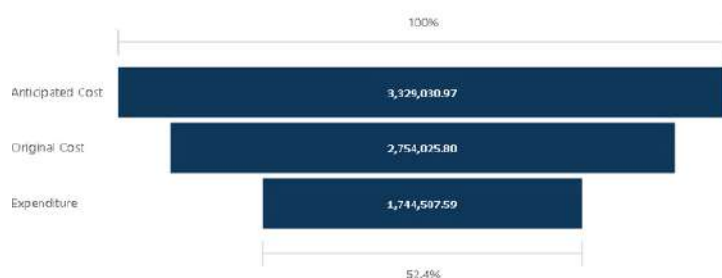


Total North East Region Ongoing Projects
(221, Rs. 1,77,558.5 crore)

Mega*
(23 projects,
Rs. 1,00,224.07
crore)

Major*
(198 projects,
Rs. 77,334.43
crore)

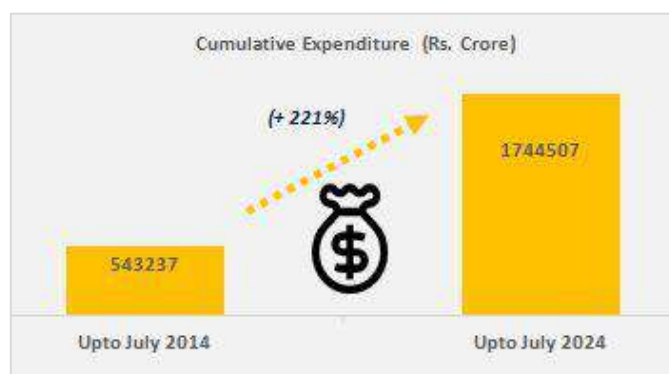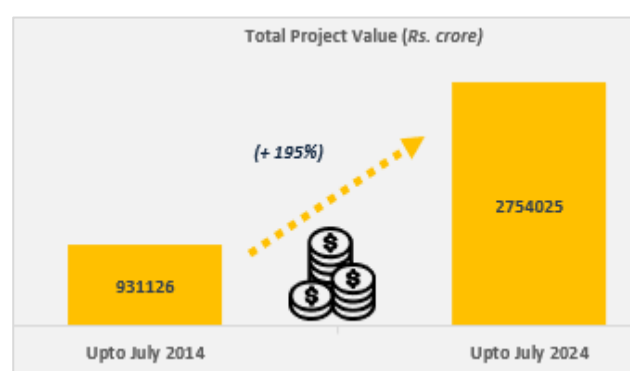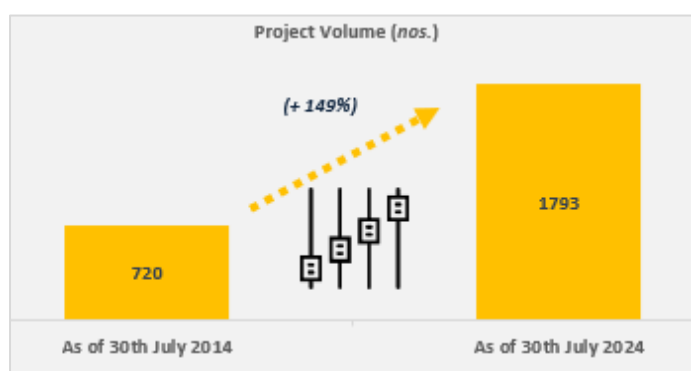


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

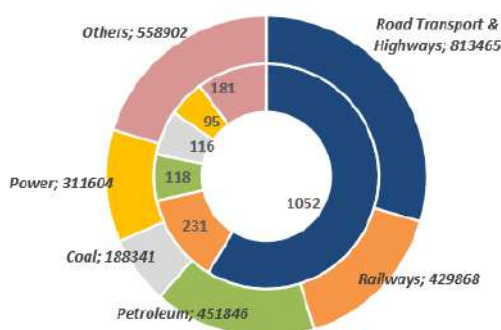


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

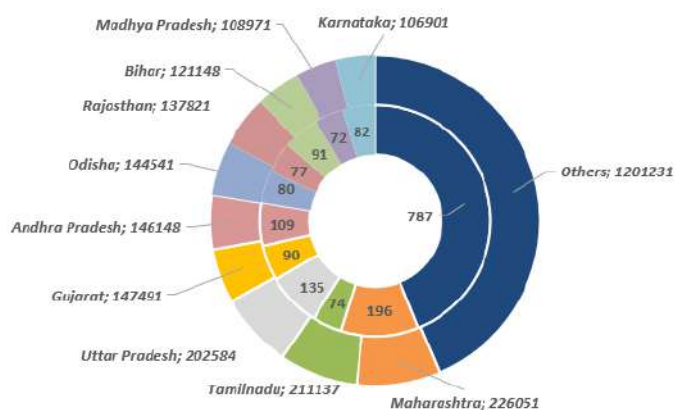

*Others include Jharkhand, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Assam, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N

Sectoral Distribution of total 640 projects with reported Physical Progress between 80-100%

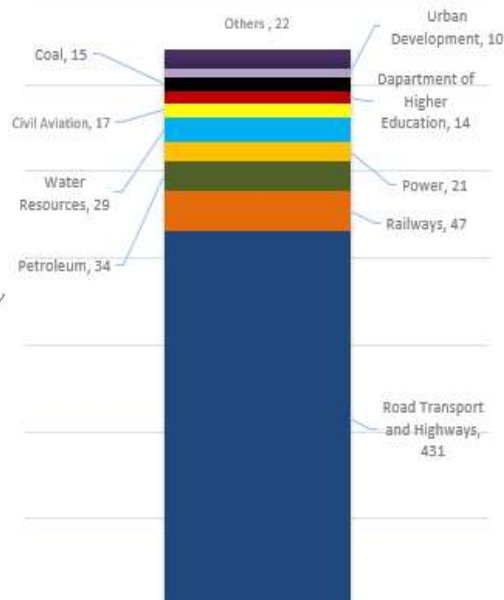

Note: This report is as of July 2024, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/ implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th August 2024.



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
