



Government of India
Ministry of Statistics and
Programme Implementation



OCMS
Ministry of Statistics & Programme Implementation

468th

Flash Report on Central Sector Infrastructure Projects



**(Rs. 150 crore
& above)**

October 2024

CONTENTS


Synopsis	1-2
List of Tables	3-269
Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	3-4
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	5-7
Table:-3. Project List: Completed during October 2024.....	8-14
Table:-4. Project List: Added during October 2024.....	15-18
Table:-5. Project List: Frozen/Deleted during October 2024.....	19-20
Table:-6. Project List: Ongoing Projects of North-East Region.....	21-46
Table:-7. Project List: Ongoing Projects as of 31 st October 2024.....	47-269




SYNOPSIS

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above


Total Ongoing Projects (1747, ₹26,09,935.22 crore)

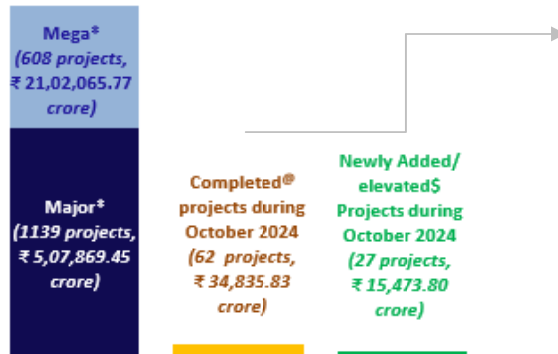

Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
 other Indicated legends are in format (Project count, Original Cost)
 * Mega Project if having original cost $\geq$ 1000 crore
 * Major Project if original cost < 1000 crore
 \$ reported Anticipated cost more than 150 crore

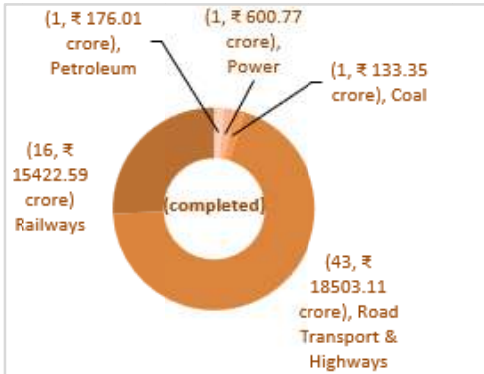


Note: all indicated legends are in format (Project count, Cumulative expenditure)

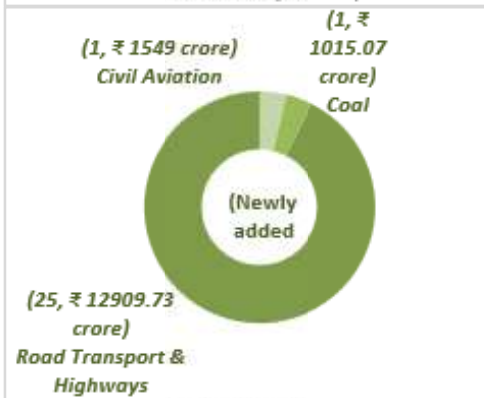

Note: all indicated legends are in format (Project count, Original Cost)


Cost and Expenditure Details (Amount is in ₹ Crore)

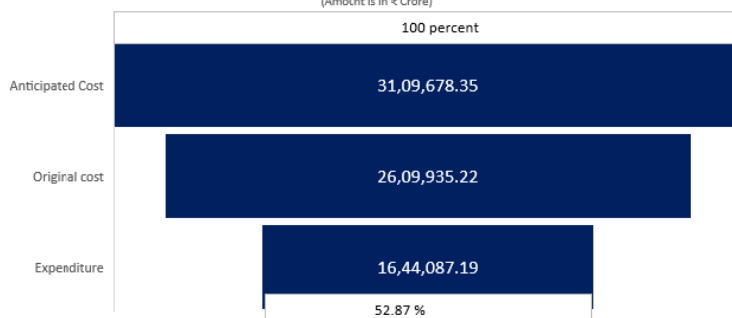


Total North East Region Ongoing Projects (221, ₹178,090.02 crore)




Project Volume (nos.)

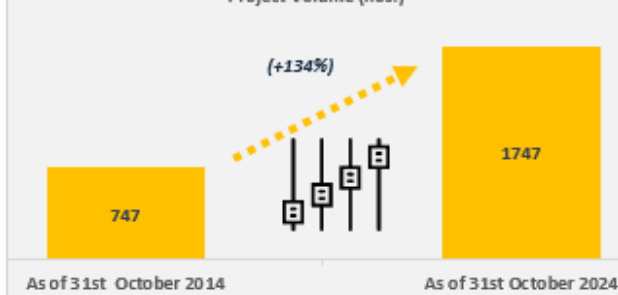


Project Volume (nos.)

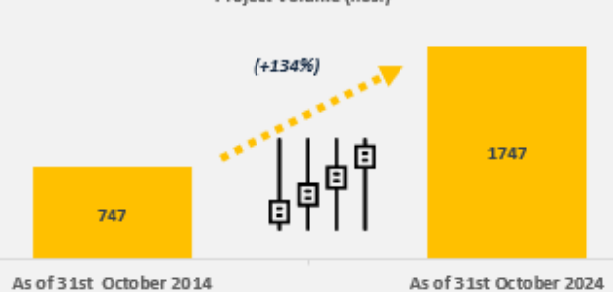

Cumulative Expenditure (in crore)

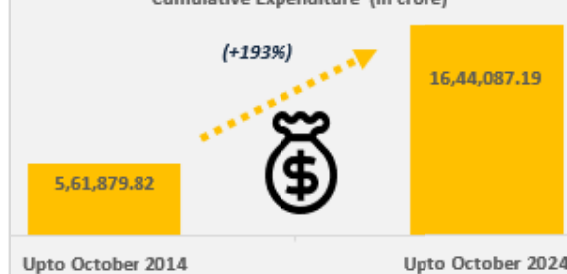


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

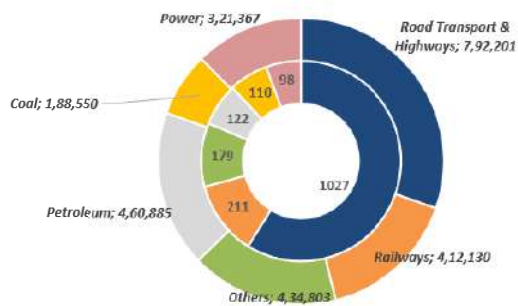


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DNER, Renewable Energy, Shipping & Ports, and Social Justice

Sectoral Distribution of total 612 projects with reported Physical Progress between 80-100%

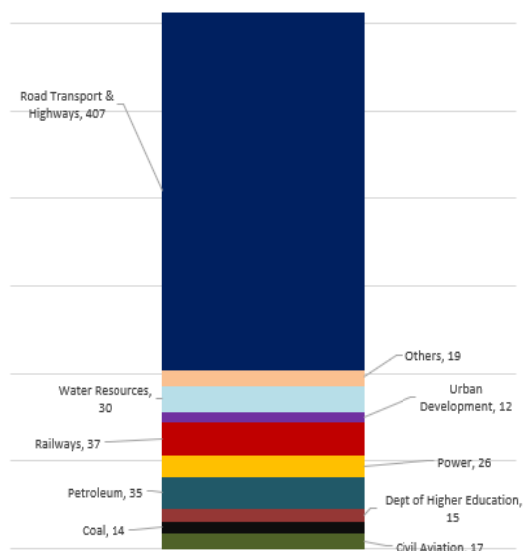

State Comparison : Major States (as per count)
 [Outer Ring: Original Approved Cost in ₹ Crore] & [Inner Ring: Project Count]

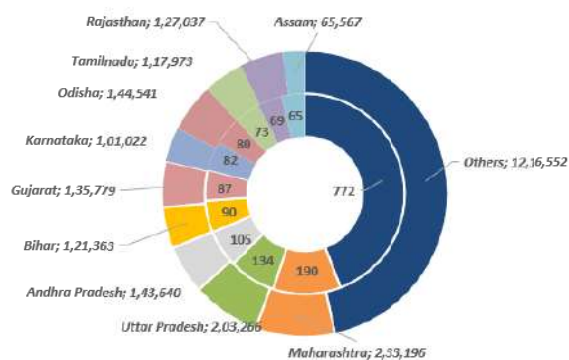

*Others include Jharkhand, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Madhya Pradesh, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa,

Note: This report is as of October 2024, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th October 2024.

LIST OF TABLES

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	CIVIL AVIATION	41	28,039.58 (28,927.84) {32,047.70}	16,011.48
2	COAL	110	188,549.79 (190,719.01) {193,291.69}	72,151.74
3	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,294.08) {10,338.99}	7,267.10
4	DONER	1	151.33 (151.33) {151.33}	148.33
5	DPIIT	2	24,857.00 (24,857.00) {25,485.00}	15,041.18
6	FINANCE	2	577.27 (577.27) {569.04}	399.67
7	HEALTH AND FAMILY WELFARE	9	7,561.27 (7,730.18) {7,727.97}	4,558.25
8	HOME AFFAIRS	5	2,025.73 (2,946.02) {2,946.00}	2,391.38
9	MINES	8	7,559.78 (9,356.73) {9,833.57}	5,321.37
10	PETROLEUM	122	460,884.92 (520,024.77) {530,766.62}	253,575.66
11	POWER	98	321,366.69 (340,634.43) {385,802.81}	206,634.20
12	RAILWAYS	211	412,130.16 (521,249.02) {642,193.76}	411,707.54
13	ROAD TRANSPORT AND HIGHWAYS	1027	792,200.93 (826,850.88) {841,025.51}	395,793.23
14	SHIPPING AND PORTS	1	5,369.18 (5,061.15) {5,061.15}	3,115.95
15	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	STEEL	12	11,337.99 (12,682.15) {12,682.15}	5,863.91
17	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	4,802.26
18	URBAN DEVELOPMENT	30	287,043.72 (294,057.08) {312,556.91}	209,727.99
19	WATER RESOURCES	41	23,466.28 (23,420.50) {70,077.27}	29,502.15
	Total	1747	2,609,935.22 (2,846,660.32) {3,109,678.35}	1,644,087.19

***Either Revised or Original Cost**

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	9	2,847.18 (3,137.68) {3,118.54}	2,042.36
2	ANDHRA PRADESH	105	143,639.67 (153,820.00) {207,081.71}	118,576.41
3	ARUNACHAL PRADESH	23	47,724.71 (47,788.24) {62,810.39}	30,873.88
4	ASSAM	65	65,566.55 (65,758.02) {75,298.98}	42,932.19
5	BIHAR	90	121,362.68 (140,432.52) {147,497.07}	93,427.26
6	CHHATTISGARH	53	82,054.75 (83,970.20) {84,743.01}	35,684.67
7	DELHI	27	92,995.74 (98,711.59) {97,266.78}	74,727.94
8	GOA	4	1,526.58 (1,526.58) {1,613.08}	733.41
9	GUJARAT	87	135,779.29 (138,863.22) {145,051.88}	72,859.31
10	HARYANA	31	71,959.27 (82,037.39) {82,787.07}	36,523.63
11	HIMACHAL PRADESH	29	27,418.92 (28,706.60) {43,798.61}	29,131.11
12	JAMMU AND KASHMIR	54	77,239.47 (112,890.02) {119,007.32}	73,553.60
13	JHARKHAND	63	102,972.42 (107,849.19) {111,530.61}	55,580.37
14	KARNATAKA	82	101,021.61 (104,474.82) {107,169.36}	48,025.03
15	KERALA	33	69,127.95 (76,413.45) {76,356.72}	38,259.92
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	1,112.75

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	MADHYA PRADESH	63	105,123.08 (109,933.40) {117,997.98}	38,922.06
18	MAHARASHTRA	190	233,195.82 (237,496.61) {266,628.51}	129,861.47
19	MANIPUR	32	15,304.69 (23,160.75) {30,368.22}	18,841.93
20	MEGHALAYA	15	6,028.77 (6,019.79) {5,974.15}	3,299.64
21	MIZORAM	19	10,895.92 (15,973.53) {19,461.27}	16,018.81
22	MULTI STATE	56	285,457.50 (329,875.58) {349,879.13}	226,440.14
23	NAGALAND	32	11,633.24 (17,318.60) {17,017.57}	7,812.94
24	ODISHA	80	144,541.42 (147,690.19) {155,572.45}	63,704.14
25	PUNJAB	39	37,885.48 (37,828.79) {37,917.03}	14,066.03
26	RAJASTHAN	69	127,036.80 (156,986.75) {156,285.50}	83,326.26
27	SIKKIM	22	14,500.36 (14,896.52) {22,320.65}	12,366.62
28	TAMIL NADU	73	117,973.21 (128,349.94) {138,011.83}	54,281.20
29	TELANGANA	53	39,244.93 (39,638.81) {41,966.88}	24,455.01
30	TRIPURA	13	6,435.78 (6,558.15) {6,558.15}	1,034.68
31	UTTAR PRADESH	134	203,265.95 (209,631.05) {224,018.59}	106,991.35
32	UTTARAKHAND	33	36,816.79 (42,040.90) {59,857.18}	43,507.95

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	WEST BENGAL	63	68,883.72 (74,406.47) {92,077.49}	45,113.12
	Total	1747	2,609,935.22 (2,846,660.32) {3,109,678.35}	1,644,087.19

***Either Revised or Original Cost**

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
<u>COAL</u>					
	1	CHURI BENTI UG (0.81 MTY) (CCL) (N06000083) (JHARKHAND)	163.51	03/2011	133.35
<u>PETROLEUM</u>					
	2	CONSTRUCTION OF TWO PRODUCED WATER TREATMENT PLANTS (PWTP) AT BECHARAJI AND SOBHASAN INSTALLATION OF (ONGC) (N16000482) (GUJARAT)	320.20	07/2024	176.01
<u>POWER</u>					
	3	OMKARESHWAR FLOATING SOLAR POWER PROJECT (90 MW) (SJVN) (N18000342) (MADHYA PRADESH)	646.17	04/2024	600.77
<u>RAILWAYS</u>					
	4	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR (ECR) (220100240) (BIHAR)	324.73	03/2012	1,236.97
	5	DAUSA-GANGAPUR CITY(NL),NWR (NWR) (220100184) (RAJASTHAN)	410.08	02/2019	1,060.42
	6	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) (WR) (N22000123) (GUJARAT)	318.24	03/2012	1,317.64
	7	PHULERA - DIGANA DOUBLING (NWR) (N22000326) (MULTI STATE)	600.00	03/2020	765.54
	8	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) (ECR) (N22000180) (BIHAR)	372.14	N.A.	2,538.48
	9	AGARTALA-AKHAURA NL (NFR) (N22000195) (TRIPURA)	569.63	03/2020	380.92

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	10	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI (SR) (N22000079) (TAMIL NADU)	724.69	02/2019	1,931.12
	11	KALOL-KADI-KATOSAN ROAD (37.23 KM) (WR) (N22000549) (GUJARAT)	279.23	06/2027	397.87
	12	POWARKHEDA - JUJHARPUR - SINGLE LINE FLYOVER IN UP DIRECTION (15.89 KM) (WCR) (N22000552) (MADHYA PRADESH)	199.63	03/2024	150.00
	13	Chinnasalem-Kallakurichi New Line (MM of cuddalore- Salem 191 KM) (SR) (N22000567) (TAMIL NADU)	417.50	03/2025	184.32
	14	BARABANKI AKBARPUR DOUBLING (NR) (N22000578) (UTTAR PRADESH)	1,200.00	03/2025	1,650.00
	15	JAUNPUR AKBARPUR (TANDA) DOUBLING (NR) (N22000582) (UTTAR PRADESH)	515.50	03/2025	670.00
	16	RAJPURA-BHATINDA (172.64 KM) (MEGA) (N22000597) (PUNJAB)	1,775.73	03/2024	1,750.00
	17	NATHDWARA-NEW NATHDWARA NEW LINE (MM OF AJMER-CHITTAURGARH-UDAIPUR) (WR) (N22000623) (GUJARAT)	166.33	06/2025	55.81
	18	KATNI-BINA 3RD LINE (263 KM) (WCR) (N22000415) (MADHYA PRADESH)	2,478.23	03/2022	1,279.35
	19	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K (SCR) (N22000432) (TELANGANA)	119.73	03/2022	54.15

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
ROAD TRANSPORT AND HIGHWAYS					
	20	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K (NHAI) (N24000854) (JHARKHAND)	1,005.08	03/2021	699.05
	21	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM (NHIDCL) (N24000903) (MEGHALAYA)	306.28	03/2022	233.49
	22	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 (MoRTH) (N24000928) (ANDHRA PRADESH)	333.21	12/2015	342.71
	23	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU (MoRTH) (N24000929) (ANDHRA PRADESH)	372.68	02/2017	274.76
	24	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD (MoRTH) (N24000932) (ANDHRA PRADESH)	319.28	08/2017	245.55
	25	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P (MoRTH) (N24000963) (ANDHRA PRADESH)	418.03	08/2018	370.55
	26	WAKAN PALI KHOPOLI (MoRTH) (N24001026) (MAHARASHTRA)	376.19	05/2019	118.74
	27	AHMADPUR TO PIMPLA (MoRTH) (N24001029) (MAHARASHTRA)	422.38	08/2019	269.59

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	28	PIMPLA TO MANJARSUMBHA (MoRTH) (N24001030) (MAHARASHTRA)	595.77	08/2019	357.73
	29	MANSAR TO SALAIKHURD (MoRTH) (N24001035) (MAHARASHTRA)	418.36	12/2019	263.13
	30	JAHIRABAD TO LATUR (MoRTH) (N24001040) (MAHARASHTRA)	461.96	11/2019	329.59
	31	SHIROD SHAHPURER TO NANDED (MoRTH) (N24001041) (MAHARASHTRA)	211.34	07/2019	136.33
	32	SALAIKHURD TO TIRORA (MoRTH) (N24001042) (MAHARASHTRA)	415.25	12/2019	274.02
	33	NILAJPHATA TO BHANDARA (MoRTH) (N24001043) (MAHARASHTRA)	420.63	05/2020	219.40
	34	MEHKAR TO AJISPUR (MoRTH) (N24001048) (MAHARASHTRA)	232.77	07/2019	151.60
	35	CHIKALI TO DHAD (MoRTH) (N24001061) (MAHARASHTRA)	189.46	12/2019	133.07
	36	DHAD BHOKARDAN TO BHOKARDHAN SILLOD (MoRTH) (N24001062) (MAHARASHTRA)	336.21	12/2019	236.11
	37	PARBHANI TO GANGKHED (MoRTH) (N24001065) (MAHARASHTRA)	238.19	12/2019	194.54
	38	KOTHARI TO DHANORA (MoRTH) (N24001073) (MAHARASHTRA)	301.38	08/2020	240.32
	39	OSMANNAGAR TO KUNDRA (MoRTH) (N24001075) (MAHARASHTRA)	344.25	08/2020	194.72

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	40	CHIMUR TO WARORA (MoRTH) (N24001105) (MAHARASHTRA)	467.70	03/2019	235.04
	41	BARASGAON TO RAHATEE (MoRTH) (N24001113) (MAHARASHTRA)	289.11	09/2018	232.56
	42	FARDAPUR TO JALGAON (MoRTH) (N24001126) (MAHARASHTRA)	456.45	06/2019	427.43
	43	WARDHA TO ARVI (MoRTH) (N24001150) (MAHARASHTRA)	313.58	04/2020	230.41
	44	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) (NHIDCL) (N24001280) (NAGALAND)	320.97	06/2022	182.21
	45	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) (NHIDCL) (N24001284) (NAGALAND)	361.53	06/2022	200.22
	46	DULTE- KWALKULH - CHAMPAI PKG.3 (NHIDCL) (N24001357) (MIZORAM)	674.71	06/2023	589.25
	47	JORAM ? KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) (NHIDCL) (N24001392) (ARUNACHAL PRADESH)	199.03	04/2022	102.85
	48	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA- PATRAN ROAD (SH-1 (NHAI) (N24001414) (PUNJAB)	733.00	01/2024	868.44
	49	MOPA AIRPORT (MoRTH) (N24001458) (GOA)	1,183.16	04/2022	1,106.30

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	50	REHABILITATION AND UPGRADATION OF AMBOLI JUNCTION (DESIGN CH. 71+530) TO AJARA (DESIGN CH.100+835) SE (MoRTH) (N24001881) (MAHARASHTRA)	574.00	11/2024	574.00
	51	SHEWALI (SAKRI) - NANDURBAR (MoRTH) (N24001893) (MAHARASHTRA)	232.59	04/2024	97.70
	52	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA (NHAI) (N24001784) (HARYANA)	1,935.61	09/2021	856.41
	53	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH- 66) ON PANJIM-MANGALORE (MoRTH) (N24000444) (GOA)	936.40	N.A.	770.90
	54	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR (MoRTH) (N24000516) (GOA)	819.95	N.A.	504.65
	55	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T (MoRTH) (N24000282) (ANDHRA PRADESH)	195.45	11/2014	294.47
	56	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V (NHAI) (N24001514) (PUNJAB)	1,060.29	01/2024	975.55
	57	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH (NHAI) (N24001549) (ASSAM)	442.23	04/2020	647.30

Table:-3. Project List: Completed during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	58	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0 (NHAI) (N24001645) (PUNJAB)	366.85	06/2023	276.34
	59	SIX LANNING OF MANDI DABWALI (PUNJAB/HARYANA BORDER)- CHAUTALA ROAD SECTION FROM PROPOSED MANDI DABW (NHAI) (N24001672) (HARYANA)	864.27	01/2024	787.78
	60	CONSTRUCTION OF 4 LANE BANGALORE -CHENNAI EXPRESSWAY FROM KM 53.500 TO KM 71.000 SECTION OF NE-7 (BA (NHAI) (N24001685) (KARNATAKA)	1,069.00	01/2024	840.40
	61	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE- 7(ALONG WITH 0.700 (NHAI) (N24001688) (KARNATAKA)	3,184.00	09/2023	1,165.00
	62	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M (NHAI) (N24001689) (KARNATAKA)	1,745.00	09/2023	1,252.90
		Total	37,744.85		34,835.83

Table:-4. Project List: Added during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>CIVIL AVIATION</u>	1	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115) (WEST BENGAL)	8/2024	1,549.00 (N.A.) {1,549.00}	3/2027 (N.A.) {3/2027}
<u>COAL</u>	2	GAURI CENTRAL OCM (WCL) (N06000278) (MAHARASHTRA)	8/2023	1,015.07 (N.A.) {1,015.07}	3/2030 (N.A.) {3/2030}
	3	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166) (MADHYA PRADESH)	3/2024	799.20 (N.A.) {799.20}	3/2026 (Mar-26) {3/2026}
	4	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167) (RAJASTHAN)	3/2024	334.64 (N.A.) {334.64}	10/2026 (N.A.) {10/2026}
	5	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168) (RAJASTHAN)	3/2023	606.61 (N.A.) {606.61}	10/2026 (N.A.) {10/2026}
	6	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169) (MAHARASHTRA)	3/2022	316.44 (N.A.) {316.44}	9/2025 (N.A.) {9/2025}
	7	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170) (MAHARASHTRA)	3/2022	163.86 (N.A.) {163.86}	5/2025 (N.A.) {5/2025}

Table:-4. Project List: Added during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	8	REHABILITATION & UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START F (MoRTH) (N24002171) (MAHARASHTRA)	2/2023	249.13 (N.A.) {249.13}	4/2025 (N.A.) {4/2025}
	9	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172) (MAHARASHTRA)	2/2023	856.82 (N.A.) {856.82}	12/2025 (N.A.) {12/2025}
	10	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173) (MAHARASHTRA)	2/2023	253.78 (N.A.) {253.78}	4/2025 (N.A.) {4/2025}
	11	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174) (MAHARASHTRA)	2/2023	984.07 (N.A.) {984.07}	8/2026 (N.A.) {8/2026}
	12	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175) (MAHARASHTRA)	2/2023	328.11 (N.A.) {328.11}	8/2025 (N.A.) {8/2025}
	13	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STANDA (MoRTH) (N24002176) (MAHARASHTRA)	3/2023	594.44 (N.A.) {594.44}	2/2026 (N.A.) {2/2026}
	14	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177) (MAHARASHTRA)	3/2023	153.79 (N.A.) {153.79}	7/2025 (N.A.) {7/2025}

Table:-4. Project List: Added during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>ROAD TRANSPORT AND HIGHWAYS</u>	15	REHABILITATION, UPGRADATION & WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHOUL (MoRTH) (N24002178) (MAHARASHTRA)	2/2023	723.13 (N.A.) {723.13}	7/2026 (N.A.) {7/2026}
	16	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179) (JAMMU AND KASHMIR)	3/2023	980.21 (N.A.) {980.21}	7/2026 (N.A.) {7/2026}
	17	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180) (JAMMU AND KASHMIR)	9/2021	734.64 (N.A.) {734.64}	7/2026 (N.A.) {7/2026}
	18	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (MoRTH) (N24002181) (GOA)	4/2023	641.46 (N.A.) {641.46}	4/2026 (N.A.) {4/2026}
	19	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION (MoRTH) (N24002182) (GUJARAT)	3/2023	530.20 (N.A.) {530.20}	3/2026 (N.A.) {3/2026}
	20	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183) (GUJARAT)	3/2022	151.13 (N.A.) {171.00}	3/2026 (N.A.) {3/2026}
	21	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184) (WEST BENGAL)	3/2023	410.83 (N.A.) {410.83}	3/2026 (Mar-26) {3/2026}

Table:-4. Project List: Added during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	22	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185) (JAMMU AND KASHMIR)	3/2023	992.43 (N.A.) {992.43}	9/2026 (N.A.) {9/2026}
	23	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186) (KARNATAKA)	3/2024	166.58 (N.A.) {166.58}	9/2025 (N.A.) {9/2025}
	24	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH- 766C ((MoRTH) (N24002187) (KARNATAKA)	2/2024	313.56 (N.A.) {313.56}	2/2026 (N.A.) {2/2026}
	25	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188) (KARNATAKA)	3/2024	445.62 (N.A.) {445.62}	3/2026 (N.A.) {3/2026}
	26	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189) (KARNATAKA)	9/2024	196.05 (N.A.) {196.05}	3/2026 (N.A.) {3/2026}
	27	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM-VIJAYAWADA) (NHAI) (N24002190) (TELANGANA)	3/2023	983.00 (N.A.) {983.00}	8/2026 (N.A.) {8/2026}
Grand Total				15,473.80 (-) {15,493.67}	

Table:-5. Project List: Frozen/Deleted during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
<u>ATOMIC ENERGY</u>						
	1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, (BHAVNI) (020100044) (TAMIL NADU)	3,492.00	09/2010	6,921.72	0
	2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 (NPCIL) (N02000010) (GUJARAT)	11,459.00	12/2015	21,479.00	0
	3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) (NPCIL) (N02000027) (RAJASTHAN)	12,320.00	12/2016	19,056.00	0
	4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 (NPCIL) (N02000028) (TAMIL NADU)	39,849.00	11/2020	45,718.00	0
	5	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 (NPCIL) (N02000029) (TAMIL NADU)	49,621.00	09/2027	18,135.00	0
<u>RAILWAYS</u>						
	6	MEHSANA-PALANPUR (65.1 KM) (WR) (N22000534) (GUJARAT)	529.30	09/2026	371.32	0
	7	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE (MRTP) (N22000135) (WEST BENGAL)	4,874.58	03/2016	8,008.94	0
	8	NEW BG LINE FROM BYRNIHAT TO SHILLONG (NFR) (N22000205) (MEGHALAYA)	906.46	03/2021	269.80	2
	9	MADURAI-TUTICORIN VIA ARUPPUKOTTAI (SR) (N22000215) (MULTI STATE)	120.70	03/2019	342.13	14

Table:-5. Project List: Frozen/Deleted during October 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
	10	TURAVUR-AMBALAPUZHA DOUBLING (SR) (N22000400) (KERALA)	1,000.00	N.A.	1.63	0
		Total	124,172.04		120,303.54	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
<u>ARUNACHAL PRADESH</u>	<u>CIVIL AVIATION</u>	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2/2019	8/2022 (Dec-24) {12/2024}	645.63 (N.A.) {712.15}	670.15	98.58
	<u>POWER</u>	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9/2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {21,247.54}	22,512.54	94.01
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2/2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,628.95	12.95
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2/2017	11/2023 (Mar-24) {11/2024}	180.57 (244.10) {180.57}	154.17	90.01
		5	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2/2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	144.91	100
		6	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3/2017	3/2022 (Jun-25) {6/2025}	1,718.59 (1,718.59) {1,718.59}	683.02	69.07
		7	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9/2016	12/2019 (Aug-24) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		8	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1/2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8/2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	140.75	62.76
		10	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9/2020	5/2022 (Oct-22) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3/2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3/2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100
		13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3/2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100
		14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3/2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	371.45	92.72
		15	TADADEGE - HENKAR (NHIDCL) (N24001315)	2/2021	3/2023 (Jun-24) {9/2024}	550.45 (N.A.) {550.45}	113.92	44.05
		16	LADDA - BASAI (NHIDCL) (N24001316)	2/2021	4/2023 (Jan-25) {3/2025}	445.96 (N.A.) {445.96}	117.91	49.63

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		17	DOGINALA - GAU (NHIDCL) (N24001320)	12/2020	9/2022 (N.A.) {12/2024}	242.30 (N.A.) {242.30}	21.47	17.81
		18	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8/2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		19	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8/2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		20	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8/2020	4/2022 (Feb-24) {11/2024}	184.88 (N.A.) {184.88}	95.64	93.83
		21	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2/2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	480.10	94.25
		22	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6/2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	365.27	100
		23	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6/2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	142.05	35.74
ASSAM	CIVIL AVIATION	24	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12/2016	3/2021 (N.A.) {5/2025}	1,142.00 (N.A.) {2,333.00}	1,414.84	68.99

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HEALTH AND FAMILY WELFARE</u>	25	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5/2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	769.30	99.07
	<u>PETROLEUM</u>	26	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9/2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	3.05	4.6
		27	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3/2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	78
		28	DCU REVAMP PROJECT (NRL) (N16000511)	8/2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	161.76	35.6
		29	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1/2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	139.67	40.3
		30	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1/2018	2/2020 (Dec-23) {12/2024}	543.91 (N.A.) {670.90}	491.56	93.83
		31	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1/2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	13,286.18	65.01
		32	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1/2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,304.39	78.74
		33	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5/2021	10/2023 (Feb-25) {2/2025}	412.00 (509.84) {509.84}	358.18	78.3
		34	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON (ONGC) (N16000433)	8/2021	2/2023 (Jun-24) {11/2024}	218.38 (N.A.) {218.38}	207.18	98.3

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		35	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3/2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	158.33	52.4
		36	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6/2021	12/2024 (N.A.) {12/2024}	860.00 (N.A.) {860.00}	401.83	88.7
		37	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12/2020	7/2024 (Mar-24) {12/2024}	430.76 (N.A.) {430.76}	245.08	73.76
		38	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6/2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	62.57	8.9
		39	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3/2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	1.38	12
		40	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3/2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	37.48	4.5
	<u>RAILWAYS</u>	41	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4/2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,494.15	92
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	42	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2/2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	192.50	30.65
		43	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12/2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		44	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8/2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	299.82	58.2
		45	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3/2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	243.26	98.58
		46	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3/2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	87.43	34.43
		47	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9/2021	7/2024 (N.A.) {12/2024}	625.64 (N.A.) {625.64}	472.63	85.15
		48	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3/2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	150.92	100
		49	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 (NHIDCL) (N24001452)	4/2022	7/2024 (N.A.) {8/2024}	170.95 (N.A.) {170.95}	125.71	100
		50	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11/2021	7/2024 (N.A.) {12/2024}	204.10 (N.A.) {204.10}	127.65	83.53
		51	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11/2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,060.96	52.57
		52	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE (NHIDCL) (N24000902)	10/2017	6/2020 (Dec-23) {4/2024}	818.00 (887.68) {887.68}	874.30	100
		53	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3/2020	6/2022 (May-25) {5/2025}	261.13 (N.A.) {261.13}	64.96	54.59
		54	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3/2020	6/2022 (Apr-25) {4/2025}	217.50 (N.A.) {217.50}	84.36	64.15

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		55	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3/2020	12/2022 (N.A.) {8/2024}	220.20 (N.A.) {220.20}	216.04	97.76
		56	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8/2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	193.58	100
		57	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3/2020	3/2022 (Jan-25) {1/2025}	216.49 (241.52) {216.49}	104.36	79.48
		58	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6/2015	8/2023 (N.A.) {12/2024}	437.39 (N.A.) {437.39}	335.90	26.59
		59	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6/2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	368.62	1.43
		60	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH- 52 (NHIDCL) (N24000431)	1/1991	6/2019 (Jun-19) {3/2025}	520.01 (N.A.) {520.01}	304.80	90.01
		61	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12/2015	12/2018 (Jul-21) {3/2025}	289.99 (N.A.) {289.99}	232.66	87.62
		62	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1/2016	1/2016 (N.A.) {12/2024}	294.17 (N.A.) {294.17}	296.22	46.44

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		63	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1/2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	146.28	12.19
		64	FOUR LANING OF SRIRAMPUR-DHUBRI PKG- 2 (NHIDCL) (N24001544)	3/2022	1/2025 (N.A.) {1/2025}	909.02 (N.A.) {909.02}	408.84	77.21
		65	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8/2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	178.56	99.04
		66	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3/2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	480.84	52.48
		67	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3/2022	6/2024 (N.A.) {12/2024}	457.72 (N.A.) {457.72}	313.97	89.68
		68	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3/2022	2/2025 (N.A.) {12/2025}	613.89 (N.A.) {613.89}	17.15	9.23
		69	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1/2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	153.42	43.85
		70	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3/2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	4.07	10.6

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		71	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3/2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	301.41	38.71
		72	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3/2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	287.76	39.05
		73	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3/2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	347.95	36.05
		74	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3/2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	187.98	53.3
		75	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3/2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	178.24	52.85
		76	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3/2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	359.25	25.65
		77	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3/2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	212.32	10.38
		78	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3/2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	270.76	14.23
		79	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1/2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	177.39	50.11

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		80	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1/2023	12/2025 (N.A.) {12/2025}	356.65 (N.A.) {356.65}	115.18	5.55
		81	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3/2023	12/2025 (N.A.) {12/2025}	643.42 (N.A.) {643.42}	67.22	8.45
		82	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2/2020	3/2022 (N.A.) {10/2024}	592.06 (N.A.) {592.06}	304.02	100
		83	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2/2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	320.55	12.96
		84	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3/2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	744.22	32.05
		85	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2/2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	177.78	19.59
		86	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12/2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	284.84	31.35
		87	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3/2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	91.62	0

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		88	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3/2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	73.01	0
MANIPUR	CIVIL AVIATION	89	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11/2021	7/2024 (Dec-25) {12/2025}	499.00 (N.A.) {499.00}	115.07	37.88
	RAILWAYS	90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4/2003	3/2011 (Mar-28) {12/2028}	4,454.17 (12,274.06) {19,517.70}	14,882.06	80.1
	ROAD TRANSPORT AND HIGHWAYS	91	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3/2023	2/2026 (Mar-26) {3/2026}	578.98 (N.A.) {578.98}	68.30	34.04
		92	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9/2021	1/2025 (Jan-25) {1/2025}	315.56 (N.A.) {315.56}	73.38	52.02
		93	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1/2023	12/2025 (Dec-25) {12/2025}	760.16 (N.A.) {760.16}	67.05	28.83
		94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3/2020	6/2022 (Jan-25) {1/2025}	292.24 (N.A.) {292.24}	127.86	85.33
		95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6/2020	8/2022 (Jan-25) {1/2025}	365.53 (N.A.) {365.53}	156.31	77.36
		96	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3/2020	6/2022 (Jan-25) {1/2025}	167.95 (204.12) {167.95}	88.05	69.89

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		97	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7/2020	8/2022 (Feb-25) {2/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		98	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8/2020	4/2022 (Jun-25) {6/2025}	379.39 (N.A.) {379.39}	189.86	45.88
		99	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO (NHIDCL) (N24001275)	8/2020	4/2022 (N.A.) {12/2025}	268.98 (N.A.) {268.98}	22.08	0
		100	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8/2020	4/2022 (N.A.) {12/2025}	228.97 (N.A.) {228.97}	0.00	0
		101	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2/2021	12/2022 (Mar-25) {3/2025}	226.32 (N.A.) {226.32}	87.99	66.07
		102	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2/2021	12/2022 (Oct-24) {11/2024}	188.36 (N.A.) {188.36}	126.71	97.95
		103	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3/2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100
		104	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3/2021	12/2022 (Mar-25) {3/2025}	195.14 (N.A.) {195.14}	59.99	50.77
		105	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3/2021	12/2022 (Jan-25) {1/2025}	234.08 (N.A.) {234.08}	139.45	90.34
		106	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12/2021	5/2024 (Feb-25) {2/2025}	410.68 (N.A.) {410.68}	105.71	50.81
		107	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12/2021	2/2025 (Sep-25) {9/2025}	504.76 (N.A.) {504.76}	113.57	48.76

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		108	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3/2022	2/2025 (Feb-25) {2/2025}	152.11 (N.A.) {152.11}	53.26	75
		109	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9/2021	2/2024 (Mar-25) {3/2025}	310.76 (N.A.) {310.76}	121.05	77.4
		110	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8/2021	12/2023 (Jul-25) {7/2025}	579.63 (N.A.) {579.63}	131.58	52.65
		111	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8/2021	5/2023 (Oct-24) {1/2025}	467.41 (N.A.) {467.41}	243.19	92.31
		112	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8/2021	5/2023 (Jan-25) {1/2025}	477.86 (N.A.) {477.86}	235.67	80.3
		113	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9/2021	5/2023 (Nov-24) {4/2025}	311.18 (N.A.) {311.18}	171.57	72.7
		114	IMPHAL ? MOREH (PACKAGE 4) (NHIDCL) (N24001399)	3/2021	1/2023 (N.A.) {4/2024}	277.99 (N.A.) {277.99}	146.35	100
		115	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3/2021	1/2023 (May-25) {5/2025}	211.70 (N.A.) {211.70}	35.16	38.2
		116	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7/2021	3/2023 (Mar-25) {3/2025}	467.00 (N.A.) {467.00}	183.55	75.27
		117	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7/2021	3/2023 (Jan-25) {1/2025}	185.80 (N.A.) {185.80}	112.31	92.65
		118	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7/2021	3/2023 (Aug-24) {1/2025}	483.87 (N.A.) {483.87}	278.89	91.03
		119	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7/2021	3/2023 (Feb-25) {2/2025}	198.77 (N.A.) {198.77}	110.09	85.12
		120	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7/2021	10/2023 (Feb-24) {6/2025}	673.27 (N.A.) {673.27}	361.21	72.82

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA	<u>DEPARTMENT OF HIGHER EDUCATION</u>	121	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (<i>RITES OF HIGHER</i>) (<i>N42000001</i>)	9/2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	276.05	74
	<u>DONER</u>	122	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR (<i>HSCL FOR DONER</i>) (<i>N12000103</i>)	4/2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	98.5
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	123	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (<i>NHIDCL</i>) (<i>N24001474</i>)	9/2021	5/2024 (N.A.) {12/2024}	359.86 (N.A.) {359.86}	220.56	78.5
		124	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (<i>MoRTH</i>) (<i>N24001441</i>)	8/2020	2/2022 (Nov-24) {11/2024}	302.88 (N.A.) {302.88}	213.32	93.11
		125	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (<i>NHIDCL</i>) (<i>N24001541</i>)	11/2021	6/2024 (N.A.) {12/2024}	283.50 (N.A.) {283.50}	203.23	70.68
		126	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (<i>NHIDCL</i>) (<i>N24001334</i>)	11/2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	193.78	7
		127	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (<i>NHIDCL</i>) (<i>N24001335</i>)	11/2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	45.46	3
		128	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (<i>NHIDCL</i>) (<i>N24001360</i>)	3/2021	12/2022 (Jun-24) {11/2024}	260.21 (N.A.) {260.21}	216.59	90

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		129	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11/2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	232.71	29
		130	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11/2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	385.00	14.5
		131	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4/2017	9/2021 (Jul-23) {3/2025}	553.51 (610.09) {553.51}	344.90	67.41
		132	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10/2020	4/2022 (Jun-24) {12/2024}	157.86 (146.92) {157.86}	146.19	97.49
		133	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3/2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	168.64	0
		134	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3/2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	241.74	0
		135	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3/2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	263.14	0
MIZORAM	RAILWAYS	136	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4/2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,562.76	93
	ROAD TRANSPORT AND HIGHWAYS	137	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12/2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	148.05	39

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROADWAYS</u>	138	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9/2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	248.74	42.3
		139	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4/2017	4/2023 (Nov-24) {1/2025}	519.09 (785.65) {785.65}	649.83	90
		140	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4/2017	7/2023 (May-24) {7/2024}	640.07 (990.88) {1,286.35}	1,217.65	98.9
		141	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4/2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.84	99.34
		142	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4/2017	4/2023 (Nov-24) {2/2025}	473.18 (688.25) {688.25}	520.26	84.88
		143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4/2017	4/2023 (Jul-24) {2/2025}	537.82 (789.05) {789.05}	747.56	91.6
		144	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4/2017	6/2023 (Oct-24) {3/2025}	518.53 (906.76) {906.76}	791.68	89.25

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		145	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4/2017	4/2024 (Nov-24) {3/2025}	404.29 (750.32) {750.32}	593.23	84.4
		146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4/2017	9/2023 (Nov-24) {3/2025}	428.11 (746.39) {746.39}	579.70	87.3
		147	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9/2020	10/2022 (Mar-24) {3/2024}	275.02 (247.25) {247.25}	231.19	99.73
		148	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3/2020	7/2022 (Jun-24) {6/2024}	206.88 (219.33) {219.33}	206.58	97.01
		149	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3/2020	7/2022 (Oct-24) {7/2025}	292.24 (331.17) {331.17}	293.90	91.64
		150	DULTE- KWALKULH - CHAMPAL PKG.1 (NHIDCL) (N24001355)	3/2021	12/2022 (Mar-24) {3/2024}	374.39 (318.92) {318.92}	292.37	100
		151	DULTE- KWALKULH - CHAMPAL PKG.2 (NHIDCL) (N24001356)	3/2021	12/2022 (Apr-24) {4/2024}	233.25 (233.25) {233.25}	178.37	100
		152	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3/2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	388.33	42.55
		153	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3/2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	281.51	41.6
		154	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9/2021	5/2023 (Jun-24) {12/2024}	492.94 (492.94) {492.94}	357.26	84.7

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
<u>NAGALAND</u>	<u>PETROLEUM</u>	155	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8/2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	0.22	9.5
	<u>RAILWAYS</u>	156	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4/2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	3,846.75	60
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	157	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6/2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	0
		158	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3/2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	109.49	59.56
		159	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3/2021	2/2024 (Jan-25) {1/2025}	226.44 (N.A.) {226.44}	115.35	81.12
		160	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3/2022	12/2024 (N.A.) {12/2024}	605.36 (N.A.) {605.36}	227.62	88.43
		161	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7/2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	65.31	58.44
		162	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2/2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	0.00	0
		163	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7/2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	43.05	27.33

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		164	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3/2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3/2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	60.49
		166	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3/2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		167	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4/2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	115.30	61.37
		168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8/2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	42.39	1.91
		169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9/2020	10/2022 (Apr-24) {9/2024}	277.44 (N.A.) {277.44}	160.86	62.33
		170	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8/2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	79.96	16.82
		171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8/2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	72.03	26.96

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		172	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9/2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		173	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3/2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		174	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3/2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
		175	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3/2016	9/2019 (Nov-22) {12/2024}	373.07 (534.41) {534.41}	382.50	99.81
		176	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3/2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	291.85	83.66
		177	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2/2017	9/2020 (Feb-23) {12/2024}	387.00 (688.12) {688.12}	387.50	99.32
		178	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3/2018	11/2022 (Aug-24) {12/2024}	500.09 (698.81) {698.81}	373.62	95.65

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		179	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA- ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3/2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	174.28	99.9
		180	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3/2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	110.43	38.55
		181	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU- MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3/2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	85.56	21.85
		182	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12/2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	41.48	22.46
		183	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12/2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	12.03
		184	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12/2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	78.00	34.64
		185	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2/2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	65.73	63.23
		186	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2/2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	19.80	30.93

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
SIKKIM	<u>CIVIL AVIATION</u>	187	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11/2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	11.30	4.5
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	188	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8/2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54
	<u>POWER</u>	189	TEESTA VI HE PROJECT (NHPC) (N18000325)	3/2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,807.48	63.56
		190	RANGIT IV HE PROJECT (NHPC) (N18000326)	3/2021	5/2024 (N.A.) {5/2025}	938.29 (N.A.) {1,871.23}	1,247.61	80.24
	<u>RAILWAYS</u>	191	SEVOK RANGPO, NEFR (NFR) (N22000102)	4/2008	12/2015 (N.A.) {12/2023}	1,339.48 (N.A.) {7,876.92}	3,290.96	39.8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	192	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3/2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	0.00	71.74
		193	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3/2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.54	95.26
		194	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11/2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		195	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8/2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	240.60	93.88

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		196	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7/2020	4/2023 (Aug-24) {3/2025}	345.38 (395.59) {395.59}	356.67	89.39
		197	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3/2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	238.46	73.11
		198	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8/2020	4/2023 (Nov-24) {3/2025}	295.97 (N.A.) {295.97}	243.94	93.43
		199	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3/2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		200	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8/2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	184.85	50
		201	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9/2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.80	46.68
		202	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9/2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		203	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1/2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {332.20}	149.38	40.99
		204	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12/2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	193.96	43.81
		205	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8/2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	200.82	77.2
		206	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10/2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	272.34	40.46
		207	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10/2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	278.65	36.42
		208	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10/2021	5/2024 (Jan-25) {1/2025}	385.15 (N.A.) {385.15}	167.49	78
TRIPURA	PETROLEUM	209	GRASS ROOT RAIL FED DEPOT AT SEKEREKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6/2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	308.81	65.6
	ROAD TRANSPORT AND HIGHWAYS	210	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2/2022	1/2025 (N.A.) {1/2025}	456.88 (N.A.) {456.88}	95.50	39.93
		211	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3/2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		212	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6/2020	1/2022 (Jul-24) {11/2024}	201.99 (287.47) {287.47}	144.07	95.5
		213	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 (NHIDCL) (N24001318)	9/2020	4/2022 (Oct-22) {10/2023}	173.17 (N.A.) {173.17}	93.35	100
		214	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11/2020	6/2022 (Oct-23) {10/2024}	159.13 (171.50) {171.50}	81.51	99.39
		215	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6/2020	1/2022 (Feb-24) {11/2024}	277.50 (302.02) {302.02}	253.50	99.2
		216	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5/2023	11/2024 (N.A.) {2/2025}	195.95 (N.A.) {195.95}	15.55	18.53
		217	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH- 8 (NHIDCL) (N24002132)	3/2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	1.45
		218	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2/2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	0.00	0.02
		219	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1/2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	0.00	0.54
		220	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1/2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	5

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		221	KHOWAI ?TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1/2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
			Total			178,090.02 (-) {239,809.38}	133,180.69	

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10/2013	9/2018 (May-23) {6/2023}	417.23 (707.73) {707.73}	698.80	100
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3/2019	3/2025 (N.A.) {3/2025}	235.72 (N.A.) {235.72}	42.62	0
	ROAD TRANSPORT AND HIGHWAYS	3	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 () (NHIDCL) (N24000744)	3/2015	1/2022 (N.A.) {2/2026}	262.97 (N.A.) {262.97}	92.73	41.55
		4	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3/2017	12/2019 (Mar-23) {9/2024}	409.85 (N.A.) {409.85}	214.23	94.59
		5	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM (NHIDCL) (N24000748)	2/2018	9/2020 (Jan-23) {8/2025}	391.00 (N.A.) {391.00}	170.37	57.55
		6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3/2018	9/2020 (Nov-22) {12/2024}	234.27 (N.A.) {234.27}	126.50	80.26
		7	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11/2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	97.46

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDHRA PRADESH		8	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11/2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100
		9	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2/2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97
	CIVIL AVIATION	10	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8/2017	2/2020 (Dec-21) {1/2024}	177.10 (N.A.) {177.10}	143.08	100
		11	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4/2020	3/2023 (N.A.) {6/2025}	611.80 (N.A.) {611.80}	351.30	57
		12	RAJAHMUNDRY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12/2022	8/2025 (N.A.) {8/2025}	347.15 (N.A.) {347.15}	45.30	28
		13	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3/2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	23.97	16
	DEPARTMENT OF HIGHER EDUCATION	14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2/2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT (CPWD EDUCATION) (N42000007)	9/2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	666.18	100
	PETROLEUM	16	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235)	7/2016	7/2020 (Feb-25) {2/2025}	20,928.00 (30,609.00) {30,609.00}	27,360.11	98.5
		17	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3/2016	6/2020 (Mar-25) {3/2025}	34,012.00 (N.A.) {34,012.00}	30,909.17	94.2
		18	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4/2018	4/2022 (Mar-25) {3/2025}	355.00 (N.A.) {355.00}	242.84	77.3
		19	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378)	9/2019	7/2020 (N.A.) {3/2025}	196.26 (196.26) {196.26}	168.60	87.2
		20	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9/2021	6/2024 (Mar-26) {3/2026}	160.00 (220.00) {220.00}	13.35	42
		21	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3/2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	117.34	4.8
		22	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9/2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.59	68.4
		23	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7/2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.04	6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	24	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9/2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	117.81	24
		25	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5/2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	0.00	0
	RAILWAYS	26	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12/2001	3/2009 (N.A.) {3/2027}	1,045.20 (N.A.) {2,500.98}	1,150.74	0
		27	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4/2011	3/2021 (N.A.) {5/2027}	2,288.70 (N.A.) {3,122.35}	1,730.90	0
		28	GUNTUR-GUNTAKAL (SCR) (N22000368)	4/2016	3/2022 (N.A.) {12/2025}	3,631.00 (N.A.) {3,887.48}	3,179.18	0
		29	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4/2015	12/2023 (N.A.) {12/2024}	3,246.26 (N.A.) {6,238.67}	5,883.89	0
		30	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4/2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,747.39	68
		31	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4/2019	3/2026 (N.A.) {2/2025}	294.67 (307.66) {307.66}	141.30	41
		32	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9/2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	39.46	12
		33	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3/2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		34	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4/2016	12/2025 (N.A.) {12/2025}	226.72 (N.A.) {226.72}	170.77	0
		35	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4/2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	160.25	50
	ROAD TRANSPORT AND HIGHWAYS	36	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3/2015	10/2015 (May-21) {5/2021}	271.45 (N.A.) {271.45}	238.23	100
		37	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 (MoRTH) (N24000422)	3/2015	9/2015 (Aug-17) {5/2018}	309.01 (N.A.) {309.01}	0.00	100
		38	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE- I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3/2018	12/2020 (Dec-22) {12/2024}	314.43 (N.A.) {348.72}	85.61	64.74
		39	REHABILITATION AND UPGRADATION OF EXISTING NH- 167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11/2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	0
		40	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3/2018	8/2018 (N.A.) {11/2024}	289.67 (290.00) {285.29}	254.19	98.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		41	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8/2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	457.55	98.2
		42	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1/2017	9/2017 (N.A.) {3/2025}	263.45 (N.A.) {263.45}	246.85	85
		43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11/2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,187.49	75.93
		44	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT (MoRTH) (N24001386)	8/2020	3/2021 (N.A.) {10/2024}	222.61 (N.A.) {222.61}	143.53	87.32
		45	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9/2021	9/2022 (Sep-24) {3/2025}	517.05 (N.A.) {655.06}	521.52	60.77
		46	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9/2021	9/2022 (Sep-24) {5/2025}	622.00 (N.A.) {817.91}	507.68	53.59
		47	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2/2019	3/2023 (Oct-24) {10/2024}	757.45 (N.A.) {757.45}	487.37	85.11

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		48	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHA/) (N24001818)	2/2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	343.60	20.09
		49	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHA/) (N24001819)	3/2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	823.10	79.03
		50	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHA/) (N24001820)	2/2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,032.32	62.47
		51	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHA/) (N24001821)	11/2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	923.26	83.52
		52	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHA/) (N24001822)	12/2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	801.02	67.1
		53	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHA/) (N24001823)	1/2022	1/2025 (Jan-23) {1/2025}	1,852.12 (N.A.) {1,787.00}	525.31	70.71
		54	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHA/) (N24001824)	3/2020	1/2024 (Dec-24) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	94.11

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		55	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2/2021	10/2024 (N.A.) {10/2024}	824.29 (N.A.) {924.00}	389.00	61.7
		56	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2/2021	3/2024 (Jul-24) {9/2024}	663.60 (N.A.) {768.00}	342.30	92.8
		57	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2/2021	3/2024 (N.A.) {3/2025}	922.50 (N.A.) {1,128.68}	361.95	70.48
		58	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12/2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	149.11	24.73
		59	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12/2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	99.64	24.5
		60	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12/2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	94.42	11.5
		61	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12/2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	131.39	10.77

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		62	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2/2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	70.84	3.5
		63	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2/2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.64	1.5
		64	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1/2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	95.51	14.72
		65	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK (NHAI) (N24001848)	2/2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	60.01	6.65
		66	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5/2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	346.39	40.97
		67	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5/2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	114.12	33.45

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		68	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3/2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	393.81	97.92
		69	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3/2022	9/2024 (N.A.) {9/2024}	401.72 (N.A.) {401.72}	162.74	64
		70	MULAKALACHERUVU TO MADANAPALLE SECTION OF NH42 FROM KM 202.050 TO KM 245.640 EXCLUDING RETAINED STRE (MoRTH) (N24001933)	12/2021	12/2024 (N.A.) {12/2024}	480.10 (N.A.) {480.10}	443.87	96.74
		71	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12/2021	5/2024 (N.A.) {7/2025}	439.82 (N.A.) {439.82}	193.63	26.73
		72	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3/2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	338.52	63
		73	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3/2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	312.17	51.78
		74	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3/2021	7/2024 (N.A.) {3/2025}	423.67 (N.A.) {423.67}	228.15	69.82
		75	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12/2021	3/2024 (N.A.) {12/2025}	277.30 (N.A.) {277.30}	182.67	93

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		76	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3/2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	252.53	85
		77	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1/2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	262.08	88.17
		78	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3/2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	120.73	58
		79	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12/2021	9/2024 (N.A.) {9/2024}	388.71 (N.A.) {388.71}	181.43	67
		80	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3/2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	299.13	80
		81	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3/2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	181.63	47
		82	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8/2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	216.41	78.8
		83	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8/2020	7/2024 (N.A.) {3/2025}	349.29 (N.A.) {349.29}	138.22	55.75

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		84	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8/2020	10/2024 (N.A.) {10/2024}	311.22 (N.A.) {311.22}	102.34	44
		85	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3/2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	259.12	46
		86	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8/2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	26.9
		87	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10/2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	271.66	52.49
		88	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7/2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	7.45
		89	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3/2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	273.30	79.23
		90	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10/2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	192.22	37.21

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		91	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3/2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	108.03	30.14
		92	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3/2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	1,009.52	43.8
		93	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10/2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	258.82	63.3
		94	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6/2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	100.99	56.72
		95	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2/2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	277.13	42.38
		96	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7/2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	14.51

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		97	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9/2022	1/2025 (N.A.) {1/2025}	166.52 (N.A.) {166.52}	43.74	0
		98	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2/2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	13.15	3.57
		99	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2/2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	51.20	2.68
		100	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2/2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	54.66	4.56
		101	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2/2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	128.18	18
		102	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2/2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	54.54	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		103	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3/2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	284.28	35
		104	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4/2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	205.10	42
		105	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6/2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	151.37	72
		106	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8/2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	24.93	9.11
		107	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8/2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	37.08	23
		108	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE- I) (MoRTH) (N24002144)	8/2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	255.03	21
		109	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11/2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	50.76	48

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		110	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH- 167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11/2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	6.00	0
		111	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE-2) (MoRTH) (N24002147)	12/2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	35.33	14.35
		112	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3/2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	8.72	0
		113	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1/2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	41.66	0
	<u>WATER RESOURCES</u>	114	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2/2009	3/2020 (N.A.) {3/2026}	10,151.04 (N.A.) {55,548.87}	21,644.53	76.75
<u>ARUNACHAL PRADESH</u>	<u>CIVIL AVIATION</u>	115	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2/2019	8/2022 (Dec-24) {12/2024}	645.63 (N.A.) {712.15}	670.15	98.58
	<u>POWER</u>	116	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9/2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {21,247.54}	22,512.54	94.01
		117	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2/2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,628.95	12.95

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD</u> <u>TRANSPORT</u> <u>AND</u> <u>HIGHWAYS</u>	118	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2/2017	11/2023 (Mar-24) {11/2024}	180.57 (244.10) {180.57}	154.17	90.01
		119	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2/2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	144.91	100
		120	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3/2017	3/2022 (Jun-25) {6/2025}	1,718.59 (1,718.59) {1,718.59}	683.02	69.07
		121	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9/2016	12/2019 (Aug-24) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		122	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1/2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		123	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8/2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	140.75	62.76

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		124	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9/2020	5/2022 (Oct-22) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		125	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3/2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		126	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3/2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	588.85	100
		127	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3/2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	480.44	100
		128	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3/2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	371.45	92.72
		129	TADADEGE - HENKAR (NHIDCL) (N24001315)	2/2021	3/2023 (Jun-24) {9/2024}	550.45 (N.A.) {550.45}	113.92	44.05
		130	LADDA - BASAI (NHIDCL) (N24001316)	2/2021	4/2023 (Jan-25) {3/2025}	445.96 (N.A.) {445.96}	117.91	49.63
		131	DOGINALA - GAU (NHIDCL) (N24001320)	12/2020	9/2022 (N.A.) {12/2024}	242.30 (N.A.) {242.30}	21.47	17.81

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		132	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2/2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	480.10	94.25
		133	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6/2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	365.27	100
		134	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6/2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	142.05	35.74
		135	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8/2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		136	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8/2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		137	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8/2020	4/2022 (Feb-24) {11/2024}	184.88 (N.A.) {184.88}	95.64	93.83
ASSAM	CIVIL AVIATION	138	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12/2016	3/2021 (N.A.) {5/2025}	1,142.00 (N.A.) {2,333.00}	1,414.84	68.99
	HEALTH AND FAMILY WELFARE	139	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5/2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	769.30	99.07

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>PETROLEUM</u>	140	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1/2018	2/2020 (Dec-23) {12/2024}	543.91 (N.A.) {670.90}	491.56	93.83
		141	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY (NRL) (N16000379)	1/2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	13,286.18	65.01
		142	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1/2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,304.39	78.74
		143	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5/2021	10/2023 (Feb-25) {2/2025}	412.00 (509.84) {509.84}	358.18	78.3
		144	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON (ONGC) (N16000433)	8/2021	2/2023 (Jun-24) {11/2024}	218.38 (N.A.) {218.38}	207.18	98.3
		145	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3/2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	158.33	52.4
		146	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6/2021	12/2024 (N.A.) {12/2024}	860.00 (N.A.) {860.00}	401.83	88.7

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		147	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12/2020	7/2024 (Mar-24) {12/2024}	430.76 (N.A.) {430.76}	245.08	73.76
		148	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6/2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	62.57	8.9
		149	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3/2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	1.38	12
		150	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3/2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	37.48	4.5
		151	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3/2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	78
		152	DCU REVAMP PROJECT (NRL) (N16000511)	8/2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	161.76	35.6
		153	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1/2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	139.67	40.3
		154	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9/2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	3.05	4.6
	RAILWAYS	155	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4/2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,494.15	92

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD</u> <u>TRANSPORT</u> <u>AND</u> <u>HIGHWAYS</u>	156	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6/2015	8/2023 (N.A.) {12/2024}	437.39 (N.A.) {437.39}	335.90	26.59
		157	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6/2015	3/2024 (N.A.) {10/2025}	463.49 (N.A.) {463.49}	368.62	1.43
		158	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1/1991	6/2019 (Jun-19) {3/2025}	520.01 (N.A.) {520.01}	304.80	90.01
		159	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12/2015	12/2018 (Jul-21) {3/2025}	289.99 (N.A.) {289.99}	232.66	87.62
		160	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1/2016	1/2016 (N.A.) {12/2024}	294.17 (N.A.) {294.17}	296.22	46.44
		161	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1/2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	146.28	12.19
		162	FOUR LANING OF BALACHERA- HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE (NHIDCL) (N24000902)	10/2017	6/2020 (Dec-23) {4/2024}	818.00 (887.68) {887.68}	874.30	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		163	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3/2020	12/2022 (N.A.) {8/2024}	220.20 (N.A.) {220.20}	216.04	97.76
		164	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8/2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	193.58	100
		165	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3/2020	3/2022 (Jan-25) {1/2025}	216.49 (241.52) {216.49}	104.36	79.48
		166	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11/2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,060.96	52.57
		167	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3/2020	6/2022 (May-25) {5/2025}	261.13 (N.A.) {261.13}	64.96	54.59
		168	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3/2020	6/2022 (Apr-25) {4/2025}	217.50 (N.A.) {217.50}	84.36	64.15
		169	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3/2021	1/2023 (N.A.) {11/2024}	288.85 (N.A.) {288.85}	243.26	98.58
		170	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3/2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	87.43	34.43
		171	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2/2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	192.50	30.65

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		172	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12/2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100
		173	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8/2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	299.82	58.2
		174	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9/2021	7/2024 (N.A.) {12/2024}	625.64 (N.A.) {625.64}	472.63	85.15
		175	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3/2022	7/2024 (N.A.) {10/2024}	215.27 (N.A.) {215.27}	150.92	100
		176	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 (NHIDCL) (N24001452)	4/2022	7/2024 (N.A.) {8/2024}	170.95 (N.A.) {170.95}	125.71	100
		177	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11/2021	7/2024 (N.A.) {12/2024}	204.10 (N.A.) {204.10}	127.65	83.53
		178	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 (NHIDCL) (N24001544)	3/2022	1/2025 (N.A.) {1/2025}	909.02 (N.A.) {909.02}	408.84	77.21
		179	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8/2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	178.56	99.04
		180	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3/2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	480.84	52.48

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		181	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3/2022	6/2024 (N.A.) {12/2024}	457.72 (N.A.) {457.72}	313.97	89.68
		182	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3/2022	2/2025 (N.A.) {12/2025}	613.89 (N.A.) {613.89}	17.15	9.23
		183	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1/2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	153.42	43.85
		184	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3/2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	4.07	10.6
		185	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001969)	3/2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	301.41	38.71
		186	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3/2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	287.76	39.05
		187	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3/2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	347.95	36.05

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		188	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3/2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	187.98	53.3
		189	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3/2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	178.24	52.85
		190	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3/2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	359.25	25.65
		191	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3/2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	212.32	10.38
		192	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3/2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	270.76	14.23
		193	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1/2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	177.39	50.11
		194	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1/2023	12/2025 (N.A.) {12/2025}	356.65 (N.A.) {356.65}	115.18	5.55
		195	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3/2023	12/2025 (N.A.) {12/2025}	643.42 (N.A.) {643.42}	67.22	8.45

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		196	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2/2020	3/2022 (N.A.) {10/2024}	592.06 (N.A.) {592.06}	304.02	100
		197	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2/2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	320.55	12.96
		198	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3/2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	744.22	32.05
		199	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2/2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	177.78	19.59
		200	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12/2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	284.84	31.35
		201	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3/2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	91.62	0
		202	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3/2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	73.01	0
BIHAR	CIVIL AVIATION	203	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5/2018	10/2022 (Dec-24) {12/2024}	1,216.90 (N.A.) {1,216.90}	823.96	74.2

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		204	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7/2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	0.00	0
		205	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2/2016	6/2017 (N.A.) {1/2024}	496.18 (496.00) {460.00}	436.15	100
		206	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9/2018	9/2020 (N.A.) {9/2020}	375.00 (N.A.) {375.00}	327.75	98.9
	PETROLEUM	207	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1/2020	4/2023 (Dec-24) {12/2025}	14,810.00 (N.A.) {14,810.00}	9,847.73	80.3
		208	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6/2019	12/2029 (Mar-30) {3/2030}	163.00 (N.A.) {163.00}	84.82	23.5
		209	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1/2022	4/2025 (N.A.) {4/2025}	389.00 (N.A.) {389.00}	22.13	20.1
		210	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12/2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	197.02	12.6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		211	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12/2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	231.17	13.5
	POWER	212	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2/2005	10/2011 (Jul-23) {11/2024}	8,692.97 (21,312.11) {21,312.11}	22,311.28	90
		213	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3/2019	1/2024 (N.A.) {6/2025}	10,439.09 (N.A.) {10,439.09}	10,407.27	83.5
	RAILWAYS	214	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4/1997	(N.A.) {12/2026}	162.87 (614.45) {614.45}	457.16	50
		215	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4/2003	(N.A.) {12/2024}	528.65 (2,087.36) {2,087.36}	2,045.11	48
		216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9/2006	3/2019 (N.A.) {6/2025}	532.87 (2,132.03) {4,415.08}	2,913.58	81
		217	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4/1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	579.54	78
		218	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4/2008	(N.A.) {1/2025}	1,605.17 (1,605.17) {1,605.17}	1,390.28	26
		219	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC (ECR) (N22000181)	4/2009	3/2020 (N.A.) {3/2026}	548.00 (548.00) {783.83}	544.31	78
		220	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5/2015	(N.A.) {3/2025}	380.00 (519.33) {519.33}	550.20	62
		221	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12/2015	3/2020 (N.A.) {11/2024}	1,200.20 (1,200.20) {1,771.07}	1,758.88	96

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		222	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12/2015	3/2020 (N.A.) {5/2025}	1,491.47 (1,491.47) {1,600.00}	1,647.46	77
		223	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4/2016	3/2021 (N.A.) {12/2024}	744.04 (1,215.54) {1,215.54}	1,426.74	85
		224	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM (ECR) (N22000473)	4/2016	3/2021 (N.A.) {12/2024}	731.64 (1,185.73) {1,300.00}	1,403.88	80
		225	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, (ECR) (N22000476)	4/1991	(N.A.) {12/2024}	329.39 (803.09) {2,722.16}	2,589.76	90
		226	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6/2019	6/2025 (N.A.) {9/2024}	983.62 (253.23) {415.00}	386.22	80
		227	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7/2022	7/2027 (N.A.) {6/2025}	486.00 (N.A.) {486.00}	102.42	30
		228	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2/2019	6/2028 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	2.53	0
		229	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10/2022	10/2027 (N.A.) {6/2025}	234.00 (223.69) {223.69}	15.22	0
		230	KATIHAR-KUMEDPUR & KATIHAR- MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8/2022	8/2027 (N.A.) {8/2027}	745.00 (N.A.) {745.00}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	ROAD TRANSPORT AND HIGHWAYS	231	PATNA-MUZZAFFARPUR (NHAI) (N24000165)	8/2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.15
		232	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1/2011	7/2013 (Dec-24) {12/2024}	575.00 (N.A.) {575.00}	552.79	86.41
		233	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1/2014	10/2019 (Dec-24) {12/2024}	675.00 (780.77) {780.77}	702.20	88
		234	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12/2015	4/2019 (Mar-25) {3/2025}	1,041.10 (567.00) {639.58}	553.73	97.27
		235	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12/2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	94.25
		236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2/2016	11/2018 (Sep-24) {9/2024}	319.68 (503.28) {503.28}	430.14	99
		237	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2/2016	5/2016 (Sep-24) {9/2024}	178.85 (225.06) {278.54}	232.61	98
		238	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2/2016	5/2016 (Sep-24) {9/2024}	553.30 (706.39) {706.39}	607.49	98

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		239	FOUR LANING OF GAYA-HISUA- RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH- 82 IN BIHAR (MoRTH) (N24000579)	1/2014	10/2016 (Dec-24) {12/2024}	1,408.85 (2,138.16) {2,138.16}	1,703.04	96
		240	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT- SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3/2017	3/2020 (Mar-25) {3/2025}	672.89 (736.01) {830.31}	616.15	76.19
		241	SIX LANNING OF AUNTA- SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8/2017	2/2022 (Oct-24) {3/2025}	950.64 (1,161.00) {1,168.33}	1,010.99	87.08
		242	CONSTRUCTION OF NEW LINK (NH- 133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12/2017	10/2024 (Apr-25) {6/2025}	2,598.00 (N.A.) {1,962.50}	1,249.32	68.57
		243	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1/2018	12/2021 (Dec-24) {3/2025}	573.70 (644.50) {726.99}	468.93	75.75
		244	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3/2018	11/2021 (Dec-24) {12/2024}	496.20 (470.18) {537.17}	379.06	95.46

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		245	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9/2018	6/2024 (Feb-26) {2/2026}	1,478.40 (N.A.) {1,478.40}	806.35	58
		246	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2/2019	9/2024 (N.A.) {2/2026}	2,926.42 (N.A.) {2,926.42}	970.95	47
		247	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10/2013	12/2020 (Dec-24) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.3
		248	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10/2013	11/2020 (Dec-24) {12/2024}	446.97 (598.48) {740.50}	638.80	96.3
		249	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10/2013	11/2020 (Dec-24) {12/2024}	464.09 (605.53) {765.12}	698.25	97.3
		250	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10/2019	8/2023 (Dec-24) {12/2024}	1,101.99 (N.A.) {1,101.99}	786.48	67.18
		251	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2/2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	146.66	11.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		252	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8/2022	8/2024 (N.A.) {8/2024}	1,198.02 (N.A.) {1,198.02}	0.00	0
		253	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH- 3 (NHAI) (N24001699)	3/2022	12/2024 (N.A.) {3/2025}	312.58 (N.A.) {312.58}	146.52	60.04
		254	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12/2021	3/2024 (Dec-24) {12/2024}	552.55 (553.00) {553.00}	414.79	54.95
		255	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4/2022	4/2024 (N.A.) {4/2024}	1,769.50 (N.A.) {1,769.50}	0.00	0
		256	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT- GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12/2021	9/2024 (N.A.) {9/2024}	184.90 (185.00) {185.00}	163.01	90.67
		257	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2/2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		258	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3/2021	3/2024 (Dec-24) {12/2024}	1,020.84 (N.A.) {1,020.84}	84.78	0
		259	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3/2022	3/2024 (Dec-24) {12/2024}	1,485.66 (N.A.) {1,485.66}	0.00	0
		260	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. (NHAI) (N24001706)	3/2021	1/2024 (Dec-24) {12/2024}	1,097.18 (1,097.00) {1,097.00}	518.04	99.79
		261	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH- 327E (NHAI) (N24001707)	3/2021	1/2024 (Dec-24) {12/2024}	1,143.46 (1,143.46) {1,143.46}	551.35	98.69
		262	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9/2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	96.57
		263	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9/2020	4/2023 (Dec-24) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		264	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S (NHAI) (N24001710)	9/2020	3/2023 (Dec-24) {12/2024}	2,334.68 (2,494.20) {2,494.20}	916.00	99.2

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		265	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9/2020	3/2023 (Dec-24) {12/2024}	939.43 (N.A.) {939.43}	370.62	100
		266	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8/2020	7/2023 (Dec-24) {12/2024}	690.00 (N.A.) {690.00}	770.73	98.7
		267	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12/2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100
		268	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2/2022	11/2024 (Mar-25) {3/2025}	624.43 (N.A.) {624.43}	188.90	68
		269	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3/2021	1/2025 (Mar-25) {3/2025}	477.54 (N.A.) {477.54}	215.22	57
		270	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH- 80 (MoRTH) (N24001876)	3/2021	3/2024 (Jun-25) {6/2025}	566.15 (N.A.) {566.15}	159.74	35
		271	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7/2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	263.84	29

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		272	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH- 319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2/2022	12/2024 (Mar-25) {3/2025}	427.29 (N.A.) {427.29}	166.86	56
		273	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3/2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	31.83	27
		274	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3/2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	7.62	0.69
		275	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12/2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	100.28	68.58
		276	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12/2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	32.97	16.01
		277	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2/2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	8.17
		278	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2/2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		279	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N240002133)	3/2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	54.73	46
	URBAN DEVELOPMENT	280	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2/2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	2,710.61	39.09
	WATER RESOURCES	281	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3/2018	7/2021 (Dec-19) {12/2024}	230.06 (N.A.) {230.06}	237.44	96
		282	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10/2017	9/2020 (Nov-20) {10/2024}	254.13 (413.29) {413.29}	120.95	83
		283	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028)	11/2018	12/2020 (N.A.) {2/2024}	236.15 (N.A.) {236.15}	142.08	100
		284	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3/2018	8/2021 (Mar-18) {12/2024}	305.19 (N.A.) {305.19}	311.72	91
		285	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3/2018	10/2021 (Mar-18) {6/2024}	294.02 (350.79) {522.85}	413.94	100
		286	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037)	12/2014	3/2020 (N.A.) {6/2022}	225.77 (N.A.) {398.90}	363.79	100
		287	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4/2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	489.65	100
		288	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040)	5/2017	4/2021 (May-17) {2/2023}	356.37 (364.00) {356.37}	312.24	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		289	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043)	5/2017	11/2020 (May-17) {5/2022}	191.62 (N.A.) {191.62}	123.27	100
		290	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3/2017	5/2021 (Mar-17) {2/2023}	277.42 (253.98) {277.42}	355.31	100
		291	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8/2017	6/2022 (N.A.) {9/2024}	578.89 (453.83) {578.89}	155.42	46
		292	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8/2017	6/2022 (N.A.) {9/2024}	824.00 (734.09) {824.00}	377.18	48
CHHATTISGA RH	COAL	293	GEVRA EXPANSION OCP (SECL) (35- 70) MTY (SECL) (060100093)	6/2010	3/2023 (N.A.) {3/2025}	11,816.40 (N.A.) {11,816.40}	6,185.85	77
		294	KUSMUNDA EXPN.OCP(SECL)(15- 50)MTY (SECL) (N06000008)	8/2013	3/2023 (N.A.) {3/2025}	7,612.33 (N.A.) {7,612.33}	4,610.30	81
		295	PELMA OCP(15.00MTY) (SECL) (N06000045)	11/2014	3/2023 (N.A.) {3/2030}	1,624.59 (N.A.) {1,624.59}	13.65	17
		296	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12/2013	3/2022 (Mar-25) {3/2025}	610.63 (N.A.) {610.63}	568.37	85
		297	AMERA OC RCE (SECL) (N06000123)	2/2015	3/2018 (Mar-26) {3/2026}	335.97 (N.A.) {335.97}	173.32	42
		298	AMGAON OPENCAST PROJECT RCE (SECL) (N06000135)	7/2015	3/2020 (Mar-26) {3/2026}	316.10 (N.A.) {316.10}	187.50	65
		299	MAHAMAYA OPENCAST PROJECT (SECL) (N06000164)	5/2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	178.92	38

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		300	JHIRIA WEST OPENCAST PROJECT (SECL) (N06000166)	11/2018	3/2026 (N.A.) {3/2026}	366.94 (N.A.) {366.94}	32.49	36
		301	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8/2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	852.12	39
		302	JAMPALI OCP RCE (SECL) (N06000198)	5/2020	3/2024 (Mar-25) {3/2025}	278.64 (N.A.) {278.64}	207.81	73
		303	PORDA CHIMTAPANI OCP (10 MTY) (SECL) (N06000199)	12/2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	42.74	10
		304	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12/2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,688.71	31
		305	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7/2016	3/2020 (Mar-05) {3/2025}	459.49 (N.A.) {459.49}	258.51	92
		306	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1/2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	0.00	2
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	307	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3/2020	7/2022 (N.A.) {7/2022}	808.62 (N.A.) {808.62}	640.70	99.2
	<u>PETROLEUM</u>	308	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3/2021	3/2024 (Mar-25) {3/2025}	456.00 (N.A.) {456.00}	350.05	85.2
	<u>POWER</u>	309	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2/2023	11/2023 (N.A.) {1/2025}	385.84 (N.A.) {385.84}	171.71	62

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		310	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3/2023	9/2024 (N.A.) {12/2024}	271.69 (N.A.) {271.69}	277.04	57
		311	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME- XXVIII AND XXIX (PGCIL) (N18000355)	3/2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	117.79	84
		312	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (BHEL) (N18000381)	8/2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	709.38	0
	RAILWAYS	313	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12/2012	3/2020 (N.A.) {3/2024}	1,160.00 (N.A.) {1,440.00}	1,449.46	88.5
		314	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4/2015	3/2021 (Dec-23) {8/2025}	1,973.00 (2,135.34) {2,135.34}	2,069.50	80
		315	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR- PHASE I (IRCON) (N22000489)	4/2013	9/2018 (N.A.) {12/2024}	3,055.00 (3,438.39) {3,438.39}	3,041.21	93
		316	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7/2011	10/2024 (N.A.) {2/2025}	1,171.30 (N.A.) {1,171.30}	497.45	45
		317	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9/2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.10	0
		318	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12/2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	0.21	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		319	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9/2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	1.17	0
		320	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9/2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	0.22	0
		321	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9/2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	3.17	2
		322	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9/2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	0
		323	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6/2022	6/2030 (N.A.) {6/2030}	1,376.20 (N.A.) {775.82}	59.40	5
		324	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA- JAGDALPUR (235 KM)} (RVNL) (N22000602)	3/2008	6/2025 (N.A.) {6/2025}	631.78 (N.A.) {1,627.56}	1,349.09	0
		325	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10/2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	0
	ROAD TRANSPORT AND HIGHWAYS	326	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1/2016	8/2016 (N.A.) {12/2024}	497.14 (572.66) {572.66}	367.31	57.8
		327	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1/2016	10/2016 (N.A.) {12/2024}	624.98 (N.A.) {731.50}	607.59	99

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		328	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3/2016	7/2016 (N.A.) {3/2025}	452.94 (N.A.) {435.61}	297.82	63.86
		329	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3/2018	1/2019 (N.A.) {12/2024}	349.03 (N.A.) {349.03}	316.52	97.9
		330	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A (MoRTH) (N24001228)	11/2017	5/2019 (N.A.) {12/2024}	188.80 (N.A.) {188.80}	136.81	97
		331	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12/2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	504.46	57.6
		332	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11/2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	801.30	80.21
		333	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH-130A (NHAI) (N24001611)	4/2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	388.38	71.68
		334	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3/2020	5/2024 (N.A.) {12/2024}	278.97 (N.A.) {278.97}	170.04	74.1

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		335	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001919)	12/2020	9/2023 (Nov-24) {12/2024}	193.16 (N.A.) {193.16}	80.60	69.18
		336	UPGRADATION OF NH 130A MUNGELI TO PONDRI FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3/2021	9/2024 (N.A.) {1/2025}	218.57 (N.A.) {218.57}	96.43	77.12
		337	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3/2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	135.17	13.97
		338	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6/2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	318.96	11.76
		339	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6/2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	585.16	22.1
	STEEL	340	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11/2015	6/2023 (Jul-24) {12/2025}	2,907.00 (N.A.) {2,907.00}	2,226.02	60
		341	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3/2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,252.10	64.42
		342	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7/2021	11/2024 (N.A.) {12/2025}	282.44 (N.A.) {282.44}	130.20	48.6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		343	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10/2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	38.21	2.8
		344	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11/2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	247.82	46.9
	URBAN DEVELOPMENT	345	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV- 112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5/2019	9/2020 (Oct-24) {10/2024}	299.97 (299.97) {299.97}	245.83	82
DELHI	CIVIL AVIATION	346	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11/2016	4/2020 (Apr-24) {4/2024}	303.80 (374.98) {351.21}	328.13	100
	DPIIT	347	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11/2017	12/2019 (N.A.) {11/2024}	4,773.00 (N.A.) {5,401.00}	4,823.97	97.4
	FINANCE	348	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7/2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85
	HOME AFFAIRS	349	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10/2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,916.06	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		350	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6/2019	7/2022 (N.A.) {5/2025}	277.35 (N.A.) {277.35}	92.78	55
	<u>RAILWAYS</u>	351	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4/2012	(N.A.) {9/2023}	295.68 (N.A.) {419.00}	133.78	30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	352	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6/2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	99
		353	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5/2020	7/2024 (N.A.) {9/2025}	1,467.44 (N.A.) {1,942.89}	913.93	78.85
		354	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7/2020	10/2023 (N.A.) {12/2024}	2,171.80 (N.A.) {2,171.80}	958.13	99.25
		355	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778)	7/2020	10/2023 (N.A.) {12/2024}	801.46 (N.A.) {801.46}	382.03	99.33
		356	DWARKA EXPRESSWAY FROM KM - 0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3/2018	9/2022 (N.A.) {3/2025}	2,507.00 (N.A.) {3,030.73}	1,155.70	85.78

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		357	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1/2018	10/2021 (N.A.) {11/2024}	2,067.67 (N.A.) {2,160.00}	1,496.49	97.05
		358	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7/2020	10/2023 (N.A.) {12/2024}	1,894.96 (N.A.) {1,894.96}	741.88	85
	TELECOMMUNICATIONS	359	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10/2014	3/2018 (N.A.) {3/2025}	248.20 (N.A.) {248.20}	224.32	98
	URBAN DEVELOPMENT	360	DELHI MRTS PHASE-III (DMRC) (N28000056)	9/2011	3/2016 (Aug-21) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,535.62	99.99
		361	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7/2016	(N.A.) {10/2024}	2,694.00 (N.A.) {2,694.00}	2,402.68	98
		362	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10/2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2
		363	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10/2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	576.45	48
		364	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7/2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	13,503.45	56

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		365	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND (DMRC) (N28000136)	5/2017	12/2020 (Nov-22) {11/2022}	565.00 (739.49) {565.00}	522.33	100
		366	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1/2022	11/2024 (May-25) {5/2025}	646.52 (N.A.) {646.52}	333.90	65
		367	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10/2016	3/2024 (N.A.) {3/2025}	1,536.72 (N.A.) {1,536.72}	334.65	77
	WATER RESOURCES	368	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3/2017	12/2022 (N.A.) {12/2024}	665.78 (N.A.) {665.78}	782.51	96
		369	REHABILITATION AND UP- GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015)	5/2016	12/2021 (N.A.) {2/2024}	211.79 (223.70) {211.79}	208.71	100
		370	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016)	5/2016	2/2022 (Sep-23) {7/2023}	239.11 (314.71) {239.11}	268.13	100
		371	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (DJB) (N30000017)	12/2018	1/2021 (N.A.) {3/2022}	515.07 (N.A.) {515.07}	388.08	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		372	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO (<i>DJB</i>) (<i>N30000018</i>)	5/2017	5/2020 (N.A.) {5/2020}	344.81 (N.A.) {344.81}	0.00	0
GOA	CIVIL AVIATION	373	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (<i>AAI</i>) (<i>N04000095</i>)	11/2017	9/2021 (N.A.) {3/2025}	255.69 (N.A.) {255.69}	78.95	60
	DEPARTMENT OF HIGHER EDUCATION	374	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (<i>CPWD EDUCATION</i>) (<i>N42000002</i>)	5/2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	364.00	99
	PETROLEUM	375	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (<i>ONGC</i>) (<i>N16000502</i>)	3/2023	6/2024 (N.A.) {1/2025}	325.53 (N.A.) {325.53}	290.46	99.2
	ROAD TRANSPORT AND HIGHWAYS	376	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 508.000 TO KM. 513.150 INCLUDING APPROACHES ON N (<i>MoRTH</i>) (<i>N24002181</i>)	4/2023	4/2026 (N.A.) {4/2026}	641.46 (N.A.) {641.46}	0.00	0
GUJARAT	CIVIL AVIATION	377	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (<i>AAI</i>) (<i>N04000088</i>)	1/2018	8/2022 (May-24) {10/2024}	1,405.00 (N.A.) {1,405.00}	1,292.60	100
		378	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (<i>AAI</i>) (<i>N04000093</i>)	8/2018	2/2021 (N.A.) {12/2024}	353.25 (N.A.) {353.25}	341.37	98.25

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	379	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6/2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	242.65	33
		380	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2/2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,109.08	96.8
		381	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11/2019	5/2023 (Mar-24) {12/2024}	5,251.00 (5,894.00) {5,894.00}	4,584.10	98.6
		382	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9/2020	8/2024 (Dec-25) {12/2025}	18,936.00 (N.A.) {18,936.00}	9,321.56	76.1
		383	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10/2020	8/2023 (Nov-24) {11/2024}	1,614.00 (N.A.) {1,614.00}	1,036.13	91.95
		384	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4/2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	271.12	54.8
		385	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8/2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	410.13	40.5
		386	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1/2022	11/2024 (N.A.) {11/2024}	621.40 (N.A.) {621.40}	101.08	20.2
		387	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1/2022	9/2024 (N.A.) {8/2025}	328.00 (N.A.) {328.00}	29.15	22.9

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		388	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5/2022	2/2025 (N.A.) {2/2025}	249.43 (N.A.) {249.43}	109.19	80.7
		389	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8/2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	734.50	54
		390	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7/2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	125.77	77.8
		391	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11/2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	49.56	23.1
	POWER	392	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1/2021	7/2022 (N.A.) {3/2025}	842.27 (N.A.) {842.27}	668.86	30
		393	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5/2021	9/2022 (N.A.) {1/2025}	674.92 (N.A.) {674.92}	540.90	91
		394	Bagodara Solar Power Project (SJVN) (N18000297)	5/2021	10/2022 (N.A.) {3/2025}	339.35 (N.A.) {339.35}	335.65	51
		395	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11/2021	5/2023 (N.A.) {12/2024}	937.80 (N.A.) {937.80}	773.34	98
		396	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7/2022	3/2025 (N.A.) {1/2026}	1,316.02 (N.A.) {1,316.02}	267.77	23
		397	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9/2022	9/2024 (N.A.) {1/2026}	7,179.54 (N.A.) {7,179.54}	2,137.13	61

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		398	BHUIJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11/2022	3/2024 (N.A.) {3/2025}	1,442.60 (N.A.) {1,442.60}	711.35	2
		399	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3/2023	12/2024 (N.A.) {2/2025}	922.30 (N.A.) {922.30}	327.67	43
		400	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3/2023	3/2025 (N.A.) {3/2025}	815.12 (N.A.) {815.12}	7.99	35
		401	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3/2023	12/2024 (N.A.) {2/2025}	966.79 (N.A.) {966.79}	159.22	48
		402	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3/2023	3/2025 (N.A.) {3/2025}	1,167.55 (N.A.) {1,167.55}	521.14	26
		403	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3/2023	3/2025 (N.A.) {3/2025}	2,820.99 (N.A.) {2,820.99}	1,858.46	22
		404	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6/2023	12/2024 (N.A.) {1/2026}	6,283.81 (N.A.) {6,283.81}	967.79	15
		405	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5/2023	1/2025 (N.A.) {5/2025}	1,095.01 (N.A.) {1,095.01}	297.33	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		406	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7/2023	7/2025 (N.A.) {7/2025}	334.00 (N.A.) {334.00}	0.00	0
		407	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12/2023	12/2025 (N.A.) {12/2025}	3,752.00 (N.A.) {3,752.00}	241.02	1.5
		408	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5/2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	0.00	0
	RAILWAYS	409	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4/2011	(Oct-25) {10/2025}	844.10 (844.10) {844.10}	574.54	41
		410	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4/2017	3/2020 (Dec-24) {12/2024}	692.25 (692.26) {692.26}	576.46	93
		411	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4/2018	3/2024 (Oct-24) {10/2024}	537.31 (537.31) {537.31}	679.54	97
		412	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2/2023	3/2027 (Feb-27) {2/2027}	961.67 (961.67) {961.67}	39.50	2
		413	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2/2023	12/2025 (Oct-25) {10/2025}	152.44 (152.44) {152.44}	32.85	6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		414	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10/2021	10/2026 (Dec-25) {12/2025}	1,011.72 (1,080.58) {1,080.58}	1,013.64	62
		415	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6/2022	2/2030 (Feb-25) {2/2025}	354.99 (482.42) {482.42}	554.24	56
		416	PETLAD-BHADRAN (22.5 KM) (WR) (N22000538)	5/2022	5/2030 (N.A.) {12/2025}	202.50 (307.12) {307.12}	47.30	7
		417	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5/2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	58.96	7
		418	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2/2023	3/2030 (N.A.) {1/2027}	401.48 (670.17) {670.17}	72.05	9
		419	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5/2022	3/2030 (Apr-26) {4/2026}	216.72 (349.93) {349.93}	66.38	25
		420	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5/2022	3/2030 (Feb-25) {2/2025}	309.81 (415.38) {415.38}	467.95	75
		421	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5/2022	5/2030 (N.A.) {5/2030}	296.54 (N.A.) {296.54}	0.00	0
		422	NEW BG LINE BETWEEN NALIYA- JAKHAU PORT (WR) (N22000550)	2/2023	1/2028 (Sep-26) {9/2026}	410.46 (410.46) {410.46}	27.80	2
		423	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR- SANAND & BOTAD-AHMEDABAD (16.51 KM) (PB#29/NR/202 (WR) (N22000551)	10/2022	10/2027 (N.A.) {10/2027}	437.21 (N.A.) {437.21}	0.00	0
		424	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7/2022	7/2030 (N.A.) {12/2026}	1,695.82 (N.A.) {2,798.16}	798.17	10
		425	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6/2022	12/2026 (N.A.) {12/2026}	492.83 (N.A.) {492.83}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD</u> <u>TRANSPORT</u> <u>AND</u> <u>HIGHWAYS</u>	426	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD- HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9/2012	3/2027 (Mar-26) {3/2026}	261.68 (261.68) {261.68}	479.71	42
		427	FOUR LANING OF BHAVNAGAR- TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5/2016	8/2019 (N.A.) {2/2024}	998.18 (N.A.) {998.18}	802.04	100
		428	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE- IV) IN THE ST (NHAI) (N24000569)	5/2016	9/2019 (May-24) {11/2024}	723.64 (N.A.) {723.64}	559.55	96
		429	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5/2016	8/2019 (N.A.) {11/2024}	763.08 (N.A.) {763.08}	512.85	95.91
		430	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7/2016	7/2020 (N.A.) {10/2024}	829.97 (N.A.) {829.97}	465.75	92.23
		431	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP- V(PKG VI)REG. (NHAI) (N24000649)	1/2017	12/2020 (Jun-25) {6/2025}	1,251.11 (1,527.75) {1,527.75}	684.13	83.84
		432	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3/2018	10/2021 (Sep-24) {9/2024}	1,161.39 (1,404.00) {1,404.00}	418.51	39.17

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		433	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10/2018	11/2020 (Sep-24) {9/2024}	400.76 (394.44) {394.44}	287.39	87
		434	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6/2020	4/2023 (Sep-24) {9/2024}	166.21 (N.A.) {166.21}	98.65	93
		435	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5/2020	3/2024 (Nov-24) {11/2024}	690.30 (929.95) {929.95}	696.31	79.7
		436	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5/2020	1/2024 (Nov-24) {11/2024}	882.00 (N.A.) {882.00}	746.00	72.32
		437	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5/2020	7/2023 (Nov-24) {11/2024}	691.52 (903.85) {903.85}	728.37	86.5
		438	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5/2020	12/2023 (Nov-24) {11/2024}	894.00 (1,210.06) {1,210.06}	885.68	82.41

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		439	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9/2020	2/2024 (N.A.) {1/2025}	1,542.02 (N.A.) {1,542.02}	893.71	62.3
		440	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9/2020	2/2024 (Aug-24) {8/2024}	1,185.69 (N.A.) {1,185.69}	896.09	85.6
		441	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11/2019	9/2023 (N.A.) {10/2024}	1,669.56 (N.A.) {1,669.56}	967.79	89.46
		442	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9/2020	11/2023 (N.A.) {9/2024}	1,198.55 (N.A.) {1,198.55}	846.73	90.22
		443	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11/2019	5/2024 (N.A.) {11/2024}	1,604.06 (N.A.) {1,604.06}	1,220.67	95.73
		444	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3/2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	501.52	62.01
		445	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3/2021	3/2024 (N.A.) {3/2025}	1,259.00 (N.A.) {1,910.00}	137.93	15.02
		446	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7/2020	12/2023 (N.A.) {6/2024}	2,271.86 (N.A.) {3,916.00}	518.25	74.55

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		447	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7/2020	8/2023 (N.A.) {6/2024}	1,710.30 (N.A.) {1,927.00}	362.81	68.11
		448	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2/2020	8/2023 (Dec-24) {11/2024}	752.30 (N.A.) {766.20}	451.11	98.14
		449	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791)	2/2020	6/2023 (Mar-24) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
		450	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3/2021	9/2022 (N.A.) {11/2024}	536.03 (N.A.) {536.03}	451.87	98.87
		451	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3/2021	9/2022 (N.A.) {11/2024}	485.75 (N.A.) {485.75}	383.55	97.71
		452	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2/2020	3/2023 (Dec-24) {11/2024}	778.15 (N.A.) {785.67}	547.22	99.61
		453	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE) (NHAI) (N24001827)	3/2022	3/2023 (N.A.) {7/2024}	162.73 (N.A.) {162.73}	131.79	95.3

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		454	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9/2022	12/2023 (Dec-25) {12/2025}	237.28 (N.A.) {237.28}	0.59	0
		455	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12/2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	370.68	53.75
		456	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9/2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	169.45	14
		457	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10/2022	2/2024 (Feb-26) {2/2026}	246.60 (291.00) {291.00}	29.33	15
		458	UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12/2022	2/2024 (Aug-25) {8/2025}	173.06 (N.A.) {219.00}	0.15	0
		459	WORK OF DEVELOPMENT AND CONSTRUCTION OF ELEVATED CORRIDOR FROM KM 38/660 TO KM 42/690 (ISCON JUNCTION) (MoRTH) (N24002182)	3/2023	3/2026 (N.A.) {3/2026}	530.20 (N.A.) {530.20}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>URBAN DEVELOPMENT</u>	460	WIDENING 2 LANE TO 4-LANE FROM KM 92/320 TO KM 115/320 (VAV CHOKDI-SATLASANA TO TO VRUNDAVAN CHOKDI, (MoRTH) (N24002183)	3/2022	3/2026 (N.A.) {3/2026}	151.13 (N.A.) {171.00}	0.00	0
		461	AHMEDABAD METRO RAIL PROJECT PHASE 1 (MEGA) (N28000122)	11/2014	12/2018 (N.A.) {3/2025}	10,773.00 (N.A.) {12,924.55}	12,364.30	99.8
		462	AHMEDABAD METRO RAIL PROJECT PHASE II (MEGA) (N28000137)	3/2019	3/2024 (N.A.) {6/2025}	5,384.17 (N.A.) {5,384.17}	3,510.54	75.05
		463	SURAT METRO RAIL PROJECT (MEGA) (N28000138)	3/2019	3/2024 (N.A.) {10/2025}	12,020.32 (N.A.) {12,020.32}	5,701.41	55.3
HARYANA	<u>HEALTH AND FAMILY WELFARE</u>	464	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3/2019	3/2023 (Mar-26) {3/2026}	1,294.34 (1,294.34) {1,294.34}	118.14	4.01
	<u>HOME AFFAIRS</u>	465	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1/2020	10/2023 (Jan-25) {1/2025}	166.98 (167.00) {166.98}	108.99	85
	<u>PETROLEUM</u>	466	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6/2019	12/2022 (Jul-25) {7/2025}	2,281.94 (3,219.94) {3,219.94}	1,600.47	61.7
		467	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2/2021	9/2024 (Dec-25) {12/2025}	34,627.00 (38,231.00) {38,231.00}	14,597.25	74.6
		468	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3/2022	3/2025 (N.A.) {12/2025}	1,459.00 (2,102.79) {2,102.79}	542.29	44
	<u>RAILWAYS</u>	469	DOUBLING BETWEEN BHIWANI- DOBH BAHALI (NWR) (N22000604)	2/2023	2/2028 (N.A.) {2/2026}	471.06 (N.A.) {471.06}	45.43	27

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD</u> <u>TRANSPORT</u> <u>AND</u> <u>HIGHWAYS</u>	470	DOUBLING BETWEEN REWARI-KATHUWAS (27.73 KM) (NWR) (N22000606)	2/2023	6/2027 (N.A.) {6/2025}	352.41 (N.A.) {352.41}	39.27	15
		471	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P (NHAI) (N24000835)	3/2018	12/2020 (Dec-24) {3/2024}	1,484.30 (N.A.) {2,182.41}	1,237.02	100
		472	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11/2021	11/2023 (Jan-24) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100
		473	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11/2020	12/2023 (N.A.) {12/2024}	1,690.23 (N.A.) {2,010.17}	1,311.87	96.15
		474	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12/2020	1/2024 (Apr-24) {12/2024}	1,334.04 (N.A.) {1,334.00}	974.53	97.31
		475	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7/2020	7/2022 (May-24) {12/2024}	899.00 (1,882.46) {1,882.46}	1,123.98	92.11
		476	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7/2020	7/2022 (N.A.) {12/2024}	817.00 (1,605.00) {1,605.00}	1,025.56	98.9

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		477	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12/2020	12/2023 (Feb-24) {11/2024}	1,430.88 (N.A.) {1,430.88}	1,035.67	96.8
		478	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1/2021	12/2023 (Mar-24) {12/2024}	1,306.95 (N.A.) {1,306.95}	942.53	98.44
		479	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3/2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	187.00	47
		480	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3/2020	3/2023 (Nov-24) {12/2024}	510.97 (N.A.) {510.97}	529.00	88.5
		481	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH- 352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12/2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,085.28	59.84
		482	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2/2020	1/2023 (Dec-24) {12/2024}	808.31 (N.A.) {958.00}	817.03	99.64
		483	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) (NHAI) (N24001780)	1/2018	11/2020 (Dec-24) {3/2024}	2,228.00 (N.A.) {2,228.00}	1,411.27	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		484	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11/2018	9/2021 (N.A.) {11/2024}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95
		485	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1/2023	12/2025 (N.A.) {12/2025}	609.32 (609.00) {609.00}	96.06	22.1
		486	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11/2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	590.77	42
		487	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2/2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	354.90	35
		488	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS! (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4/2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	409.06	36.1
		489	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4/2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	606.10	35.22

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		490	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11/2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	195.39	49.1
		491	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3/2022	6/2025 (N.A.) {6/2025}	927.22 (N.A.) {927.22}	389.09	54.35
		492	4L AMBALA - KALAAMB FROM KM. - 0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6/2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	127.00	70
		493	6L ACCESS CONTROLLED HIGHWAY FROM JN WITH JAIPUR PUSHTA ROAD TO JN WITH SECTOR 62/65 DIVIDING ROAD (NHAI) (N24002047)	5/2020	8/2023 (N.A.) {10/2024}	1,328.07 (2,346.00) {2,346.00}	1,087.16	100
		494	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7/2022	6/2025 (N.A.) {6/2025}	2,414.67 (2,898.00) {2,898.00}	1,029.63	27.66
HIMACHAL PRADESH	DEPARTMENT OF HIGHER EDUCATION	495	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9/2018	6/2022 (Dec-24) {1/2025}	392.51 (N.A.) {446.43}	299.17	88.5
		496	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3/2021	8/2022 (Jul-25) {7/2025}	512.37 (512.37) {512.37}	116.30	55

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HEALTH AND FAMILY WELFARE</u>	497	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH (CPWD FOR HEALTH) (N28000127)	12/2018	6/2021 (Aug-26) {8/2026}	260.00 (371.78) {371.78}	46.24	7
	<u>POWER</u>	498	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9/2002	9/2009 (N.A.) {2/2025}	3,919.59 (N.A.) {12,160.00}	11,931.85	98.02
		499	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11/2020	1/2026 (N.A.) {6/2027}	1,810.56 (N.A.) {3,060.71}	1,531.81	50.99
		500	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10/2020	11/2025 (N.A.) {5/2026}	687.97 (N.A.) {1,426.00}	716.94	60.73
		501	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1/2023	4/2028 (N.A.) {4/2028}	2,614.51 (N.A.) {2,614.51}	803.18	26
	<u>RAILWAYS</u>	502	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4/2008	12/2026 (N.A.) {3/2025}	2,966.99 (N.A.) {6,753.42}	5,369.57	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	503	FOUR LANNING OF NERCHOWK- PANDOH BYPASS SECTION OF NH- 21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9/2016	7/2020 (N.A.) {8/2024}	1,273.71 (N.A.) {1,478.61}	1,383.76	92.6
		504	FOUR LANING OF SOLAN- KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3/2018	5/2021 (Dec-24) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		505	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8/2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	137.79	97.43
		506	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8/2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	86.43	84.45
		507	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8/2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100
		508	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI- SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2/2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	152.01	81.98
		509	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR- KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8/2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	187.96	13
		510	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN- MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8/2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	68.39	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		511	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3/2021	12/2024 (Dec-24) {12/2024}	1,322.95 (1,442.47) {1,442.47}	829.61	82.64
		512	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5/2022	3/2024 (Dec-24) {12/2024}	469.95 (N.A.) {280.00}	299.33	95.68
		513	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2/2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100
		514	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4/2021	6/2024 (N.A.) {12/2024}	583.93 (704.30) {704.30}	170.92	98.2
		515	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH- 20 (NEW NH-154) (NHAI) (N24001812)	3/2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.79}	189.07	40.97
		516	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7/2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.6
		517	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3/2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	0.00	20

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		518	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3/2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	0.00	41
		519	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3/2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.5
		520	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2/2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	346.53	41.5
		521	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7/2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	288.28	54.24
		522	REHABILITATION AND UP- GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2/2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	889.44	51.11
	URBAN DEVELOPMENT	523	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4/2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	0
JAMMU AND KASHMIR	CIVIL AVIATION	524	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7/2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	67.00	14

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	525	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3/2019	7/2022 (Aug-24) {8/2024}	424.93 (500.91) {500.91}	467.62	98
		526	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1/2018	4/2023 (Sep-24) {9/2024}	676.00 (1,148.68) {1,144.68}	64.75	98.5
	<u>HEALTH AND FAMILY WELFARE</u>	527	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3/2019	9/2023 (Nov-24) {11/2024}	1,404.00 (1,642.00) {1,642.00}	1,446.12	99.6
		528	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3/2019	9/2025 (Jan-25) {11/2025}	1,828.00 (1,577.00) {1,577.00}	1,126.55	58.2
	<u>PETROLEUM</u>	529	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4/2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	439.02	52
		530	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3/2022	3/2032 (Sep-34) {9/2034}	538.00 (N.A.) {538.00}	4.11	0.4
	<u>POWER</u>	531	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10/2014	4/2020 (Jul-25) {9/2026}	8,112.12 (N.A.) {8,112.12}	5,116.22	61.3
		532	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3/2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {4,287.59}	1,926.64	44.73
		533	RATLE HE PROJECT (NHPC) (N18000324)	2/2021	2/2026 (N.A.) {12/2026}	5,281.94 (N.A.) {5,281.94}	811.57	16.5
		534	KWAR HE PROJECT (CVPPPL) (N18000363)	5/2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	768.93	12.13

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	535	UDHAMPUR-SRINAGAR- BARAMULLA (NL),NR (NR) (220100133)	3/1995	11/2002 (Dec-24) {12/2024}	2,500.00 (37,012.26) {42,500.00}	41,186.87	99
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	536	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12/2015	12/2018 (Nov-24) {11/2024}	2,136.97 (2,644.00) {2,644.00}	2,377.88	99.5
		537	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12/2017	7/2021 (Nov-24) {11/2024}	1,471.75 (1,471.75) {1,903.98}	1,613.41	97.3
		538	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH- 144A FROM GANESH VIHA (NHIDCL) (N24000868)	3/2018	7/2021 (Aug-23) {12/2024}	253.44 (N.A.) {253.44}	180.32	78.28
		539	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA (NHIDCL) (N24001253)	12/2019	12/2023 (N.A.) {7/2024}	2,680.42 (N.A.) {2,680.42}	0.00	95.05
		540	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8/2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		541	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7/2020	4/2022 (Oct-24) {10/2025}	228.39 (N.A.) {228.39}	65.27	85.08

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		542	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7/2020	4/2022 (Nov-23) {12/2024}	210.79 (N.A.) {210.79}	67.63	86.77
		543	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3/2021	9/2022 (Oct-24) {12/2024}	486.45 (N.A.) {486.45}	120.08	95.32
		544	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3/2021	12/2022 (Oct-24) {11/2024}	398.51 (N.A.) {398.51}	76.47	91.06
		545	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342)	3/2021	12/2022 (N.A.) {7/2024}	260.40 (N.A.) {260.40}	191.88	93.8
		546	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7/2021	2/2023 (Jun-25) {12/2025}	512.43 (N.A.) {512.43}	65.31	48.32
		547	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7/2021	8/2023 (Dec-25) {12/2025}	859.67 (N.A.) {859.67}	175.40	40.38
		548	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7/2021	2/2023 (Mar-25) {3/2025}	497.09 (N.A.) {497.09}	149.27	74.47
		549	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2/2021	3/2023 (Oct-24) {12/2024}	431.28 (N.A.) {431.28}	309.97	89.58
		550	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9/2021	12/2023 (Oct-24) {10/2024}	811.19 (N.A.) {811.19}	808.06	99
		551	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3/2021	2/2024 (Aug-24) {6/2025}	2,919.96 (N.A.) {2,919.96}	2,181.63	61.7
		552	FOUR LANING OF JAMMU- AKHNOOR PKG-1 (NHIDCL) (N24001543)	7/2022	1/2025 (N.A.) {1/2025}	245.34 (N.A.) {245.34}	53.27	32.68

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		553	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)- KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9/2021	9/2024 (Sep-25) {9/2025}	1,821.72 (1,917.32) {1,917.32}	792.04	62.6
		554	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 (NHAI) (N24001551)	10/2021	9/2024 (Jul-25) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,349.97	51.37
		555	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10/2021	9/2024 (Sep-25) {9/2025}	2,714.95 (2,714.95) {2,714.95}	1,485.42	66.59
		556	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8/2022	6/2024 (Jun-25) {6/2025}	200.05 (200.05) {208.92}	96.70	39.4
		557	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9/2021	10/2023 (May-25) {5/2025}	442.14 (N.A.) {442.14}	260.53	19.88
		558	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7/2021	8/2024 (Jun-25) {6/2025}	614.48 (N.A.) {614.48}	159.00	7

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		559	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7/2021	6/2024 (Jun-25) {6/2025}	1,401.87 (N.A.) {1,401.87}	558.21	0
		560	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1/2020	1/2024 (Dec-24) {12/2024}	336.01 (N.A.) {336.01}	179.36	34
		561	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7/2019	10/2020 (Apr-23) {9/2024}	157.05 (N.A.) {157.05}	134.60	100
		562	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7/2021	2/2025 (Feb-25) {2/2025}	1,912.17 (N.A.) {1,912.17}	56.68	0
		563	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7/2022	3/2025 (N.A.) {3/2025}	198.28 (N.A.) {198.28}	72.01	53.9
		564	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3/2021	7/2024 (N.A.) {12/2024}	642.24 (N.A.) {642.24}	483.08	92
		565	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7/2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	177.33	87

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		566	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2/2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	198.77	60
		567	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3/2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	459.00	79
		568	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3/2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	103.81	78.25
		569	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3/2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	251.99	36.98
		570	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6/2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	301.83	35
		571	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9/2022	6/2026 (N.A.) {6/2026}	1,183.60 (N.A.) {1,183.60}	125.74	3.63

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		572	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3/2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {1,107.00}	77.75	14.25
		573	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8/2022	6/2025 (N.A.) {6/2025}	2,474.47 (N.A.) {2,675.93}	715.57	20.59
		574	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10/2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	80.79	18
		575	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER (PATTAN BYPASS) GREENFIELD BYPASS FROM EXISTING CH. KM 24 (BRO) (N24002179)	3/2023	7/2026 (N.A.) {7/2026}	980.21 (N.A.) {980.21}	222.74	5
		576	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 166.100 TO KM (BRO) (N24002180)	9/2021	7/2026 (N.A.) {7/2026}	734.64 (N.A.) {734.64}	19.60	8
		577	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDERS (BARAMULLA BYPASS) GREENFIELD BYPASS FROM EXISTING CH. K (BRO) (N24002185)	3/2023	9/2026 (N.A.) {9/2026}	992.43 (N.A.) {992.43}	315.99	0
JHARKHAND	COAL	578	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12/2009	3/2016 (N.A.) {3/2025}	510.85 (N.A.) {510.85}	488.31	74.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		579	MURAIIDH UG TURN-KEY PROJECT (BCCL) (N06000096)	2/2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	151.61	70
		580	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8/2011	3/2019 (N.A.) {2/2026}	1,230.27 (N.A.) {1,230.27}	593.92	80
		581	MADHUBAND NLW WASHERY (BCCL) (N06000126)	8/2010	5/2014 (N.A.) {11/2023}	289.45 (N.A.) {302.00}	299.98	100
		582	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8/2018	3/2024 (Mar-26) {3/2026}	513.98 (N.A.) {513.98}	184.31	51
		583	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11/2019	3/2023 (N.A.) {3/2025}	243.52 (N.A.) {243.52}	44.35	46.6
		584	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7/2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	226.14	43
		585	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10/2015	4/2018 (N.A.) {6/2025}	334.27 (N.A.) {334.27}	122.47	40
		586	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8/2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,267.12	19
		587	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8/2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	765.31	19
		588	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7/2021	3/2026 (N.A.) {3/2026}	778.80 (N.A.) {778.80}	683.05	75
		589	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8/2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	411.40	38
		590	CHANDRAGUPT OCP (CCL) (N06000238)	8/2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	7.95	12.4

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		591	SIRKA OCP (CCL) (N06000239)	5/2020	3/2025 (N.A.) {3/2025}	222.82 (N.A.) {222.82}	139.31	60
		592	JHARKHAND LAIYO OCP (CCL) (N06000240)	8/2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	20
		593	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11/2020	3/2025 (N.A.) {3/2025}	230.41 (N.A.) {230.41}	18.14	18.3
		594	EPR PUNDI OCP (CCL) (N06000242)	11/2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	39
		595	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1/2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	82.92	11.7
		596	EXPANSION OF KONAR OCP (CCL) (N06000245)	1/2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	389.17	32
		597	EXPANSION OF KARO OCP (CCL) (N06000246)	1/2022	3/2026 (N.A.) {3/2026}	908.47 (N.A.) {908.47}	145.93	17.2
		598	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5/2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	175.01	12.1
		599	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1/2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	389.65	24.2
		600	HURA C OC (ECL) (N06000275)	8/2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	33.33	62
	DEPARTMENT OF HIGHER EDUCATION	601	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9/2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	175.30	0
	PETROLEUM	602	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239)	12/2015	3/2023 (Mar-24) {3/2025}	823.27 (1,137.79) {1,137.79}	1,056.73	83.1
		603	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11/2019	1/2024 (Mar-24) {12/2024}	431.00 (N.A.) {431.00}	162.34	56.65

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		604	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3/2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	45.05	33.82
		605	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6/2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	184.22	18.4
	POWER	606	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2/2014	6/2019 (Oct-22) {12/2024}	16,242.90 (N.A.) {17,007.00}	15,361.62	85
		607	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11/2017	3/2023 (N.A.) {11/2025}	17,112.00 (N.A.) {17,112.00}	13,151.45	68
		608	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2/2019	10/2024 (N.A.) {10/2024}	501.79 (N.A.) {501.79}	40.35	0
		609	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9/2015	11/2019 (N.A.) {11/2019}	1,553.00 (N.A.) {2,804.00}	0.00	0
	RAILWAYS	610	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4/2002	(N.A.) {3/2025}	459.91 (1,625.87) {1,700.00}	1,779.61	70
		611	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3/2016	3/2021 (N.A.) {6/2026}	1,724.20 (3,029.04) {3,029.04}	2,183.61	80
		612	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4/2018	6/2022 (N.A.) {6/2026}	428.65 (N.A.) {472.50}	272.61	2
		613	DOUBLING OF PRADHANKHUNTA JN -PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11/2022	11/2027 (N.A.) {11/2027}	202.00 (349.22) {349.22}	9.54	0
		614	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12/2015	3/2025 (N.A.) {3/2025}	1,116.00 (N.A.) {3,270.07}	2,899.45	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		615	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11/2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,705.38	0
		616	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3/2017	3/2024 (N.A.) {3/2025}	262.71 (N.A.) {262.71}	197.22	73
		617	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1/2018	12/2025 (N.A.) {12/2025}	487.73 (N.A.) {487.73}	308.80	16
	ROAD TRANSPORT AND HIGHWAYS	618	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 (NHAI) (N24000725)	1/2018	11/2021 (Oct-24) {10/2024}	273.46 (N.A.) {276.17}	255.63	98
		619	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1/2018	11/2021 (Jun-25) {6/2025}	1,155.16 (N.A.) {950.49}	629.74	69
		620	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12/2016	9/2021 (Dec-24) {12/2024}	196.00 (N.A.) {196.00}	164.21	90
		621	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9/2020	3/2024 (Dec-24) {12/2024}	755.26 (N.A.) {1,039.00}	548.17	82.55
		622	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9/2020	10/2023 (Dec-24) {12/2024}	748.99 (N.A.) {903.00}	811.52	99.98

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		623	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2/2022	1/2025 (N.A.) {1/2025}	534.73 (N.A.) {534.73}	14.87	73
		624	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8/2020	3/2024 (N.A.) {12/2024}	1,034.00 (1,785.18) {1,785.18}	41.50	83.15
		625	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11/2021	7/2023 (Jun-25) {6/2025}	1,302.72 (1,504.80) {1,504.80}	837.10	55.56
		626	BALANCE WORK OF RANCHI- MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG- (NHAI) (N24001597)	1/2019	12/2020 (Jul-24) {7/2024}	466.55 (518.00) {466.55}	0.00	100
		627	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6/2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,324.95}	650.50	43
		628	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH- 143A INCLU (MoRTH) (N24001922)	2/2020	8/2023 (Dec-24) {12/2024}	153.01 (N.A.) {153.01}	83.63	84

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		629	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1/2022	7/2024 (Dec-24) {12/2024}	315.21 (N.A.) {315.21}	81.74	75
		630	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3/2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	10.49	6
		631	WIDENING AND STRENGTHENING/RECONSTRUCTI ON TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3/2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	0
		632	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC- V ON HAM (NHAI) (N24002053)	4/2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	344.60	51.48
		633	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC-III (NHAI) (N24002054)	10/2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	205.88	54.03
		634	FOUR LANING OF BASUKINATH- DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3/2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		635	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6/2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	362.33	30.23
		636	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12/2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	0
	STEEL	637	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3/2015	10/2017 (Nov-26) {11/2026}	1,034.01 (1,752.30) {1,752.30}	871.91	51.74
		638	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9/2023	7/2025 (N.A.) {7/2025}	513.82 (N.A.) {513.82}	80.57	45
		639	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11/2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	50.84	22
		640	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3/2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	0.00	2
	KARNATAKA CIVIL AVIATION	641	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6/2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	42.91	20
		642	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6/2023	2/2026 (N.A.) {1/2026}	320.47 (N.A.) {320.47}	18.21	16

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	643	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7/2019	3/2022 (Oct-22) {3/2023}	851.00 (851.00) {851.00}	886.26	100
		644	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8/2021	2/2024 (Nov-24) {11/2024}	316.25 (N.A.) {316.25}	333.42	94
	<u>PETROLEUM</u>	645	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12/2018	12/2022 (Mar-25) {3/2025}	854.00 (854.00) {854.00}	637.12	90
		646	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1/2022	7/2025 (Dec-25) {12/2025}	463.00 (500.62) {500.62}	180.65	57.3
		647	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10/2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	57.52	29.84
		648	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536)	3/2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	5.34	0.5
	<u>POWER</u>	649	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A and B) AND GADAG II (PHASE A) IN KARN (PGCIL) (N18000385)	12/2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	5.00	2.5
		650	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2/2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	0.00	6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	651	TUMKUR-CHITRADURGA- DAVENGERE NL (SWR) (N22000256)	4/2011	(N.A.) {12/2027}	1,801.01 (N.A.) {1,801.01}	479.33	12
		652	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4/2010	3/2016 (N.A.) {12/2026}	986.30 (1,378.00) {1,378.00}	553.26	34
		653	HOSPET-HUBLI-LONDA- VASCODAGAMA DL (RVNL) (N22000297)	4/2010	3/2023 (N.A.) {12/2026}	2,127.00 (N.A.) {3,692.60}	3,505.49	0
		654	GADAG-WADI NL (SWR) (N22000299)	4/2013	12/2018 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,203.98	28
		655	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4/2012	3/2016 (N.A.) {12/2026}	279.54 (296.72) {296.72}	99.49	14
		656	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3/1996	3/2017 (N.A.) {12/2025}	644.78 (825.31) {825.31}	615.15	66
		657	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4/2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	0
		658	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4/2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	0
		659	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9/2020	3/2026 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.39	0
		660	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018- 19/NR) (SWR) (N22000558)	6/2019	4/2028 (N.A.) {12/2027}	663.03 (748.85) {748.85}	0.34	1
		661	SHIMOGA-SHIKARIPURA- RANEBENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9/2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	66.02	7

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD</u> <u>TRANSPORT</u> <u>AND</u> <u>HIGHWAYS</u>	662	BANGALORE-WHITEFIELD- BANGALORE CITY- KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3/2018	3/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	169.03	46
		663	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3/2015	11/2015 (Aug-24) {8/2024}	165.67 (N.A.) {165.67}	126.47	99
		664	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	5/2014	8/2016 (Dec-24) {12/2024}	1,655.01 (2,639.00) {2,639.00}	1,803.36	97.8
		665	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552)	3/2016	3/2019 (Dec-23) {3/2025}	701.40 (591.86) {701.40}	461.05	80
		666	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8/2016	3/2019 (May-25) {5/2025}	1,167.42 (N.A.) {1,224.01}	821.77	78.97
		667	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH- 209(EXISTING CHAINAGE FROM (NHAI) (N24000622)	9/2016	8/2019 (Jun-24) {12/2024}	950.69 (1,487.46) {2,525.02}	1,913.36	99.3
		668	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1/2017	9/2017 (May-23) {5/2023}	166.67 (N.A.) {264.34}	192.08	100
		669	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8/2016	2/2017 (Jul-24) {7/2024}	175.50 (N.A.) {241.60}	189.72	90.1

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		670	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3/2018	6/2019 (Dec-23) {12/2023}	159.97 (N.A.) {242.61}	113.15	100
		671	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1/2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100
		672	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9/2017	10/2018 (Apr-22) {4/2022}	191.60 (N.A.) {191.60}	112.03	100
		673	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12/2017	1/2019 (Apr-22) {4/2022}	297.30 (N.A.) {318.28}	280.25	100
		674	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3/2018	10/2018 (Nov-22) {11/2022}	325.86 (N.A.) {386.41}	356.78	100
		675	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10/2016	3/2017 (Jul-22) {7/2022}	396.96 (N.A.) {396.96}	329.58	100
		676	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11/2016	3/2017 (Oct-21) {10/2021}	314.90 (N.A.) {314.90}	233.95	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		677	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3/2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98
		678	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5/2018	5/2018 (Dec-23) {12/2023}	171.60 (N.A.) {171.60}	134.81	100
		679	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1/2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100
		680	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2/2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	62.31	60
		681	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1/2017	9/2017 (May-23) {5/2023}	264.34 (N.A.) {264.34}	201.07	100
		682	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3/2019	12/2019 (Nov-24) {11/2024}	423.15 (N.A.) {423.15}	284.58	82
		683	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3/2021	11/2021 (Mar-25) {3/2025}	1,100.88 (1,713.98) {1,713.98}	938.22	64

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		684	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3/2021	10/2021 (Mar-25) {3/2025}	317.90 (576.32) {576.32}	340.53	94.7
		685	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1/2022	4/2025 (Apr-25) {4/2025}	1,388.70 (1,388.70) {1,388.70}	299.54	52.1
		686	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3/2018	12/2022 (Apr-25) {4/2025}	440.16 (N.A.) {440.16}	309.33	58.84
		687	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2/2023	2/2025 (N.A.) {2/2025}	1,240.60 (N.A.) {1,240.60}	657.58	60.22
		688	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11/2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	540.35	95.57
		689	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12/2022	6/2025 (N.A.) {6/2025}	2,718.46 (N.A.) {2,718.46}	312.90	34.97
		690	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11/2022	5/2024 (May-24) {5/2024}	226.76 (226.76) {226.76}	70.45	53.11

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		691	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10/2022	4/2025 (Apr-25) {4/2025}	1,479.30 (1,479.30) {1,479.30}	395.27	61.52
		692	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3/2021	10/2024 (Jun-25) {6/2025}	1,409.68 (1,633.91) {1,633.91}	817.35	42
		693	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8/2022	8/2025 (Aug-25) {12/2025}	2,032.15 (2,032.15) {2,032.15}	164.69	43.8
		694	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	3/2022	3/2024 (Sep-25) {9/2025}	294.62 (N.A.) {294.62}	32.56	13.47
		695	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9/2021	4/2023 (Dec-24) {12/2024}	912.37 (N.A.) {424.16}	330.84	98.19
		696	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI - HASSAN SECTION (NHAI) (N24001684)	9/2020	1/2023 (Sep-20) {5/2025}	688.00 (602.09) {688.00}	474.14	75.59
		697	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3/2021	3/2023 (Jan-25) {1/2025}	1,065.06 (1,444.50) {1,444.50}	158.70	88.96
		698	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10/2021	10/2023 (Mar-25) {3/2025}	1,331.77 (2,082.98) {2,082.98}	337.71	69.02

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		699	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10/2019	10/2021 (Jan-25) {1/2025}	1,225.24 (1,505.85) {1,505.85}	78.09	93.65
		700	BALANCE WORK OF CONTRSUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3/2021	3/2023 (Jul-24) {7/2024}	344.79 (N.A.) {344.79}	10.00	90
		701	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2/2023	2/2024 (Feb-25) {2/2025}	398.48 (N.A.) {398.48}	5.00	50
		702	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6/2021	6/2024 (Jun-25) {6/2025}	298.00 (N.A.) {298.00}	10.70	52
		703	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1/2023	1/2026 (Sep-25) {9/2025}	166.58 (N.A.) {166.58}	3.54	0
		704	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1/2023	1/2025 (Jan-25) {1/2025}	350.69 (N.A.) {350.69}	10.00	56
		705	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9/2022	3/2024 (Jan-25) {1/2025}	172.98 (N.A.) {172.98}	6.48	65

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		706	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANAGES KM 112.750 TO (MoRTH) (N24001944)	1/2023	6/2024 (Jul-24) {7/2024}	255.88 (N.A.) {255.88}	60.99	78
		707	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 116.800 TO 149.070(DSIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8/2022	2/2024 (Dec-24) {12/2024}	170.34 (N.A.) {170.34}	4.25	72
		708	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11/2022	11/2024 (Nov-24) {11/2024}	218.93 (N.A.) {218.93}	10.00	95
		709	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2/2023	2/2025 (Feb-25) {2/2025}	177.94 (N.A.) {177.94}	6.66	47
		710	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10/2022	10/2024 (Dec-24) {12/2024}	355.72 (N.A.) {355.72}	11.32	60
		711	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3/2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	428.14	52.32

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		712	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12/2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	400.50	44.55
		713	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5/2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	231.38	44.71
		714	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12/2021	6/2024 (Dec-24) {12/2024}	516.96 (N.A.) {516.96}	19.93	70
		715	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3/2023	3/2025 (Mar-25) {3/2025}	718.52 (N.A.) {718.52}	24.81	23
		716	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE (MoRTH) (N24002013)	3/2021	2/2022 (Oct-24) {10/2024}	766.64 (N.A.) {766.64}	13.55	75
		717	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24002186)	3/2024	9/2025 (N.A.) {9/2025}	166.58 (N.A.) {166.58}	3.62	0
		718	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM 55.6 TO KM 90.7 (EXISTING CHAINAGES) OF NH-766C ((MoRTH) (N24002187)	2/2024	2/2026 (N.A.) {2/2026}	313.56 (N.A.) {313.56}	53.65	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		719	WIDENING TO 2L+PS FROM KM 71.00 TO 104.00 (EXISTING CHAINAGES) (SARJAPUR TO PATTADKALLU) ON BHANAPUR (MoRTH) (N24002188)	3/2024	3/2026 (N.A.) {3/2026}	445.62 (N.A.) {445.62}	33.24	0
		720	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0.00 (DESIGN CHAINAGE 0.00) TO KM 23.338 (DESIGN C (MoRTH) (N24002189)	9/2024	3/2026 (N.A.) {3/2026}	196.05 (N.A.) {196.05}	2.34	0
	URBAN DEVELOPMENT	721	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRL) (N28000058)	2/2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89
		722	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRL) (N28000151)	6/2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30
KERALA	CIVIL AVIATION	723	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6/2023	9/2025 (N.A.) {9/2025}	323.98 (N.A.) {323.98}	0.00	3
	DEPARTMENT OF HIGHER EDUCATION	724	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7/2019	3/2021 (Mar-23) {11/2025}	753.63 (N.A.) {753.63}	412.37	66
	HEALTH AND FAMILY WELFARE	725	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9/2017	3/2020 (May-24) {9/2024}	150.29 (N.A.) {162.00}	149.49	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>PETROLEUM</u>	726	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3/2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	101.30	65.3
		727	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12/2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	71.31	5.1
	<u>RAILWAYS</u>	728	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2/2015	(Dec-26) {12/2026}	1,431.90 (3,785.45) {3,785.45}	3,097.41	40
		729	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12/2010	3/2028 (Nov-26) {11/2026}	600.82 (595.39) {595.39}	270.57	5
		730	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12/2011	8/2023 (Dec-26) {12/2026}	812.85 (802.80) {802.80}	258.69	2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	731	4-LANNING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704)	9/2017	5/2020 (Nov-23) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,522.66	100
		732	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2/2018	2/2023 (Dec-24) {3/2025}	1,424.77 (2,065.95) {2,065.95}	778.68	78.35
		733	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2/2017	8/2017 (Mar-22) {8/2024}	294.28 (296.53) {296.53}	285.47	98
		734	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2/2017	9/2017 (Jan-23) {8/2024}	380.76 (372.87) {372.87}	337.83	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		735	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8/2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	617.95	38.98
		736	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12/2021	2/2025 (Feb-25) {2/2025}	3,273.61 (N.A.) {3,273.61}	468.60	46.3
		737	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH- 66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12/2021	1/2025 (Aug-25) {8/2025}	3,635.64 (N.A.) {3,635.64}	280.92	36.8
		738	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9/2021	9/2024 (Mar-26) {9/2024}	2,878.97 (N.A.) {2,878.97}	346.36	27.04
		739	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3/2020	6/2022 (Feb-24) {6/2024}	210.37 (216.94) {216.94}	198.10	100
		740	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH 66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 () (NHAI) (N24001653)	11/2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,910.24	43.89

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		741	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6/2021	3/2025 (Feb-25) {2/2025}	2,641.37 (N.A.) {2,641.37}	450.72	56.62
		742	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6/2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	3,033.98	55.34
		743	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6/2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	2,917.21	47.81
		744	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6/2021	10/2024 (Dec-25) {12/2025}	2,842.14 (N.A.) {2,842.14}	463.03	58.12
		745	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1/2021	7/2024 (Mar-25) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,365.33	86.17
		746	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH- 66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2/2021	7/2024 (Mar-25) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,240.35	85.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		747	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8/2020	2/2024 (Nov-21) {12/2025}	2,714.60 (3,319.41) {2,714.60}	1,774.87	61.2
		748	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10/2020	4/2024 (May-25) {12/2025}	3,219.47 (3,713.14) {3,713.14}	2,079.48	48.3
		749	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5/2020	5/2024 (Nov-21) {3/2025}	1,981.07 (2,467.68) {1,981.07}	1,368.63	77.02
		750	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6/2020	4/2024 (Oct-21) {12/2025}	3,041.65 (3,799.76) {3,041.65}	2,156.43	54.5
		751	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6/2020	4/2024 (Oct-21) {11/2025}	1,746.45 (2,377.88) {1,746.45}	1,125.92	60.1
		752	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074)	8/2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	112.40	19.4
		753	KOCHI METRO RAIL PROJECT (KMRCL) (N28000081)	7/2012	7/2017 (Sep-20) {9/2020}	5,181.79 (N.A.) {6,218.14}	6,059.17	100
	URBAN DEVELOPMENT	754	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7/2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	2.81	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		755	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIUNITHURA (KMRCL) (N28000159)	6/2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	0
LADAKH	CIVIL AVIATION	756	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7/2018	9/2021 (Oct-24) {10/2025}	480.33 (N.A.) {640.00}	377.61	61.31
	ROAD TRANSPORT AND HIGHWAYS	757	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3/2021	1/2023 (Dec-24) {10/2025}	384.23 (N.A.) {384.23}	115.95	58.5
		758	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3/2021	1/2023 (Nov-23) {10/2025}	404.89 (N.A.) {404.89}	156.11	60.05
		759	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8/2020	1/2023 (Jun-24) {11/2024}	381.01 (N.A.) {381.01}	181.54	70.86
		760	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3/2021	1/2023 (Aug-24) {11/2024}	398.37 (N.A.) {398.37}	204.79	82.11
		761	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11/2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	76.75	37
MADHYA PRADESH	CIVIL AVIATION	762	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6/2016	6/2021 (N.A.) {7/2024}	412.24 (N.A.) {412.24}	401.34	100
		763	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10/2021	8/2023 (Jun-24) {8/2024}	446.12 (N.A.) {446.12}	431.65	100
	COAL	764	KANCHAN OC EXPANSION (SECL) (N06000125)	12/2014	3/2021 (Mar-26) {3/2026}	371.04 (N.A.) {371.04}	134.03	47
		765	AMADAND OPENCASET EXPANSION PROJECT (SECL) (N06000148)	3/2016	3/2021 (Mar-27) {3/2027}	869.44 (N.A.) {869.44}	250.82	64

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		766	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162)	11/2017	3/2022 (N.A.) {3/2025}	1,255.17 (N.A.) {1,255.17}	1,236.92	97.14
		767	GANDHIGRAM UG MINE (WCL) (N06000183)	8/2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	24.98	28
		768	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7/2019	3/2023 (N.A.) {3/2025}	998.71 (N.A.) {998.71}	375.01	26.84
		769	NIGAH EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11/2020	3/2025 (N.A.) {3/2025}	1,729.68 (N.A.) {1,729.68}	659.12	41.1
		770	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7/2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	472.39	44
		771	TAWA III UG MINE (WCL) (N06000250)	12/2021	3/2027 (N.A.) {3/2027}	324.25 (N.A.) {324.25}	12.32	9
		772	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9/2022	3/2027 (N.A.) {3/2027}	497.01 (N.A.) {497.01}	160.98	42
		773	VISHNUPURI UG TO OC (WCL) (N06000260)	11/2022	3/2029 (N.A.) {3/2029}	227.65 (N.A.) {227.65}	7.02	7
		774	URDHAN OC (WCL) (N06000265)	7/2022	3/2031 (N.A.) {3/2031}	228.42 (N.A.) {228.42}	27.67	9
		775	SHARDA UG (WCL) (N06000266)	7/2022	3/2028 (N.A.) {3/2028}	200.16 (N.A.) {200.16}	34.40	11
	PETROLEUM	776	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5/2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	808.00	6.8
	POWER	777	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6/2022	3/2024 (N.A.) {3/2025}	1,530.49 (N.A.) {1,530.49}	1,129.94	70

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	778	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART- 2:5.5GW) (JAISALMER/BARMER COMPLEX); PART-C (PGCIL) (N18000392)	8/2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	0.00	0
		779	RAMGANJMUHDI-BHOPAL (NL),WCR (WCR) (220100314)	4/2001	3/2021 (Dec-25) {12/2025}	424.60 (3,032.46) {5,125.16}	3,137.92	68
		780	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4/2008	3/2022 (Feb-27) {2/2027}	3,503.69 (5,677.80) {6,203.51}	3,937.49	80
		781	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12/2015	3/2020 (N.A.) {10/2024}	1,763.93 (N.A.) {2,445.30}	2,857.25	100
		782	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8/2016	3/2022 (N.A.) {9/2024}	582.13 (N.A.) {1,247.64}	1,180.23	75
		783	ANUPPUR-KATNI (SECR) (N22000485)	4/2015	12/2021 (Dec-23) {12/2024}	1,370.00 (1,680.00) {2,311.02}	1,660.04	74
		784	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4/2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	181.72	10
		785	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10/2021	10/2027 (Mar-25) {3/2025}	910.00 (1,095.88) {1,095.88}	795.26	87
		786	SATNA - REWA (50 KM) (WCR) (N22000554)	11/2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80
		787	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9/2018	9/2030 (N.A.) {9/2030}	4,340.00 (N.A.) {7,393.75}	1,004.86	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	788	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3/2015	8/2017 (Dec-23) {12/2024}	511.83 (N.A.) {511.83}	485.18	93.06

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		789	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12/2017	2/2020 (Sep-24) {9/2024}	950.27 (N.A.) {786.43}	627.68	98.44
		790	2L+PS OF THIKRI ANJAD SECTION OF NH-347B (MoRTH) (N24000892)	11/2017	7/2018 (N.A.) {9/2023}	249.05 (N.A.) {249.05}	221.19	100
		791	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2/2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,152.44	35
		792	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3/2021	4/2024 (May-24) {8/2024}	790.78 (N.A.) {790.78}	1,450.94	46
		793	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1/2021	10/2023 (N.A.) {12/2024}	428.04 (N.A.) {428.04}	351.20	98.89
		794	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9/2019	9/2022 (N.A.) {12/2024}	194.40 (N.A.) {194.40}	176.08	87.3
		795	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756)	10/2020	10/2024 (N.A.) {1/2025}	1,352.56 (N.A.) {1,480.94}	832.87	94.35
		796	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH-752D (PKG-III) (NHAI) (N24001758)	1/2020	10/2024 (N.A.) {2/2025}	823.05 (N.A.) {823.05}	371.04	99.38
		797	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1/2020	6/2024 (Dec-24) {12/2024}	909.84 (N.A.) {909.84}	429.45	77.01

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		798	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761)	2/2023	2/2025 (Feb-25) {2/2025}	520.28 (N.A.) {520.28}	369.21	95.11
		799	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10/2021	1/2024 (Dec-24) {12/2024}	1,146.22 (N.A.) {1,146.22}	556.11	79.27
		800	ADDITIONAL WORKS (2VUPS, MR- 10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE- DEWAS SECTION OF N (NHAI) (N24001765)	8/2022	7/2024 (N.A.) {5/2025}	207.77 (N.A.) {207.77}	46.09	34.51
		801	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1/2022	10/2024 (N.A.) {5/2025}	1,011.29 (N.A.) {1,011.29}	153.90	33.67
		802	4L OF INDORE - BOREGAON (PKG- III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1/2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	482.27	78
		803	BALANCE WORK OF 4L OF INDORE- GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8/2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	50.43	100
		804	DHANGAON - BORGAEON SECTION (KM 81.000 TO KM 139.000) [INDORE - EDLABAD PKG IV] (NHAI) (N24001769)	11/2018	8/2023 (Nov-24) {11/2024}	831.00 (N.A.) {831.00}	840.30	99.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		805	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2/2022	3/2024 (Dec-24) {12/2024}	417.51 (N.A.) {417.51}	230.95	75.39
		806	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 90F EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8/2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	127.98	24.67
		807	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3/2022	12/2024 (N.A.) {12/2024}	179.19 (N.A.) {179.19}	75.91	60
		808	UPGRADATION OF NASRULLAGANI- REHTI-BUDHNI SCCTION TO 2- LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12/2021	10/2024 (N.A.) {3/2025}	305.12 (N.A.) {305.12}	73.80	17.25
		809	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3/2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	151.39	64
		810	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3/2022	2/2025 (N.A.) {2/2025}	386.49 (N.A.) {386.49}	103.75	32

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		811	BALANCE WORK FOR REHABILITATION AND UP- GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12/2020	4/2023 (May-23) {12/2024}	529.44 (N.A.) {529.44}	165.60	45.69
		812	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL- KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11/2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	58.23	16.03
		813	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR- SUSNER-MP-RJ B (MoRTH) (N24002018)	1/2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	129.45	80.71
		814	UPGRADATION OF DINDORI- SAGARTOLA-KABICHABUTRA (MP- CG BORDER) SECTION OF NH -45 FROM KM 0+00(DSIGN) (MoRTH) (N24002019)	1/2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	111.42	23.5
		815	CONSTRUCTION OF KAITHI- PADARIA KALA BYPASS, PATNA- TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3/2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	37.78	17
		816	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE- SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1/2021	7/2023 (N.A.) {12/2024}	178.18 (N.A.) {178.18}	161.64	84.39

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		817	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12/2022	3/2025 (N.A.) {3/2025}	652.33 (N.A.) {652.33}	253.55	50.95
		818	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7/2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	125.83	95.1
		819	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1/2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	472.07	72.8
		820	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9/2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	135.06	17.5
		821	FOUR LANING OF RAGHOGARH (DESIGN CH.29.300/EXISTING CH. 29.555) TO NANASA (DESIGN CH.92.971/EXISTING (NHAI) (N24002166)	3/2024	3/2026 (Mar-26) {3/2026}	799.20 (N.A.) {799.20}	195.31	10.04
	<u>SOCIAL JUSTICE</u>	822	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2/2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74
	<u>URBAN DEVELOPMENT</u>	823	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11/2018	2/2023 (Jun-28) {6/2028}	6,941.40 (N.A.) {6,941.40}	2,474.71	32.68
		824	INDORE METRO RAIL (MPMRCL) (N28000125)	11/2018	2/2023 (Dec-28) {12/2028}	7,500.80 (N.A.) {7,500.80}	3,244.68	48.19

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MAHARASHTRA	CIVIL AVIATION	825	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3/2017	4/2021 (N.A.) {12/2023}	475.39 (N.A.) {520.00}	508.41	100
		826	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6/2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	267.86	100
	COAL	827	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8/2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	534.87	86
		828	UKNI DEEP OC (WCL) (N06000179)	11/2018	3/2021 (Mar-25) {3/2025}	318.14 (N.A.) {318.14}	253.27	91
		829	BELLORA-NAIGAON DEEP OC (WCL) (N06000180)	11/2018	3/2021 (Mar-25) {3/2025}	252.71 (N.A.) {252.71}	122.94	56
		830	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3/2021	3/2028 (N.A.) {3/2028}	241.72 (N.A.) {241.72}	59.30	6
		831	SASTI EXPANSION OC (WCL) (N06000206)	8/2020	3/2026 (N.A.) {3/2026}	371.59 (N.A.) {371.59}	105.64	24
		832	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	2/2019	3/2028 (N.A.) {3/2028}	720.87 (N.A.) {720.87}	179.54	33
		833	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11/2018	3/2024 (Mar-25) {3/2025}	333.43 (N.A.) {333.43}	223.17	78
		834	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2/2020	3/2027 (N.A.) {3/2027}	1,184.33 (N.A.) {1,184.33}	849.44	48
		835	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9/2018	3/2024 (Mar-25) {3/2025}	313.34 (N.A.) {313.34}	205.45	87

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		836	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (WCL) (N06000231)	11/2020	3/2026 (N.A.) {3/2026}	826.80 (N.A.) {826.80}	518.85	52
		837	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1/2022	3/2028 (N.A.) {3/2028}	253.51 (N.A.) {253.51}	111.68	27
		838	SINGHORI DEEP OC (WCL) (N06000252)	5/2022	3/2029 (N.A.) {3/2029}	421.84 (N.A.) {421.84}	115.89	16
		839	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6/2022	3/2026 (N.A.) {3/2026}	497.06 (N.A.) {497.06}	144.88	12
		840	BHATADI EXPANSION OC (WCL) (N06000254)	2/2020	3/2028 (N.A.) {3/2028}	729.86 (N.A.) {729.86}	159.12	17
		841	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	5/2019	3/2027 (N.A.) {3/2027}	496.38 (N.A.) {496.38}	143.72	27
		842	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9/2022	3/2028 (N.A.) {3/2028}	494.60 (N.A.) {494.60}	99.87	7
		843	GOKUL EXPANSION OC (WCL) (N06000264)	4/2021	3/2026 (N.A.) {3/2026}	456.95 (N.A.) {456.95}	148.57	7
		844	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	1/2023	3/2027 (N.A.) {3/2027}	206.19 (N.A.) {206.19}	7.75	5
		845	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3/2024	3/2030 (N.A.) {3/2030}	1,428.25 (N.A.) {1,428.25}	203.03	17
		846	GAURI CENTRAL OCM (WCL) (N06000278)	8/2023	3/2030 (N.A.) {3/2030}	1,015.07 (N.A.) {1,015.07}	0.00	0
	DEPARTMENT OF HIGHER EDUCATION	847	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1/2018	7/2020 (Nov-23) {2/2024}	223.37 (275.00) {230.00}	141.16	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	HEALTH AND FAMILY WELFARE	848	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7/2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	27.16	0
	PETROLEUM	849	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12/2015	4/2018 (Dec-23) {5/2026}	3,190.69 (3,375.90) {3,375.90}	2,961.86	87.6
		850	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4/2019	3/2022 (Jun-24) {2/2025}	3,228.80 (3,976.67) {3,976.67}	3,948.68	98.9
		851	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5/2019	4/2025 (Oct-25) {10/2025}	8,797.00 (11,256.00) {11,256.00}	5,169.05	75
		852	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436)	1/2022	5/2024 (Jan-25) {1/2025}	3,183.58 (N.A.) {3,645.23}	3,417.00	99.1
		853	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4/2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	585.32	58.4
		854	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9/2021	10/2023 (May-24) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08
		855	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5/2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	181.30	65.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		856	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9/2022	8/2025 (N.A.) {8/2025}	165.00 (N.A.) {165.00}	52.95	52.16
		857	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6/2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	243.43	17.6
		858	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3/2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	46.15	1.5
		859	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6/2017	5/2025 (N.A.) {5/2025}	281.35 (N.A.) {281.35}	86.75	42.4
		860	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4/2022	10/2024 (Aug-26) {8/2026}	341.43 (N.A.) {341.43}	200.11	28.1
		861	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3/2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	67.43	56
		862	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11/2022	5/2024 (Dec-24) {12/2024}	1,219.48 (N.A.) {1,145.10}	35.95	46.7
		863	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5/2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	127.63	33.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		864	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2/2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	188.75	16.4
		865	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6/2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	0.00	0
		866	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6/2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	6.80	9.4
		867	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5/2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	0
	POWER	868	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4/2022	5/2024 (N.A.) {7/2025}	5,491.89 (532.00) {5,491.89}	2,701.37	62
		869	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11/2023	7/2025 (N.A.) {7/2025}	224.00 (N.A.) {224.00}	0.00	0
	RAILWAYS	870	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2/1997	3/2021 (N.A.) {12/2025}	2,271.50 (N.A.) {4,909.82}	4,397.13	89
		871	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4/2008	3/2014 (N.A.) {3/2014}	5,300.00 (N.A.) {918.53}	7,135.77	21
		872	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4/2008	3/2023 (N.A.) {12/2026}	3,168.29 (N.A.) {3,445.48}	2,797.79	47
		873	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4/2011	3/2021 (N.A.) {12/2025}	792.89 (N.A.) {1,432.61}	796.09	50
		874	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4/2012	3/2022 (N.A.) {5/2025}	540.02 (N.A.) {540.02}	655.76	72

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		875	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2/2015	3/2022 (N.A.) {8/2025}	1,272.19 (N.A.) {1,384.72}	1,226.29	67
		876	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2/2015	3/2023 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,466.41	42
		877	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2/2015	3/2024 (N.A.) {1/2025}	3,627.47 (3,627.00) {6,463.49}	4,166.41	84
		878	DAUND - MANMAD (236 KM) (CR) (N22000360)	2/2016	3/2023 (N.A.) {12/2024}	1,876.00 (N.A.) {2,081.27}	2,361.34	87
		879	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2/2016	3/2022 (N.A.) {3/2025}	1,035.16 (N.A.) {1,552.24}	1,405.99	75
		880	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2/2016	3/2023 (N.A.) {5/2025}	637.95 (N.A.) {637.95}	816.61	70
		881	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9/2016	3/2023 (N.A.) {12/2025}	1,908.51 (N.A.) {3,544.25}	2,828.26	80
		882	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3/2010	(N.A.) {3/2024}	265.88 (N.A.) {311.36}	0.00	0
		883	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6/2018	12/2021 (N.A.) {12/2026}	229.00 (N.A.) {1,886.05}	511.88	22
		884	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8/2022	8/2027 (N.A.) {3/2029}	955.00 (N.A.) {2,093.82}	60.57	0
		885	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1/2019	3/2028 (N.A.) {10/2027}	904.92 (N.A.) {3,295.74}	1,026.38	5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		886	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1/2019	3/2026 (N.A.) {9/2027}	492.76 (N.A.) {1,102.50}	151.37	5
		887	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2/2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	8.32	0
		888	BARAMATI - LONAND (CR) (N22000615)	2/1999	3/2027 (N.A.) {2/2026}	736.44 (N.A.) {1,843.90}	569.32	50
		889	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4/2019	3/2025 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	846.83	0
		890	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10/2019	6/2024 (N.A.) {6/2024}	1,400.00 (N.A.) {1,400.00}	0.00	77
	ROAD TRANSPORT AND HIGHWAYS	891	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1/2015	(N.A.) {}	225.81 (N.A.) {225.81}	167.96	96
		892	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12/2015	3/2019 (Nov-23) {12/2024}	649.50 (N.A.) {649.50}	585.49	88.67
		893	NAGPUR RING ROAD PACKAGE-1 (NHAI) (N24000558)	3/2016	7/2019 (Jul-23) {9/2024}	546.00 (N.A.) {546.00}	528.35	100
		894	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3/2016	7/2019 (Mar-24) {12/2024}	591.66 (N.A.) {591.66}	617.70	91.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		895	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3/2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17
		896	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3/2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	0
		897	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655)	3/2017	3/2020 (Nov-24) {11/2024}	247.02 (N.A.) {157.49}	91.81	98.9
		898	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3/2017	3/2020 (Jul-22) {7/2024}	744.64 (N.A.) {1,007.00}	380.66	74.89
		899	4-LANNING OF WARANGA- MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3/2017	3/2017 (May-21) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	82.04
		900	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3/2018	7/2021 (N.A.) {6/2025}	1,162.92 (1,182.87) {1,182.87}	371.48	55
		901	SARSAM TO KOTHARI (MoRTH) (N24001002)	2/2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		902	AKOLA TO AKOT (MoRTH) (N24001003)	1/2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99
		903	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1/2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		904	DAHEGAON TO KUHI (MoRTH) (N24001017)	1/2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99
		905	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1/2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100
		906	AMD1 TO SAONER (MoRTH) (N24001021)	1/2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69
		907	WADI TO ASOLA (MoRTH) (N24001022)	1/2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		908	SHAHPUR PATGAON SECTION I (MoRTH) (N24001027)	1/2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	70.66
		909	JINTUR TO PARBHANI (MoRTH) (N24001039)	1/2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	80.48
		910	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1/2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	97
		911	VITA TO NAGAJ (MoRTH) (N24001050)	3/2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		912	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2/2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	89.97
		913	KARWANDI TO RAJURI (MoRTH) (N24001058)	3/2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		914	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3/2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95
		915	NANDED TO JALKOT (MoRTH) (N24001069)	12/2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	0
		916	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3/2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	93.83
		917	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12/2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		918	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3/2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98
		919	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3/2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	90
		920	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3/2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100
		921	KOLDE TO KHETIYA (MoRTH) (N24001090)	1/2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81
		922	SATARA TO MHASWAD (MoRTH) (N24001092)	1/2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	76.76
		923	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1/2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	88.16
		924	SELDOH TO PANVAR (MoRTH) (N24001097)	7/2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	0
		925	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1/2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.5
		926	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1/2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27
		927	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7/2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		928	PEN TO KHOPOLI (MoRTH) (N24001106)	3/2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		929	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7/2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	0
		930	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4/2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		931	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7/2016	9/2019 (N.A.) {3/2024}	406.54 (407.00) {406.54}	274.30	80.7
		932	INDAPUR TO VADPALE (MoRTH) (N24001114)	1/2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		933	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3/2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.6
		934	SHIRUR TO KHARDA (MoRTH) (N24001123)	2/2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		935	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2/2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		936	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2/2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		937	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2/2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	87.84
		938	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9/2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		939	KANTE TO WAKED (MoRTH) (N24001134)	3/2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	0
		940	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2/2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100
		941	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377)	2/2019	1/2022 (Aug-23) {8/2023}	731.89 (731.99) {731.99}	689.19	0.2
		942	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378)	2/2019	1/2022 (Jun-23) {6/2023}	362.46 (372.46) {372.46}	352.01	0.7

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		943	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379)	2/2019	1/2022 (Aug-23) {8/2023}	594.75 (594.75) {613.75}	585.20	0.5
		944	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11/2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	87.88
		945	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3/2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	0
		946	TUNNEL AT KHAMBATAKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2/2019	2/2022 (Dec-24) {12/2024}	493.00 (N.A.) {493.00}	374.15	72.82
		947	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9/2021	9/2023 (Dec-24) {12/2024}	618.45 (N.A.) {618.45}	600.38	90.2
		948	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12/2022	12/2024 (N.A.) {12/2024}	1,749.86 (N.A.) {1,749.86}	1,611.00	59.02
		949	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 ((NHAI) (N24001495)	11/2022	11/2024 (N.A.) {11/2024}	930.00 (N.A.) {930.00}	590.45	63.49
		950	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501)	9/2021	9/2023 (Jul-23) {7/2023}	531.86 (532.41) {532.41}	520.71	0.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		951	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9/2021	9/2023 (Mar-24) {3/2025}	624.45 (580.15) {580.15}	398.06	2
		952	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9/2021	9/2023 (Mar-24) {12/2024}	667.66 (666.21) {666.21}	590.90	13
		953	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5/2022	5/2024 (Jan-25) {1/2025}	1,260.00 (N.A.) {1,260.00}	608.72	91
		954	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3/2022	3/2024 (May-25) {5/2025}	1,549.02 (N.A.) {1,549.02}	537.10	52
		955	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2/2022	2/2024 (Jun-25) {6/2025}	2,747.00 (N.A.) {2,747.00}	929.38	64.25
		956	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11/2022	5/2024 (Jun-25) {6/2025}	1,124.00 (N.A.) {1,124.00}	299.43	44.5
		957	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11/2022	10/2024 (Jun-25) {6/2025}	1,450.00 (N.A.) {1,450.00}	545.51	64.61

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		958	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11/2022	10/2024 (Apr-25) {4/2025}	990.00 (N.A.) {990.00}	296.63	51.55
		959	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1/2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	758.28	47.67
		960	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10/2022	5/2024 (N.A.) {5/2024}	332.00 (N.A.) {332.00}	194.88	42.44
		961	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9/2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	411.34	53.48
		962	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1/2023	12/2023 (Dec-24) {12/2024}	151.26 (N.A.) {151.26}	115.47	67.03
		963	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1/2022	5/2024 (Mar-25) {3/2025}	1,833.73 (N.A.) {1,833.73}	443.48	81.19
		964	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10/2022	7/2024 (N.A.) {12/2024}	490.40 (N.A.) {289.00}	241.93	77

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		965	4L OF RAJURA-KORPANA- ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3/2022	10/2024 (Apr-25) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		966	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10/2021	1/2024 (N.A.) {3/2025}	815.77 (N.A.) {815.77}	652.04	91.92
		967	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2/2021	11/2023 (N.A.) {1/2025}	540.21 (N.A.) {540.21}	425.12	96.22
		968	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2/2021	10/2023 (N.A.) {12/2024}	1,166.96 (N.A.) {1,251.00}	1,041.36	80
		969	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12/2019	9/2022 (Jun-24) {6/2024}	1,654.07 (N.A.) {980.00}	835.19	91.76
		970	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5/2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	412.49	39.7
		971	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5/2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	373.70	39.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		972	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3/2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	27.35
		973	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3/2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8
		974	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3/2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65
		975	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3/2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		976	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2/2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	0
		977	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10/2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		978	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8/2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	0
		979	UP-GRADATION OF TIRORA- GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8/2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31
		980	2 LANE + PS PIMPLNER TO SATANA -[DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9/2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	0
		981	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2/2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46
		982	BALANCE WORK OF REHABILITATION AND UP- GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7/2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66
		983	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2/2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		984	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9/2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95
		985	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11/2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99
		986	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11/2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
		987	REHABILITATION AND UP- GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12/2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34
		988	REHABILITATION AND UP- GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8/2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	0
		989	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9/2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		990	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10/2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	96

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		991	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8/2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48
		992	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6/2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		993	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12/2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
		994	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11/2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
		995	REHABILITATION AND UPGRADATION OF JAMKHED TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9/2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		996	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3/2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		997	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3/2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	127.21	16.75

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		998	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7/2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	12.74	19.6
		999	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2/2024	3/2025 (N.A.) {3/2025}	175.00 (N.A.) {175.00}	83.42	44
		1000	REHABILITATION/UPGRADATION OF EXISTING HIGHWAY TO 2L+PS/4 LANE OF DHAWALI TO RAJOLI FROM DESIGN KM.1 (MoRTH) (N24002169)	3/2022	9/2025 (N.A.) {9/2025}	316.44 (N.A.) {316.44}	0.00	0
		1001	REHABILITATION/ UPGRADATION OF EXISTING HIGHWAY TO FOUR LANE STANDARDS IN KURKHEDA TOWN FROM (KM.413 (MoRTH) (N24002170)	3/2022	5/2025 (N.A.) {5/2025}	163.86 (N.A.) {163.86}	0.00	0
		1002	REHABILITATION & UP-GRADATION FOR TALERE A?? GAGANBAWDAA?? KOLHAPUR ROAD (NH-166G) STRETCHES START F (MoRTH) (N24002171)	2/2023	4/2025 (N.A.) {4/2025}	249.13 (N.A.) {249.13}	0.00	0
		1003	UP-GRADATION TO 4 LANE CONFIGURATION FOR THE WORK OF PETH NAKA TO SANGLI ROAD, NH-166H, FROM KM 0+00 (MoRTH) (N24002172)	2/2023	12/2025 (N.A.) {12/2025}	856.82 (N.A.) {856.82}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1004	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF MAHUD SANGOLA ROAD NH (MoRTH) (N24002173)	2/2023	4/2025 (N.A.) {4/2025}	253.78 (N.A.) {253.78}	0.00	0
		1005	UP-GRADATION TO FOUR LANE/ TWO LANE WITH PAVED SHOULDERS CONFIGURATION OF KALYAN - MURBAD - MALSHEJ (MoRTH) (N24002174)	2/2023	8/2026 (N.A.) {8/2026}	984.07 (N.A.) {984.07}	0.00	0
		1006	CONSTRUCTION OF FOUR-LANE CONCRETE ROAD FROM POLICE HEADQUARTER GONDIA CITY TO RAWANWADI VILLAGE (BI (MoRTH) (N24002175)	2/2023	8/2025 (N.A.) {8/2025}	328.11 (N.A.) {328.11}	0.00	0
		1007	REHABILITATION/UP GRADATION OF KARANJA ? KHERDA - MURTIZAPUR SECTION TO 4LANE+PAVED SHOULDER STANDAR (MoRTH) (N24002176)	3/2023	2/2026 (N.A.) {2/2026}	594.44 (N.A.) {594.44}	0.00	0
		1008	REHABILITATION / UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF EXISTING SECTION IN SILLOD TOWN WITH D (MoRTH) (N24002177)	3/2023	7/2025 (N.A.) {7/2025}	153.79 (N.A.) {153.79}	0.00	0
		1009	REHABILITATION, UPGRADATION & WIDENING OF EXISTING HIGHWAY TO RIGID PAVEMENT 2 LANE WITH PAVED SHOULDER (MoRTH) (N24002178)	2/2023	7/2026 (N.A.) {7/2026}	723.13 (N.A.) {723.13}	0.00	0
	URBAN DEVELOPMENT	1010	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) (MMRCL) (N28000086)	7/2013	3/2020 (N.A.) {12/2023}	23,136.00 (N.A.) {37,276.00}	23,687.33	87.2

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1011	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12/2016	11/2021 (Sep-24) {9/2024}	11,420.00 (13,656.22) {13,656.22}	12,735.40	100
		1012	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12/2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	321.78	13.64
		1013	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10/2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	12.35	6.2
	<u>WATER RESOURCES</u>	1014	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA (BPB) (N30000001)	3/2017	12/2019 (Aug-24) {12/2023}	233.57 (N.A.) {233.57}	217.42	
MANIPUR	<u>CIVIL AVIATION</u>	1015	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11/2021	7/2024 (Dec-25) {12/2025}	499.00 (N.A.) {499.00}	115.07	37.88
	<u>RAILWAYS</u>	1016	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4/2003	3/2011 (Mar-28) {12/2028}	4,454.17 (12,274.06) {19,517.70}	14,882.06	80.1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1017	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3/2020	6/2022 (Jan-25) {1/2025}	292.24 (N.A.) {292.24}	127.86	85.33
		1018	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6/2020	8/2022 (Jan-25) {1/2025}	365.53 (N.A.) {365.53}	156.31	77.36

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1019	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3/2020	6/2022 (Jan-25) {1/2025}	167.95 (204.12) {167.95}	88.05	69.89
		1020	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7/2020	8/2022 (Feb-25) {2/2025}	177.76 (N.A.) {177.76}	89.67	80.53
		1021	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8/2020	4/2022 (Jun-25) {6/2025}	379.39 (N.A.) {379.39}	189.86	45.88
		1022	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO (NHIDCL) (N24001275)	8/2020	4/2022 (N.A.) {12/2025}	268.98 (N.A.) {268.98}	22.08	0
		1023	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8/2020	4/2022 (N.A.) {12/2025}	228.97 (N.A.) {228.97}	0.00	0
		1024	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2/2021	12/2022 (Mar-25) {3/2025}	226.32 (N.A.) {226.32}	87.99	66.07
		1025	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2/2021	12/2022 (Oct-24) {11/2024}	188.36 (N.A.) {188.36}	126.71	97.95
		1026	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3/2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100
		1027	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3/2021	12/2022 (Mar-25) {3/2025}	195.14 (N.A.) {195.14}	59.99	50.77
		1028	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3/2021	12/2022 (Jan-25) {1/2025}	234.08 (N.A.) {234.08}	139.45	90.34

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1029	IMPHAL ? MOREH (PACKAGE 4) (NHIDCL) (N24001399)	3/2021	1/2023 (N.A.) {4/2024}	277.99 (N.A.) {277.99}	146.35	100
		1030	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3/2021	1/2023 (May-25) {5/2025}	211.70 (N.A.) {211.70}	35.16	38.2
		1031	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7/2021	3/2023 (Mar-25) {3/2025}	467.00 (N.A.) {467.00}	183.55	75.27
		1032	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7/2021	3/2023 (Jan-25) {1/2025}	185.80 (N.A.) {185.80}	112.31	92.65
		1033	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7/2021	3/2023 (Aug-24) {1/2025}	483.87 (N.A.) {483.87}	278.89	91.03
		1034	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7/2021	3/2023 (Feb-25) {2/2025}	198.77 (N.A.) {198.77}	110.09	85.12
		1035	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7/2021	10/2023 (Feb-24) {6/2025}	673.27 (N.A.) {673.27}	361.21	72.82
		1036	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8/2021	5/2023 (Jan-25) {1/2025}	477.86 (N.A.) {477.86}	235.67	80.3
		1037	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9/2021	5/2023 (Nov-24) {4/2025}	311.18 (N.A.) {311.18}	171.57	72.7
		1038	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8/2021	5/2023 (Oct-24) {1/2025}	467.41 (N.A.) {467.41}	243.19	92.31
		1039	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8/2021	12/2023 (Jul-25) {7/2025}	579.63 (N.A.) {579.63}	131.58	52.65
		1040	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9/2021	2/2024 (Mar-25) {3/2025}	310.76 (N.A.) {310.76}	121.05	77.4
		1041	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12/2021	5/2024 (Feb-25) {2/2025}	410.68 (N.A.) {410.68}	105.71	50.81
		1042	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12/2021	2/2025 (Sep-25) {9/2025}	504.76 (N.A.) {504.76}	113.57	48.76

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1043	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3/2022	2/2025 (Feb-25) {2/2025}	152.11 (N.A.) {152.11}	53.26	75
		1044	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9/2021	1/2025 (Jan-25) {1/2025}	315.56 (N.A.) {315.56}	73.38	52.02
		1045	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1/2023	12/2025 (Dec-25) {12/2025}	760.16 (N.A.) {760.16}	67.05	28.83
		1046	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3/2023	2/2026 (Mar-26) {3/2026}	578.98 (N.A.) {578.98}	68.30	34.04
MEGHALAYA	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1047	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9/2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	276.05	74
	<u>DONER</u>	1048	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4/2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	98.5
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1049	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4/2017	9/2021 (Jul-23) {3/2025}	553.51 (610.09) {553.51}	344.90	67.41
		1050	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4- LANING FROM ((NHIDCL) (N24001313)	11/2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	232.71	29

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1051	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11/2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	385.00	14.5
		1052	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11/2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	193.78	7
		1053	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11/2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	45.46	3
		1054	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10/2020	4/2022 (Jun-24) {12/2024}	157.86 (146.92) {157.86}	146.19	97.49
		1055	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3/2021	12/2022 (Jun-24) {11/2024}	260.21 (N.A.) {260.21}	216.59	90
		1056	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8/2020	2/2022 (Nov-24) {11/2024}	302.88 (N.A.) {302.88}	213.32	93.11
		1057	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9/2021	5/2024 (N.A.) {12/2024}	359.86 (N.A.) {359.86}	220.56	78.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1058	RANIKOR- MAHESKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11/2021	6/2024 (N.A.) {12/2024}	283.50 (N.A.) {283.50}	203.23	70.68
		1059	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3/2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	168.64	0
		1060	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3/2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	241.74	0
		1061	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3/2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	263.14	0
MIZORAM	RAILWAYS	1062	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4/2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,562.76	93
	ROAD TRANSPORT AND HIGHWAYS	1063	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4/2017	4/2023 (Nov-24) {1/2025}	519.09 (785.65) {785.65}	649.83	90
		1064	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4/2017	7/2023 (May-24) {7/2024}	640.07 (990.88) {1,286.35}	1,217.65	98.9
		1065	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4/2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.84	99.34

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1066	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4/2017	4/2023 (Nov-24) {2/2025}	473.18 (688.25) {688.25}	520.26	84.88
		1067	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4/2017	4/2023 (Jul-24) {2/2025}	537.82 (789.05) {789.05}	747.56	91.6
		1068	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4/2017	6/2023 (Oct-24) {3/2025}	518.53 (906.76) {906.76}	791.68	89.25
		1069	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4/2017	4/2024 (Nov-24) {3/2025}	404.29 (750.32) {750.32}	593.23	84.4
		1070	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4/2017	9/2023 (Nov-24) {3/2025}	428.11 (746.39) {746.39}	579.70	87.3
		1071	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9/2020	10/2022 (Mar-24) {3/2024}	275.02 (247.25) {247.25}	231.19	99.73

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1072	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3/2020	7/2022 (Jun-24) {6/2024}	206.88 (219.33) {219.33}	206.58	97.01
		1073	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3/2020	7/2022 (Oct-24) {7/2025}	292.24 (331.17) {331.17}	293.90	91.64
		1074	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3/2021	12/2022 (Mar-24) {3/2024}	374.39 (318.92) {318.92}	292.37	100
		1075	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3/2021	12/2022 (Apr-24) {4/2024}	233.25 (233.25) {233.25}	178.37	100
		1076	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3/2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	388.33	42.55
		1077	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3/2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	281.51	41.6
		1078	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9/2021	5/2023 (Jun-24) {12/2024}	492.94 (492.94) {492.94}	357.26	84.7
		1079	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWL RANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9/2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	248.74	42.3
		1080	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12/2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	148.05	39
MULTI STATE	COAL	1081	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8/2016	3/2022 (Mar-25) {3/2025}	319.76 (319.76) {319.76}	281.40	98

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1082	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) (WCL) (N06000157)	2/2017	3/2021 (Mar-25) {3/2025}	328.00 (N.A.) {328.00}	321.43	96
		1083	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8/2020	3/2024 (N.A.) {3/2025}	836.42 (N.A.) {836.42}	701.49	55.73
	DPIIT	1084	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9/2011	3/2027 (Mar-27) {3/2027}	20,084.00 (20,084.00) {20,084.00}	10,217.21	50.99
	PETROLEUM	1085	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6/2009	12/2012 (Feb-25) {3/2025}	2,915.00 (5,909.00) {5,909.00}	4,092.70	92.3
		1086	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9/2019	7/2022 (Jun-25) {6/2025}	2,658.34 (N.A.) {2,658.34}	1,985.10	92.2
		1087	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3/2020	11/2022 (Mar-25) {3/2025}	1,030.65 (N.A.) {1,030.65}	787.60	84.7
		1088	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6/2020	5/2023 (Jun-25) {6/2025}	7,844.25 (N.A.) {7,844.25}	5,825.60	90.1
		1089	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6/2019	12/2029 (Mar-30) {3/2030}	169.00 (N.A.) {169.00}	71.21	17.9
		1090	NORTH EAST GAS GRID (IGGL) (N16000439)	11/2020	3/2024 (Mar-25) {3/2027}	9,265.00 (9,265.00) {9,265.00}	5,479.01	83.83
		1091	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7/2023	7/2026 (Jul-26) {7/2026}	521.92 (521.92) {521.92}	7.70	16.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	POWER	1092	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO (PGCIL) (N18000184)	3/2015	3/2018 (N.A.) {12/2024}	197.40 (N.A.) {197.40}	161.89	96
		1093	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12/2014	12/2018 (Mar-25) {3/2025}	4,754.42 (9,129.32) {9,129.32}	6,841.94	77.5
		1094	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12/2014	12/2018 (Mar-25) {3/2025}	5,111.33 (6,700.00) {6,700.00}	4,954.66	95.2
		1095	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264)	8/2017	2/2020 (Apr-23) {9/2025}	1,931.39 (2,635.55) {2,635.55}	1,964.44	99
		1096	NORTH EASTERN REGION STRENGTHENING SCHEME-XII (PGCIL) (N18000316)	5/2021	3/2023 (N.A.) {8/2024}	576.42 (576.42) {576.42}	419.96	100
		1097	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2/2022	4/2025 (N.A.) {4/2025}	318.12 (N.A.) {318.12}	143.75	85
		1098	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR- LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3/2022	12/2024 (N.A.) {9/2025}	288.71 (N.A.) {288.71}	128.79	44

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1099	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2/2022	9/2023 (N.A.) {12/2024}	359.47 (N.A.) {359.47}	225.97	66
		1100	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5/2022	11/2023 (N.A.) {12/2024}	1,666.00 (N.A.) {1,666.00}	1,339.62	81
		1101	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7/2022	6/2023 (N.A.) {12/2024}	4,546.26 (N.A.) {4,546.26}	2,255.35	70
		1102	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7/2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	66.53	68
		1103	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10/2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	88.31	52
		1104	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3/2023	11/2024 (N.A.) {3/2025}	3,546.94 (N.A.) {3,546.94}	1,465.14	57
		1105	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3/2023	3/2025 (N.A.) {3/2025}	281.16 (N.A.) {281.16}	35.14	31
		1106	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3/1981	7/2012 (Jan-27) {1/2027}	450.00 (N.A.) {2,017.96}	1,433.55	69
	RAILWAYS							

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1107	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (N220100232)	9/1998	5/2008 (N.A.) {3/2025}	247.66 (63.57) {8,248.50}	2,520.04	43
		1108	CHHAPRA-BALLIA UP (NER) (N22000134)	3/2013	1/2019 (N.A.) {2/2025}	295.00 (954.00) {995.82}	987.32	95
		1109	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4/2007	3/2022 (Dec-27) {12/2027}	1,347.26 (1,793.63) {1,793.63}	1,485.12	58
		1110	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4/2007	3/2022 (Feb-27) {2/2027}	1,640.04 (1,873.10) {2,873.11}	2,145.20	58
		1111	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4/2011	3/2022 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	0
		1112	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR (NCR) (N22000158)	4/2010	(Dec-26) {12/2026}	2,030.50 (746.83) {746.83}	81.25	19
		1113	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4/2013	3/2019 (N.A.) {10/2024}	1,798.00 (N.A.) {2,832.35}	3,188.00	99
		1114	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4/2010	3/2020 (N.A.) {3/2027}	242.22 (N.A.) {1,195.95}	389.33	5
		1115	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4/2010	(N.A.) {3/2023}	241.52 (N.A.) {401.65}	343.30	85.42
		1116	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4/2011	3/2020 (N.A.) {5/2025}	414.84 (N.A.) {1,265.16}	608.04	35
		1117	PIRPAINTI-JASIDIH (ER) (N22000219)	4/2013	3/2022 (Mar-28) {3/2028}	915.98 (N.A.) {2,610.84}	809.34	45

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1118	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4/2012	3/2023 (N.A.) {3/2025}	1,856.95 (N.A.) {1,952.68}	1,413.19	0
		1119	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4/2007	(N.A.) {2/2024}	336.91 (N.A.) {791.39}	572.99	40
		1120	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4/2007	(N.A.) {2/2027}	2,062.30 (2,495.59) {2,495.59}	1,413.42	60
		1121	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3/2015	3/2019 (N.A.) {6/2025}	1,614.59 (1,877.81) {2,458.87}	2,408.17	89
		1122	KAZIPET-BALHRSHA (SCR) (N22000367)	4/2015	3/2021 (N.A.) {1/2025}	2,063.03 (N.A.) {2,909.00}	2,627.09	0
		1123	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12/2015	12/2023 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	67,486.00	47.17
		1124	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11/2007	3/2020 (N.A.) {3/2020}	16,592.00 (51,101.00) {51,101.00}	47,476.00	83
		1125	CHANDIGARH-BADDI (NR) (N22000467)	4/2007	3/2023 (N.A.) {6/2025}	328.14 (N.A.) {1,540.14}	482.67	10
		1126	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3/2019	5/2023 (N.A.) {12/2025}	1,866.31 (N.A.) {1,866.31}	1,660.96	55
		1127	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9/2011	3/2014 (N.A.) {9/2024}	2,848.00 (N.A.) {3,241.56}	3,901.66	86.01
	ROAD TRANSPORT AND HIGHWAYS	1128	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11/2021	2/2025 (N.A.) {2/2025}	2,155.95 (N.A.) {2,155.95}	1,178.79	50.62

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1129	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4/2022	11/2024 (N.A.) {11/2024}	796.65 (N.A.) {796.65}	293.17	65.95
	SHIPPING AND PORTS	1130	JAL MARG VIKAS PROJECT (IWA)) (N25000072)	1/2018	3/2023 (Dec-25) {12/2025}	5,369.18 (5,061.15) {5,061.15}	3,115.95	61.79
	TELECOMMUNI CATIONS	1131	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3/2020	6/2021 (Nov-21) {12/2024}	461.42 (461.42) {461.42}	159.98	81
		1132	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (PMPLS) NETWORK and (BSNL) (N26000115)	3/2023	3/2024 (Jul-24) {12/2024}	239.60 (N.A.) {239.60}	169.10	100
		1133	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5/2023	8/2024 (Nov-24) {11/2024}	645.13 (N.A.) {645.13}	263.80	75.33
		1134	PLANNIN ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGARTION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6/2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	3,711.06	50.71
		1135	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2/2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	274.00	27.42
	URBAN DEVELOPMENT	1136	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3/2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	22,955.39	80.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
NAGALAND	PETROLEUM	1137	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8/2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	0.22	9.5
	RAILWAYS	1138	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4/2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	3,846.75	60
	ROAD TRANSPORT AND HIGHWAYS	1139	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3/2016	9/2019 (Nov-22) {12/2024}	373.07 (534.41) {534.41}	382.50	99.81
		1140	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3/2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	291.85	83.66
		1141	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2/2017	9/2020 (Feb-23) {12/2024}	387.00 (688.12) {688.12}	387.50	99.32
		1142	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3/2018	11/2022 (Aug-24) {12/2024}	500.09 (698.81) {698.81}	373.62	95.65
		1143	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3/2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	174.28	99.9

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1144	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3/2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	110.43	38.55
		1145	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3/2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	85.56	21.85
		1146	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3/2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		1147	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3/2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
		1148	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9/2020	10/2022 (Apr-24) {9/2024}	277.44 (N.A.) {277.44}	160.86	62.33
		1149	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8/2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	79.96	16.82

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1150	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8/2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	72.03	26.96
		1151	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9/2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		1152	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3/2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	60.49
		1153	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG- I) (NHIDCL) (N24001286)	3/2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		1154	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4/2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	115.30	61.37
		1155	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8/2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	42.39	1.91
		1156	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3/2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		1157	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7/2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	65.31	58.44
		1158	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2/2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1159	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7/2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	43.05	27.33
		1160	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6/2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	0
		1161	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3/2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	109.49	59.56
		1162	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3/2021	2/2024 (Jan-25) {1/2025}	226.44 (N.A.) {226.44}	115.35	81.12
		1163	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3/2022	12/2024 (N.A.) {12/2024}	605.36 (N.A.) {605.36}	227.62	88.43
		1164	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2/2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	65.73	63.23
		1165	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2/2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	19.80	30.93

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1166	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12/2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	41.48	22.46
		1167	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12/2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	12.03
		1168	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12/2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	78.00	34.64
ODISHA	COAL	1169	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5/2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	266.76	62
		1170	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2/2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,405.83	42.5
		1171	GARJANBAHAL OCP (MCL) (N06000117)	11/2014	3/2021 (N.A.) {3/2026}	1,375.38 (N.A.) {1,375.38}	836.84	58
		1172	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP (MCL) (N06000167)	5/2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,833.50	51
		1173	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11/2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,672.72	44
		1174	TALABIRA II AND III OCP (NLC) (N06000189)	7/2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,384.47	53.6
		1175	NAINI COAL MINE (SCCL) (N06000203)	3/2020	3/2024 (N.A.) {3/2026}	494.30 (N.A.) {494.30}	491.33	35

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1176	BHUBANESWARI EXPANSION OCP (MCL) (N06000227)	3/2024	3/2031 (N.A.) {3/2031}	6,321.73 (N.A.) {6,321.73}	1,143.45	18
		1177	GOPALJI-KANIHA OCP (MCL) (N06000229)	4/2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,624.88	16.5
		1178	BALARAM EXPANSION OCP (MCL) (N06000230)	8/2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	908.31	49
		1179	KULDA EXPANSION OCP- 15 MTY (MCL) (N06000248)	6/2014	3/2018 (N.A.) {3/2026}	348.16 (N.A.) {348.16}	203.65	60
		1180	SUBHADRA OCP (MCL) (N06000249)	5/2021	3/2029 (Mar-29) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,167.82	39
		1181	RPR OF HINGULA -II EXPANSION PH-III (MCL) (N06000261)	12/2022	3/2029 (N.A.) {3/2029}	2,264.68 (N.A.) {2,264.68}	1,004.23	39
		1182	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1/2024	5/2029 (N.A.) {5/2029}	27,213.00 (N.A.) {27,213.00}	970.30	1.51
	DEPARTMENT OF HIGHER EDUCATION	1183	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1/2019	3/2022 (N.A.) {2/2025}	790.79 (N.A.) {790.79}	674.84	94
	MINES	1184	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12/2014	4/2021 (Sep-25) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,263.64	68.59
		1185	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5/2016	1/2020 (Nov-23) {3/2024}	534.00 (N.A.) {1,021.97}	752.42	80.5
		1186	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12/2015	11/2020 (Sep-25) {11/2026}	355.00 (581.00) {581.00}	109.88	12.6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1187	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11/2017	4/2021 (May-25) {5/2025}	483.00 (483.00) {483.00}	348.65	86.02
		1188	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5/2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	649.96	50.3
		1189	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9/2019	3/2023 (May-24) {5/2024}	225.79 (N.A.) {270.66}	5.00	100
	PETROLEUM	1190	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11/2018	9/2021 (Dec-24) {12/2024}	462.30 (552.44) {552.44}	469.84	95.1
		1191	Fuel Quality Upgradation Project at Paradip Refinery (IOCL) (N16000362)	5/2019	8/2021 (Dec-24) {12/2024}	3,361.00 (N.A.) {3,361.00}	2,710.85	98.3
		1192	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY (IOCL) (N16000368)	6/2019	9/2022 (Dec-24) {12/2024}	427.10 (427.10) {427.10}	304.40	94.6
		1193	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7/2020	1/2024 (Apr-25) {4/2025}	13,805.00 (N.A.) {13,805.00}	6,794.30	85.9
	POWER	1194	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3/2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	312.97	58
		1195	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8/2022	5/2027 (N.A.) {5/2027}	11,844.00 (N.A.) {11,844.00}	1,405.09	8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	1196	KHURDA ROAD- BOLANGIR(NL)ECOR (<i>ECOR</i>) (220100284)	4/1994	3/2009 (Dec-26) {12/2026}	2,923.13 (3,791.66) {5,089.37}	4,175.46	78
		1197	TALCHER-BIMALAGARH(NL)(ECOR) (<i>ECOR</i>) (220100328)	4/2005	6/2021 (N.A.) {3/2026}	810.78 (N.A.) {1,928.07}	1,539.54	40
		1198	BHADRAK - NERGUNDI 3RD LINE (<i>ECOR</i>) (N22000316)	3/2013	10/2020 (Oct-25) {10/2025}	843.04 (1,284.39) {1,284.39}	1,138.09	75
		1199	JAGADALPUR-KORAPUT DOUBLING (<i>ECOR</i>) (N22000376)	4/2015	3/2022 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,211.47	88.5
		1200	KORAPUT - SINGAPUR ROAD DOUBLING (<i>ECOR</i>) (N22000379)	4/2015	3/2022 (Mar-26) {3/2026}	2,361.74 (2,361.74) {2,361.74}	1,576.71	69
		1201	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (<i>ECOR</i>) (N22000380)	4/2015	11/2018 (Aug-26) {8/2026}	701.61 (N.A.) {810.02}	547.64	75
		1202	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (<i>ECOR</i>) (N22000381)	4/2015	12/2018 (Jul-25) {7/2025}	1,172.92 (N.A.) {2,022.75}	1,615.89	72
		1203	VIZIANAGARAM -SAMABALPUR 3RD LINE (<i>RVNL</i>) (N22000409)	1/1991	12/2024 (N.A.) {12/2026}	2,335.67 (N.A.) {4,803.16}	4,691.52	0
		1204	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (<i>IRCON</i>) (N22000418)	4/2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	0.00	17.4
		1205	JEYPORE MALKANGIRI NEW LINE (<i>ECOR</i>) (N22000516)	2/2018	7/2033 (N.A.) {7/2033}	642.69 (N.A.) {642.69}	164.45	0.1

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1206	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7/2017	7/2028 (N.A.) {7/2028}	499.99 (N.A.) {747.91}	0.00	0
		1207	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7/2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	0
		1208	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8/2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	0
		1209	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9/2022	9/2027 (N.A.) {9/2027}	189.93 (N.A.) {189.93}	5.14	0
		1210	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12/2009	12/2026 (N.A.) {12/2026}	48.44 (N.A.) {297.00}	146.95	10
		1211	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8/2019	8/2027 (Aug-27) {8/2027}	183.00 (257.97) {257.97}	0.25	0
		1212	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9/2022	9/2026 (N.A.) {3/2026}	209.75 (N.A.) {244.99}	45.45	8
	ROAD TRANSPORT AND HIGHWAYS	1213	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9/2016	8/2019 (N.A.) {12/2024}	2,510.04 (N.A.) {2,510.04}	1,104.98	98
		1214	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12/2017	7/2020 (N.A.) {12/2024}	686.65 (565.00) {686.65}	574.26	86.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1215	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (<i>(NHAI)</i>) (N24000733)	1/2018	8/2022 (N.A.) {2/2025}	633.68 (492.83) {633.68}	560.38	81
		1216	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (<i>(NHAI)</i>) (N24000734)	1/2018	8/2021 (N.A.) {11/2024}	614.48 (503.30) {757.12}	664.48	99
		1217	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (<i>(NHAI)</i>) (N24000736)	1/2018	9/2020 (N.A.) {12/2024}	686.65 (504.09) {1,015.16}	435.85	82
		1218	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (<i>(NHAI)</i>) (N24000738)	1/2018	9/2021 (N.A.) {3/2025}	999.00 (1,152.70) {1,152.70}	387.08	78.28
		1219	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (<i>(NHAI)</i>) (N24000739)	1/2018	6/2021 (Dec-24) {12/2024}	503.88 (609.03) {609.03}	536.89	95
		1220	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (<i>(MoRTH)</i>) (N24000912)	8/2016	2/2017 (N.A.) {12/2024}	287.70 (N.A.) {293.66}	272.95	98.66
		1221	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (<i>(MoRTH)</i>) (N24000914)	12/2016	8/2018 (N.A.) {3/2025}	223.50 (N.A.) {223.50}	220.50	92

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1222	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3/2018	8/2018 (N.A.) {12/2024}	199.16 (N.A.) {199.16}	155.44	98
		1223	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8/2020	3/2022 (N.A.) {11/2024}	200.00 (154.73) {154.73}	137.04	100
		1224	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHAI) (N24001665)	12/2021	10/2024 (N.A.) {8/2025}	1,592.00 (1,592.00) {1,592.00}	884.70	63.37
		1225	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE-OD (NHAI) (N24001666)	12/2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	463.69	75.02
		1226	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130- CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9/2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	1,057.84	73.5
		1227	6L OF BADA KUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH-130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3/2021	4/2024 (N.A.) {3/2025}	1,249.00 (N.A.) {1,249.00}	405.98	71.84
		1228	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH-130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2/2021	3/2024 (N.A.) {3/2025}	586.00 (N.A.) {586.00}	186.65	63.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1229	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH-130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2/2021	3/2024 (N.A.) {12/2024}	593.00 (N.A.) {593.00}	251.76	88.06
		1230	6L OF HATIBENA - BADAUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2/2021	3/2024 (N.A.) {12/2024}	925.00 (N.A.) {925.00}	398.30	94.91
		1231	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8/2021	6/2024 (N.A.) {6/2025}	1,460.00 (1,460.00) {1,460.00}	852.25	80
		1232	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6/2020	12/2023 (N.A.) {12/2024}	414.24 (N.A.) {414.24}	277.23	60
		1233	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR-BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3/2022	6/2025 (N.A.) {6/2025}	499.79 (N.A.) {499.79}	232.34	7.25
		1234	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3/2021	3/2024 (N.A.) {3/2025}	196.94 (N.A.) {196.94}	66.09	10.58
		1235	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1/2022	4/2025 (N.A.) {4/2025}	300.33 (N.A.) {300.33}	162.15	47.32

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1236	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2/2022	11/2024 (Mar-25) {3/2025}	157.49 (N.A.) {157.49}	62.14	31.74
		1237	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2/2022	10/2025 (Nov-25) {11/2025}	238.78 (N.A.) {238.78}	17.26	2
		1238	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3/2021	6/2024 (N.A.) {6/2025}	154.05 (N.A.) {154.05}	47.47	10
		1239	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11/2021	6/2025 (N.A.) {6/2025}	154.49 (N.A.) {154.49}	50.75	0
		1240	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH- 201 (PRESENT (MoRTH) (N24001865)	12/2021	5/2025 (N.A.) {5/2025}	324.09 (N.A.) {324.09}	74.19	15
		1241	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12/2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	96.90	20.5
		1242	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12/2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	146.86	23.01

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1243	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12/2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	161.57	26.5
		1244	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8/2022	1/2025 (N.A.) {6/2025}	153.61 (N.A.) {153.61}	14.22	15.6
		1245	WIDENING AND STRENGTHENLNG TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3/2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	22.06	0
		1246	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3/2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	188.50	16.66
	STEEL	1247	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11/2020	5/2023 (N.A.) {11/2024}	377.18 (N.A.) {377.18}	414.08	92.25
		1248	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1/2022	5/2025 (N.A.) {5/2025}	970.18 (N.A.) {970.18}	505.32	66.67

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
PUNJAB	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1249	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10/2019	5/2022 (N.A.) {12/2024}	348.24 (N.A.) {348.24}	275.88	88
	<u>PETROLEUM</u>	1250	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5/2020	2/2023 (Sep-24) {12/2024}	1,421.46 (N.A.) {1,421.46}	1,069.00	95.1
		1251	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11/2021	5/2024 (Feb-25) {2/2025}	367.00 (397.00) {397.00}	290.79	83.61
		1252	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3/2022	3/2030 (N.A.) {9/2033}	151.00 (N.A.) {151.00}	7.77	1.5
	<u>RAILWAYS</u>	1253	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6/2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	60
		1254	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9/2020	3/2025 (N.A.) {3/2025}	82.99 (N.A.) {235.00}	0.00	0
		1255	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4/2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {299.74}	0.00	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1256	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3/2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100
		1257	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10/2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	44

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1258	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3/2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	104.98	79
		1259	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941)	3/2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100
		1260	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12/2020	4/2024 (Jul-24) {7/2024}	881.00 (N.A.) {881.00}	867.69	88.64
		1261	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12/2020	1/2024 (Mar-25) {3/2025}	989.66 (N.A.) {989.66}	319.95	31.08
		1262	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH- 5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12/2020	4/2024 (Sep-25) {9/2025}	1,234.40 (N.A.) {1,234.40}	744.28	57.09
		1263	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12/2020	4/2024 (Sep-25) {9/2025}	1,094.46 (N.A.) {1,094.46}	773.92	60.97

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1264	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2/2021	4/2024 (Nov-24) {11/2024}	1,269.96 (N.A.) {1,269.96}	585.86	43.45
		1265	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR- MEHTA-SRIHARGOBINDPUR- (NHAI) (N24001420)	2/2021	4/2024 (Dec-25) {12/2025}	853.66 (N.A.) {853.66}	113.95	13.6
		1266	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7/2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	288.00	65
		1267	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3/2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	283.00	69
		1268	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1/2021	5/2024 (Apr-25) {4/2025}	1,741.86 (N.A.) {1,741.86}	1,123.85	86.5
		1269	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5/2021	12/2024 (Dec-24) {12/2024}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
		1270	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3/2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	990.38	30.02

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1271	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11/2021	7/2024 (Dec-24) {12/2024}	646.42 (646.42) {646.42}	481.67	92
		1272	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5/2020	12/2024 (Aug-25) {8/2025}	864.23 (864.23) {864.23}	434.88	40
		1273	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3/2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	680.13	31.56
		1274	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3/2021	10/2024 (Sep-25) {9/2025}	1,641.75 (N.A.) {1,641.75}	179.85	23.6
		1275	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2/2021	8/2024 (Mar-25) {3/2025}	1,474.77 (N.A.) {1,474.77}	389.27	64.44
		1276	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12/2020	6/2024 (Jun-25) {6/2025}	857.91 (N.A.) {857.91}	127.71	35.7
		1277	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12/2020	9/2023 (Mar-25) {3/2025}	524.88 (416.58) {416.58}	157.14	69

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1278	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR- MUKTS (MoRTH) (N24001960)	3/2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	94.08	42
		1279	WORK OF WIDENING/UPGRADATION OF 2- LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3/2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	81.25	69
		1280	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12/2020	8/2025 (Aug-25) {8/2025}	757.13 (757.00) {757.00}	246.51	91
		1281	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3/2021	10/2025 (Oct-25) {10/2025}	2,029.17 (2,029.00) {2,029.00}	84.23	25
		1282	6L ACCESS CONTROLLED LUDHIANA-BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6/2021	9/2025 (Sep-25) {9/2025}	906.51 (906.51) {906.51}	134.05	30.48
		1283	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70 (NHAI) (N24002092)	3/2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	867.81	20.71

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1284	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3/2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	86.00	31.5
		1285	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10/2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	231.73	60.3
		1286	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8/2021	6/2025 (N.A.) {6/2025}	809.51 (N.A.) {809.51}	130.42	36.62
		1287	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1/2020	4/2026 (N.A.) {4/2026}	2,165.23 (N.A.) {2,165.23}	125.28	14.85
RAJASTHAN	CIVIL AVIATION	1288	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5/2022	11/2024 (N.A.) {6/2025}	480.00 (N.A.) {480.00}	133.61	55
		1289	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6/2023	3/2026 (Sep-26) {9/2026}	887.00 (N.A.) {887.00}	165.35	31.78
	COAL	1290	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3/2023	9/2024 (N.A.) {3/2025}	1,813.00 (N.A.) {1,813.00}	403.48	54
	PETROLEUM	1291	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12/2021	10/2024 (Dec-24) {12/2025}	9,028.00 (N.A.) {9,028.00}	5,813.03	67.74

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1292	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAU DISTRICTS (IOCL) (N16000489)	3/2022	3/2030 (N.A.) {3/2031}	575.00 (N.A.) {575.00}	120.36	7.7
		1293	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARALI (HPCL) (N16000496)	3/2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	188.25	19.9
		1294	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12/2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	27.28	22.5
		1295	RAJASTHAN REFINERY PROJECT (HPCLRRRL(JV)) (N16000513)	10/2017	10/2022 (Mar-25) {3/2025}	43,129.00 (72,937.00) {72,937.00}	50,785.89	82.7
		1296	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12/2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	193.00	16.3
	POWER	1297	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3/2020	9/2021 (N.A.) {3/2025}	1,782.00 (N.A.) {1,782.00}	1,336.50	95
		1298	ANTA SOLAR 90 MW (NTPC) (N18000292)	1/2021	3/2022 (N.A.) {3/2022}	382.22 (N.A.) {382.22}	497.17	100
		1299	BHENSARA 320 MW (NTPC) (N18000293)	1/2021	7/2022 (N.A.) {3/2025}	1,221.73 (1,521.00) {1,221.73}	973.44	0
		1300	CHHATTARGARH 150 MW (NTPC) (N18000294)	2/2021	7/2022 (N.A.) {3/2024}	599.99 (N.A.) {599.99}	599.99	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1301	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000306)	6/2021	12/2022 (N.A.) {12/2024}	1,562.00 (N.A.) {1,562.00}	1,240.25	98
		1302	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000307)	6/2021	12/2022 (N.A.) {10/2024}	1,006.00 (N.A.) {1,006.00}	884.11	100
		1303	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3/2022	8/2023 (N.A.) {3/2025}	1,352.71 (N.A.) {1,352.71}	849.99	45
		1304	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3/2022	8/2023 (N.A.) {3/2025}	1,409.52 (N.A.) {1,409.52}	1,295.38	95
		1305	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3/2022	8/2023 (N.A.) {3/2025}	1,426.94 (N.A.) {1,426.94}	953.00	80
		1306	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6/2022	3/2024 (N.A.) {12/2024}	2,598.92 (N.A.) {2,598.92}	1,304.43	12
		1307	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3/2023	9/2024 (N.A.) {12/2024}	1,433.28 (N.A.) {1,433.28}	605.47	44
		1308	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5/2022	11/2023 (N.A.) {3/2025}	1,677.12 (N.A.) {1,677.12}	729.12	64

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1309	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372)	6/2023	1/2025 (N.A.) {12/2024}	202.39 (N.A.) {202.39}	20.04	70
		1310	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8/2023	2/2025 (N.A.) {2/2025}	688.74 (N.A.) {688.74}	121.10	23
		1311	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10/2023	4/2025 (N.A.) {4/2025}	2,211.00 (N.A.) {2,211.00}	230.63	17
		1312	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10/2023	4/2025 (N.A.) {4/2025}	1,796.00 (N.A.) {1,796.00}	405.48	18
		1313	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9/2023	4/2025 (N.A.) {4/2025}	2,191.00 (N.A.) {2,191.00}	457.26	22
		1314	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12/2022	3/2025 (N.A.) {8/2025}	331.00 (N.A.) {331.00}	7.66	26
		1315	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11/2023	6/2025 (N.A.) {6/2025}	428.00 (N.A.) {428.00}	0.00	2

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1316	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12/2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	126.98	4
		1317	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12/2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	180.00	10
		1318	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSI (PGCIL) (N18000389)	2/2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	0.00	8
		1319	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8/2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	0.00	0
		1320	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8/2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	0.00	0
		1321	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8/2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	0.00	0
	<u>RAILWAYS</u>	1322	AGRA FORT-BANDIKUI (NCR) (N22000553)	6/2022	6/2027 (May-26) {5/2026}	1,389.81 (N.A.) {987.83}	4.10	11

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1323	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4/2019	3/2025 (N.A.) {3/2025}	528.48 (N.A.) {528.48}	331.74	70
		1324	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11/2021	11/2026 (N.A.) {12/2024}	466.42 (N.A.) {466.42}	582.74	72
		1325	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2/2023	2/2028 (N.A.) {1/2026}	422.60 (N.A.) {422.60}	124.09	38
		1326	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12/2022	6/2026 (N.A.) {12/2025}	304.00 (239.54) {239.54}	78.96	20
		1327	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1/2023	6/2028 (N.A.) {1/2027}	968.92 (N.A.) {968.92}	231.11	18
	ROAD TRANSPORT AND HIGHWAYS	1328	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT- RAMGARH BHADASAR-JA (NHAI) (N24000795)	2/2018	4/2021 (Dec-24) {12/2024}	741.86 (649.00) {649.00}	672.53	96
		1329	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER- NAGOUR SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241)	3/2020	10/2022 (Dec-24) {12/2024}	255.23 (N.A.) {255.23}	256.00	97
		1330	4L+PS OF NH -58 FROM BEAWAR- GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12/2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	233.62	92.75

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1331	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12/2021	5/2024 (N.A.) {12/2024}	411.40 (N.A.) {411.40}	162.61	55
		1332	WIDENING OF PACHPADRA- BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1/2022	12/2024 (N.A.) {12/2024}	194.88 (N.A.) {194.88}	104.69	69
		1333	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12/2021	8/2024 (N.A.) {12/2024}	451.66 (N.A.) {451.66}	401.78	97
		1334	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN- LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12/2021	9/2024 (N.A.) {3/2025}	150.11 (N.A.) {150.11}	57.83	63
		1335	4L GREENFIELD SPUR FROM DELHI- VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3/2022	11/2024 (Dec-24) {12/2024}	1,636.15 (N.A.) {1,636.15}	717.61	78.98
		1336	4L OF KARWAR (KM. 281.980 OF NH- 62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11/2021	8/2024 (Dec-24) {12/2024}	736.75 (N.A.) {736.75}	216.39	78.25
		1337	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE -0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9/2021	6/2024 (Jan-25) {1/2025}	672.35 (N.A.) {672.35}	392.43	94.25

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1338	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561)	10/2019	10/2023 (Nov-24) {11/2024}	839.63 (N.A.) {839.63}	213.85	100
		1339	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10/2019	8/2023 (Dec-24) {12/2024}	846.59 (N.A.) {846.59}	145.98	97.8
		1340	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10/2019	7/2023 (Dec-24) {12/2024}	662.08 (N.A.) {662.08}	110.81	96.5
		1341	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566)	11/2019	5/2023 (Nov-24) {11/2023}	1,640.10 (N.A.) {1,640.10}	1,159.50	100
		1342	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11/2019	10/2022 (Nov-24) {11/2024}	1,272.97 (N.A.) {1,272.97}	595.50	82.82
		1343	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11/2019	5/2023 (Nov-24) {11/2024}	1,119.35 (N.A.) {1,119.35}	1,435.93	99.8
		1344	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569)	11/2019	3/2023 (Jun-24) {6/2024}	1,425.02 (N.A.) {1,425.02}	1,386.89	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1345	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571)	11/2019	12/2023 (Nov-24) {11/2024}	1,341.36 (N.A.) {1,341.36}	1,085.98	99.65
		1346	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11/2019	12/2022 (Nov-24) {11/2024}	1,658.06 (N.A.) {1,658.06}	180.39	99.9
		1347	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7/2020	1/2024 (Sep-25) {9/2025}	1,788.69 (N.A.) {1,788.69}	823.67	68.81
		1348	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3/2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	72
		1349	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH- 248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3/2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	104.08	62
		1350	Sagwara Bypass and Garhi- Partapur Bypass of NH- 927A in the State of Rajasthan. (MoRTH) (N24001868)	3/2022	8/2025 (N.A.) {2/2025}	187.65 (N.A.) {187.65}	66.57	44
		1351	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12/2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	92.69	66

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1352	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2/2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	237.87	42
		1353	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3/2022	4/2025 (N.A.) {4/2025}	317.74 (N.A.) {317.74}	136.23	5
		1354	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8/2022	6/2024 (N.A.) {6/2025}	409.64 (N.A.) {409.64}	191.15	44.8
		1355	UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF HANUMANGARH TO KENCHIYAN OF NH 54 ON EPC MODE IN THE ST (MoRTH) (N24002167)	3/2024	10/2026 (N.A.) {10/2026}	334.64 (N.A.) {334.64}	0.00	0
		1356	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM NEECHLI ODEN (NATHDWARA) AT DESIGN KM 88.800 TO BHATE (MoRTH) (N24002168)	3/2023	10/2026 (N.A.) {10/2026}	606.61 (N.A.) {606.61}	0.00	0
SIKKIM	CIVIL AVIATION	1357	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11/2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	11.30	4.5
	DEPARTMENT OF HIGHER EDUCATION	1358	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8/2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>POWER</u>	1359	TEESTA VI HE PROJECT (NHPC) (N18000325)	3/2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,807.48	63.56
		1360	RANGIT IV HE PROJECT (NHPC) (N18000326)	3/2021	5/2024 (N.A.) {5/2025}	938.29 (N.A.) {1,871.23}	1,247.61	80.24
	<u>RAILWAYS</u>	1361	SEVOK RANGPO, NEFR (NFR) (N22000102)	4/2008	12/2015 (N.A.) {12/2023}	1,339.48 (N.A.) {7,876.92}	3,290.96	39.8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1362	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3/2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.54	95.26
		1363	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11/2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	100
		1364	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3/2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	238.46	73.11
		1365	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8/2020	4/2023 (Nov-24) {3/2025}	295.97 (N.A.) {295.97}	243.94	93.43
		1366	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3/2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1367	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8/2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	240.60	93.88
		1368	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7/2020	4/2023 (Aug-24) {3/2025}	345.38 (395.59) {395.59}	356.67	89.39
		1369	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9/2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.80	46.68
		1370	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9/2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17
		1371	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8/2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	184.85	50
		1372	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8/2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	200.82	77.2

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1373	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10/2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	272.34	40.46
		1374	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10/2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	278.65	36.42
		1375	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1/2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {332.20}	149.38	40.99
		1376	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12/2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	193.96	43.81
		1377	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10/2021	5/2024 (Jan-25) {1/2025}	385.15 (N.A.) {385.15}	167.49	78
		1378	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3/2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	0.00	71.74
TAMIL NADU	CIVIL AVIATION	1379	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6/2018	2/2022 (N.A.) {12/2025}	2,467.00 (N.A.) {2,467.00}	1,506.37	60

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1380	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8/2018	10/2021 (N.A.) {12/2023}	951.28 (N.A.) {1,112.49}	1,112.49	100
		1381	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6/2019	3/2022 (Dec-24) {12/2024}	380.87 (N.A.) {452.93}	323.27	93
	COAL	1382	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12/2021	3/2025 (N.A.) {3/2025}	297.88 (N.A.) {297.88}	45.15	20
	FINANCE	1383	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11/2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100
	MINES	1384	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9/2017	6/2019 (Mar-24) {12/2024}	166.62 (163.17) {163.17}	135.63	65
	PETROLEUM	1385	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11/2012	2/2017 (Oct-25) {10/2025}	678.00 (1,732.00) {1,732.00}	532.06	42.6
		1386	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE (IOCL) (N16000253)	5/2016	12/2018 (Mar-25) {3/2025}	4,497.00 (6,025.00) {6,025.00}	5,519.37	100
		1387	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI (IOCL) (N16000403)	10/2020	9/2023 (Dec-24) {12/2024}	921.00 (N.A.) {921.00}	729.00	94.5

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1388	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI (IOCL) (N16000405)	10/2020	12/2023 (Dec-24) {12/2024}	1,398.00 (1,587.00) {1,587.00}	1,219.00	95
		1389	CBR 9 MMTA PROJECT (CPCL) (N16000434)	1/2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,260.94	10.2
		1390	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1/2022	7/2024 (Dec-24) {6/2025}	827.00 (887.71) {887.71}	493.84	75
		1391	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE (IOCL) (N16000451)	3/2022	11/2024 (N.A.) {11/2024}	564.00 (N.A.) {564.00}	144.55	35.67
		1392	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1/2022	7/2024 (May-26) {5/2026}	829.00 (N.A.) {829.00}	209.56	52.66
		1393	EXTENSION OF ASANUR-SANKARI SECTION OF CHENNAI-TRICHY- MADURAI PIPELINE UPTO COIMBATORE (IRUGUR) (IOCL) (N16000479)	1/2023	1/2025 (N.A.) {1/2025}	346.70 (N.A.) {346.70}	0.72	17.25
		1394	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3/2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	87.44	4
		1395	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS (IOCL) (N16000490)	3/2022	3/2030 (N.A.) {12/2030}	1,328.00 (N.A.) {1,328.00}	138.80	4.4

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1396	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS (IOCL) (N16000492)	3/2022	3/2030 (N.A.) {12/2030}	1,295.00 (N.A.) {1,295.00}	135.92	4.6
		1397	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12/2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	89.61	4.9
	RAILWAYS	1398	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (M RTP) (N22000028)	4/2006	6/2013 (Dec-24) {12/2024}	495.74 (N.A.) {734.01}	631.34	98
		1399	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9/2006	(Dec-26) {3/2027}	582.83 (3,631.34) {3,631.34}	779.31	10
		1400	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3/2022	3/2026 (Dec-24) {12/2024}	359.60 (274.20) {274.20}	231.05	80
		1401	MORAPPUR-DHARMAPURI (SR) (N22000618)	2/2019	3/2028 (Mar-27) {3/2027}	358.95 (N.A.) {358.95}	37.70	1
		1402	KARAIKAL PERALAM(23KM)-NEW LINE PROJECT (SR) (N22000625)	1/2019	3/2026 (Dec-24) {12/2024}	304.22 (N.A.) {373.42}	232.47	75
		1403	NAGAPATTINAM THIRUTURAIPUNDI (38KM)- NEW LINE PROJECT (SR) (N22000626)	7/2008	3/2026 (Mar-27) {3/2027}	677.12 (N.A.) {788.05}	129.22	18
	ROAD TRANSPORT AND HIGHWAYS	1404	FOUR LANNING OF VIKRAVANDI- SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. (NHAI) (N24000652)	3/2017	3/2020 (May-24) {5/2024}	848.45 (N.A.) {848.45}	303.04	48.26

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1405	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8/2017	9/2020 (Sep-24) {9/2024}	1,176.37 (N.A.) {1,176.37}	1,325.06	97.5
		1406	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9/2017	8/2020 (Nov-24) {11/2024}	1,227.87 (N.A.) {1,227.87}	1,333.76	91.05
		1407	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3/2018	10/2022 (Jan-24) {1/2024}	505.35 (N.A.) {837.69}	376.61	99.75
		1408	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) (NHAI) (N24000827)	3/2018	11/2020 (Apr-23) {4/2023}	628.71 (N.A.) {756.13}	583.02	100
		1409	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428)	3/2018	11/2021 (Dec-24) {12/2024}	998.70 (1,358.32) {1,358.32}	872.68	97.34
		1410	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3/2018	11/2021 (Dec-24) {12/2024}	1,294.47 (1,588.40) {1,588.40}	854.65	96.3
		1411	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3/2018	1/2022 (Dec-24) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,464.94	99.8

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1412	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3/2018	10/2020 (Aug-25) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,274.82	52.6
		1413	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2/2022	8/2022 (N.A.) {10/2024}	191.33 (N.A.) {191.33}	185.78	88
		1414	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10/2020	5/2023 (Dec-24) {12/2024}	434.12 (N.A.) {434.12}	258.89	99.3
		1415	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH- 209 (NHAI) (N24001601)	1/2019	1/2023 (Jun-25) {6/2025}	1,051.69 (N.A.) {1,051.69}	552.46	76.73
		1416	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1/2019	12/2022 (Nov-25) {11/2025}	1,409.38 (N.A.) {1,409.38}	623.22	86.08
		1417	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH- 209 (NEW NH-83) (NHAI) (N24001603)	1/2019	10/2022 (Dec-23) {12/2023}	1,518.53 (N.A.) {1,607.54}	915.40	100
		1418	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS (NHAI) (N24001604)	2/2019	3/2021 (N.A.) {10/2023}	166.90 (N.A.) {166.90}	121.94	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1419	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH-383 (NHAI) (N24001605)	6/2018	3/2022 (N.A.) {1/2025}	1,103.86 (N.A.) {1,103.86}	461.32	70.06
		1420	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH- 744A (MADURAI RING ROAD) (NHAI) (N24001606)	12/2018	3/2022 (Jun-25) {6/2025}	854.94 (N.A.) {854.94}	334.05	66.66
		1421	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1/2022	9/2024 (N.A.) {9/2024}	467.99 (N.A.) {468.00}	18.83	12.2
		1422	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9/2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	0
		1423	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2/2019	12/2023 (Dec-24) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	0
		1424	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH- 844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2/2019	8/2023 (Dec-24) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	0
		1425	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7/2022	8/2023 (Dec-24) {12/2024}	186.50 (210.81) {210.81}	12.92	90

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1426	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11/2020	8/2024 (N.A.) {3/2025}	1,155.49 (1,458.45) {1,458.45}	485.62	52.39
		1427	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12/2020	7/2024 (N.A.) {3/2025}	843.48 (1,051.36) {1,051.36}	389.23	88.02
		1428	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2/2021	7/2024 (N.A.) {7/2025}	2,948.31 (3,516.83) {3,516.83}	728.20	65.78
		1429	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10/2020	5/2024 (N.A.) {3/2025}	1,023.91 (1,341.51) {1,341.51}	574.44	72.41
		1430	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2/2019	5/2024 (Aug-25) {8/2025}	1,008.99 (1,360.53) {1,360.53}	167.67	38.5
		1431	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11/2021	2/2023 (N.A.) {11/2024}	463.44 (463.07) {463.44}	331.22	98.5
		1432	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10/2018	2/2021 (N.A.) {3/2025}	707.90 (766.51) {766.51}	441.67	82.85

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1433	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1/2019	5/2021 (N.A.) {3/2026}	819.89 (1,314.82) {922.85}	384.20	57.32
		1434	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1/2022	11/2024 (N.A.) {11/2024}	221.03 (243.95) {243.95}	131.16	70
		1435	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10/2022	11/2024 (N.A.) {11/2024}	172.15 (N.A.) {172.15}	120.23	78.5
		1436	CONSTRUCTION OF STRR (WEST SIDE)-NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4/2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	453.63	44.26
		1437	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3/2022	2/2025 (N.A.) {3/2025}	1,076.97 (N.A.) {1,076.97}	325.73	64.01
		1438	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3/2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	0
		1439	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3/2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1440	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3/2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	0
		1441	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3/2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	0
		1442	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH- 332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2/2019	12/2025 (Dec-25) {12/2025}	825.94 (1,116.13) {1,116.13}	157.89	25.84
		1443	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH- 138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3/2023	7/2024 (N.A.) {1/2025}	200.30 (N.A.) {200.30}	57.34	67.11
		1444	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3/2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	197.80	23.72
		1445	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2/2022	4/2025 (N.A.) {4/2025}	1,097.59 (N.A.) {1,317.06}	564.93	78.95

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1446	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3/2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {294.70}	111.53	30
		1447	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3/2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	165.73	58
		1448	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3/2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	53.13	35
		1449	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3/2022	8/2026 (N.A.) {8/2026}	238.97 (260.07) {238.97}	34.51	5
	URBAN DEVELOPMENT	1450	CHENNAI METRO RAIL LTD (PHASE 1) (CMRL) (N28000084)	2/2009	12/2015 (N.A.) {12/2015}	14,600.00 (N.A.) {18,380.00}	17,619.68	100
		1451	CHENNAI METRO RAIL LTD (PHASE 1 EXT) (CMRL) (N28000097)	6/2016	3/2018 (N.A.) {2/2021}	3,770.00 (N.A.) {3,770.00}	2,527.73	100
TELANGANA	CIVIL AVIATION	1452	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5/2020	5/2022 (Jun-23) {6/2023}	353.61 (N.A.) {353.61}	303.22	100
	COAL	1453	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 (SCCL) (N06000161)	3/2017	3/2022 (N.A.) {3/2025}	413.84 (N.A.) {413.84}	379.13	60

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1454	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7/2019	3/2023 (N.A.) {3/2025}	438.98 (N.A.) {438.98}	155.37	68
		1455	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10/2020	3/2023 (N.A.) {3/2026}	484.51 (N.A.) {484.51}	167.03	30
		1456	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11/2015	3/2023 (N.A.) {3/2025}	489.62 (N.A.) {489.62}	405.54	70
		1457	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8/2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	399.96	80
		1458	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3/2016	3/2020 (N.A.) {3/2025}	384.32 (N.A.) {384.32}	246.00	75
		1459	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8/2017	3/2020 (N.A.) {3/2025}	442.42 (N.A.) {442.42}	200.67	63
		1460	GOLETI OPENCAST MINE (SCCL) (N06000258)	7/2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	55.12	18
	<u>HEALTH AND FAMILY WELFARE</u>	1461	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12/2018	7/2024 (N.A.) {3/2025}	1,110.55 (N.A.) {1,110.55}	623.74	0
		1462	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10/2016	3/2020 (Jan-25) {1/2025}	209.84 (281.05) {281.05}	251.51	97.5
	<u>POWER</u>	1463	TELANGANA SUPER THERMAL POWER PROJECT PHASE I (NTPC) (N18000212)	1/2016	11/2020 (N.A.) {2/2024}	10,598.98 (N.A.) {10,998.00}	10,437.71	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	1464	MANOHARABAD-KOTHPALL NEW LINE(SCR) (<i>SCR</i>) (N22000032)	4/2006	3/2010 (N.A.) {3/2025}	1,160.48 (N.A.) {3,014.00}	1,344.94	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1465	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (<i>MoRTH</i>) (N24000245)	1/2014	3/2016 (Sep-19) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15
		1466	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (<i>MoRTH</i>) (N24000247)	10/2014	2/2017 (Dec-22) {3/2025}	295.47 (N.A.) {295.47}	224.42	98.51
		1467	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (<i>MoRTH</i>) (N24000248)	3/2015	1/2017 (N.A.) {12/2023}	153.21 (N.A.) {153.21}	101.15	93.11
		1468	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (<i>MoRTH</i>) (N24000980)	10/2016	2/2019 (Jun-22) {8/2024}	298.32 (N.A.) {298.32}	178.47	98
		1469	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (<i>MoRTH</i>) (N24000981)	10/2016	3/2019 (Apr-23) {8/2024}	248.83 (N.A.) {248.83}	173.82	100
		1470	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE (<i>MoRTH</i>) (N24000982)	1/2017	5/2019 (Aug-19) {8/2019}	244.54 (N.A.) {244.54}	176.32	99.9

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1471	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1/2017	10/2019 (Oct-19) {2/2024}	196.52 (N.A.) {196.52}	125.53	95.7
		1472	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1/2017	12/2019 (Dec-19) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.3
		1473	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1/2017	5/2019 (Jul-21) {1/2024}	300.00 (N.A.) {300.00}	242.86	96.05
		1474	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1/2018	5/2020 (Dec-22) {8/2024}	283.15 (N.A.) {283.15}	278.69	92.59
		1475	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1/2018	12/2019 (Nov-20) {11/2020}	230.03 (N.A.) {230.03}	231.34	99.9
		1476	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2/2018	6/2020 (Jan-21) {1/2021}	206.13 (N.A.) {206.13}	190.94	98.36

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1477	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2/2018	11/2019 (Mar-22) {1/2024}	294.13 (N.A.) {294.13}	200.10	87.44
		1478	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3/2018	9/2020 (Jun-22) {6/2023}	322.81 (N.A.) {322.81}	317.05	98.09
		1479	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3/2018	7/2020 (Jun-24) {2/2026}	626.76 (N.A.) {626.76}	282.78	44.3
		1480	REHABILITATION AND UP- GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1/2017	10/2019 (Oct-19) {6/2021}	605.08 (N.A.) {605.08}	416.32	99.84
		1481	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3/2018	7/2019 (Jun-22) {8/2024}	192.67 (N.A.) {192.67}	176.37	92
		1482	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1/2019	(Jan-23) {8/2024}	193.19 (249.72) {249.72}	224.10	95

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1483	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8/2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	452.54	57.12
		1484	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUEM V (NHAI) (N24001483)	2/2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	324.52	56.5
		1485	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9/2022	2/2024 (Dec-24) {12/2024}	804.69 (N.A.) {804.69}	417.59	60.49
		1486	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1/2021	1/2024 (Dec-24) {12/2024}	1,307.95 (N.A.) {1,307.95}	586.56	96.41
		1487	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3/2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	175.60	28.39
		1488	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12/2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	222.40	43.7

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1489	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1/2022	1/2025 (N.A.) {7/2025}	1,227.57 (N.A.) {1,227.57}	288.58	30.51
		1490	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2/2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	368.38	42.27
		1491	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3/2021	7/2024 (N.A.) {8/2024}	317.19 (N.A.) {317.19}	164.72	67
		1492	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1/2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	255.05	56.17
		1493	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1/2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	198.05	63.8
		1494	REHABILITATION AND UP- GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1/2022	12/2024 (N.A.) {3/2025}	549.28 (N.A.) {549.28}	173.25	56.79

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1495	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3/2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	292.55	67.08
		1496	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3/2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	212.33	63.5
		1497	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10/2017	6/2023 (N.A.) {12/2024}	186.71 (N.A.) {186.71}	177.53	85.75
		1498	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3/2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	147.22	43.44
		1499	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET- ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1/2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	172.76	70
		1500	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1/2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	249.04	48.53

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1501	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR- CHINCHOLI SECTION (MoRTH) (N24002010)	3/2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	45.12	17.65
		1502	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2/2022	9/2024 (N.A.) {9/2024}	541.58 (N.A.) {541.58}	20.82	0
		1503	FOUR LANING OF KARIMNAGAR- WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3/2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,413.00}	741.05	50.21
		1504	CONSTRUCTION OF 4-LANE ACCESS CONTROLLED GREENFIELD HIGHWAY SECTION ON NH-163G (KHAMMAM- VIJAYAWADA) (NHAI) (N24002190)	3/2023	8/2026 (N.A.) {8/2026}	983.00 (N.A.) {983.00}	0.00	0
TRIPURA	PETROLEUM	1505	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6/2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	308.81	65.6
	ROAD TRANSPORT AND HIGHWAYS	1506	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT- KAILASHAHAR SECTION (NHIDCL) (N24001263)	6/2020	1/2022 (Feb-24) {11/2024}	277.50 (302.02) {302.02}	253.50	99.2
		1507	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11/2020	6/2022 (Oct-23) {10/2024}	159.13 (171.50) {171.50}	81.51	99.39

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1508	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6/2020	1/2022 (Jul-24) {11/2024}	201.99 (287.47) {287.47}	144.07	95.5
		1509	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 (NHIDCL) (N24001318)	9/2020	4/2022 (Oct-22) {10/2023}	173.17 (N.A.) {173.17}	93.35	100
		1510	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3/2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2
		1511	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2/2022	1/2025 (N.A.) {1/2025}	456.88 (N.A.) {456.88}	95.50	39.93
		1512	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5/2023	11/2024 (N.A.) {2/2025}	195.95 (N.A.) {195.95}	15.55	18.53
		1513	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3/2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	1.45
		1514	REHABILITATION AND UP- GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGH: 11.210 KM) (NHIDCL) (N24002159)	2/2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	0.00	0.02
		1515	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1/2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	0.00	0.54

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
UTTAR PRADESH		1516	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1/2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	8.31	5
		1517	KHOWAI ?TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1/2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
	CIVIL AVIATION	1518	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6/2018	9/2021 (Oct-26) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,125.02	76.29
		1519	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3/2021	12/2022 (Nov-24) {11/2024}	242.14 (328.00) {358.00}	338.51	99.9
		1520	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5/2023	11/2024 (N.A.) {12/2024}	185.75 (232.52) {232.52}	98.02	51
		1521	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6/2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	0.00	0
		1522	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7/2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	0.00	0
	COAL	1523	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7/2016	11/2021 (Mar-25) {6/2025}	17,237.00 (19,406.12) {19,406.12}	18,538.02	86.72
		1524	KHADIA EXPANSION OCP (NCL) (N06000208)	6/2021	3/2025 (N.A.) {3/2026}	491.67 (N.A.) {491.67}	44.54	5.2

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HOME AFFAIRS</u>	1525	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI (CPWD FOR MHA) (N45000003)	5/2019	1/2022 (Mar-23) {3/2023}	199.31 (N.A.) {199.31}	86.49	85
	<u>PETROLEUM</u>	1526	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3/2019	4/2024 (Apr-24) {3/2025}	910.56 (1,299.02) {1,299.02}	831.40	91.4
		1527	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4/2022	4/2025 (Dec-26) {12/2026}	260.12 (N.A.) {260.12}	0.97	18.4
		1528	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9/2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	131.85	35.6
		1529	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12/2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	284.46	4.6
	<u>POWER</u>	1530	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3/2019	9/2023 (N.A.) {3/2025}	11,089.42 (N.A.) {13,129.25}	11,283.16	92.7
		1531	KALPI SOLAR POWER PROJECT (NHPC) (N18000323)	7/2020	3/2022 (Mar-24) {3/2024}	314.64 (N.A.) {350.46}	325.57	92
		1532	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (BHEL) (N18000382)	3/2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	531.00	0
	<u>RAILWAYS</u>	1533	VARANASI-MODHOSINGH- ALLAHABAD DOUBLING (RVNL) (N22000401)	4/2015	3/2022 (N.A.) {12/2024}	943.60 (N.A.) {2,018.23}	1,780.22	0
		1534	RAMNA - SINGRAULI DOUBLING (ECR) (N22000417)	8/2015	3/2020 (N.A.) {9/2024}	2,436.21 (2,880.40) {2,880.40}	2,930.49	90

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1535	KARAILA ROAD - SHAKTINAGAR DOUBLING (<i>ECR</i>) (N22000419)	8/2015	3/2019 (N.A.) {8/2024}	528.57 (762.97) {762.97}	780.34	90
		1536	BURHWAL - GONDA - 3RD RUNNING LINE. (<i>NER</i>) (N22000468)	4/2016	(N.A.) {9/2025}	602.50 (N.A.) {1,015.59}	906.06	48
		1537	SHAHGANJ-BHATNI-PHEPHNA- INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (<i>NER</i>) (N22000470)	4/2016	12/2019 (N.A.) {12/2024}	1,177.96 (N.A.) {1,777.39}	1,734.71	76
		1538	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (<i>NCR</i>) (N22000495)	3/2018	3/2023 (Mar-27) {3/2027}	4,329.53 (N.A.) {4,329.53}	1,291.69	32
		1539	JHANSI BINA DOUBLING (<i>NCR</i>) (N22000496)	9/2016	3/2021 (Mar-27) {3/2027}	2,001.00 (N.A.) {2,001.00}	1,671.51	85
		1540	MATHURA-JHANSI-3RD LINE (273.80 KM) (<i>RVNL</i>) (N22000501)	6/2016	12/2023 (N.A.) {12/2024}	3,677.76 (N.A.) {5,190.26}	5,046.07	0
		1541	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (<i>ECR</i>) (N22000525)	10/2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	0
		1542	MUGHALSARAI - ALLAHABAD - 3RD LINE (<i>NCR</i>) (N22000544)	8/2019	12/2026 (N.A.) {12/2026}	2,390.00 (N.A.) {2,390.00}	83.10	55
		1543	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (<i>NCR</i>) (N22000545)	4/2020	6/2026 (N.A.) {6/2026}	1,456.89 (1,244.13) {1,456.89}	0.00	8
		1544	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (<i>NCR</i>) (N22000546)	3/2017	12/2024 (Jun-25) {6/2025}	260.00 (356.00) {356.00}	147.52	45

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1545	ALIGARH-DAUD KHAN - 3RD LINE 6.9 KM AND CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4/2019	12/2025 (N.A.) {12/2025}	451.99 (779.49) {779.49}	0.00	30
		1546	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4/2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	0.00	42
		1547	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4/2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.75	0
		1548	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8/2019	3/2029 (N.A.) {6/2027}	371.77 (N.A.) {1,319.75}	409.88	1
		1549	BAHRAICH - NANPARA -NEPALGANJ (56.15 KM) (NER) (N22000566)	7/2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	126.04	18
		1550	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10/2018	10/2030 (N.A.) {12/2026}	1,600.00 (N.A.) {4,939.78}	997.61	5
		1551	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11/2017	3/2025 (N.A.) {3/2025}	701.98 (N.A.) {1,100.00}	0.00	0
		1552	BARABANKI-MALHAUR - 3RD & 4TH LINE (32.84 KM) (NR) (N22000590)	1/2019	3/2025 (N.A.) {3/2025}	323.85 (N.A.) {323.85}	0.00	0
		1553	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3/2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.00	0
		1554	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11/2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	362.09	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1555	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5/2018	3/2024 (N.A.) {2/2025}	1,177.96 (N.A.) {2,529.46}	1,636.33	0
		1556	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8/2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	0
		1557	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11/2016	6/2024 (N.A.) {5/2025}	186.85 (N.A.) {470.47}	442.90	85
	ROAD TRANSPORT AND HIGHWAYS	1558	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12/2019	4/2022 (N.A.) {12/2024}	282.41 (N.A.) {319.96}	271.03	83
		1559	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE- IV] (NHAI) (N24000551)	3/2016	4/2019 (Dec-24) {12/2024}	1,587.49 (3,473.59) {3,500.00}	3,356.11	95.75
		1560	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH- 24) TO KM 42.791 (NHAI) (N24000556)	3/2016	4/2019 (Nov-24) {11/2024}	899.00 (1,623.88) {1,623.88}	1,134.40	92.15
		1561	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3/2016	7/2020 (Mar-25) {3/2025}	1,408.00 (1,659.12) {1,659.12}	1,207.12	80.38

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1562	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3/2018	12/2021 (Dec-23) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,198.22	99.66
		1563	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3/2018	11/2021 (N.A.) {12/2024}	2,140.93 (N.A.) {2,140.93}	2,063.06	97.94
		1564	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH ? 14 (NHAI) (N24001185)	11/2017	7/2021 (Dec-24) {12/2024}	2,159.00 (2,262.00) {2,262.00}	2,249.93	97.5
		1565	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10/2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	84.92
		1566	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7/2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	966.06	70
		1567	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT (MoRTH) (N24001423)	4/2021	9/2023 (N.A.) {3/2026}	309.48 (N.A.) {309.48}	112.99	51

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1568	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3/2021	9/2023 (N.A.) {12/2024}	185.09 (269.81) {269.81}	261.90	96
		1569	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4/2020	2/2024 (N.A.) {11/2024}	199.39 (212.96) {199.39}	154.01	94
		1570	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4/2020	7/2024 (N.A.) {3/2025}	172.50 (169.56) {172.50}	94.30	61
		1571	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4/2020	3/2024 (N.A.) {12/2024}	236.47 (N.A.) {236.47}	129.32	81
		1572	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4/2020	7/2024 (N.A.) {12/2024}	211.09 (N.A.) {211.09}	118.93	84
		1573	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 (MoRTH) (N24001463)	4/2020	7/2024 (N.A.) {2/2024}	294.84 (309.99) {294.84}	287.37	100
		1574	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3/2021	8/2023 (N.A.) {1/2025}	264.86 (N.A.) {264.86}	106.25	73

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1575	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11/2021	5/2024 (N.A.) {3/2025}	307.11 (N.A.) {307.11}	172.40	75
		1576	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH- 730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4/2020	11/2024 (N.A.) {11/2024}	325.24 (340.16) {325.24}	220.97	83
		1577	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3/2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	256.82	57
		1578	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH- 334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10/2021	4/2024 (N.A.) {12/2024}	227.06 (N.A.) {227.06}	119.19	88
		1579	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO (NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3/2021	10/2023 (Dec-24) {12/2024}	836.24 (N.A.) {836.24}	780.44	98.57
		1580	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3/2021	10/2023 (Dec-24) {12/2024}	990.28 (N.A.) {990.28}	997.51	98.89

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1581	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3/2020	9/2024 (N.A.) {12/2024}	262.37 (343.77) {343.77}	240.47	68
		1582	4L SPUR OF SHAMLI- MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI- MUZAFFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1/2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	78.5
		1583	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3/2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	423.87	68.5
		1584	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12/2021	7/2025 (N.A.) {7/2025}	1,138.81 (N.A.) {1,138.81}	307.88	91.41
		1585	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZAFFARNAGAR) AND NH-709A (KARN (NHAI) (N24001729)	8/2022	4/2024 (N.A.) {12/2024}	326.79 (N.A.) {329.79}	97.49	79.11
		1586	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12/2021	1/2025 (N.A.) {1/2025}	1,384.79 (N.A.) {1,384.79}	657.86	97

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1587	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12/2021	5/2025 (May-25) {5/2025}	2,470.64 (N.A.) {2,335.00}	523.01	65.84
		1588	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12/2021	10/2024 (N.A.) {4/2025}	540.97 (N.A.) {540.97}	205.31	66.86
		1589	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.- MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3/2022	8/2024 (N.A.) {12/2024}	1,602.48 (N.A.) {1,602.48}	359.95	75.5
		1590	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3/2022	8/2024 (N.A.) {12/2024}	1,335.45 (N.A.) {1,335.45}	357.70	70.5
		1591	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL-LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3/2022	8/2024 (N.A.) {12/2024}	1,428.19 (N.A.) {1,428.19}	432.66	71
		1592	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1/2022	8/2024 (N.A.) {12/2024}	1,159.96 (N.A.) {1,159.96}	510.48	98
		1593	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11/2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	97.62

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1594	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9/2021	10/2023 (Dec-24) {12/2024}	300.79 (N.A.) {300.79}	122.56	66.5
		1595	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10/2019	11/2023 (Dec-24) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,044.00	99.15
		1596	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5/2019	11/2022 (N.A.) {12/2024}	779.17 (N.A.) {779.17}	54.69	95.5
		1597	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12/2021	7/2025 (Jul-25) {7/2025}	1,972.10 (N.A.) {1,936.00}	431.50	55.14
		1598	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3/2021	4/2024 (Jan-25) {1/2025}	364.47 (N.A.) {364.47}	133.55	67.3
		1599	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2/2022	6/2024 (Nov-24) {11/2024}	570.98 (578.02) {578.02}	342.45	80.35
		1600	SPUR OF MEERUT-GARH- MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1/2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	43.06

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1601	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10/2019	3/2023 (Dec-24) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	98.8
		1602	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8/2021	3/2024 (Dec-24) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	36
		1603	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12/2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	51.2
		1604	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2/2019	2/2022 (Dec-24) {12/2024}	927.77 (N.A.) {1,603.00}	1,202.77	79.45
		1605	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6/2020	11/2023 (Dec-24) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99
		1606	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1/2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	741.68	65

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1607	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10/2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	651.03	85
		1608	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10/2021	9/2024 (Mar-25) {9/2024}	772.05 (N.A.) {772.05}	553.91	67
		1609	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1/2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	254.40	64
		1610	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8/2022	2/2024 (Nov-24) {11/2024}	199.31 (199.38) {199.38}	130.59	65.4
		1611	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH-731B ON (MoRTH) (N24001996)	3/2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	346.24	44
		1612	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH- 730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10/2022	5/2025 (N.A.) {5/2025}	189.31 (N.A.) {189.31}	50.71	15

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1613	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11/2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	90.91	18
		1614	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH-330 (MoRTH) (N24002016)	10/2022	6/2025 (N.A.) {6/2025}	225.17 (N.A.) {225.17}	94.39	43
		1615	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH- 731B ON EPC MODE (MoRTH) (N24002029)	3/2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	483.86	24
		1616	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12/2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	349.53	8
		1617	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDER FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1/2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	241.12	24
		1618	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4/2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	774.19	33

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1619	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10/2019	10/2023 (N.A.) {6/2024}	2,068.99 (2,171.00) {2,171.00}	209.60	47.4
		1620	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11/2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	16.37
		1621	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10/2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	688.34	40.3
		1622	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10/2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	45.30	21
		1623	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10/2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	474.79	26.28
		1624	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10/2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	95.37	40

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1625	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR-RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3/2021	11/2024 (Apr-25) {4/2025}	646.27 (N.A.) {646.27}	45.12	20.85
		1626	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10/2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	219.02	28.2
		1627	IMPROVEMENT AND UP- GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9/2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	296.13	16.17
		1628	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12/2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	770.48	36.77
		1629	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2/2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	545.40	23.01
		1630	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 ((NHAI) (N24002097)	2/2023	9/2025 (N.A.) {3/2025}	526.45 (N.A.) {526.45}	139.37	62.1

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1631	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1/2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	218.15	14.5
		1632	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8/2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	100.15	15.5
		1633	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8/2023	3/2025 (N.A.) {3/2025}	993.77 (N.A.) {349.48}	180.56	55.1
		1634	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3/2023	8/2025 (N.A.) {8/2025}	438.24 (362.39) {438.24}	169.48	12
		1635	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1/2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	46.94	19
		1636	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 () (MoRTH) (N24002120)	2/2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	76.74	48

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1637	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1/2022	9/2025 (N.A.) {9/2025}	509.65 (N.A.) {509.65}	135.93	12
		1638	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ ? NICHLOUL ? TH (MoRTH) (N24002134)	3/2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	152.15	0
		1639	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3/2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	216.82	7
		1640	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12/2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	120.11	0
	URBAN DEVELOPMENT	1641	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5/2019	3/2024 (N.A.) {6/2026}	11,076.48 (N.A.) {11,076.48}	7,845.03	66.8
		1642	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5/2019	3/2024 (N.A.) {12/2025}	8,379.62 (N.A.) {8,379.62}	4,101.50	44.6
	WATER RESOURCES	1643	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UPJalNigam) (N30000006)	5/2017	9/2021 (N.A.) {6/2023}	767.59 (N.A.) {767.59}	276.97	100
		1644	FARRUKHABAD I AND D AND STP WORKS HAM (UPJalNigam) (N30000008)	10/2017	3/2022 (Feb-21) {11/2024}	213.62 (261.12) {261.12}	177.62	95

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1645	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UPJalNigam) (N30000010)	3/2018	9/2021 (N.A.) {7/2023}	967.23 (708.70) {967.23}	254.98	100
		1646	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UPJalNigam) (N30000013)	3/2019	8/2021 (N.A.) {7/2024}	271.39 (N.A.) {271.39}	182.26	100
		1647	MATHURA SEWERAGE SCHEME (UPJalNigam) (N30000019)	12/2017	12/2020 (Jun-18) {6/2022}	460.45 (N.A.) {460.45}	315.30	100
		1648	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1/2019	12/2021 (Jan-20) {12/2024}	231.79 (234.03) {234.03}	141.79	96
		1649	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UPJalNigam) (N30000022)	1/2019	10/2021 (N.A.) {7/2023}	206.05 (N.A.) {206.05}	139.86	100
		1650	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2/2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	0
		1651	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UPJalNigam) (N30000025)	3/2019	7/2021 (May-20) {9/2024}	298.12 (N.A.) {240.93}	94.86	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
UTTARAKHAND	<u>CIVIL AVIATION</u>	1652	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7/2018	9/2020 (N.A.) {9/2024}	456.86 (N.A.) {500.00}	483.59	100
	<u>POWER</u>	1653	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7/2006	2/2016 (Jun-22) {8/2025}	1,657.00 (4,825.60) {7,686.32}	7,121.33	97.7
		1654	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11/2006	3/2013 (N.A.) {4/2029}	2,978.48 (N.A.) {7,103.00}	6,298.38	75
		1655	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8/2008	6/2013 (N.A.) {6/2026}	2,491.58 (3,860.35) {6,303.00}	4,137.59	68.6
		1656	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7/2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	0
	<u>RAILWAYS</u>	1657	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4/2011	12/2024 (N.A.) {3/2025}	16,216.00 (N.A.) {24,659.00}	18,820.04	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1658	4-LANING OF KASHIPUR- SITARGANJ SECTION (MEGA) (N24000465)	11/2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	0
		1659	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHAI) (N24000559)	3/2016	10/2019 (Nov-24) {11/2024}	720.00 (1,150.00) {1,150.00}	644.24	94.56
		1660	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3/2018	11/2020 (Dec-22) {3/2024}	274.31 (N.A.) {274.31}	251.61	99

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1661	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3/2018	11/2020 (Dec-22) {3/2024}	403.36 (N.A.) {403.36}	337.72	95.91
		1662	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3/2018	11/2020 (Dec-22) {3/2024}	417.24 (N.A.) {417.24}	344.20	98.72
		1663	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12/2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100
		1664	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12/2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100
		1665	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12/2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100
		1666	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6/2017	6/2019 (Mar-23) {3/2023}	282.08 (N.A.) {282.08}	234.97	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1667	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11/2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100
		1668	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11/2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100
		1669	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11/2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100
		1670	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2/2018	2/2020 (Mar-23) {3/2023}	418.88 (N.A.) {418.88}	339.71	94
		1671	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2/2018	(Apr-23) {4/2023}	293.68 (N.A.) {293.68}	244.25	100
		1672	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5/2018	5/2020 (Dec-23) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1673	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3/2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	0
		1674	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3/2018	7/2022 (Jul-22) {1/2026}	1,383.78 (N.A.) {1,383.78}	597.48	61.66
		1675	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8/2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100
		1676	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3/2021	3/2024 (Dec-24) {12/2024}	169.08 (N.A.) {169.08}	94.67	98.87
		1677	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8/2021	10/2024 (Oct-24) {10/2024}	1,377.79 (1,384.11) {1,377.79}	679.10	46.81
		1678	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3/2022	2/2025 (Feb-25) {2/2025}	1,092.90 (1,092.90) {1,092.90}	461.92	60.5
		1679	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6/2022	5/2025 (May-25) {5/2025}	524.54 (683.26) {683.26}	74.94	50.6

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1680	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5/2022	9/2024 (May-25) {5/2025}	314.31 (N.A.) {314.31}	150.55	54.5
		1681	4L OF DUDHADHARI ELEVATED FLYOVER (MUZAFFARNAGAR ?HARIDWAR SECTION) FROM KM 356.450 TO KM 353.800 OF (NHAI) (N24001995)	5/2021	11/2023 (Dec-24) {12/2024}	154.52 (N.A.) {154.52}	150.26	100
		1682	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00- UTTARAKHAND-TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12/2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	0.00	5
		1683	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00- UTTARAKHAND-TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12/2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	0.00	5
	<u>WATER RESOURCES</u>	1684	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UKJalNigam) (N30000004)	3/2017	11/2019 (N.A.) {2/2022}	158.00 (N.A.) {158.00}	105.88	100
<u>WEST BENGAL</u>	<u>CIVIL AVIATION</u>	1685	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA (AAI) (N04000080)	1/2016	3/2020 (Jun-22) {12/2023}	458.00 (N.A.) {458.00}	246.68	100
		1686	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1/2019	11/2021 (N.A.) {5/2023}	389.71 (N.A.) {397.00}	396.49	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1687	NSCBI AIRPORT KOLKATA: RE- CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4/2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	52.94	25
		1688	BAGDOGRA AIRPORT: DEVELOPMENT OF NEW CIVIL ENCLAVE AT BAGDOGRA AIRPORT. SUB-HEAD : CONSTRUCTION OF N (AAI) (N04000115)	8/2024	3/2027 (N.A.) {3/2027}	1,549.00 (N.A.) {1,549.00}	29.46	0.3
	COAL	1689	RANIGANJ MASTER PLAN (ECL) (N06000163)	8/2009	8/2019 (N.A.) {8/2024}	2,661.73 (N.A.) {5,146.48}	765.22	40.5
		1690	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5/2018	3/2026 (N.A.) {3/2026}	535.18 (N.A.) {535.17}	4.22	13.2
		1691	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8/2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	58.93	25.3
		1692	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4/2020	3/2025 (Mar-26) {3/2026}	483.65 (N.A.) {483.65}	32.96	12
		1693	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12/2015	3/2017 (N.A.) {11/2024}	341.22 (341.22) {341.22}	322.21	94
		1694	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7/2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	516.46	17
		1695	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4/2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	404.50	38
		1696	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11/2020	3/2025 (Mar-26) {3/2026}	888.99 (N.A.) {888.99}	93.00	30

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1697	BONJEME HARI EXPANSION OCP (ECL) (N06000244)	8/2021	3/2025 (Mar-26) {3/2026}	570.12 (N.A.) {570.11}	53.07	16
		1698	ITAPARA OC (ECL) (N06000272)	12/2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	54.92	7
		1699	UCE OF TILABONI UG (ECL) (N06000276)	1/2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	3.15	10
		1700	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1/2023	3/2029 (N.A.) {3/2029}	389.10 (N.A.) {389.10}	0.00	14
	DEPARTMENT OF HIGHER EDUCATION	1701	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3/2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	185.75	99
	HOME AFFAIRS	1702	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10/2014	4/2018 (N.A.) {12/2024}	162.88 (210.83) {210.83}	187.06	88.5
	MINES	1703	CONSTRUCTION OF BASEMENTG FLOOR10 STORES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4/2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	56.19	26
	PETROLEUM	1704	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3/2017	12/2020 (Mar-25) {3/2025}	1,740.00 (2,433.15) {2,433.15}	2,025.40	87.2
		1705	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3/2019	3/2031 (Mar-29) {3/2029}	5,830.20 (N.A.) {5,830.20}	764.54	23.7
		1706	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11/2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	291.21	56.08

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1707	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3/2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	57.23	1.3
		1708	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6/2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	161.36	18.2
		1709	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12/2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	79.01	20.4
	POWER	1710	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9/2014	9/2019 (N.A.) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,042.24	45.1
		1711	DURGAPUR PP-III (2X20 MW) - NSPCL (NTPC) (N18000277)	12/2016	11/2018 (Mar-24) {3/2024}	529.68 (633.80) {679.00}	558.39	89
	RAILWAYS	1712	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4/2000	3/2019 (Mar-25) {3/2025}	1,188.91 (N.A.) {2,582.49}	1,087.01	75
		1713	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4/2010	3/2016 (N.A.) {3/2016}	2,397.72 (N.A.) {2,397.72}	197.20	17
		1714	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4/2010	3/2014 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.98	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1715	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4/2010	3/2016 (N.A.) {3/2026}	3,951.98 (N.A.) {8,964.35}	7,387.40	0
		1716	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4/2010	3/2016 (N.A.) {12/2026}	2,913.51 (N.A.) {4,834.54}	3,918.86	0
		1717	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4/2018	6/2022 (N.A.) {12/2024}	338.00 (N.A.) {393.83}	198.67	60
		1718	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10/2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	157.27	100
		1719	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7/2015	3/2025 (Mar-26) {3/2026}	283.54 (N.A.) {283.54}	159.30	44
		1720	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2/2009	9/2016 (N.A.) {6/2024}	4,874.58 (8,575.00) {10,442.41}	0.00	0
	ROAD TRANSPORT AND HIGHWAYS	1721	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12/2015	6/2018 (May-24) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100
		1722	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4/2014	9/2016 (N.A.) {12/2024}	1,665.00 (N.A.) {4,920.68}	4,920.68	93.4

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1723	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3/2018	9/2022 (Dec-22) {3/2025}	841.57 (708.30) {708.30}	7,093.85	93.25
		1724	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH- 81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3/2016	11/2018 (Dec-23) {12/2024}	271.17 (291.20) {291.20}	180.63	76.9
		1725	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2/2018	9/2020 (Jan-24) {11/2024}	426.18 (426.18) {426.18}	364.92	90.29
		1726	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND (MoRTH) (N24000885)	3/2016	9/2023 (Mar-24) {7/2024}	160.27 (213.97) {213.97}	144.31	100
		1727	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N (MoRTH) (N24000887)	6/2016	9/2021 (Feb-24) {11/2024}	236.78 (263.26) {263.26}	232.54	99.79
		1728	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3/2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	1,905.34	80.08
		1729	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3/2021	9/2024 (N.A.) {6/2025}	2,200.93 (N.A.) {2,614.65}	2,614.65	90.48

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1730	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8/2021	8/2023 (N.A.) {11/2024}	557.55 (N.A.) {557.55}	472.79	90.93
		1731	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8/2018	12/2021 (N.A.) {2/2025}	622.04 (N.A.) {622.04}	494.31	80.33
		1732	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 (NHAI) (N24001752)	12/2018	2/2023 (Aug-23) {11/2024}	2,375.87 (2,843.79) {2,843.79}	2,371.78	100
		1733	DEVELOPMENT TO 4/6-LANNING OF NH-31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3/2022	9/2025 (Sep-25) {9/2025}	995.04 (995.04) {995.04}	270.02	34.2
		1734	CONSTRUCTION OR 4 LANE RANIGANJ BYPASS OF LENGTH 5 261 KM ON NH 60 NEW NH 14 FROM KM 273 00 OF NH (MoRTH) (N24002184)	3/2023	3/2026 (Mar-26) {3/2026}	410.83 (N.A.) {410.83}	92.21	6.5
	STEEL	1735	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11/2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	46.84	3
	WATER RESOURCES	1736	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS (KMDA) (N30000029)	1/2019	4/2022 (Feb-19) {12/2024}	384.96 (N.A.) {384.96}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1737	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL (KMDA) (N30000030)	3/2019	4/2022 (N.A.) {12/2024}	287.53 (N.A.) {287.53}	0.00	0
		1738	I AND D AND STP WORKS AT BURDWAN WEST BENGAL (KMDA) (N30000031)	12/2018	4/2022 (N.A.) {12/2024}	234.31 (N.A.) {234.31}	0.00	0
		1739	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5/2018	2/2022 (N.A.) {3/2025}	198.43 (224.69) {224.69}	75.82	83
		1740	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS (KMDA) (N30000033)	3/2018	6/2022 (N.A.) {3/2024}	165.16 (N.A.) {165.16}	0.00	0
		1741	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8/2017	9/2022 (Jan-23) {12/2026}	307.12 (N.A.) {653.67}	0.00	0
		1742	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH (KMDA) (N30000042)	5/2018	2/2022 (Sep-20) {12/2024}	160.00 (154.73) {154.73}	84.27	88
		1743	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045)	8/2017	12/2021 (Feb-21) {2/2024}	185.22 (N.A.) {185.22}	49.99	100
		1744	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046)	2/2014	12/2019 (N.A.) {6/2022}	274.76 (N.A.) {332.56}	276.93	100
		1745	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047)	12/2014	4/2020 (N.A.) {6/2022}	272.32 (341.68) {272.32}	307.26	100

Table:-7. Project List: Ongoing Projects as of 31st October 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1746	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048)	1/2018	12/2021 (Feb-21) {2/2024}	172.10 (N.A.) {172.10}	47.20	100
		1747	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049)	10/2017	12/2021 (Feb-21) {2/2024}	164.93 (N.A.) {164.93}	45.45	100
			Total			2,609,935.22 (-) {3,109,678.35}	1,644,087.19	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
