



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation

Synopsis-Quarterly Project

Implementation Status Report

←
Costing Rs. 150 Crore & above
(Part-I)*



Quarter-4 FY 2023-24
(January-March)

*Refer Part-II for tables comprising detailed project listing.



www.mospi.gov.in



@GoIStats

Contents

1. Overview	2
2. Monitoring of Project Implementation	3
3. Analysis of project cost/expenditure.....	4
4. Type of Projects: Major & Mega	5
5. Status of implementation of projects	6
5.1 Completed projects	6
5.2 Ongoing Projects	6
6. Time Overrun (TOR)	6
7. Cost Overrun (COR)	8
8. Cost and time overrun.....	8
9. Projects requiring examination of the revised cost estimate.....	8
10. Reasons for cost and time overrun	9
11. PRAGATI meetings	9
12. Limitations of data used in the Report	10
Annex 1: Sector-wise distribution: Project summary - Added/dropped in the 4th Quarter January-March (2023-24) (Project Count)	11
Annex 2: Sector-wise distribution: Original Cost/ Anticipated Cost/ Cumulative Expenditure/ Balance Expenditure (Rs. crore)	12
Annex 3: Project Type (Mega & Major) distribution, as of 4th quarter end, January-March (2023-24) (Rs. crore)	13
Annex 4: Sector-wise distribution - Ongoing Projects as of 4th quarter end, January-March (2023-24) (Rs. Crore)	14
Annex 5: Sector-wise distribution – Ahead/On schedule/ Without Anticipated Date of Completion (DOC) / Without Original Project Completion Date (ODC) but with reported DOC, as of 4th quarter end, January-March (2023-24) (Project Count).....	15
Annex 6: Sector-wise distribution - Extent of the time overruns with respect to Original Project Completion date, as of 4 th Quarter end, January-March 2023-24 (Rs. Crore)	16
Annex 7: Sector-wise distribution - Extent of time overruns with respect to Latest approved completion date, as of 4 th Quarter end, January-March 2023-24 (Rs. Crore).....	17
Annex 8: Sector-wise distribution - Extent of cost overruns with respect to Original Sanctioned cost, as of 4 th Quarter end, January-March 2023-24 (Rs. Crore).....	18
Annex 9: Sector-wise distribution - Extent of cost overruns with respect to Latest Approved Cost, as of 4 th Quarter end, January-March 2023-24 (Rs. crore)	19
Annex 10: Sector-wise distribution - Extent of time & cost overruns in projects with respect to original schedule as of 4 th Quarter end, January-March 2023-24 (Rs. Crore)	20
Annex 11: Sector-wise distribution: requiring review/sanctions of Revised Cost Estimate (RCE*), as of 4 th Quarter end, January-March 2023-24 (Project Count)	21

1. Overview

The Quarterly Project Implementation Status Report is prepared by the Programme Implementation Wing of the Ministry of Statistics and Programme Implementation (MoSPI). The report is prepared on the basis of data and information updated/reported by various Ministries and Departments on the Online Computerised Monitoring System (OCMS) Portal of MoSPI, in respect of Central Sector Projects (costing Rs.150 crore and above) implemented by them.

The Report presents an overview of the projects under implementation by various Ministries and Departments and provides sector-wise analysis of time/cost overruns in these projects with respect to approved time schedule and cost estimates and reasons thereof.

The present report pertains to the fourth quarter of 2023-24 viz. January-March 2024. It also provides year-on-year comparison of the status of implementation of projects during the respective quarters of 2022-23 and 2023-24.

Highlights		
	2023-24	2022-23
Total number of projects on the monitor	1952	1566
Total Original estimated cost of these projects	Rs. 27,55,676.40 crore	Rs. 21,62,319.31 crore
Total latest approved cost of these projects	Rs. 29,93,231.65 crore	Rs. 24,32,124.58 crore
Total anticipated cost of these projects	Rs. 32,66,261.91 crore	Rs. 26,29,193.77 crore
Cumulative Expenditure till March 2024	Rs. 17,62,511.92 crore	Rs. 14,71,873.93 crore
Overall percentage cost overrun with respect to original estimates	18.53 %	21.59%
Overall percentage cost overrun with respect to latest sanctioned estimates	9.12 %	8.10%
Total number of projects showing cost overrun w.r.t original approved cost	463	384
Total number of projects showing time overrun w.r.t original schedule	853 (ranging from 1 to 275 months)	931 (ranging from 1 to 276 months)
Percentage cost overrun in delayed Projects (w.r.t original schedule)	25.80 %	27.86%
No. of projects due for commissioning during FY 2023-24	1099	1030
No. of projects completed during FY 2023-24	280	329
Total sanctioned cost* of completed projects during FY 2023-24	Rs. 2,11,437.32 crore	Rs. 2,89,871.97 crore
Total final cost of the completed projects during FY 2023-24	Rs. 2,42,643 crore	Rs. 3,06,629 crore


*Original cost or Latest Board Approved cost.

2. Monitoring of Project Implementation

As of 4th Quarter end January-March (2023-24), there are total 1952 projects (sector-wise distribution at **Annex 1**) in the monitoring shelf of this Ministry with the anticipated cost of completion of the projects as Rs. 32,66,261.91 crore and the total expenditure as Rs. 17,62,511.92 crore, which is 53.96 *per cent* of the total anticipated completion cost and 63.9 *per cent* of the original cost.

Out of these 1952 projects, the count of ongoing projects, completed and dropped/frozen stand at 1872, 65 and 15 respectively.

Also, the top 5 sectors contributing to total 1952 on-monitor projects are Road Transport & Highways (1130 projects, 57.8 *per cent*), Railways (249 projects, 12.8 *per cent*), Petroleum (161 projects, 8.24 *per cent*), Coal (126 projects, 6.4 *per cent*), and Power (105 projects, 5.4 *per cent*).

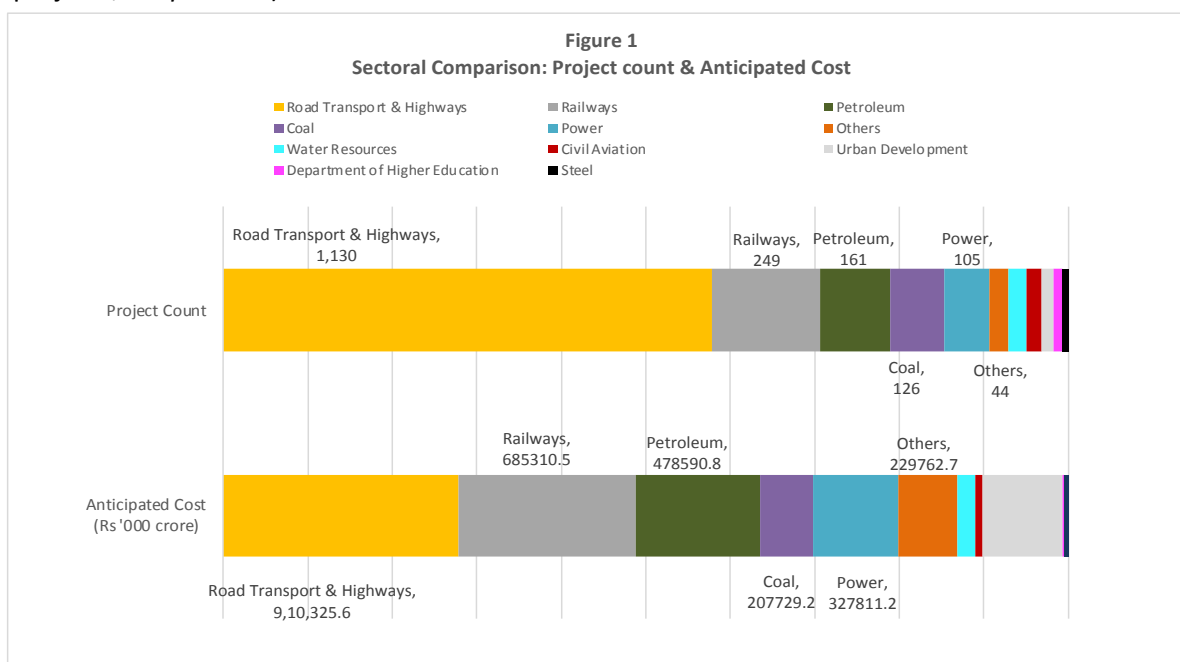


The graph above illustrates a sectoral comparison across two indicators: project count and the anticipated cost of these projects within the top 10 sectors, considering their project scale, out of a total 22 sectors currently under monitoring.

It indicates that while there's considerable variation in project counts among the three major sectors - Road Transport & Highways, Railways, and Petroleum; the distribution of anticipated costs across these sectors doesn't show the same degree of variance.

The sector-wise project distribution and related cost/expenditure details is at **Annex 2**.


3. Analysis of project cost/expenditure

- A graphical presentation of the sector-wise anticipated cost vis-à-vis latest approved cost based on 1952 projects at the end of 4th quarter of 2023-24 can be seen in Figure 2 below:

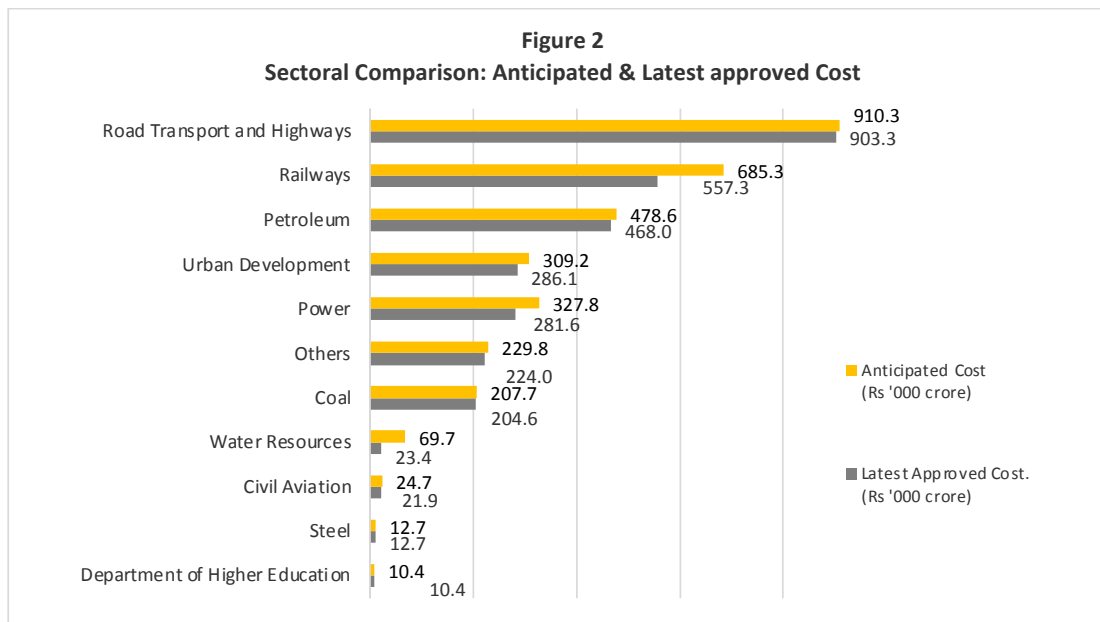

The above indicates that revised/anticipated costs in respect to the extent of Rs.273,030.26 in respect of 290 projects is yet to be approved by competent authorities.

- Further, the status of sector-wise cumulative Expenditure and the balance expenditure in respect of the 1952 projects can be seen in the Graph below. (For details, refer Annex 2)

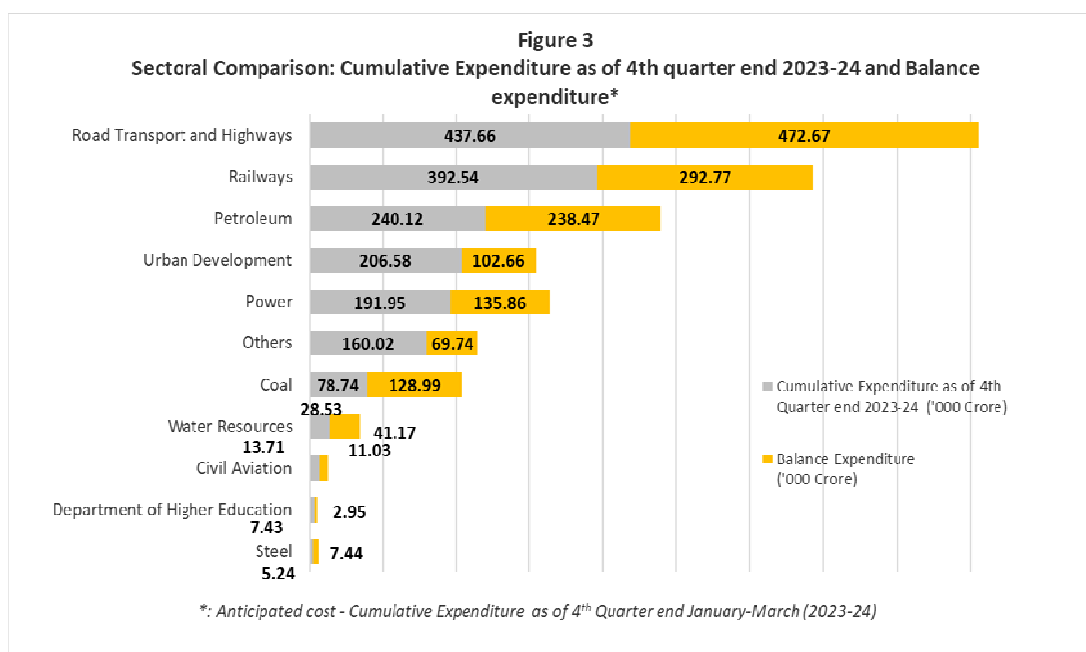

4. Type of Projects: Major & Mega

While the projects costing Rs.1000 crore and above fall under the category of **mega projects**, the projects costing Rs.150 crore to Rs.1000 crore fall under the category of the **major projects**.

The details of Mega and Major Projects during the 4th quarter of 2023-24 are tabulated below:

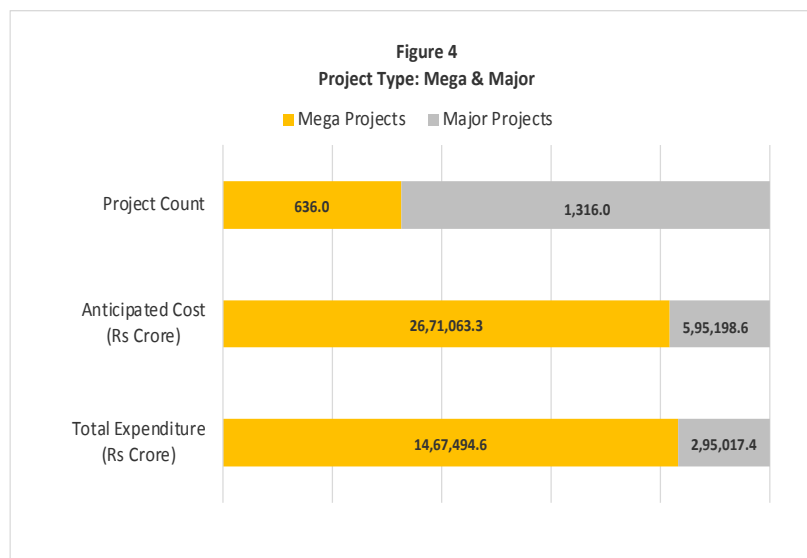


Table - Mega and Major Projects					
	Number of projects	Anticipated Cost (Rs. crore)	% of total projects	Exp. As of 4 th quarter end (Rs. crore)	Original Cost (Rs.crore)
Mega Projects	636	26,71,063.3	81.8	14,67,494.56	21,65,470.07
Major Projects	1316	5,95,198.6	18.2	2,95,017.36	5,90,206.33
Total	1952	32,66,261.91	100	17,62,511.92	27,55,676.4

It can be seen that out of total 1952 projects,

- 636 Mega projects accounted for about 81.78 *per cent* of the total anticipated cost, whereas the share of 1316 major projects were about 18.22 *per cent* of the anticipated cost.
- Also, against the original cost of Rs.27,55,676.4 crore, an expenditure of Rs. 17,62,511.92 crore has been incurred till end of March 2024.

The sector-wise distribution of Mega and Major Projects is at **Annex 3**.

5. Status of implementation of projects

5.1 Completed projects

During the 4th quarter (January-March) of 2023-24, 65 projects reported completion with completion cost of Rs. 48,080 crore. The completed projects contributed by sectors namely Road Transport & Highways (29 nos.), Petroleum (29 nos.), Power (4 nos.), Coal (2 nos.) and Health & Family welfare (1 no.).

5.2 Ongoing Projects

During the 4th quarter (January-March) of 2023-24, there are 1872 ongoing projects with anticipated cost as Rs. 31,88,359.02 and the total expenditure was Rs.17,62,511.9 crore, which was 55.2% of the total anticipated completion cost and 65.5% of the original cost.


Of these 1872 projects, 779 projects are delayed (with respect to the original date of completion). There was a cost overrun of Rs. 5,01,323.33 crore (with respect to the sanctioned cost) in 449 projects, which is 18.7 % of their sanctioned cost.

The sector-wise distribution of the Ongoing projects and related details is given at **Annex 4**.

6. Time Overrun (TOR)


Out of 1952 projects

- 56 projects were ahead of schedule
- 665 projects were on schedule; and

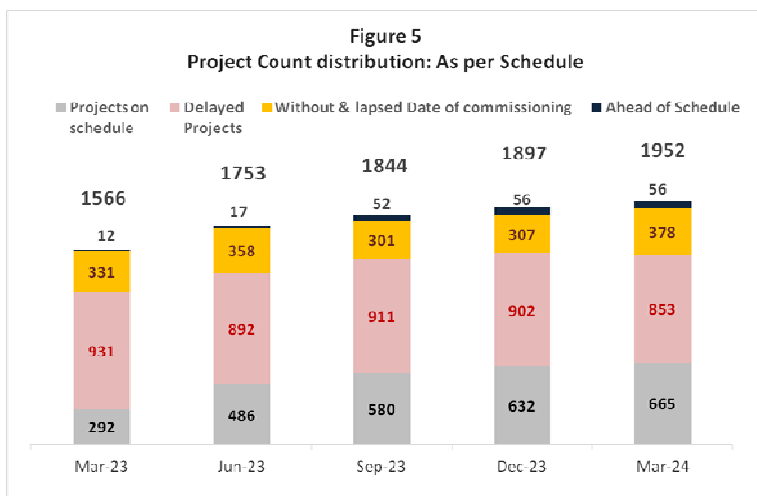

- 853 projects were delayed beyond the original date of completion. Further, for 378 projects, either original or the anticipated date of completion was not reported or lapsed. **Figure 5** shows the number of projects on schedule and delayed vis-à-vis total projects monitored during the last five quarters up to March 2024.

Figure 6 shows the trend of the percentage of projects delayed. As can be seen from the graph, the percentage of delayed projects reduced from 59.45 per cent in quarter ending March 2023 to 43.70 per cent in quarter ending March 2024.

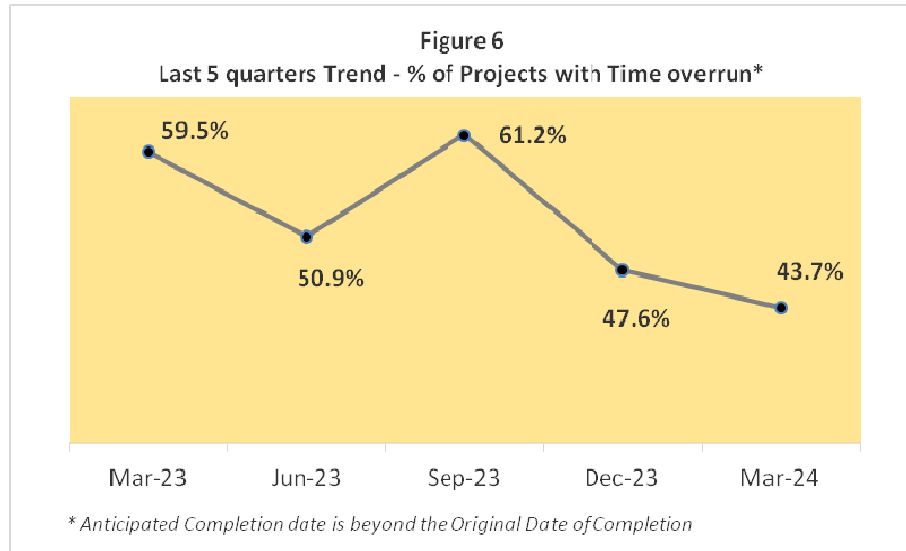

- Sector-wise number of delayed and on schedule projects as of 4th quarter end 2023-24 is given in **Annex 5**. In this regard, the following was observed:
 - a) **Ahead of schedule:** The total 56 projects which are ahead of schedule (with respect to Original Schedule) contributed by Railways (41 projects), Road Transport and Highways (9 projects), Petroleum (3 projects), Power (2 projects) and Department of Higher Education (1 project)
 - b) **On schedule:** The top five contributing sectors in achieving on schedule completion (with respect to the original schedule) of the total 665 nos. projects are Road Transport and Highways (418 projects), Coal (69 projects), Petroleum (61 projects), Railways (54 projects), and Power (34 projects).
 - c) **Delayed Projects:** The sectors where delayed projects (with respect to the original schedule) are most prevalent are Road Transport and Highways, Railways, Petroleum, Power and Coal contributing to ~53 per cent, ~13 per cent, ~11 per cent, ~7 per cent, and ~6 per cent of total 853 delayed projects.

Sector-wise distribution of projects and time overrun related details are given in **Annex 6** (with respect to the Original Date of Completion) & **Annex 7** (with respect to the Latest approved Date of Completion).


7. Cost Overrun (COR)

Out of 1952 projects, 463 projects have cost overrun of Rs.5,33,491.72 crore which is 59.6 per cent of their sanctioned cost.

The 3 (three) major contributing sectors with prevalent cost overrun are Road Transport and Highways, Railways, and Petroleum contributing to ~45 per cent, ~31 per cent, and ~7 per cent of total 463 projects. However, with regard to the latest approved cost, 290 projects reported cost overrun of Rs2,99,036.95 crore.

Figure

7 shows quarter-wise trend of cost overruns. As can be seen, percentage of cost overrun reduced from 21.6 per cent in quarter ending March 2023 to 18.5 per cent in quarter ending March 2024.

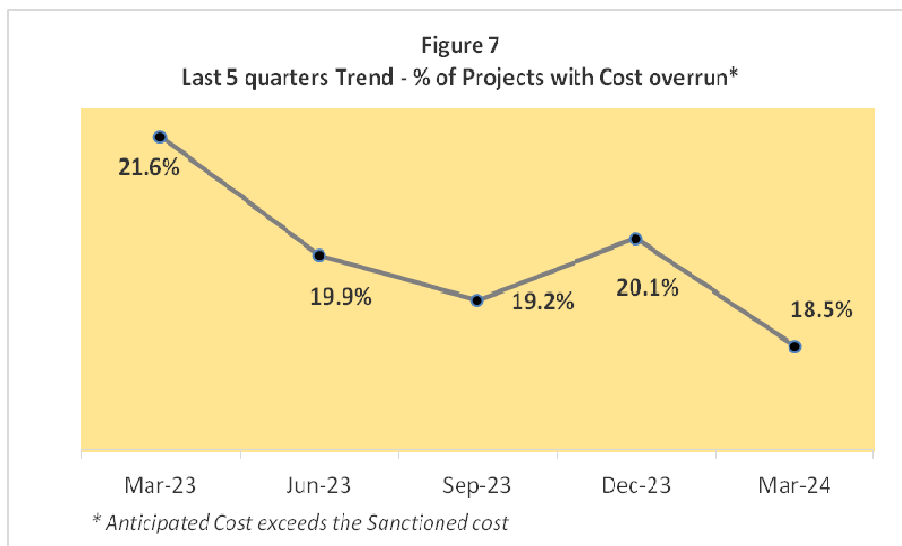

The Sector-wise distribution of projects and Cost overrun related details are at **Annex 8** (with respect to the original sanctioned cost) & **Annex 9** (with respect to the latest approved cost).

8. Cost and time overrun

Out of 1952 Projects, there are 283 projects reporting both time (with respect to the original completion date) and cost overrun (with respect to the Original cost). The time overrun is ranging from 2-261 months and the cost overrun for such projects is Rs. 3,90,008.29 crore which is 67.4 per cent of their original sanctioned cost.

The sectors where both time and cost slippage are most prevalent are Road Transport and Highways, Railways, Petroleum, Power and Civil Aviation contributing to ~42 per cent, ~29 per cent, ~9 per cent, ~5.3 per cent, and ~2 per cent respectively of total 283 projects.

The Sector-wise distribution of projects and related details of projects having both time and cost overrun is given at **Annex 10**.

9. Projects requiring examination of the revised cost estimate

It is seen that as many as 290 (161 Mega and 129 Major) of the 1952 projects on the OCMS require review/sanction of the cost estimates, as their anticipated costs have exceeded the

approved (Latest board approved or Original) cost. It is also seen that in 175 (87 Mega and 88 Major) projects, the actual expenditure up to March 2024 had already exceeded the approved cost. The exercise for the review of cost is required for 290 projects and in the case of 175 projects, Revised Cost Estimate (RCE) needs to be approved by PIB/ CCEA and needs to be updated on OCMS. The sector-wise details of such projects are given at **Annex 11**.

10. Reasons for cost and time overrun

While the cost overruns due to general price escalation are not avoidable, the cost escalation on account of delay could be minimized. The mechanism of Standing Committees (under chairmanship of Additional Secretary of concerned Ministry) in each Ministry to review the time and cost overruns in projects and to fix the responsibility thereof has to be made more effective. Rigorous monitoring and initiating appropriate remedial measures on priority by administrative Ministries are warranted to ensure timely completion of projects.

The major factors responsible for time overruns as reported by project implementing agencies can be seen in the figure below:



11. PRAGATI meetings

The Government has launched the Pro-Active Governance and Timely Implementation (PRAGATI) initiative in March 2015. PRAGATI is a unique interactive platform aimed at

addressing common man's grievances and simultaneously monitoring and reviewing important programmes and projects of the Government of India as well as projects flagged by State Governments. PRAGATI meetings facilitate expeditious resolution of pending issues affecting swift implementation of project by all concerned stakeholder agencies.

PRAGATI meetings are convened under the Chairmanship of the Hon'ble Prime Minister with the Secretaries of all the Central Government Ministries/Departments and Chief Secretaries of the State Governments. It also offers a unique combination in the direction of cooperative federalism since it brings on one stage the Secretaries of Government of India and the Chief Secretaries of the States.

More than 362 Central Sector Infrastructure projects from different sectors such as Railways, Road Transport & Highways, Power, Steel, Coal etc. have been reviewed in 43 PRAGATI meetings held so far. These projects are at different stages of implementation and are monitored regularly by the implementing Ministries/Departments and concerned State Governments. The last PRAGATI meeting was held on 25 October 2023.

12. Limitations of data used in the Report

The list of projects included in the Report is not exhaustive. Only those projects, which are reported by the implementing agencies, are included in the Report. All administrative Ministries/ Departments have been asked to advise concerned agencies to send complete details of their projects as approved by their Boards. Recently sanctioned projects by the Government where the execution work has not yet commenced would be included in subsequent reports once they are reported on OCMS.

One of the limitations of the information and data presented in the report is non-furnishing of complete and accurate information on time by project authorities on OCMS Portal. Some of the project authorities are not reporting the exact status of the projects for a considerable period of time and these are corrected in the report as and when the details are made available by them. In many projects the physical progress of the project is not reported.

Annex 1: Sector-wise distribution: Project summary- Added/dropped in the 4th Quarter January-March(2023-24)(Project Count)					
S. No.	Sector	As of 31st December 2023	Added/ elevated (during 4th Quarter 2023-24)	Completed/ dropped/ frozen/ deleted (during 3rd Quarter 2023-24)	As of 4 th quarter (Jan-March) end 2023-24
1	Atomic Energy	5	0	0	5
2	Civil Aviation	30	5	0	35
3	Coal	128	2	4	126
4	Finance	3	0	0	3
5	Fertilisers	0	0	0	0
6	Mines	8	0	0	8
7	Steel	9	4	0	13
8	Petroleum	161	4	4	161
9	Power	98	7	0	105
10	Health and Family Welfare	8	1	0	9
11	Railways	262	0	13	249
12	Road Transport and Highways	1076	104	50	1130
13	Shipping and ports	1	0	0	1
14	Telecommunications	6	1	0	7
15	Urban Development	27	0	0	27
16	Water Resources	41	0	0	41
17	Social Justice	1	0	0	1
18	Defence Production	1	0	0	1
19	Commerce	1	0	1	0
20	Department of Higher Education	22	0	1	21
21	Home Affairs	5	0	0	5
22	DPIIT	2	0	0	2
23	DONER	1	0	0	1
24	Renewable Energy	1	0	0	1
Total		1897	128	73	1952

Annex 2

Annex 2: Sector-wise distribution: Original Cost/ Anticipated Cost/ Cumulative Expenditure/ Balance Expenditure (Rs. crore)								
S. No.	Sector	Project Count	Sector (%) of total	Original Cost	Anticipated cost	Increase in project cost	Cumulative Expenditure as of 4 th quarter end 2023-24	Balance Expenditure* as of 4 th quarter end 2023-24
1	Atomic Energy	5.0	0.3%	116741.0	136736.0	19995.0	104689.2	32046.8
2	Civil Aviation	35.0	1.8%	21483.0	24732.0	3249.0	13705.4	11026.6
3	Coal	126.0	6.5%	200441.1	207729.2	7288.1	78741.7	1,28,987.52
4	Finance	3.0	0.2%	786.3	831.0	44.8	733.2	97.9
5	Mines	8.0	0.4%	7559.8	9788.7	2228.9	4957.9	4830.9
6	Steel	13.0	0.7%	11827.6	12680.6	853.0	5237.7	7442.9
7	Petroleum	161.0	8.2%	414707.4	478590.8	63883.4	240116.9	2,38,473.90
8	Power	105.0	5.4%	272327.8	327811.2	55483.5	191949.2	1,35,862.08
9	Health and Family Welfare	9.0	0.5%	7327.0	7722.7	395.7	4232.2	3490.6
10	Railways	249.0	12.8%	444073.6	685310.5	241237.0	392541.1	2,92,769.38
11	Road Transport and Highways	1130.0	57.9%	867946.7	910325.6	42378.9	437657.6	4,72,668.05
12	Shipping and ports	1.0	0.1%	5369.2	5061.2	-308.0	2924.1	2137.0
13	Telecommunications	7.0	0.4%	40229.6	40295.7	66.1	25101.1	15194.6
14	Urban Development	27.0	1.4%	283820.8	309241.4	25420.6	206578.3	1,02,663.06
15	Water Resources	41.0	2.1%	23466.3	69701.0	46234.7	28535.0	41166.0
16	Social Justice	1.0	0.1%	171.0	171.0	0.0	73.8	97.2
17	Defence Production	1.0	0.1%	246.3	195.0	-51.3	187.1	7.9
18	Department of Higher Education	21.0	1.1%	9846.2	10376.9	530.8	7426.2	2950.7
19	Home Affairs	5.0	0.3%	2025.7	2959.0	933.3	2272.7	686.3
20	DPIIT	2.0	0.1%	24857.0	25485.0	628.0	14374.0	11111.0
21	DONER	1.0	0.1%	151.3	151.3	0.0	148.3	3.0
22	Renewable Energy	1.0	0.1%	271.9	366.1	94.2	329.5	36.6
Total		1952.0	100.0%	2755676.4	3266261.9	510585.5	1762511.9	1503750.0

*Balance Expenditure: Anticipated Cost - Cumulative Expenditure as of 4th quarter end(2023-24)

Annex 3

Annex 3: Project Type (Mega & Major) distribution, as of 4th quarter end, January-March (2023-24) (Rs. crore)							
S. No.	Name of the Sector	Project Count	Mega Projects		Project Count	Major Projects	
			Anticipated Cost	Original Cost		Anticipated Cost	Original Cost
1	Atomic Energy	5	136736	116741	0	0	0
2	Civil Aviation	5	10714	7614	30	14018	13869
3	Coal	37	165057	156873	89	42671	43568
4	Finance	0	0	0	3	831	786
5	Mines	3	8080	6074	5	1708	1486
6	Steel	3	6660	6034	10	6021	5794
7	Petroleum	62	436440	373235	99	42150	41472
8	Power	57	305959	250685	48	21852	21642
9	Health and Family Welfare	4	5853	5637	5	1870	1690
10	Railways	117	620247	378456	132	65063	65617
11	Road Transport and Highways	312	540935	502172	818	369390	365774
12	Shipping and ports	1	5061	5369	0	0	0
13	Telecommunications	2	37890	37879	5	2405	2351
14	Urban Development	23	307217	281796	4	2024	2024
15	Water Resources	1	55549	10151	40	14152	13315
16	Social Justice	0	0	0	1	171	171
17	Defence Production	0	0	0	1	195	246
18	Department of Higher Education	1	1085	676	20	9292	9170
19	Home Affairs	1	2092	1219	4	867	807
20	DPIIT	2	25485	24857	0	0	0
21	DONER	0	0	0	1	151	151
22	Renewable Energy	0	0	0	1	366	272
Total		636	2671063	2165470	1316	595199	590206

Annex 4: Sector-wise distribution - Ongoing Projects as of 4th quarter end, January-March (2023-24) (Rs. Crore)								
S.no	Sector Name	Project Count	Original Cost	Anticipated Cost	Cumulative Expenditure as of 4 th quarter end (2023-24)	COR	No. of Projects having TOR	No. of Projects having COR
1	ATOMIC ENERGY	5	116741	136736	104689.17	19995	4	3
2	CIVIL AVIATION	35	21483.03	24732.01	13705.44	3248.98	18	8
3	COAL	120	187730.9	192685.18	78741.7	4954.33	48	8
4	DEFENCE PRODUCTION	1	246.31	195	187.12	-51.31	0	0
5	DEPARTMENT OF HIGHER EDUCATION	21	9846.15	10376.91	7426.2	530.76	12	5
6	DONER	1	151.33	151.33	148.33	0	0	0
7	DPIIT	2	24857	25485	14373.98	628	1	1
8	FINANCE	3	786.27	831.04	733.16	44.77	0	1
9	HEALTH AND FAMILY WELFARE	8	7132.02	7527.73	4232.15	395.71	7	4
10	HOME AFFAIRS	5	2025.73	2958.98	2272.68	933.25	4	3
11	MINES	8	7559.78	9788.7	4957.85	2228.92	7	3
12	PETROLEUM	131	391969.4	455341.64	240116.86	63372.22	80	27
13	POWER	101	270290.5	325150.03	191949.15	54859.52	52	19
14	RAILWAYS	248	443923.6	684968.85	392541.13	241045.3	109	143
15	RENEWABLE ENERGY	1	271.9	366.12	329.49	94.22	0	1
16	ROAD TRANSPORT AND HIGHWAYS	1093	837678.7	874683.11	437657.59	37004.43	399	204
17	SHIPPING AND PORTS	1	5369.18	5061.15	2924.12	-308.03	1	0
18	SOCIAL JUSTICE	1	170.99	170.99	73.8	0	0	0
19	STEEL	12	11285.36	11911.23	5237.65	625.87	5	1
20	TELECOMMUNICATIONS	7	40229.56	40295.69	25101.11	66.13	2	2
21	URBAN DEVELOPMENT	27	283820.8	309241.35	206578.29	25420.56	15	7
22	WATER RESOURCES	41	23466.28	69700.98	28534.95	46234.7	15	9
Grand Total		1872	2687036	3188359	1762511.9	501323.3	779	449

Annex 5: Sector-wise distribution – Ahead/On schedule/ Without Anticipated Date of Completion (DOC) / Without Original Project Completion Date (ODC) but with reported DOC, as of 4th quarter end, January-March (2023-24) (Project Count)											
S. no	Sector	Ahead		On Schedule		Delayed		Without anticipated DOC		Without ODC but with reported DOC	
		Original	Latest	Original	Latest	Original	Latest	Original	Latest	Original	Latest
1	Atomic Energy	0	0	1	1	4	4	0	0	0	0
2	Civil Aviation	0	0	10	13	19	16	6	6	0	0
3	Coal	0	0	69	79	49	39	8	8	0	0
4	Finance	0	0	0	0	0	0	3	3	0	0
5	Mines	0	0	0	3	7	4	1	1	0	0
6	Steel	0	0	7	7	6	6	0	0	0	0
7	Petroleum	3	3	61	106	91	46	6	6	0	0
8	Power	2	3	34	46	56	43	13	13	0	0
9	Health and Family Welfare	0	0	1	6	7	2	1	1	0	0
10	Railways	41	35	54	82	113	95	20	20	21	17
11	Road Transport and Highways	9	10	418	544	448	324	249	249	6	3
12	Shipping and ports	0	0	0	1	1	0	0	0	0	0
13	Telecommunications	0	0	4	4	2	2	1	1	0	0
14	Urban Development	0	0	4	10	16	10	6	6	1	1
15	Water Resources	0	0	0	0	15	15	26	26	0	0
16	Social Justice	0	0	1	1	0	0	0	0	0	0
17	Defence Production	0	0	0	0	0	0	1	1	0	0
18	Department of Higher Education	1	2	0	4	14	9	6	6	0	0
19	Home Affairs	0	0	0	1	4	3	1	1	0	0
20	DPIIT	0	0	1	1	1	1	0	0	0	0
21	DONER	0	0	0	0	0	0	1	1	0	0
22	Renewable Energy	0	0	0	0	0	0	1	1	0	0
Total		56	53	665	909	853	619	350	350	28	21

Annex 6: Sector-wise distribution - Extent of the time overruns with respect to Original Project Completion date, as of 4 th Quarter end, January-March 2023-24 (Rs. Crore)										
S. no	Sector	Project Count	Original cost	Anticipated cost	Cost overrun	Projects with time overruns [^]				
						Project Count	Original cost	Anticipated cost	% increase	Range in months
1	Atomic Energy	5	1,16,741.00	1,36,736.00	17.1	4	67,120.00	87,115.00	29.8	72 - 171
2	Civil Aviation	35	21,483.03	24,732.01	15.1	19	13,134.41	16,612.27	26.5	8 - 48
3	Coal	126	2,00,441.11	2,07,729.22	3.6	49	65,833.18	70,418.52	7	12 - 159
4	Finance	3	786.27	831.04	5.7	0	0	0	0	-
5	Mines	8	7,559.78	9,788.70	29.5	7	7,333.99	9,562.91	30.4	5 - 66
6	Steel	13	11,827.60	12,680.57	7.2	6	7,235.84	8,088.81	11.8	12 - 101
7	Petroleum	161	4,14,707.37	4,78,590.76	15.4	91	3,19,140.46	3,76,948.76	18.1	1 - 143
8	Power	105	2,72,327.75	3,27,811.23	20.4	56	1,73,536.67	2,26,490.96	30.5	1 - 193
9	Health and Family Welfare	9	7,327.02	7,722.73	5.4	7	5,304.02	5,699.73	7.5	3 - 60
10	Railways	249	4,44,073.55	6,85,310.51	54.3	113	3,17,922.78	4,74,988.25	49.4	3 - 261
11	Road Transport and Highways	1130	8,67,946.70	9,10,325.64	4.9	448	3,28,082.19	3,58,868.62	9.4	1 - 136
12	Shipping and ports	1	5,369.18	5,061.15	-5.7	1	5,369.18	5,061.15	-5.7	33 - 33
13	Telecommunications	7	40,229.56	40,295.69	0.2	2	709.62	709.62	0	40 - 74
14	Urban Development	27	2,83,820.79	3,09,241.35	9	16	1,43,006.56	1,47,874.86	3.4	3 - 63
15	Water Resources	41	23,466.28	69,700.98	197	15	15,010.48	60,907.23	305.8	21 - 51
16	Social Justice	1	170.99	170.99	0	0	0	0	0	-
17	Defence Production	1	246.31	195	-20.8	0	0	0	0	-
18	Department of Higher Education	21	9,846.15	10,376.91	5.4	14	6,204.04	6,336.27	2.1	4 - 118
19	Home Affairs	5	2,025.73	2,958.98	46.1	4	1,826.42	2,759.67	51.1	12 - 80
20	DPIIT	2	24,857.00	25,485.00	2.5	1	4,773.00	5,401.00	13.2	52 - 52
21	DONER	1	151.33	151.33	0	0	0	0	0	-
22	Renewable Energy	1	271.9	366.12	34.7	0	0	0	0	-
Total		1952	27,55,676.40	32,66,261.91	18.5	853	14,81,542.84	18,63,843.63	25.8	

\$- Time Overrun= Anticipated Date of Commissioning minus original Date of Commissioning

^~ Cost Overrun= Anticipated Cost minus Original Cost

Annex 7: Sector-wise distribution - Extent of time overruns with respect to Latest approved completion date, as of 4 th Quarter end, January-March 2023-24 (Rs. Crore)										
S. no	Sector	No. of projects	Latest approved cost	Anticipated cost	Cost overrun	Projects with time overruns [^]				
						No. of projects	Latest approved cost	Anticipated cost	% increase	Range in months
1	Atomic Energy	5	1,32,558.00	1,36,736.00	3.2	4	82,937.00	87,115.00	5	72-17
2	Civil Aviation	35	21,882.93	24,732.01	13	16	10,163.58	11,463.56	12.8	1-48
3	Coal	126	2,04,588.59	2,07,729.22	1.5	39	61,439.07	64,090.62	4.3	7-159
4	Finance	3	786.27	831.04	5.7	0	0	0	0	-
5	Mines	8	9,433.96	9,788.70	3.8	4	2,466.77	2,821.51	14.4	2-47
6	Steel	13	12,680.57	12,680.57	0	6	8,088.81	8,088.81	0	Oct-51
7	Petroleum	161	4,68,036.37	4,78,590.76	2.3	46	1,16,170.26	1,21,709.25	4.8	1-47
8	Power	105	2,81,570.54	3,27,811.23	16.4	43	1,68,800.25	2,12,541.38	25.9	1-193
9	Health and Family Welfare	9	7,696.53	7,722.73	0.3	2	1,024.21	1,022.00	-0.2	2-13
10	Railways	249	5,57,287.66	6,85,310.51	23	95	3,07,239.63	3,80,556.14	23.9	2-216
11	Road Transport and Highways	1130	9,03,263.39	9,10,325.64	0.8	324	2,48,966.58	2,52,191.80	1.3	1-127
12	Shipping and ports	1	4,633.81	5,061.15	9.2	0	0	0	0	-
13	Telecommunications	7	40,229.56	40,295.69	0.2	2	709.62	709.62	0	35-74
14	Urban Development	27	2,86,057.01	3,09,241.35	8.1	10	1,14,661.15	1,17,293.23	2.3	3-63
15	Water Resources	41	23,420.50	69,700.98	197.6	15	15,023.16	60,907.23	305.4	21-70
16	Social Justice	1	170.99	170.99	0	0	0	0	0	-
17	Defence Production	1	200	195	-2.5	0	0	0	0	-
18	Department of Higher Education	21	10,414.50	10,376.91	-0.4	9	4,031.86	3,986.86	-1.1	3-45
19	Home Affairs	5	2,946.02	2,958.98	0.4	3	2,579.71	2,592.69	0.5	34-80
20	DPIIT	2	24,857.00	25,485.00	2.5	1	4,773.00	5,401.00	13.2	52-52
21	DONER	1	151.33	151.33	0	0	0	0	0	-
22	Renewable Energy	1	366.12	366.12	0	0	0	0	0	-
Total		1952	29,93,231.65	32,66,261.91	9.1	619	11,49,074.66	13,32,490.70	16	

[^]-Time Overrun = Anticipated Date of Commissioning minus Latest Approved Date of Commissioning.

Annex 8: Sector-wise distribution - Extent of cost overruns with respect to Original Sanctioned cost, as of 4th Quarter end, January-March 2023-24 (Rs. Crore)									
S. no	Sector	Project Count	Original cost	Anticipated cost	Cost overrun	Projects with cost overruns [^]			
						Project Count	Original cost	Anticipated cost	% increase
1	Road Transport and Highways	1130	867946.7	910325.6	4.9	209.0	197338.5	247937.6	25.6
2	Railways	249	444073.6	685310.5	54.3	144.0	200865.7	452444.4	125.2
3	Petroleum	161	414707.4	478590.8	15.4	32.0	190131.1	255463.1	34.4
4	Coal	126	200441.1	207729.2	3.6	9.0	29146.4	38047.2	30.5
5	Power	105	272327.8	327811.2	20.4	20.0	72153.2	127653.6	76.9
6	Water Resources	41	23466.3	69701.0	197.0	9.0	12532.3	58856.5	369.6
7	Civil Aviation	35	21483.0	24732.0	15.1	8.0	4824.8	8627.7	78.8
8	Urban Development	27	283820.8	309241.4	9.0	7.0	117061.6	142561.3	21.8
9	Department of Higher Education	21	9846.2	10376.9	5.4	5.0	2020.7	2652.8	31.3
10	Steel	13	11827.6	12680.6	7.2	2.0	2635.2	3488.2	32.4
11	Health and Family Welfare	9	7327.0	7722.7	5.4	4.0	2024.1	2434.8	20.3
12	Mines	8	7559.8	9788.7	29.5	3.0	4992.0	7280.4	45.8
13	Telecommunications	7	40229.6	40295.7	0.2	2.0	24729.8	24796.0	0.3
14	Atomic Energy	5	116741.0	136736.0	17.1	3.0	27271.0	47266.0	73.3
15	Home Affairs	5	2025.7	2959.0	46.1	3.0	1659.4	2592.7	56.2
16	Finance	3	786.3	831.0	5.7	1.0	209.0	262.0	25.4
17	DPIIT	2	24857.0	25485.0	2.5	1.0	4773.0	5401.0	13.2
18	Shipping and ports	1	5369.2	5061.2	-5.7	0.0	0.0	0.0	0.0
19	Social Justice	1	171.0	171.0	0.0	0.0	0.0	0.0	0.0
20	Defence Production	1	246.3	195.0	-20.8	0.0	0.0	0.0	0.0
21	DONER	1	151.3	151.3	0.0	0.0	0.0	0.0	0.0
22	Renewable Energy	1	271.9	366.1	34.7	1.0	271.9	366.1	34.7
Total		1952	2755676.5	3266261.9	18.5	463.0	894639.7	1428131.4	59.6

[^]- Cost Overrun= Anticipated Cost minus Original Cost

Annex 9

Annex 9: Sector-wise distribution - Extent of cost overruns with respect to Latest Approved Cost, as of 4 th Quarter end, January-March 2023-24 (Rs. crore)									
S. no	Sector	Project Count	Latest approved cost	Anticipated cost	Cost overrun	Projects with cost overruns [^]			
						Project Count	Latest approved cost	Anticipated cost	% increase
1	Atomic Energy	5	132558.0	136736.0	3.2	1.0	3492.0	7670.0	119.6
2	Civil Aviation	35	21882.9	24732.0	13.0	6.0	4188.9	7592.0	81.2
3	Coal	126	204588.6	207729.2	1.5	5.0	3903.2	7067.0	81.1
4	Finance	3	786.3	831.0	5.7	1.0	209.0	262.0	25.4
5	Mines	8	9434.0	9788.7	3.8	1.0	667.2	1022.0	53.2
6	Steel	13	12680.6	12680.6	0.0	0.0	0.0	0.0	0.0
7	Petroleum	161	468036.4	478590.8	2.3	5.0	47899.0	59886.0	25.0
8	Power	105	281570.5	327811.2	16.4	19.0	61604.7	107973.1	75.3
9	Health and Family Welfare	9	7696.5	7722.7	0.3	2.0	402.9	443.1	10.0
10	Railways	249	557287.7	685310.5	23.0	107.0	218068.4	352784.5	61.8
11	Road Transport and Highways	1130	903263.4	910325.6	0.8	122.0	115463.7	139198.6	20.6
12	Shipping and ports	1	4633.8	5061.2	9.2	1.0	4633.8	5061.2	9.2
13	Telecommunications	7	40229.6	40295.7	0.2	2.0	24729.8	24796.0	0.3
14	Urban Development	27	286057.0	309241.4	8.1	6.0	105641.6	128905.1	22.0
15	Water Resources	41	23420.5	69701.0	197.6	9.0	13784.9	60370.9	337.9
16	Social Justice	1	171.0	171.0	0.0	0.0	0.0	0.0	0.0
17	Defence Production	1	200.0	195.0	-2.5	0.0	0.0	0.0	0.0
18	Department of Higher Education	21	10414.5	10376.9	-0.4	1.0	392.5	446.4	13.7
19	Home Affairs	5	2946.0	2959.0	0.4	1.0	277.4	290.3	4.7
20	DPIIT	2	24857.0	25485.0	2.5	1.0	4773.0	5401.0	13.2
21	DONER	1	151.3	151.3	0.0	0.0	0.0	0.0	0.0
22	Renewable Energy	1	366.1	366.1	0.0	0.0	0.0	0.0	0.0
Total		1952	2993231.69	3266262	9.1	290	610132.14	909169.1	49.0

[^]- Cost Overrun= Anticipated Cost minus Latest approved Cost

Annex 10

Annex 10: Sector-wise distribution - Extent of time & cost overruns in projects with respect to original schedule as of 4 th Quarter end, January-March 2023-24 (Rs. Crore)										
S. no	Sector	No. of projects	Original cost	Anticipated cost	Cost overrun	Projects with time & cost overruns [^]				
						No. of projects	Original cost	Anticipated cost	% increase	Range in months
1	Atomic Energy	5	1,16,741.00	1,36,736.00	17.13	3	27,271.00	47,266.00	73.3	99- 171
2	Civil Aviation	35	21,483.03	24,732.01	15.12	6	3,932.14	7,410.00	88.4	16- 48
3	Coal	126	2,00,441.11	2,07,729.22	3.64	6	21,154.83	26,512.31	25.3	35- 87
4	Finance	3	786.27	831.04	5.69	0	0	0	0	0- 0
5	Mines	8	7,559.78	9,788.70	29.48	3	4,992.00	7,280.37	45.8	50- 58
6	Steel	13	11,827.60	12,680.57	7.21	2	2,635.21	3,488.18	32.4	14- 22
7	Petroleum	161	4,14,707.37	4,78,590.76	15.4	26	1,52,666.67	2,11,680.97	38.7	4- 143
8	Power	105	2,72,327.75	3,27,811.23	20.37	15	67,076.30	1,20,030.59	78.9	24- 193
9	Health and Family Welfare	9	7,327.02	7,722.73	5.4	4	2,024.13	2,434.84	20.3	8- 60
10	Railways	249	4,44,073.55	6,85,310.51	54.32	82	1,37,810.78	2,96,651.30	115.3	3- 261
11	Road Transport and Highways	1130	8,67,946.70	9,10,325.64	4.88	119	1,03,983.33	1,38,082.11	32.8	2- 123
12	Shipping and ports	1	5,369.18	5,061.15	-5.74	0	0	0	0	0- 0
13	Telecommunications	7	40,229.56	40,295.69	0.16	0	0	0	0	0- 0
14	Urban Development	27	2,83,820.79	3,09,241.35	8.96	3	35,558.77	40,506.27	13.9	3- 63
15	Water Resources	41	23,466.28	69,700.98	197.03	6	11,806.12	57,792.35	389.5	22- 51
16	Social Justice	1	170.99	170.99	0	0	0	0	0	0- 0
17	Defence Production	1	246.31	195	-20.83	0	0	0	0	0- 0
18	Department of Higher Education	21	9,846.15	10,376.91	5.39	4	1,344.71	1,567.74	16.6	22- 43
19	Home Affairs	5	2,025.73	2,958.98	46.07	3	1,659.44	2,592.69	56.2	34- 80
20	DPIIT	2	24,857.00	25,485.00	2.53	1	4,773.00	5,401.00	13.2	52- 52
21	DONER	1	151.33	151.33	0	0	0	0	0	0- 0
22	Renewable Energy	1	271.9	366.12	34.65	0	0	0	0	0- 0
Total		1952	2755676.4	3266261.91	18.53	283	578688.43	968696.72	67.4	

[^]- Cost Overrun= Anticipated Cost minus Latest approved Cost

\$-Time Overrun = Anticipated Date of Commissioning minus Latest Approved Date of Commissioning.

Annex 11

Annex 11: Sector-wise distribution: requiring review/sanctions of Revised Cost Estimate (RCE*), as of 4 th Quarter end, January-March 2023-24 (Project Count)								
S.no	Sector	Project Count	Mega		Major		Total	
			Anticipated Cost more than Latest Board Approved Cost or Original Cost)	FY 23-24 Expenditure more than Latest Board Approved Cost or Original Cost	Anticipated Cost more than Latest Board Approved Cost or Original Cost	FY 23-24 Expenditure more than Latest Board Approved Cost or Original Cost	Anticipated Cost more than Latest Board Approved Cost or Original Cost	FY 23-24 Expenditure more than Latest Board Approved Cost or Original Cost
1	Atomic Energy	5	1	3	0	0	1	3
2	Civil Aviation	35	2	1	4	7	6	8
3	Coal	126	1	0	4	1	5	1
4	Finance	3	0	0	1	1	1	1
5	Mines	8	1	1	0	0	1	1
6	Steel	13	0	0	0	0	0	0
7	Petroleum	161	3	0	2	2	5	2
8	Power	105	15	10	4	3	19	13
9	Health and Family Welfare	9	0	0	2	0	2	0
10	Railways	249	76	48	31	12	107	60
11	Road Transport and Highways	1130	52	16	70	54	122	70
12	Shipping and ports	1	1	0	0	0	1	0
13	Telecommunications	7	1	1	1	0	2	1
14	Urban Development	27	6	6	0	0	6	6
15	Water Resources	41	1	1	8	4	9	5
16	Social Justice	1	0	0	0	0	0	0
17	Defence Production	1	0	0	0	0	0	0
18	Department of Higher Education	21	0	0	1	4	1	4
19	Home Affairs	5	0	0	1	0	1	0
20	DPIIT	2	1	0	0	0	1	0
21	DONER	1	0	0	0	0	0	0
22	Renewable Energy	1	0	0	0	0	0	0
Total		1952	161	87	129	88	290	175

**RCE: Latest of "Latest Board Approved Cost" and "Original Cost", as reported by Line Ministries*



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
