



Government of India
Ministry of Statistics and
Programme Implementation




OCMS
Ministry of Statistics & Programme Implementation

462nd FLASH REPORT ON

Synopsis Central Sector Infrastructure Projects

(Rs. 150 crore & above)
(Part - I)*

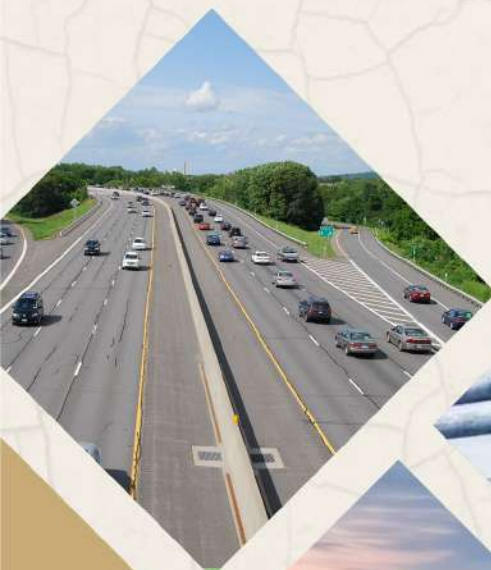

April 2024

*Refer Part-II for tables comprising detailed project listing.



www.mospi.gov.in



@GoIStats

Flash Report – Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects
(1838, Rs. 2764246.5 crore)



Note: all Indicated legends are in format (Project count, Original Cost)

* Mega Project if anticipated cost $\geq$ Rs. 1000 crore

* Major Project if anticipated cost < Rs. 1000 crore

Overview

- As of 30 April 2024 - **1838 Ongoing projects**
- As of 31 March 2024 - **1873 Ongoing projects**

During April 2024

- 64 Projects offloaded – **61 Completed and 3 Dropped/ Frozen/ downgraded***
- 29 Projects on-boarded - **Newly added/ elevated#**

Note:

*reported Anticipated cost less than Rs. 150 crore

#reported Anticipated cost more than Rs. 150 crore

Cost Details (Rs crore)




As of 30 April 2024

Total expenditure - Rs. 1,692,997.5 crore, which is


- 51 per cent of the total anticipated completion cost &
- 61.3 per cent of the original cost.

Sectoral Comparison: Project count & Anticipated Cost

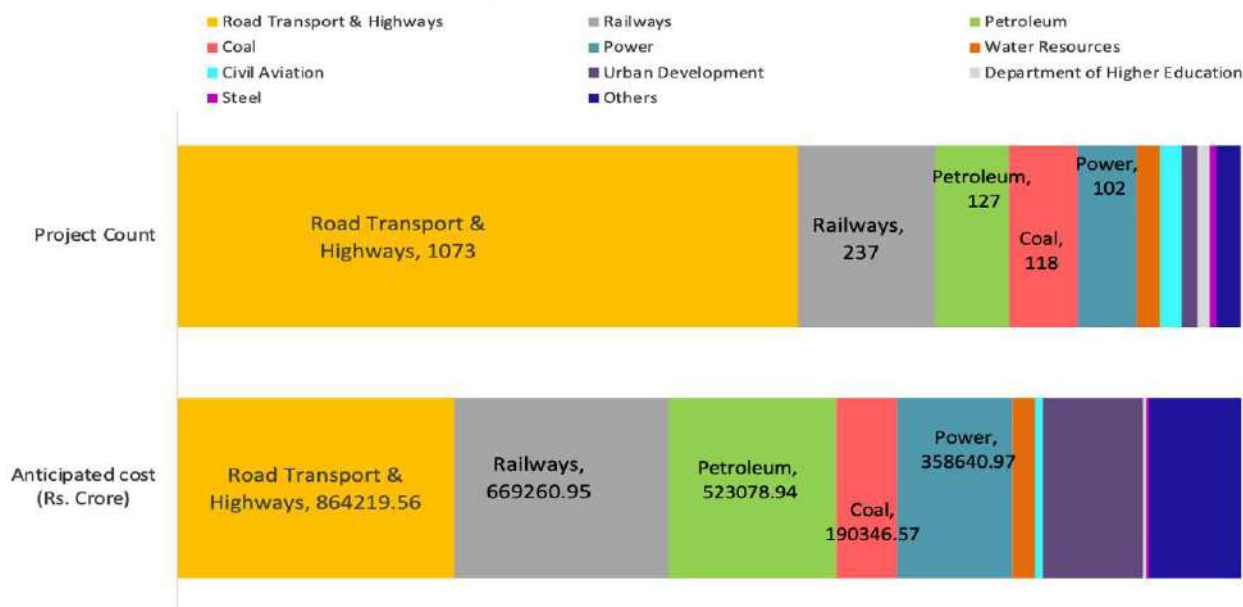

Note: Others include Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, Social Justice

Extent of Cost Overrun (%) & Project count

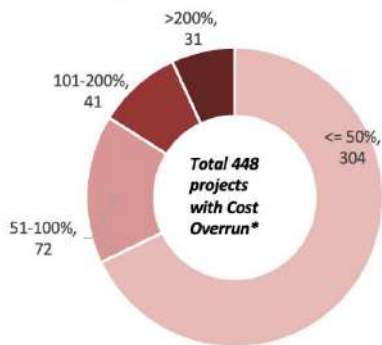

* Anticipated cost exceeds the original sanctioned cost

Project Count distribution as per schedule



*(Category, Project Count)

Cost overrun (COR)

- Of total 1838 ongoing projects,
 - 448 projects – *slippage with respect to Original cost* (COR- Rs. 5,75,309.3 crore and COR%- 62.2 per cent)
 - 288 projects – *slippage with respect to Latest approved cost* (COR- Rs. 2,89,329.97 crore and COR%- 48.2 per cent)
- Major 5 Sectors, as per Project count with COR

Sector	Project Count	Project count with COR	COR * (%)
Road Transport & Highways	1073	201	23.72
Railways	237	139	126.5
Petroleum	127	25	34.6
Civil Aviation	37	12	58.4
Coal	118	8	25.03


*COR(%) = (Anticipated Cost- Original Cost)*100/(Original Cost)

Time overrun (TOR)

- Of total 1838 ongoing projects,
 - 792 projects – *delayed with respect to Original date of completion*
 - 514 projects - *delayed with respect to Latest approved completion date*
- Average time overrun: 35.4 months.
- Major 5 Sectors, as per Project count with TOR

Sector	Project Count	Project count with TOR	TOR range (months)
Road Transport & Highways	1073	428	1-186
Railways	237	106	3-261
Petroleum	127	74	1-143
Coal	118	56	12-159
Power	102	44	1-193

Extent of Time Overrun (in months) & Project count

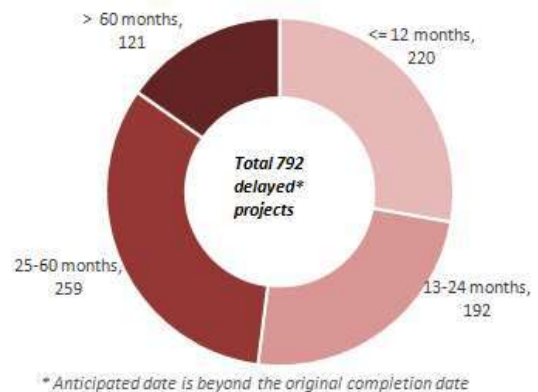

* Anticipated date is beyond the original completion date

Reasons of Cost and Time Overrun

- Land Acquisition
- Environmental clearance
- Financial issues
- Contractual/internal issues
- Manpower shortage
- Litigation issues

Cost Overrun (COR) & Time overrun (TOR)

- Of total 1838 Ongoing Projects, 275 projects have both time and cost overrun
- COR of Rs. 3,82,274.7 crore and TOR of 1-261 months
- Major 5 Sectors, as per project count with (COR & TOR)

Sector	Project Count	Project count with TOR	TOR range (months)	COR (%)
Road Transport & Highways	1073	124	1-186	27.3
Railways	237	79	3-261	115.9
Petroleum	127	21	4-143	39
Power	102	12	12-193	94.5
Coal	118	6	40-87	76

Projects requiring examination of revised cost estimate

164 of 1838 projects - **as the expenditure has exceeded the approved (Latest approved/ Original) cost.**



Projects requiring focused attention

54 of 1838 projects – **with TOR (>50 months) and COR (>50%), contributing nearly 43.39% of the total COR and 21.34% of the total TOR.**



Note:

This report is as of April 2024, based on the (non-exhaustive) list of projects and information as reported by Line ministries/implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th May 2024.



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
